

HKBCF Infrastructure (Western Portion) - Monthly Progress 36 - Three Month Rolling Programme

Activity ID	Activity Name	Original Duration	% Comp	2017				
				Jul	Aug	Sep	Oct	
HKBCF Infrastructure (Western Portion) - Monthly Progress 36								
Bridge Structure								
Bridge 3								
Pier & Abutment								
B3-0090	B3 - Pier & Abutment P305, P304 (2 nos)	14	100%	■ 22-Jul-17, B3 - Pier & Abutment P305, P304 (2 nos)				
Deck 1 (P305-P304)								
B3-0100	B3 - Concrete base portion (P305-P304)	1	100%	■ 24-Jul-17, B3 - Concrete base portion (P305-P304)				
B3-0120	B3 - Concrete top slab (P305-P304)	1	100%	■ 24-Jul-17, B3 - Concrete top slab (P305-P304)				
Deck 2 (P304-P303)								
B3-0230	B3 - Concrete base portion (P304-P303)	1	100%	■ 24-Jul-17, B3 - Concrete base portion (P304-P303)				
B3-0250	B3 - Concrete top slab (P304-P303)	1	100%	■ 24-Jul-17, B3 - Concrete top slab (P304-P303)				
Deck 3 (P303-P302)								
B3-0330	B3 - Concrete base portion (P303-P302)	1	100%	■ 25-Jul-17, B3 - Concrete base portion (P303-P302)				
B3-0350	B3 - Concrete top slab (P303-P302)	1	100%	■ 25-Jul-17, B3 - Concrete top slab (P303-P302)				
Deck 4 (P302-A301)								
B3-0430	B3 - Concrete base portion (P302-A301)	1	100%	■ 27-Jul-17, B3 - Concrete base portion (P302-A301)				
B3-0450	B3 - Concrete top slab (P302-A301)	1	100%	■ 26-Jul-17, B3 - Concrete top slab (P302-A301)				
Bridge 2N								
Deck 1 (P211-P209)								
B2-0330	B2N - Concrete base portion (P211-P209)	1	100%	■ 22-Jul-17, B2N - Concrete base portion (P211-P209)				
B2-0350	B2N - Concrete top slab (P211-P209)	1	100%	■ 24-Jul-17, B2N - Concrete top slab (P211-P209)				
Deck 2 (P212-P211)								
B2-1950	B2N - Concrete base portion (P212-P211)	1	0%	■ 25-Jul-17, B2N - Concrete base portion (P212-P211)				
B2-1970	B2N - Concrete top slab (P212-P211)	1	0%	■ 25-Jul-17, B2N - Concrete top slab (P212-P211)				
Deck 3 (P213-P212)								
B2-0430	B2N - Concrete base portion (P213-P212)	1	100%	■ 27-Jul-17, B2N - Concrete base portion (P213-P212)				
B2-0450	B2N - Concrete top slab (P213-P212)	1	100%	■ 28-Jul-17, B2N - Concrete top slab (P213-P212)				
Deck 4 (P214-A215)								
B2-0530	B2N - Concrete base portion (P214-A215)	1	100%	■ 29-Jul-17, B2N - Concrete base portion (P214-A215)				
B2-0550	B2N - Concrete top slab (P214-A215)	1	100%	■ 31-Jul-17, B2N - Concrete top slab (P214-A215)				
Deck 5 (P208-P209)								
B2-2030	B2N - Concrete base portion (P208-P209)	1	0%	■ 25-Jul-17, B2N - Concrete base portion (P208-P209)				
B2-2040	B2N - Concrete top slab (P208-P209)	1	0%	■ 26-Jul-17, B2N - Concrete top slab (P208-P209)				
Deck 6 (P206-P207)								
B2-2630	B2N - Concrete base portion (P206-P207)	1	100%	■ 27-Jul-17, B2N - Concrete base portion (P206-P207)				
B2-2650	B2N - Concrete top slab (P206-P207)	1	100%	■ 28-Jul-17, B2N - Concrete top slab (P206-P207)				
Deck 7 (P206-P205)								
B2-0730	B2N - Concrete base portion (P206-P205)	1	100%	■ 29-Jul-17, B2N - Concrete base portion (P206-P205)				
B2-0750	B2N - Concrete top slab (P206-P205)	1	100%	■ 31-Jul-17, B2N - Concrete top slab (P206-P205)				
Deck 8 (P204-P203)								
B2-0830	B2N - Concrete base portion (P204-P203)	1	100%	■ 1-Aug-17, B2N - Concrete base portion (P204-P203)				
B2-0850	B2N - Concrete top slab (P204-P203)	1	100%	■ 2-Aug-17, B2N - Concrete top slab (P204-P203)				
Deck 9 (P202-A201)								
B2-1930	B2N - Concrete base portion (P202-A201)	1	100%	■ 3-Aug-17, B2N - Concrete base portion (P202-A201)				
B2-1950	B2N - Concrete top slab (P202-A201)	1	100%	■ 4-Aug-17, B2N - Concrete top slab (P202-A201)				
Bridge 2S								
Deck 1 (P211-P209)								
B2-1230	B2S - Concrete base portion (P211-P209)	1	100%	■ 22-Jul-17, B2S - Concrete base portion (P211-P209)				
B2-1250	B2S - Concrete top slab (P211-P209)	1	100%	■ 24-Jul-17, B2S - Concrete top slab (P211-P209)				
Deck 2 (P212-P211)								
B2-2090	B2S - Concrete base portion (P212-P211)	1	0%	■ 25-Jul-17, B2S - Concrete base portion (P212-P211)				
B2-2110	B2S - Concrete top slab (P212-P211)	1	0%	■ 26-Jul-17, B2S - Concrete top slab (P212-P211)				
Deck 3 (P213-P212)								
B2-1270	B2S - Concrete base portion (P213-P212)	1	100%	■ 27-Jul-17, B2S - Concrete base portion (P213-P212)				
B2-1290	B2S - Concrete top slab (P213-P212)	1	100%	■ 29-Jul-17, B2S - Concrete top slab (P213-P212)				
Deck 4 (P214-A215)								
B2-1340	B2S - Concrete base portion (P214-A215)	1	100%	■ 29-Jul-17, B2S - Concrete base portion (P214-A215)				
B2-1360	B2S - Concrete top slab (P214-A215)	1	100%	■ 31-Jul-17, B2S - Concrete top slab (P214-A215)				
Deck 5 (P208-P209)								
B2-2160	B2S - Concrete base portion (P208-P209)	1	0%	■ 25-Jul-17, B2S - Concrete base portion (P208-P209)				
B2-2180	B2S - Concrete top slab (P208-P209)	1	0%	■ 26-Jul-17, B2S - Concrete top slab (P208-P209)				
Deck 6 (P206-P207)								

Remaining Level of Effort

Actual Work

Critical Remaining ...

Actual Level of Effort

Remaining Work

Milestone

Page 1 of 6

Date	Revision	Checked	Approved
22-Jul-17	Three Month Rolling Programme		

■ Remaining Level of Effort
 ■ Actual Work
 ■ Critical Remaining ...
■ Actual Level of Effort
 ■ Remaining Work
 ◆ Milestone

Date	Revision	Checked	Approved
22-Jul-17	Three Month Rolling Programme		

HKBCF Infrastructure (Western Portion) - Monthly Progress 36 - Three Month Rolling Programme

Activity ID	Activity Name	Original Duration	% Comp.	2017			
				Jul	Aug	Sep	Oct
B2-1410	B25 - Concrete base portion (P206-P207)	1	100%		27-Jul-17, B25 - Concrete base portion (P206-P207)		
B2-1430	B25 - Concrete top slab (P206-P207)	1	100%		28-Jul-17, B25 - Concrete top slab (P206-P207)		
Deck 7 (P206-P205)							
B2-1480	B25 - Concrete base portion (P206-P205)	1	100%		29-Jul-17, B25 - Concrete base portion (P206-P205)		
B2-1500	B25 - Concrete top slab (P206-P205)	1	100%		31-Jul-17, B25 - Concrete top slab (P206-P205)		
Deck 8 (P204-P203)							
B2-1550	B25 - Concrete base portion (P204-P203)	1	100%		1-Aug-17, B25 - Concrete base portion (P204-P203)		
B2-1570	B25 - Concrete top slab (P204-P203)	1	100%		3-Aug-17, B25 - Concrete top slab (P204-P203)		
Deck 9 (P202-A201)							
B2-1620	B25 - Concrete base portion (P202-A201)	1	100%		3-Aug-17, B25 - Concrete base portion (P202-A201)		
B2-1640	B25 - Concrete top slab (P202-A201)	1	100%		4-Aug-17, B25 - Concrete top slab (P202-A201)		
Bridge 1							
Deck 4b (P102-P103)							
B1-440	B1 - Concrete base portion (P102-A101)	1	100%		22-Jul-17, B1 - Concrete base portion (P102-A101)		
B1-460	B1 - Concrete top slab (P102-A101)	1	100%		24-Jul-17, B1 - Concrete top slab (P102-A101)		
Bridge 4							
Pile Cap							
B4-0800	B4 - Pile Cap P432, A401 (2 nos)	21	100%		3-Aug-17, B4 - Pile Cap P432, A401 (2 nos)		
Pier & Abutment							
B4-0900	B4 - Pier & Abutment P402, A401 (2 nos)	14	100%		4-Aug-17, B4 - Pier & Abutment P402, A401 (2 nos)		
B4-0900	B4 - Pier & Abutment P403, P404 (2 nos)	14	100%		24-Jul-17, B4 - Pier & Abutment P403, P404 (2 nos)		
B4-0970	B4 - Pier & Abutment P405, P406 (2 nos)	14	100%		22-Jul-17, B4 - Pier & Abutment P405, P406 (2 nos)		
Deck 1 (P405-P406)							
B4-130	B4 - Concrete base portion (P405-P406)	1	100%		24-Jul-17, B4 - Concrete base portion (P405-P406)		
B4-150	B4 - Concrete top slab (P405-P406)	1	100%		25-Jul-17, B4 - Concrete top slab (P405-P406)		
Deck 2 (P404-P403)							
B4-200	B4 - Concrete base portion (P404-P403)	1	100%		26-Jul-17, B4 - Concrete base portion (P404-P403)		
B4-220	B4 - Concrete top slab (P404-P403)	1	100%		27-Jul-17, B4 - Concrete top slab (P404-P403)		
Deck 3 (P402-A401)							
B4-270	B4 - Concrete base portion (P402-A401)	1	100%		5-Aug-17, B4 - Concrete base portion (P402-A401)		
B4-290	B4 - Concrete top slab (P402-A401)	1	100%		7-Aug-17, B4 - Concrete top slab (P402-A401)		
Bridge 7							
Pile Cap							
B7-1950	B7 - Pile Cap P702, A701 (2 nos)	21	100%		25-Jul-17, B7 - Pile Cap P702, A701 (2 nos)		
B7-1930	B7 - Pile Cap P703, P704, P705 (3 nos)	21	100%		22-Jul-17, B7 - Pile Cap P703, P704, P705 (3 nos)		
B7-1940	B7 - Pile Cap P706, A707 (2 nos)	21	100%		24-Jul-17, B7 - Pile Cap P706, A707 (2 nos)		
Pier & Abutment							
B7-1960	B7 - Pier & Abutment P703, P704, P705 (3 nos)	14	100%		24-Jul-17, B7 - Pier & Abutment P703, P704, P705 (3 nos)		
B7-1970	B7 - Pier & Abutment P706, A707 (2 nos)	14	100%		25-Jul-17, B7 - Pier & Abutment P706, A707 (2 nos)		
Deck 1 (P705-P706)							
B7-1120	B7 - Concrete base portion (P705-P706)	1	100%		25-Jul-17, B7 - Concrete base portion (P705-P706)		
B7-1140	B7 - Concrete top slab (P705-P706)	1	100%		26-Jul-17, B7 - Concrete top slab (P705-P706)		
Deck 2 (P706-A707)							
B7-1180	B7 - Concrete base portion (P706-A707)	1	100%		27-Jul-17, B7 - Concrete base portion (P706-A707)		
B7-1210	B7 - Concrete top slab (P706-A707)	1	100%		28-Jul-17, B7 - Concrete top slab (P706-A707)		
Deck 3 (P702-A701)							
B7-1290	B7 - Concrete base portion (P702-A701)	1	100%		29-Jul-17, B7 - Concrete base portion (P702-A701)		
B7-1280	B7 - Concrete top slab (P702-A701)	1	100%		31-Jul-17, B7 - Concrete top slab (P702-A701)		
Bridge 8							
Pile Cap							
B8-1050	B8 - Pile Cap P802, A801 (2 nos)	21	100%		29-Jul-17, B8 - Pile Cap P802, A801 (2 nos)		
B8-1030	B8 - Pile Cap P803, P804 (2 nos)	21	100%		22-Jul-17, B8 - Pile Cap P803, P804 (2 nos)		
B8-1040	B8 - Pile Cap P805, A806 (2 nos)	21	100%		24-Jul-17, B8 - Pile Cap P805, A806 (2 nos)		
Pier & Abutment							
B8-1080	B8 - Pier & Abutment P802, A801 (2 nos)	14	100%		31-Jul-17, B8 - Pier & Abutment P802, A801 (2 nos)		
B8-1090	B8 - Pier & Abutment P803, P804 (2 nos)	14	100%		24-Jul-17, B8 - Pier & Abutment P803, P804 (2 nos)		
B8-1070	B8 - Pier & Abutment P805, A806 (2 nos)	14	100%		25-Jul-17, B8 - Pier & Abutment P805, A806 (2 nos)		
Deck 1 (P803-P804)							
B8-1120	B8 - Concrete base portion (P803-P804)	1	100%		25-Jul-17, B8 - Concrete base portion (P803-P804)		
B8-1140	B8 - Concrete top slab (P803-P804)	1	100%		26-Jul-17, B8 - Concrete top slab (P803-P804)		
Deck 2 (P805-A806)							

■ Remaining Level of Effort
 ■ Actual Work
 ■ Critical Remaining ...
■ Actual Level of Effort
 ■ Remaining Work
 ◆ Milestone

Date	Revision	Checked	Approved
22-Jul-17	Three Month Rolling Programme		


HKBCF Infrastructure (Western Portion) - Monthly Progress 36 - Three Month Rolling Programme

Activity ID	Activity Name	Original Duration	% Comp.	2017			
				Jul	Aug	Sep	Oct
B6-1100	B6 - Concrete base portion (P605-A606)	1	100%		27-Jul-17, B6 - Concrete base portion (P605-A606)		
B6-1210	B6 - Concrete top slab (P605-A606)	1	100%		28-Jul-17, B6 - Concrete top slab (P605-A606)		
Deck 3 (P602-A601)							
B6-1200	B6 - Concrete base portion (P602-A601)	1	100%		1-Aug-17, B6 - Concrete base portion (P602-A601)		
B6-1060	B6 - Concrete top slab (P602-A601)	1	100%		2-Aug-17, B6 - Concrete top slab (P602-A601)		
Bridge 4							
Pile Cap							
B6-1060	B6 - Pile cap P602-P603 (2 nos)	14	100%		22-Jul-17, B6 - Pile cap P602-P603 (2 nos)		
B6-1050	B6 - Pile cap P604, A605 (2 nos)	21	100%		24-Jul-17, B6 - Pile cap P604, A605 (2 nos)		
Pier & Abutment							
B6-1080	B6 - Pier & Abutment P602-P603 (2 nos)	14	100%		24-Jul-17, B6 - Pier & Abutment P602-P603 (2 nos)		
B6-1090	B6 - Pier & Abutment P604, A605 (2 nos)	14	100%		25-Jul-17, B6 - Pier & Abutment P604, A605 (2 nos)		
Deck 1 (A601-P602)							
B6-1150	B6 - Concrete base portion (A601-P602)	1	100%		25-Jul-17, B6 - Concrete base portion (A601-P602)		
B6-1170	B6 - Concrete top slab (A601-P602)	1	100%		26-Jul-17, B6 - Concrete top slab (A601-P602)		
Deck 2 (P602-P603)							
B6-1220	B6 - Concrete base portion (P602-P603)	1	100%		27-Jul-17, B6 - Concrete base portion (P602-P603)		
B6-1240	B6 - Concrete top slab (P602-P603)	1	100%		28-Jul-17, B6 - Concrete top slab (P602-P603)		
Deck 3 (P603-P604)							
B6-1200	B6 - Concrete base portion (P603-P604)	1	100%		29-Jul-17, B6 - Concrete base portion (P603-P604)		
B6-1310	B6 - Concrete top slab (P603-P604)	1	100%		31-Jul-17, B6 - Concrete top slab (P603-P604)		
Deck 4 (P604-A605)							
B6-1300	B6 - Concrete base portion (P604-A605)	1	100%		1-Aug-17, B6 - Concrete base portion (P604-A605)		
B6-1380	B6 - Concrete top slab (P604-A605)	1	100%		2-Aug-17, B6 - Concrete top slab (P604-A605)		
Bridge 5							
Pile Cap							
B5-1540	B5 - Pile Cap P502, A503 (2 nos)	14	100%		22-Jul-17, B5 - Pile Cap P502, A503 (2 nos)		
B5-1600	B5 - Pile Cap P504, P505 (2 nos)	14	100%		22-Jul-17, B5 - Pile Cap P504, P505 (2 nos)		
B5-1670	B5 - Pile Cap P507, A508 (2 nos)	21	100%		24-Jul-17, B5 - Pile Cap P507, A508 (2 nos)		
Pier & Abutment							
B5-1080	B5 - Pier & Abutment P502, A503 (2 nos)	14	100%		24-Jul-17, B5 - Pier & Abutment P502, A503 (2 nos)		
B5-1100	B5 - Pier & Abutment P505, P504 (2 nos)	14	100%		24-Jul-17, B5 - Pier & Abutment P505, P504 (2 nos)		
B5-1110	B5 - Pier & Abutment P507, A508 (2 nos)	14	100%		25-Jul-17, B5 - Pier & Abutment P507, A508 (2 nos)		
Deck 1 (P501-P502)							
B5-1420	B5 - Concrete base portion (P501-P502)	1	0%		26-Jul-17, B5 - Concrete base portion (P501-P502)		
B5-1450	B5 - Concrete top slab (P501-P502)	1	0%		27-Jul-17, B5 - Concrete top slab (P501-P502)		
Deck 2 (P502-A503)							
B5-1500	B5 - Concrete base portion (P502-A503)	1	0%		28-Jul-17, B5 - Concrete base portion (P502-A503)		
B5-1520	B5 - Concrete top slab (P502-A503)	1	0%		29-Jul-17, B5 - Concrete top slab (P502-A503)		
Deck 3 (P503b-P504)							
B5-1570	B5 - Concrete base portion (P503b-P504)	1	0%		26-Jul-17, B5 - Concrete base portion (P503b-P504)		
B5-1590	B5 - Concrete top slab (P503b-P504)	1	0%		27-Jul-17, B5 - Concrete top slab (P503b-P504)		
Deck 4 (P505-P506)							
B5-1640	B5 - Concrete base portion (P505-P506)	1	100%		28-Jul-17, B5 - Concrete base portion (P505-P506)		
B5-1660	B5 - Concrete top slab (P505-P506)	1	100%		29-Jul-17, B5 - Concrete top slab (P505-P506)		
Deck 5 (P507-P508)							
B6-1710	B6 - Concrete base portion (P507-P508)	1	100%	19-Jul-17, A	31-Jul-17, B6 - Concrete base portion (P507-P508)		
B6-1720	B6 - Top slab rebar (P507-P508)	5	100%	20-Jul-17, A	3-Aug-17, B6 - Top slab rebar (P507-P508)		
Auxiliary Structure							
Retaining Wall, Slope & Earth Works							
Bridge 2M							
B2-1670	Retaining Wall RW-1 (Bay 3)	21	100%	8-Jul-17, A	15-Aug-17, Retaining Wall RW-1 (Bay 3)		
Bridge 6							
B6-2090	Retaining Wall WB-1 (Bay 1)	21	100%	21-Jul-17, A	25-Aug-17, Retaining Wall WB-1 (Bay 1)		
B6-2070	Retaining Wall WB-1 (Bay 3)	21	100%	21-Jul-17, A	25-Aug-17, Retaining Wall WB-1 (Bay 3)		
Bridge 5							
B5-2020	Retaining Wall WS-1 (Bay 1)	21	100%	7-Jul-17, A	8-Aug-17, Retaining Wall WS-1 (Bay 1)		
B5-2170	Retaining Wall WS-2 (Bay 7)	21	100%	15-Jul-17, A	7-Sep-17, Retaining Wall WS-2 (Bay 7)		
Slope & Earth Works at Bridge Abutment							
B2-1760	Slope & earth works - C2-S3 & C2-S4 at B3	35	0%		5-Aug-17, Slope & earth works - C2-S3 & C2-S4 at B3		
B2-1790	Slope & earth works - RW1 & C2-S1	42	100%	8-Jul-17, A	9-Sep-17, Slope & earth works - RW1 & C2-S1		


■ Remaining Level of Effort
 ■ Actual Work
 ■ Critical Remaining ...
■ Actual Level of Effort
 ■ Remaining Work
 ◆ Milestone

Date	Revision	Checked	Approved
22-Jul-17	Three Month Rolling Programme		


HKBCF Infrastructure (Western Portion) - Monthly Progress 36 - Three Month Rolling Programme

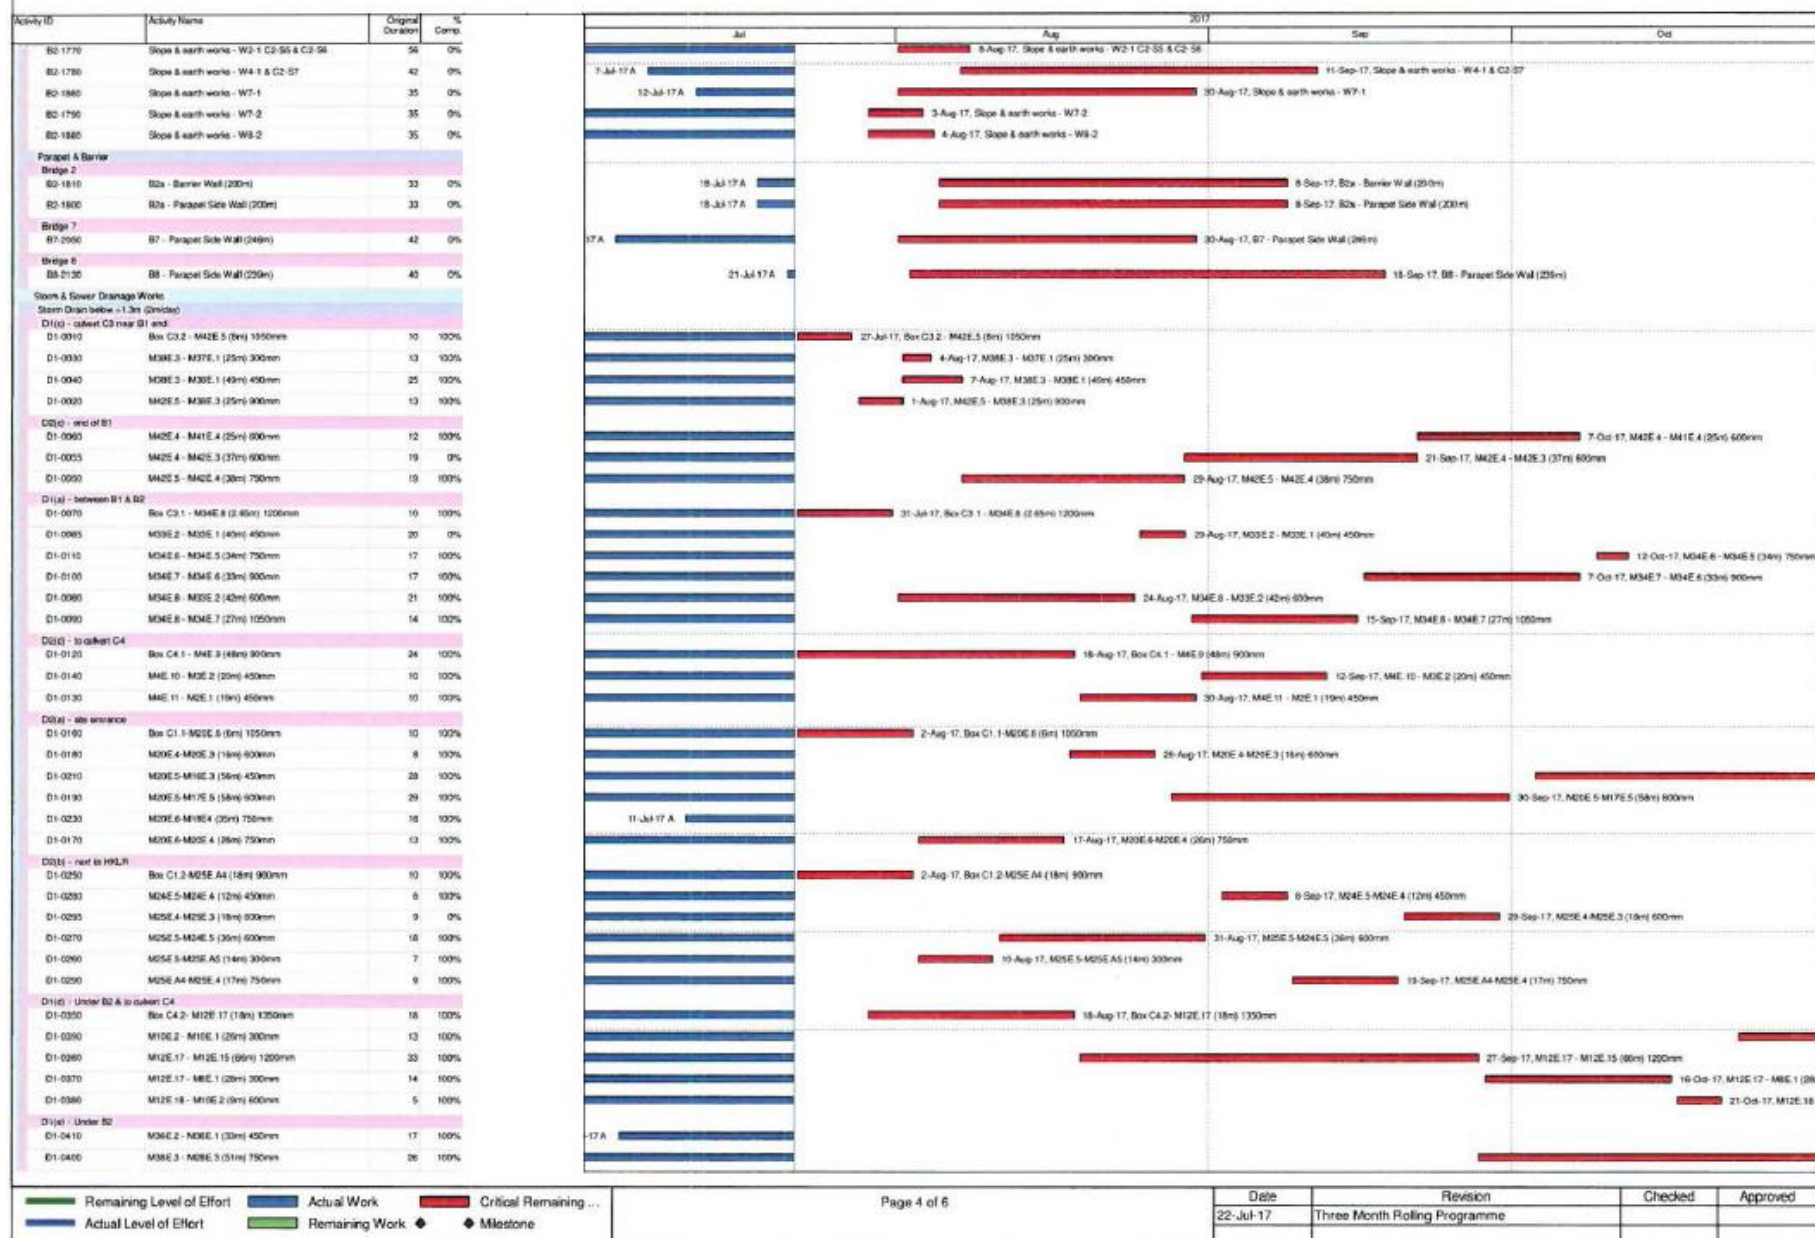

HKBCF Infrastructure (Western Portion) - Monthly Progress 36 - Three Month Rolling Programme

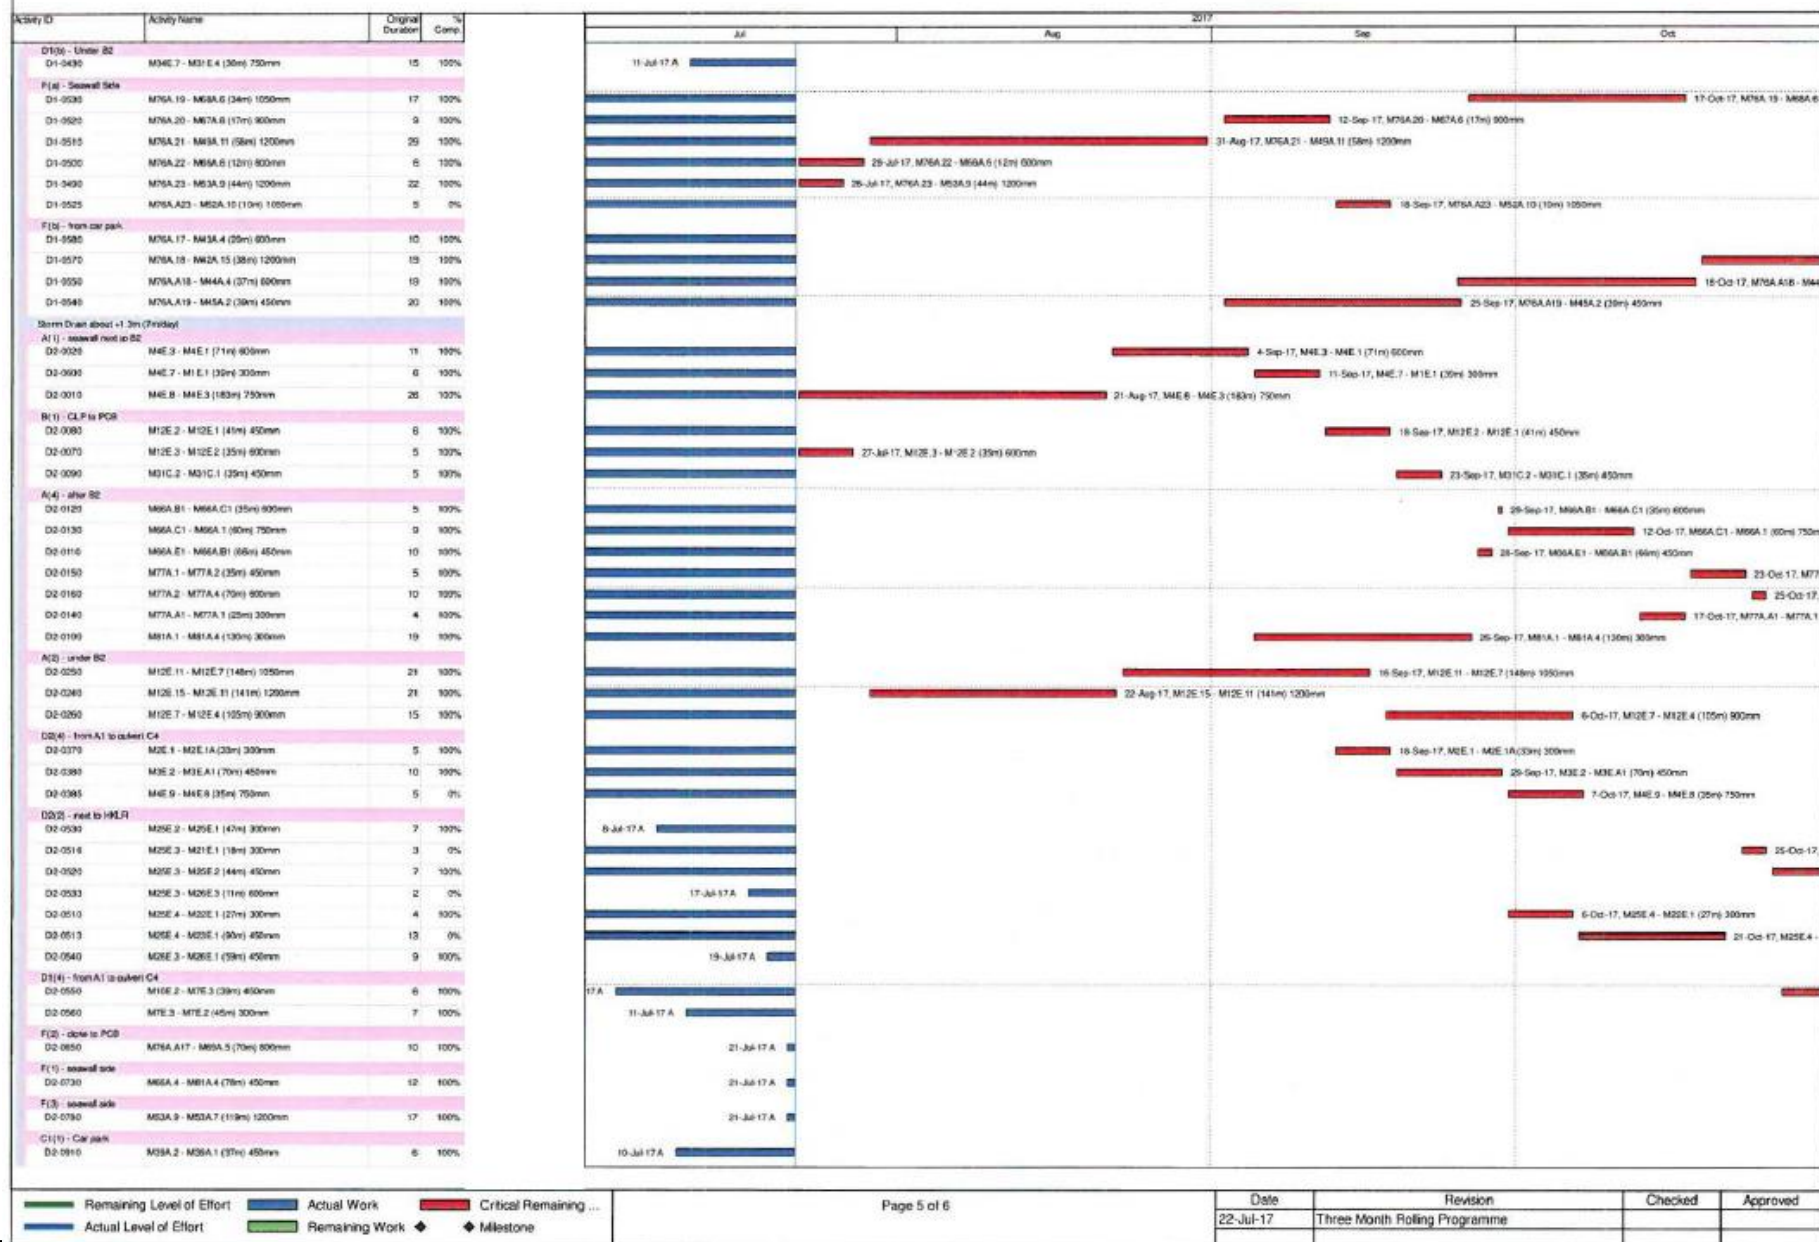

HKBCF Infrastructure (Western Portion) - Monthly Progress 36 - Three Month Rolling Programme

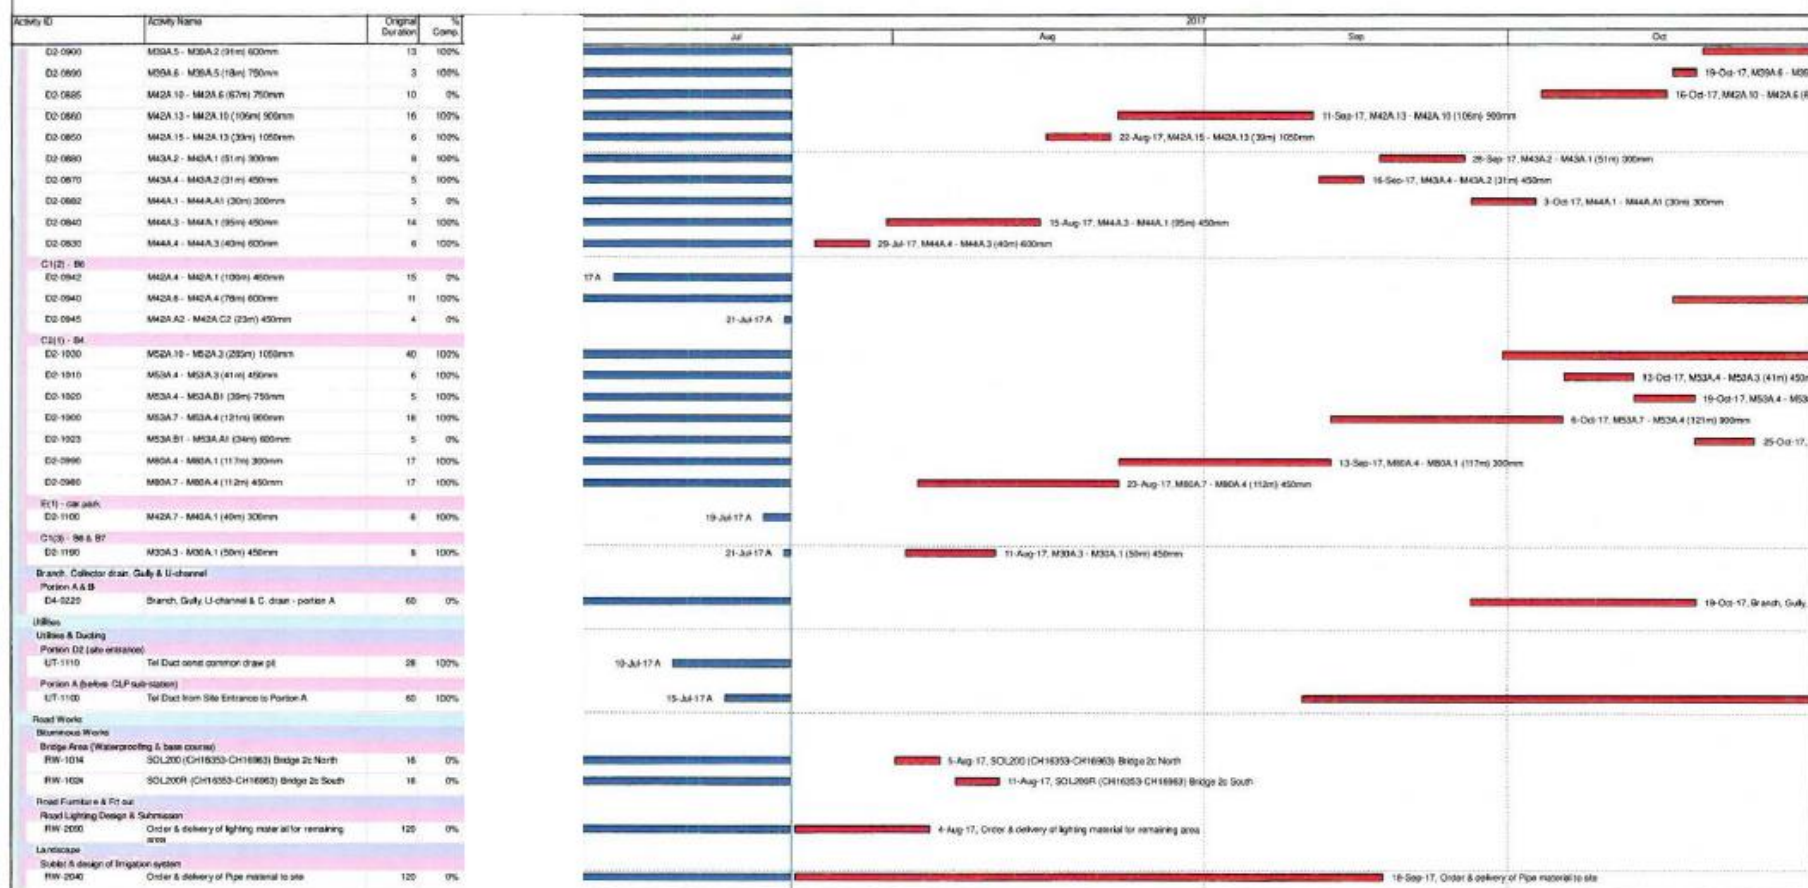

■ Remaining Level of Effort
 ■ Actual Work
 ■ Critical Remaining ...
■ Actual Level of Effort
 ■ Remaining Work
 ◆ Milestone
