


Activity ID	Activity Name	Original Duration	Start	Finish															
HY/2014/05 HKMZB HKBCF - Remaining Ancillary Buildings ar					132	27-Jun-16 A	06-Dec-16												
GENERAL/PRELIMINARIES					15	17-Jul-16 A	16-Aug-16												
Salient Key Dates and Milestones					15	17-Jul-16 A	16-Aug-16												
Commencement					15	17-Jul-16 A	16-Aug-16												
SECTION VIII		Section subject to Excision Section VIII - (Day 200) Building 044 and 045	0	17-Jul-16 A															
SECTION IX		Section subject to Excision Section IX - (Day 200) Building 050 (H1)	0	17-Jul-16 A															
SECTION X		Section subject to Excision Section X - (Day 200) Building 050 (H2)	0	18-Jul-16 A															
SECTION XI		Section subject to Excision Section XI - (Day 200) Building 050 (A1)	0	18-Jul-16 A															
SECTION XII		Section subject to Excision Section XII - (Day 200) Building 050 (A2)	0	18-Jul-16 A															
SECTION XIII		Section subject to Excision Section XIII - (Day 230) Landscaping Works	0	16-Aug-16*															
CONSTRUCTION					132	27-Jun-16 A	06-Dec-16												
Building 021 - C&ED Dangerous Goods Store					83	01-Aug-16	08-Nov-16												
RAB-21-0100		Possession of Portion G2 - II Exercised (Possession date assumed)	0	01-Aug-16*															
Raft					67	01-Aug-16	20-Oct-16												
RAB-21-0118		021 - PLT & CPT	14	01-Aug-16	16-Aug-16														
RAB-21-0120		021 - Construct Raft Foundations and Base Slab	18	28-Sep-16	20-Oct-16														
Structure					16	21-Oct-16	08-Nov-16												
RAB-21-0140		021 - Construct Supporting Columns to +11mPD GL3-4	8	21-Oct-16	29-Oct-16														
RAB-21-2230		021 - Construct External Wall to +11mPD GL3-4	8	31-Oct-16	08-Nov-16														
RAB-21-2260		021 - Construct Supporting Columns to +11mPD GL1-2	8	31-Oct-16	08-Nov-16														
Building 022 - Customs Detective Dog Base Building					85	01-Aug-16	10-Nov-16												
RAB-22-0100		Possession of Portion G3 - II Exercised	0	01-Aug-16*															
Excavation					31	01-Aug-16	05-Sep-16												
RAB-22-0118		022 - PLT & CPT	14	01-Aug-16	16-Aug-16														
RAB-22-0120		022 - Open cut excavation down to formation level (1047m³) (Incl 021)	5	17-Aug-16	22-Aug-16														
RAB-22-0130		022 - Underground Utilities/Temp Drainage (Incl 021)	12	23-Aug-16	05-Sep-16														
Raft Foundations					54	06-Sep-16	10-Nov-16												
RAB-22-0140		022 - Construct Raft Foundation and Baseslab North	18	06-Sep-16	27-Sep-16														
RAB-22-0260		022 - Construct Raft Foundations and Baseslab South	18	21-Sep-16	13-Oct-16														
RAB-22-0190		022 - Construct Raft Foundations and Baseslab Middle - Shrinkage Pour	18	21-Oct-16	10-Nov-16														
Structure					34	28-Sep-16	08-Nov-16												
External Walls					28	28-Sep-16	01-Nov-16												
RAB-22-0230		022 - Construct External Walls and Support Columns to +11.00mPD (N)	16	28-Sep-16	18-Oct-16														
RAB-22-0390		022 - Construct External Walls and Support Columns to +11.00mPD (S)	16	14-Oct-16	01-Nov-16														
Roof Slab					18	19-Oct-16	08-Nov-16												
North Structure					18	19-Oct-16	08-Nov-16												
RAB-22-0270		022 - Construct R/F Suspended Slab at +11.00mPD Bay 1 (240m³) (Approx 36m³)	18	19-Oct-16	08-Nov-16														
South Structure					18	19-Oct-16	08-Nov-16												
RAB-22-0430		022 - Construct R/F Suspended Slab at +11.00mPD Bay 1 (240m³) (Approx 36m³)	18	19-Oct-16	08-Nov-16														
ABWF/E&M					28	28-Sep-16	01-Nov-16												
Specialist Installations					28	28-Sep-16	01-Nov-16												
Window Wall					8	28-Sep-16	07-Oct-16												
RAB-23-7090		022 - Install Window Wall Cast In Items (North)	8	28-Sep-16	07-Oct-16														
Dog Swimming Pool					16	14-Oct-16	01-Nov-16												
RAB-22-0160		022 - Setting out of Dog Swimming Pool	2	14-Oct-16	15-Oct-16														
RAB-22-0170		022 - Excavate for Dog Swimming Pool	2	17-Oct-16	18-Oct-16														
RAB-22-0200		022 - RC Structure	12	19-Oct-16	01-Nov-16														
Building 023 - C&ED Outbound Cargo Examination Building and Ex					85	01-Aug-16	10-Nov-16												
Excavation					39	01-Aug-16	14-Sep-16												
RAB-23-5018		023 - PLT & CPT	14	01-Aug-16	16-Aug-16														
RAB-23-5020		023 - Open cut excavation down to formation level (GL 1-10) (2295m³)	8	06-Sep-16	14-Sep-16														
Raft Foundations - Inspection Platform					30	15-Sep-16	22-Oct-16												
RAB-23-5050		023 - Construct Raft Foundations for Platform Bay 1	12	15-Sep-16	29-Sep-16														
RAB-23-5090		023 - Construct Raft Foundations for Platform Bay 2	12	23-Sep-16	07-Oct-16														
RAB-23-5150		023 - Construct Raft Foundations for Platform Bay 3	12	30-Sep-16	15-Oct-16														
RAB-23-5190		023 - Construct Raft Foundations for Platform Bay 4	12	08-Oct-16	22-Oct-16														
Raft Foundations - Main Building					36	15-Sep-16	29-Oct-16												
RAB-23-5040		023 - Construct Raft Foundations for Main Building Bay 1 (GL8-10) (376.6m³)	12	15-Sep-16	29-Sep-16														
RAB-23-5080		023 - Construct Raft Foundations for Main Building Bay 2 (GL6-8) (376.6m³)	12	23-Sep-16	07-Oct-16														
RAB-23-5180		023 - Construct Raft Foundations for Main Building Bay 4 (GL3-5) (376.6m³)	12	30-Sep-16	15-Oct-16														
RAB-23-5240		023 - Construct Raft Foundations for Main Building Bay 5 (GL1-3) (376.6m³)	12	08-Oct-16	22-Oct-16														
RAB-23-5140		023 - Construct Raft Foundations for Main Building Bay 3 (GL5-6) (87.8m³)	12	17-Oct-16	29-Oct-16														
Structure					34	30-Sep-16	10-Nov-16												
Supporting Walls and Columns to +12.85mPD					34	30-Sep-16	10-Nov-16												
RAB-23-5110		023 - Construct External Walls to +12.85mPD Bay 1 (GL8-10)	10	30-Sep-16	13-Oct-16														
RAB-23-5160		023 - Construct External Walls to +12.85mPD Bay 2 (GL6-8)	10	08-Oct-16	20-Oct-16														
RAB-23-2180		023 - Install FS and SPR RC Water Tanks (G/F North)	10	08-Oct-16	20-Oct-16														
RAB-23-5270		023 - Construct External Walls to +12.85mPD Bay 4 (GL3-5)	10	17-Oct-16	27-Oct-16														
RAB-23-5300		023 - Construct External Walls to +12.85mPD Bay 5 (GL1-3)	10	24-Oct-16	03-Nov-16														
RAB-23-5390		023 - Construct External Walls to +12.85mPD Bay 3 (GL5-6)	10	31-Oct-16	10-Nov-16														

◆◆ Milestone

Three Month Rolling Programme

HKMZB HKBCF - Remaining Ancillary Buildings and Facilities

Date	Revision	Checked	Approved
01-Aug-16	Three Month Rolling Programme	AS	

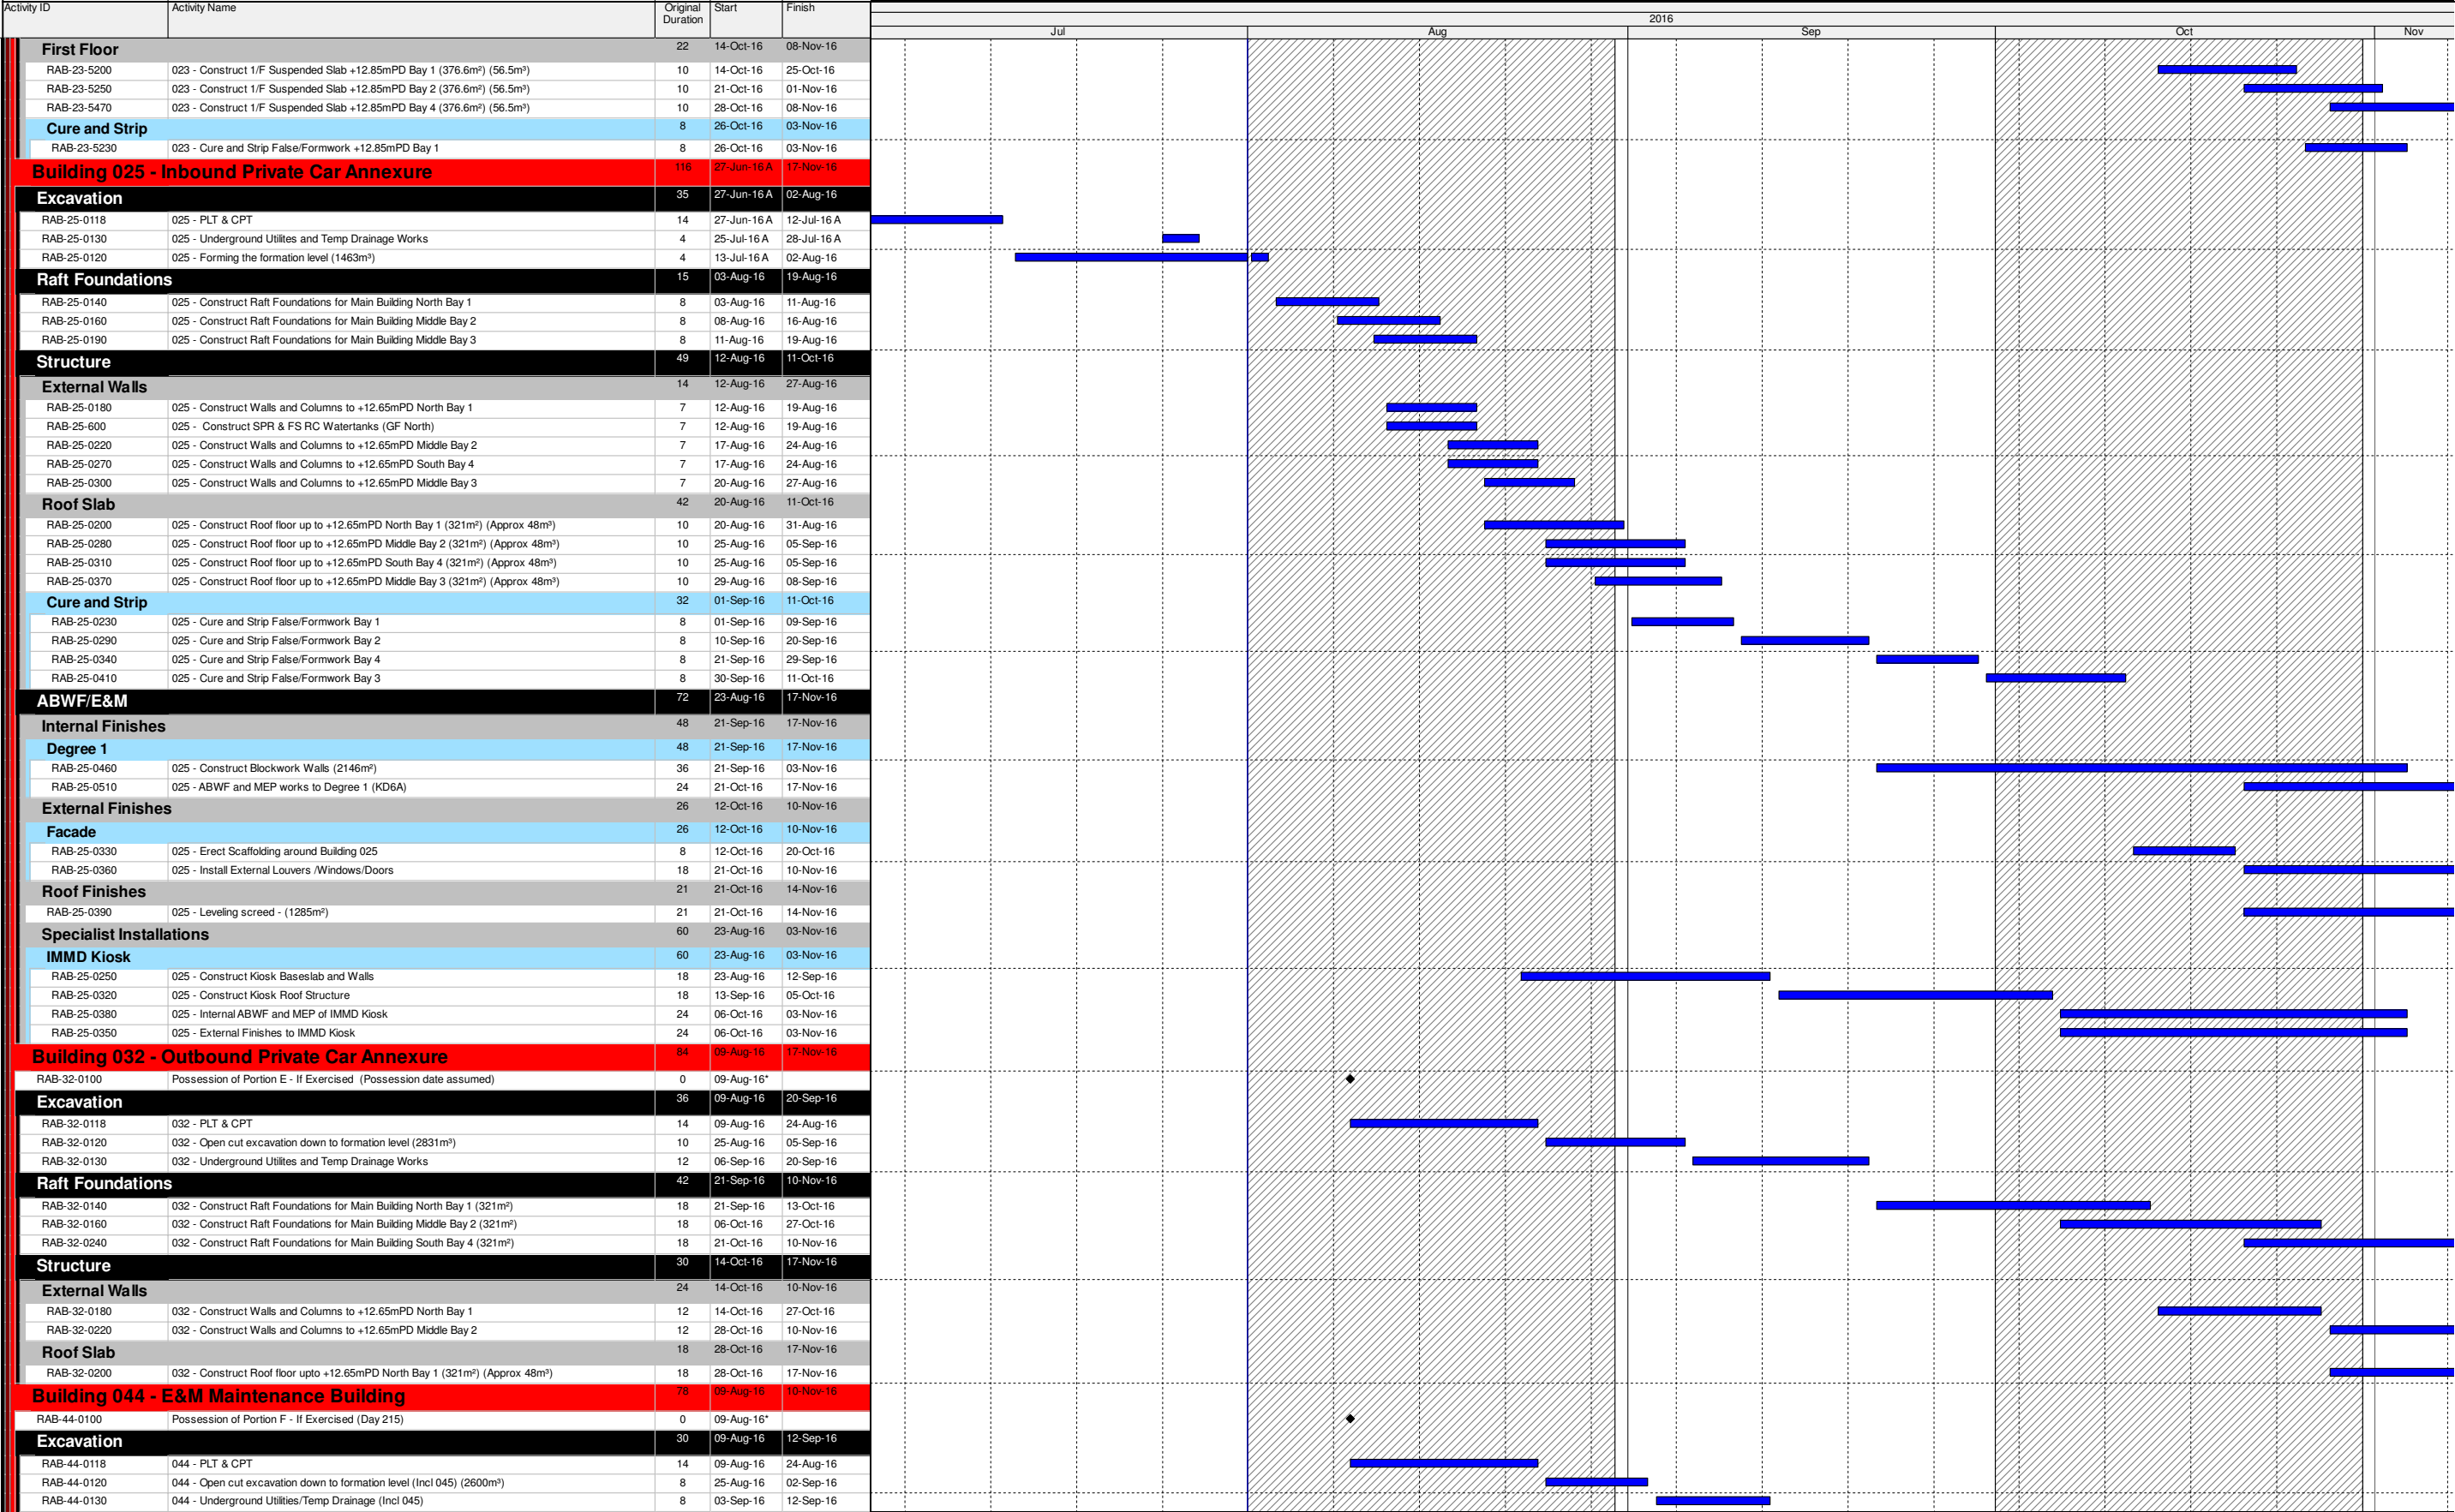

- Actual Work
- Remaining Work
- Critical Remaining Work
- ◆

◆ Milestone

Three Month Rolling Programme

HKMZB HKBCF - Remaining Ancillary Buildings and Facilities

Date	Revision	Checked	Approved
01-Aug-16	Three Month Rolling Programme	AS	

Activity ID	Activity Name	Original Duration	Start	Finish	Three Month Rolling Programme														
					Jul			Aug			2016 Sep			Oct			Nov		
Raft					26	03-Sep-16	05-Oct-16												
RAB-44-1140	044 - Construct lift pit for L-01	8	03-Sep-16	12-Sep-16															
RAB-44-0140	044 - Construct Raft Foundations for Main Building Bay 1 (North)(242m²)	12	13-Sep-16	27-Sep-16															
RAB-44-0160	044 - Construct Raft Foundations for Main Building Bay 2 (South)(242m²)	12	21-Sep-16	05-Oct-16															
Structure					36	28-Sep-16	10-Nov-16												
External Walls					18	28-Sep-16	20-Oct-16												
Ground to First Floor					18	28-Sep-16	20-Oct-16												
RAB-44-0170	044 - Construct External Walls to +12.15mPD Bay 1 (North)	12	28-Sep-16	13-Oct-16															
RAB-44-0200	044 - Construct External Walls to +12.15mPD Bay 2 (South)	12	06-Oct-16	20-Oct-16															
First Floor					20	14-Oct-16	05-Nov-16												
RAB-44-0190	044 - Construct 1/F Suspended Slab +12.15mPD Bay 1 (242m²) (72m³)	12	14-Oct-16	27-Oct-16															
RAB-44-0230	044 - Construct 1/F Suspended Slab +12.15mPD Bay 2 (242m²) (72m³)	12	21-Oct-16	03-Nov-16															
Cure and Strip					8	28-Oct-16	05-Nov-16												
RAB-44-0220	044 - Cure and Strip False/Formwork for +12.15mPD Slab Bay 1 (North)	8	28-Oct-16	05-Nov-16															
First Floor to Second Floor					12	28-Oct-16	10-Nov-16												
RAB-44-0210	044 - Construct External Walls to +16.85mPD Bay 1 (North)	12	28-Oct-16	10-Nov-16															
ABWF/E&M					30	28-Sep-16	03-Nov-16												
North Section					30	28-Sep-16	03-Nov-16												
Specialist Installations					30	28-Sep-16	03-Nov-16												
Window Wall					30	28-Sep-16	03-Nov-16												
RAB-23-7110	044 - Install Window Wall Cast in Items Base slab	6	28-Sep-16	05-Oct-16															
RAB-23-7160	044 - Install Window Wall Cast in Items F/F Slab	6	28-Oct-16	03-Nov-16															
Building 045 - Highways Depot & Administration Building					79	09-Aug-16	11-Nov-16												
RAB-45-0100	Possession of Portion F - If Exercised (Day 215)	0	09-Aug-16*																
RAB-45-0110	Possession of Portion B - If Exercised (Day 215)	0	09-Aug-16*																
Raft					44	09-Aug-16	29-Sep-16												
RAB-45-0125	PLT & CPT	14	09-Aug-16	24-Aug-16															
RAB-45-0130	045 - Construct lift pit for L-01	8	25-Aug-16	02-Sep-16															
RAB-45-0140	045 - Construct Raft Foundations for Main Building Bay 6 (428m²)	12	25-Aug-16	07-Sep-16															
RAB-45-0145	045 - Construct Raft Foundations for Main Building Bay 5 (428m²)	12	01-Sep-16	14-Sep-16															
RAB-45-0150	045 - Construct Raft Foundations for Main Building Bay 3 (428m²)	12	08-Sep-16	22-Sep-16															
RAB-45-0170	045 - Construct Raft Foundations for Main Building Bay 4 (419m²)	12	15-Sep-16	29-Sep-16															
Structure					50	08-Sep-16	08-Nov-16												
Ground to First Floor					30	08-Sep-16	15-Oct-16												
RAB-45-0260	045 - Construct External Walls and Support Columns to +12.15mPD Bay 6	12	08-Sep-16	22-Sep-16															
RAB-45-1170	045 - Construct External Walls and Support Columns to +12.15mPD Bay 5	12	15-Sep-16	29-Sep-16															
RAB-45-1180	045 - Construct External Walls and Support Columns to +12.15mPD Bay 3	12	23-Sep-16	07-Oct-16															
RAB-45-0180	045 - Construct External Walls and Support Columns to +12.15mPD Bay 4	12	30-Sep-16	15-Oct-16															
First Floor					38	23-Sep-16	08-Nov-16												
RAB-45-0290	045 - Construct 1/F Suspended Slab at +12.15mPD Bay 6 (South) (285m²) (approx 86m³)	12	23-Sep-16	07-Oct-16															
RAB-45-0320	045 - Construct 1/F Suspended Slab at +12.15mPD Bay 5 (South) (285m²) (approx 86m³)	12	30-Sep-16	15-Oct-16															
RAB-45-0250	045 - Construct 1/F Suspended Slab at +12.15mPD Bay 3 (North) (263m²) (approx 79m³)	12	08-Oct-16	22-Oct-16															
RAB-45-0190	045 - Construct 1/F Suspended Slab at +12.15mPD Bay 4 (North) (263m²) (approx 79m³)	12	17-Oct-16	29-Oct-16															
Cure and Strip					26	08-Oct-16	08-Nov-16												
RAB-45-0310	045 - Cure and Strip False/Formwork +12.15mPD Bay 6 (South)	8	08-Oct-16	18-Oct-16															
RAB-45-0350	045 - Cure and Strip False/Formwork +12.15mPD Bay 5 (South)	8	17-Oct-16	25-Oct-16															
RAB-45-0270	045 - Cure and Strip False/Formwork +12.15mPD Bay 3 (Middle)	8	24-Oct-16	01-Nov-16															
RAB-45-0230	045 - Cure and Strip False/Formwork +12.15mPD Bay 4 (Middle)	8	31-Oct-16	08-Nov-16															
First to Second Floor					18	19-Oct-16	08-Nov-16												
RAB-45-0300	045 - Construct External Walls and Support Columns to +16.85mPD Bay 6 (South)	12	19-Oct-16	01-Nov-16															
RAB-45-0420	045 - Construct External Walls and Support Columns to +16.85mPD Bay 5 (South)	12	26-Oct-16	08-Nov-16															
ABWF/E&M					53	08-Sep-16	11-Nov-16												
South Section					15	26-Oct-16	11-Nov-16												
Ground Floor					15	26-Oct-16	11-Nov-16												
RAB-45-0390	045 - Construct Blockwork Walls South G/F (430m³)	15	26-Oct-16	11-Nov-16															
Specialist Installations					30	08-Sep-16	15-Oct-16												
Window Wall					30	08-Sep-16	15-Oct-16												
RAB-23-7120	045 - Install Window Wall Cast in Items G/F	6	08-Sep-16	14-Sep-16															
RAB-23-7190	045 - Install Window Wall Cast in Items F/F	6	08-Oct-16	15-Oct-16															
Building 050 - Public Toilets Type 2					86	01-Aug-16	11-Nov-16												
RAB-50-1000	Possession of Portion H1 - If Exercised	0	01-Aug-16*																
Public Toilet (Portion H1)					82	01-Aug-16	07-Nov-16												
Excavation					24	01-Aug-16	27-Aug-16												
RAB-50-1015	050 H1- PLT	8	01-Aug-16	09-Aug-16															
RAB-50-1020	050 H1 - Open cut excavation down to formation level (370m³)	4	10-Aug-16*	13-Aug-16															
RAB-50-1030	050 H1 - Underground Utilities and Drainage	12	15-Aug-16	27-Aug-16															
Raft					18	29-Aug-16	19-Sep-16												
RAB-50-1040	050 H1 - Construct Raft Foundation (140m²) (91m³)	18	29-Aug-16	19-Sep-16															
Structure					40	20-Sep-16	07-Nov-16												
RAB-50-4310	050 H1 - Construct RC Support Columns for Aluminium Solar Shade	6	20-Sep-16	26-Sep-16															
RAB-50-1060	050 H1 - Construct RC Walls (External and Internal)	20	20-Sep-16	14-Oct-16															
RAB-50-1070	050 H1 - Construct Roof Floor at +11.525mPD (140m²) (21m³)	12	15-Oct-16	28-Oct-16															

◆◆ Milestone

Three Month Rolling Programme

HKMZB HKBCF - Remaining Ancillary Buildings and Facilities

Date	Revision	Checked	Approved
01-Aug-16	Three Month Rolling Programme	AS	

Activity ID	Activity Name	Original Duration	Start	Finish
RAB-50-1080	050 H1 - Cure and Strip False/Formwork	8	29-Oct-16	07-Nov-16
Public Toilet (Portion H2)		78	01-Aug-16	02-Nov-16
RAB-50-2000	Possession of Portion H2 - If Exercised	0	01-Aug-16*	
Excavation		28	01-Aug-16	01-Sep-16
RAB-50-2018	050 H2 - PLT	8	01-Aug-16	09-Aug-16
RAB-50-2020	050 H2 - Open cut excavation down to formation level (370m²)	4	15-Aug-16	18-Aug-16
RAB-50-2030	050 H2 - Underground Utilities and Drainage	12	19-Aug-16	01-Sep-16
Raft		18	02-Sep-16	23-Sep-16
RAB-50-2040	050 H2 - Construct Raft Foundation(140m²) (91m³)	18	02-Sep-16	23-Sep-16
Structure		32	24-Sep-16	02-Nov-16
RAB-50-4330	050 H2 - Construct RC Support Columns for Aluminium Solar Shade	6	24-Sep-16	30-Sep-16
RAB-50-2060	050 H2 - Construct RC Walls (External and Internal)	20	24-Sep-16	19-Oct-16
RAB-50-2070	050 H2 - Construct Roof Floor at +11.525mPD (140m²) (21m³)	12	20-Oct-16	02-Nov-16
Public Toilet (Portion A1)		82	01-Aug-16	07-Nov-16
RAB-50-3000	Possession of Portion A1 - If Exercised	0	01-Aug-16*	
Excavation		32	01-Aug-16	06-Sep-16
RAB-50-3018	050 A1 - PLT	8	01-Aug-16	09-Aug-16
RAB-50-3020	050 A1 - Open cut excavation down to formation level (370m²)	4	19-Aug-16	23-Aug-16
RAB-50-3030	050 A1 - Underground Utilities and Drainage	12	24-Aug-16	06-Sep-16
Raft		18	07-Sep-16	28-Sep-16
RAB-50-3040	050 A1 - Construct Raft Foundation	18	07-Sep-16	28-Sep-16
Structure		32	29-Sep-16	07-Nov-16
RAB-50-4340	050 A1 - Construct RC Support Columns for Aluminium Solar Shade	6	29-Sep-16	06-Oct-16
RAB-50-3060	050 A1 - Construct RC Walls (External and Internal)	20	29-Sep-16	24-Oct-16
RAB-50-3070	050 A1 - Construct Roof Floor at +11.525mPD (140m²) (21m³)	12	25-Oct-16	07-Nov-16
Public Toilet (Portion A2)		86	01-Aug-16	11-Nov-16
RAB-50-4000	Possession of Portion A2 - If Exercised	0	01-Aug-16*	
Excavation		36	01-Aug-16	10-Sep-16
RAB-50-4018	050 A2 - PLT	8	01-Aug-16	09-Aug-16
RAB-50-4020	050 A2 - Open cut excavation down to formation level (370m²)	4	24-Aug-16	27-Aug-16
RAB-50-4030	050 A2 - Underground Utilities and Drainage	12	29-Aug-16	10-Sep-16
Raft		18	12-Sep-16	04-Oct-16
RAB-50-4040	050 A2 - Construct Raft Foundation (140m²) (91m³)	18	12-Sep-16	04-Oct-16
Structure		32	05-Oct-16	11-Nov-16
RAB-50-4350	050 A2 - Construct RC Support Columns for Aluminium Solar Shade	6	05-Oct-16	12-Oct-16
RAB-50-4060	050 A2 - Construct RC Walls (External and Internal)	20	05-Oct-16	28-Oct-16
RAB-50-4070	050 A2 - Construct Roof Floor at +11.525mPD (140m²) (21m³)	12	29-Oct-16	11-Nov-16
Building 059 - Inbound X-Ray Scan Tunnel		107	02-Jul-16 A	06-Dec-16
Structure		51	02-Jul-16 A	29-Sep-16
Walls, Columns and Roof		40	02-Jul-16 A	15-Sep-16
RAB-59-0260	059 - Construct 600mm high kicer for Walls	8	02-Jul-16 A	11-Jul-16 A
RAB-59-0270	059 - Construct Walls to +9.5mPD	11	12-Jul-16 A	10-Aug-16
RAB-59-0300	059 - Construct Walls to +12.6mPD	12	08-Aug-16	20-Aug-16
RAB-59-0310	059 - Construct Walls to +17mPD	17	22-Aug-16	09-Sep-16
RAB-59-430	059 - Construct Roof floor	5	10-Sep-16	15-Sep-16
Cure and Strip		14	16-Sep-16	29-Sep-16
RAB-59-0340	059 - Cure and Strip formwork and falseworkup to +17.375mPD	14	16-Sep-16	29-Sep-16
ABWF/E&M		56	30-Sep-16	06-Dec-16
RAB-59-0350	ABWF and MEP Degree 1	56	30-Sep-16	06-Dec-16
Building 058 - Outbound X-Ray Scan Tunnel		93	18-Jul-16 A	19-Nov-16
RAB-58-0120	058 - CPT & PLT	14	18-Jul-16 A	30-Jul-16 A
Excavation		6	01-Aug-16	06-Aug-16
RAB-58-0150	058 - Open cut excavation down to Foundation Level and blinding	6	01-Aug-16*	06-Aug-16
Raft		31	08-Aug-16	12-Sep-16
RAB-58-0160	058 - Construct Raft Foundation - North	21	08-Aug-16	31-Aug-16
RAB-58-0170	058 - Construct Raft Foundation - South	16	25-Aug-16	12-Sep-16
Structure		66	01-Sep-16	19-Nov-16
Walls		48	01-Sep-16	29-Oct-16
RAB-58-0300	058 - Construct Walls to +9.5 - North	12	01-Sep-16	14-Sep-16
RAB-58-0310	058 - Construct Walls to +12.6 - North	12	10-Sep-16	24-Sep-16
RAB-58-0305	058 - Construct Walls to +9.5 - South	12	13-Sep-16	27-Sep-16
RAB-58-0370	058 - Construct Walls to +17 - North	12	23-Sep-16	07-Oct-16
RAB-58-0315	058 - Construct Walls to +12.6 - South	13	28-Sep-16	14-Oct-16
RAB-58-0375	058 - Construct Walls to +17 - South	13	15-Oct-16	29-Oct-16
Roof Slabs		36	08-Oct-16	19-Nov-16
RAB-58-0430	058 - Construct Roof floor to +17.375mPD - North	16	08-Oct-16	27-Oct-16
RAB-58-0435	058 - Construct Roof floor to +17.375mPD - South	18	31-Oct-16	19-Nov-16
Cure and Strip		14	28-Oct-16	

Activity ID	Activity Name	Original Duration	Start	Finish	2016												
					Jul			Aug			Sep			Oct			Nov
RAB-53-0160	053 - Construct Raft Foundations North	10	02-Jul-16 A	27-Jul-16 A													
RAB-53-0165	053 - backfill to G/L	2	01-Aug-16	02-Aug-16													
RAB-53-0200	053 - Construct Raft Foundations South	9	01-Aug-16	10-Aug-16													
RAB-53-0150	053 - Construct lift pit	10	01-Aug-16	11-Aug-16													
Structure		66	01-Aug-16	19-Oct-16													
External Walls		24	01-Aug-16	27-Aug-16													
To First Floor Level		24	01-Aug-16	27-Aug-16													
RAB-53-0190	053 - Construct External Walls and Columns to +12.85mPD North	21	01-Aug-16	24-Aug-16													
RAB-53-0250	053 - Construct External Walls and Columns to +12.85mPD South	15	11-Aug-16	27-Aug-16													
Internal Structures		24	01-Aug-16	27-Aug-16													
RAB-53-7500	053 - Construct Internal Staircase S-02 +12.85mPD North	12	01-Aug-16	13-Aug-16													
RAB-53-7490	053 - Construct Internal Staircase S-01 +12.85mPD South	12	11-Aug-16	24-Aug-16													
RAB-53-7550	053 - Construct Internal Liftshaft L-01 +12.85mPD North	12	15-Aug-16	27-Aug-16													
First Floor		40	25-Aug-16	13-Oct-16													
Slabs		8	25-Aug-16	02-Sep-16													
RAB-53-0240	053 - Construct 1/F Suspended Slab +12.85mPD North	5	25-Aug-16	30-Aug-16													
RAB-53-0310	053 - Construct 1/F Suspended Slab +12.85mPD South	5	29-Aug-16	02-Sep-16													
Cure and Strip		17	31-Aug-16	16-Sep-16													
RAB-53-0260	053 - Cure and Strip False/Formwork at +12.85mPD North	14	31-Aug-16	13-Sep-16													
RAB-53-0340	053 - Cure and Strip False/Formwork at +12.85mPD South	14	03-Sep-16	16-Sep-16													
To Roof Level		12	14-Sep-16	28-Sep-16													
RAB-53-0360	053 - Construct External Walls and Columns to +17.1mPD South	8	17-Sep-16	26-Sep-16													
RAB-53-0280	053 - Construct External Walls and Columns to +17.1mPD North	12	14-Sep-16	28-Sep-16													
Staircases		23	14-Sep-16	13-Oct-16													
RAB-53-7520	053 - Construct Internal Staircase S-02 +17.1mPD North	8	14-Sep-16	23-Sep-16													
RAB-53-7510	053 - Construct Internal Staircase S-01 +17.1mPD South	8	17-Sep-16	26-Sep-16													
RAB-53-7560	053 - Construct Internal Liftshaft L-01 +17.1mPD North	8	04-Oct-16	13-Oct-16													
Roof Floor		18	27-Sep-16	19-Oct-16													
Slabs		7	27-Sep-16	05-Oct-16													
RAB-53-0430	053 - Construct R/F Suspended Slab at +17.1mPD South	5	27-Sep-16	03-Oct-16													
RAB-53-0320	053 - Construct R/F Suspended Slab at +17.1mPD North	5	29-Sep-16	05-Oct-16													
Cure and Strip		16	04-Oct-16	19-Oct-16													
RAB-53-0480	053 - Cure and Strip False/Formwork at +17.1mPD South	14	04-Oct-16	17-Oct-16													
RAB-53-0350	053 - Cure and Strip False/Formwork at +17.1mPD North	14	06-Oct-16	19-Oct-16													
Water Tank		23	17-Sep-16	15-Oct-16													
RAB-53-0100	Formwork and rebar fixing to water tanks	18	17-Sep-16	08-Oct-16													
RAB-53-7570	Place Concrete	1	11-Oct-16	11-Oct-16													
RAB-53-7580	Formwork removal	4	12-Oct-16	15-Oct-16													
ABWF/E&M		30	06-Oct-16	10-Nov-16													
Ground Floor		16	20-Oct-16	07-Nov-16													
Degree 1		16	20-Oct-16	07-Nov-16													
RAB-53-0390	053 - Construct Blockwork Walls to G/F Rooms (706m²)	16	20-Oct-16	07-Nov-16													
External Finishes		30	06-Oct-16	10-Nov-16													
RAB-53-0410	053 - Erect External Scaffolding	10	06-Oct-16	18-Oct-16													
RAB-53-0440	053 - Install High Level Louvers	8	19-Oct-16	27-Oct-16													
RAB-53-0450	053 - External Render (465m²)	10	19-Oct-16	29-Oct-16													
RAB-53-0470	053 - External Tiling (465m²)	10	24-Oct-16	03-Nov-16													
RAB-53-0500	053 - External Painting	12	28-Oct-16	10-Nov-16													
Roof Finishes		12	19-Oct-16	01-Nov-16													
RAB-53-0420	053 - Leveling Screed - (490m²)	6	19-Oct-16	25-Oct-16													
RAB-53-0460	053 - Waterproof Membrane - (490m²)	6	26-Oct-16	01-Nov-16													
Statutory Submissions & Approvals (Day 420 Completion)		0	11-Oct-16	11-Oct-16													
EMSD - Building 053 Lift Inspection		0	11-Oct-16	11-Oct-16													
RAB-FSD-140	053 - Submit EMSD Form 3 (Commencement of Lift Installation)	0	11-Oct-16														

Actual Work Remaining Work Critical Remaining Work Milestone	Three Month Rolling Programme HKMZB HKBCF - Remaining Ancillary Buildings and Facilities	Date	Revision	Checked	Approved
		01-Aug-16	Three Month Rolling Programme	AS	
