


3-Month Rolling Programme Update, 01 Sep. 2017

RAB6			
Date	Revision	Checked	Approved
01-Sep-17	3-Month Rolling Programme, 01 Sep-17 Update	SGJ	

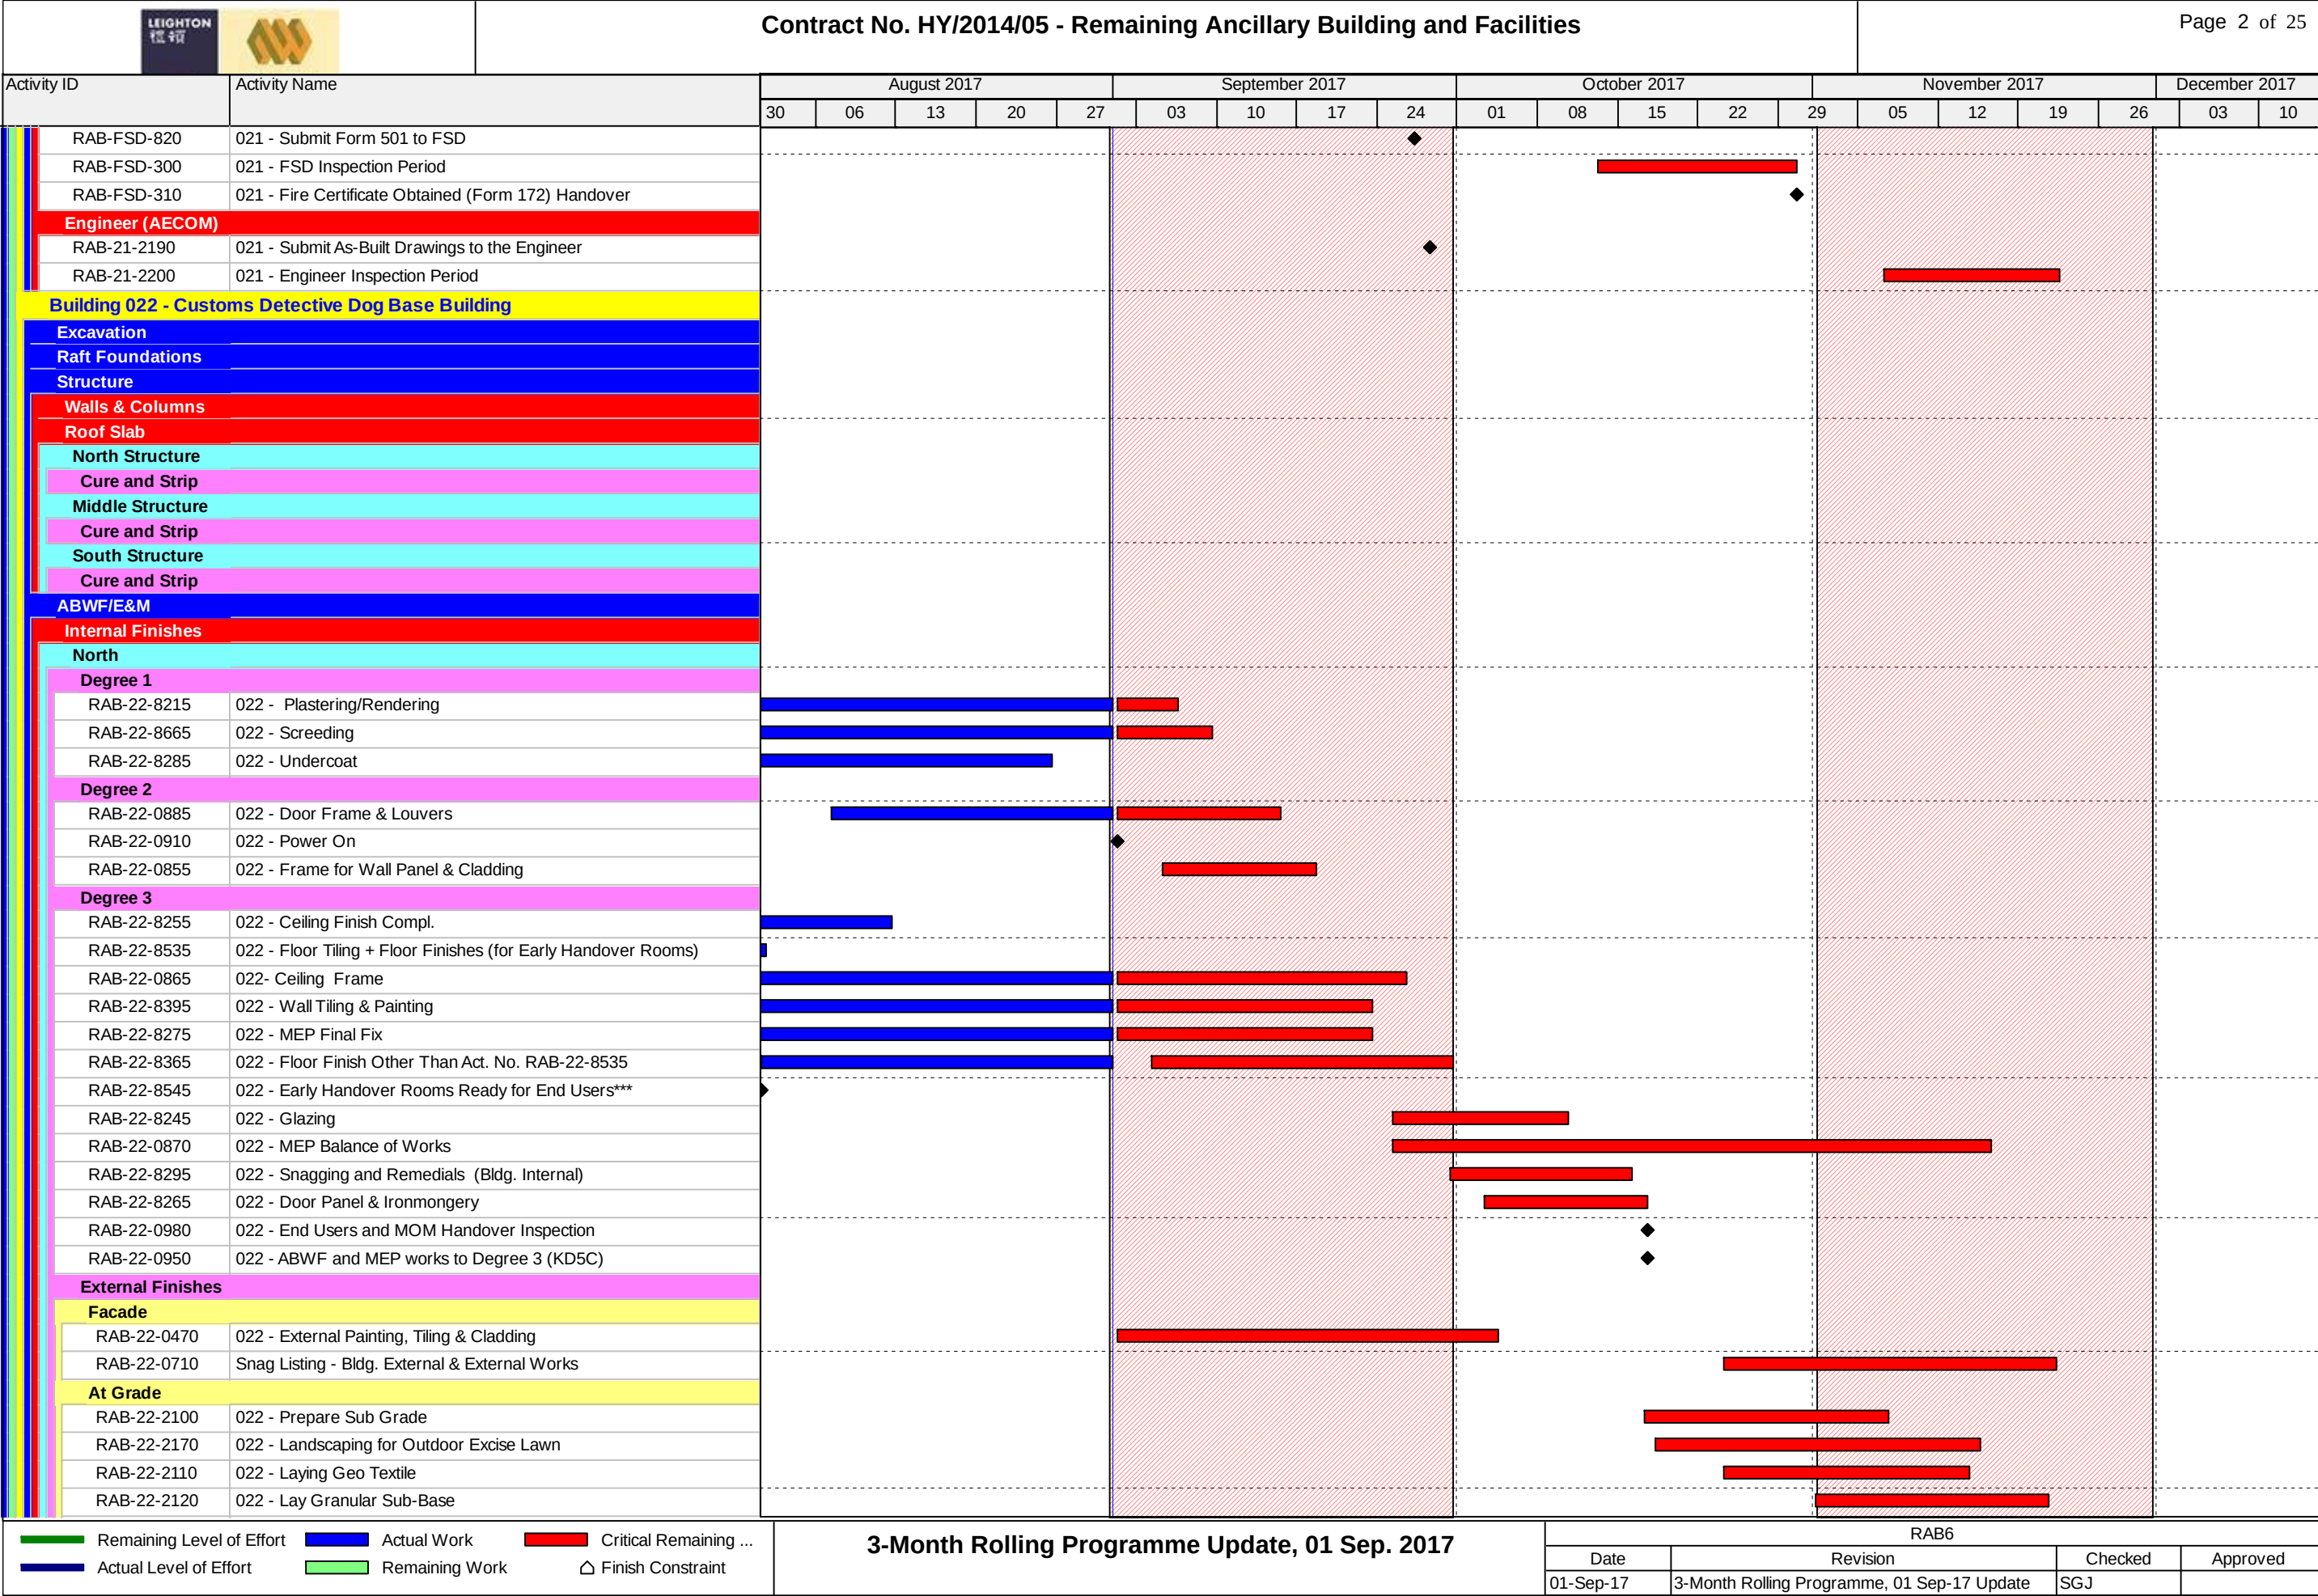

Activity ID	Activity Name	August 2017					September 2017				October 2017				November 2017				December 2017			
		30	06	13	20	27	03	10	17	24	01	08	15	22	29	05	12	19	26	03	10	
Building 023 - C&ED Outbound Cargo Examination Building and Examination PI	RAB-22-2130	022 - Laying Course																				
	Roof Finishes - North																					
	RAB-22-0530	022 - Install Railing																				
	RAB-22-0540	022 - Install Cat Ladder and Roof Hatch																				
	RAB-22-0720	022 - Make good external surfaces																				
	Specialist Installations																					
	RAB-22-0990	022 - Kennels Installation (42No)																				
	RAB-22-0550	022 - Small Glass Canopy South Entrance																				
	Window Wall																					
	RAB-22-7030	022 - Install Primary Steelwork for Window Wall																				
	RAB-22-7040	022 - Install Secondary Steelwork for Window Wall																				
	RAB-22-7050	022 - Glazing to Window Wall																				
	Dog Swimming Pool																					
	RAB-22-0480	022 - Waterproofing																				
	RAB-22-0600	022 - Tiling to Dog Swimming Pool																				
	RAB-22-0490	022 - Backfill to ground level at Dog Swimming Pool																				
	RAB-22-0640	022 - Plumbing and filtration systems																				
	RAB-22-0630	022 - Metalworks and Railings																				
	RAB-22-0700	022 - Snagging and Remedials - Dog Pool																				
	Utilities and Drainage																					
	RAB-22-8095	022 - Construct Permanent Drainage and Manholes																				
	RAB-22-8135	022 - Install FS Water main																				
	RAB-22-8115	022 - Install Flushing Water Mains																				
	RAB-22-8105	022 - Install Fresh Water Mains																				
	RAB-22-8125	022 - Utilites and Common Telecom Ducting																				
	Testing & Commissioning																					
	RAB-TC22-1000	022 - T&C (HVAC, FS, P&D, OTHERS)																				
	Statutory Submissions & Approvals (Day 670 Completion)																					
	BBEO																					
	RAB-BEE-120	022 - Registered Energy Assessor Inspection & Certification																				
	RAB-BEE-130	022 - Submit REA Certification to EDMS																				
	RAB-BEE-140	022 - EDMS Issue of Cert of Compliance Registration (COCR)																				
	Water Supplies Department (WSD)																					
	Commencement																					
	Completion																					
RAB-WSD-804	022 - Submit WWO 46 Pt. IV																					
RAB-WSD-254	022 - WSD's Processing/Inspection/Meter Connection																					
RAB-WSD-264	022 - Permanent Water ON/WSD Issue WWO 46 Part V Cert & Wa																					
Fire Servives Department (VAC)																						
RAB-FSD-860	022 - Submit Form 501																					
Fire Services Water (FS)																						
Commencement																						
Completion																						
RAB-FSD-895	022 - Submit WWO 46 Pt. IV, FS																					
RAB-FSD-984	022 - Submit WWO 46 Pt. V, FS																					
RAB-FSD-320	022 - Submit Form 501, FS																					
RAB-FSD-994	022 - Submit Form 314																					
RAB-FSD-330	022 - FSD Inspection Period, FS																					
Engineer (AECOM)																						
RAB-22-2220	022 - Submit Building 022 As Built Drawings to Engineer																					
Building 023 - C&ED Outbound Cargo Examination Building and Examination PI																						

RAB6			
Date	Revision	Checked	Approved
01-Sep-17	3-Month Rolling Programme, 01 Sep-17 Update	SGJ	


LEIGHTON 位頓		Contract No. HY/2014/05 - Remaining Ancillary Building and Facilities															Page 4 of 25				
Activity ID	Activity Name	August 2017					September 2017				October 2017					November 2017				December 2017	
		30	06	13	20	27	03	10	17	24	01	08	15	22	29	05	12	19	26	03	10
	Excavation																				
	Raft Foundations - Inspection Platform																				
	Raft Foundations - Main Building																				
	Structure																				
	Ground Floor																				
	Planters																				
	RAB-23-6140023 - Construct North Planter Box and Ramp																				
	RAB-23-6230023 - Construct South Planter Box and Ramp																				
	Supporting Walls and Columns to +12.85mPD																				
	First Floor																				
	Cure and Strip																				
	Supporting Walls and Columns to +17.1mPD																				
	Roof																				
	Cure and Strip																				
	Supporting Walls and Columns to +19.1mPD																				
	Lift Doghouse																				
	Cure and Strip																				
	ABWF/E&M																				
	Internal Finishes																				
	Ground Floor																				
	Degree 1																				
	RAB-23-5420023 - Construct Blockwork Walls to G/F																				
	RAB-23-5430023 - Plastering & Undercoat, G/F																				
	023 -23-5430023 - Screeding, G/F																				
	Degree 2																				
	RAB-23-5860023 - MEP 2nd Fix, G/F																				
	RAB-23-5610023 - Frame for Wall Panel & Cladding + Louver, G/F																				
	RAB-23-5670023 - Access to C3, C6 & C7 For Equip. Installation***, G/F																				
	RAB-23-5790023 - ABWF and MEP works to Degree 2 for others (KD3B) G/F																				
	Degree 3																				
	RAB-23-6320023 - Ceiling Paint Finish, G/F																				
	RAB-23-5930023 - Wall Finish - Paint & Tile, G/F																				
	RAB-23-6220023 - Floor Finish Other Than Carpet, G/F																				
	RAB-23-5760023 - Ceiling Frame, G/F																				
	RAB-23-6380023 - MEP Final Fix, G/F																				
	RAB-23-6080023 - Glazing, G/F																				
	RAB-23-6410023 - Ceiling Plaster Board, G/F																				
	RAB-23-5660023 - Door Frame/Panel & Ironmongery, G/F																				
	RAB-23-6180023 - Floor Carpet Finish, G/F																				
	RAB-23-6190023 - Access to End Users, KD3C' - C3, C6 & C7																				
	First Floor																				
	Degree 1																				
	RAB-23-8055023 - Construct Blockwork Walls, G/F - 1/F North (932m³), 1/F																				
	RAB-23-8065023 - Plastering & Undercoat, 1/F																				
	RAB-23-8215023 - Screeding, 1/F																				
	Degree 2																				
	RAB-23-8125023 - MEP 2nd Fix, 1/F																				
	RAB-23-8085023 - Frame for Wall Panel & Cladding + Louver, 1/F																				
	RAB-23-8235023 - Power On																				
	RAB-23-8115023 - Access for C3 for Equip. Instln***, 1/F, KD3D Target to Achieve																				
	Degree 3																				
	RAB-23-8135023 - Ceiling Paint Finish, 1/F																				
Remaining Level of Effort Actual Level of Effort Critical Remaining ... Remaining Work Finish Constraint		3-Month Rolling Programme Update, 01 Sep. 2017										RAB6									
		Date					Revision					Checked					Approved				
		01-Sep-17					3-Month Rolling Programme, 01 Sep-17 Update					SGJ									

LEIGHTON 恒耀		Contract No. HY/2014/05 - Remaining Ancillary Building and Facilities															Page 5 of 25					
Activity ID	Activity Name	August 2017					September 2017				October 2017					November 2017				December 2017		
		30	06	13	20	27	03	10	17	24	01	08	15	22	29	05	12	19	26	03	10	
	RAB-23-8175	023 - Wall Finish - Paint & Tile, 1/F																				
	RAB-23-8205	023 - Floor Finish Other Than Carpet, 1/F																				
	RAB-23-8165	023 - MEP Final Fix, 1/F																				
	RAB-23-8145	023 - Glazing, 1/F																				
	RAB-23-8105	023 - Ceiling Frame, 1/F																				
	RAB-23-8195	023 - Floor Carpet Finish, 1/F																				
	RAB-23-8185	023 - Ceiling Plaster Board, 1/F																				
	RAB-23-8155	023 - Door Panel/Ironmongery & Glass Baluster, 1/F																				
	RAB-23-8265	023 - MEP Balance of Works																				
	RAB-23-5970	023 - ABWF and MEP works to Degree 3 (KD3E)																				
	RAB-23-2290	023 - Snag Listing & Remedial Works - Building Internal																				
	RAB-23-6040	023 - End Users and MOM Handover Inspection																				
	RAB-23-8225	023 - Handover Rooms Ready to End Users***, KD3C Target to Ach																				
	RAB-23-8255	023 - ABWF and MEP works to Degree 3 - Remaining Area- 1/F																				
	Roof Level Dog House																					
RAB-23-6150	023 - ABWF and MEP works to Degree 1 R/F																					
RAB-23-6280	023 - ABWF and MEP works to Degree 2 R/F																					
RAB-23-6340	023 - ABWF and MEP works to Degree 3 R/F																					
External Finishes																						
Facade																						
RAB-23-5560	023 - External Render																					
RAB-23-5590	023 - External Tiling																					
RAB-23-5650	023 - External Painting																					
RAB-23-5990	023 - Dismantle Scaffolding																					
At Grade																						
RAB-23-5740	023 - Prepare Sub Grade																					
RAB-23-5820	023 - Laying Geo Textile																					
RAB-23-5910	023 - Lay Granular Sub-Base																					
RAB-23-5940	023 - Laying Course																					
RAB-23-6050	023 - Concrete Block Paving																					
Window Wall																						
East																						
RAB-23-6810	023 - Install Primary Steelwork for Window Wall - E																					
RAB-23-6820	023 - Install Secondary Steelwork for Window Wall - E																					
RAB-23-6830	023 - Glazing to Window Wall - E																					
West																						
RAB-23-6840	023 - Install Primary Steelwork for Window Wall - W																					
RAB-23-6850	023 - Install Secondary Steelwork for Window Wall - W																					
RAB-23-6860	023 - Glazing to Window Wall - W																					
Roof Finishes																						
RAB-23-5550	023 - Waterproof membrane																					
RAB-23-5620	023 - Top Screed																					
RAB-23-5640	023 - Roof Tiling																					
RAB-23-5920	023 - Install Railing																					
Green Roof																						
RAB-23-5720	023 - Install green Roof Irrigation Systems																					
RAB-23-5900	023 - Complete Green Roofing Works																					
Specialist Installations																						
RAB-23-6270	023 - Install Lift (1 nos)																					
RAB-23-6010	023 - Installation of Roller Shutter Header Boxes (x 3)																					

Activity ID		Activity Name	August 2017						September 2017				October 2017					November 2017				December 2017	
			30	06	13	20	27	03	10	17	24	01	08	15	22	29	05	12	19	26	03	10	
	RAB-23-7310	023 - Install Glazed Entrance Canopy																					
	RAB-23-6250	023 - Installation of Roller Shutter Curtain (x3)																					
	PV Installation																						
	RAB-23-6350	023 - Install Supporting Frame and PV panel																					
	RAB-23-6360	023 - Cable containment and grid cable wiring																					
	RAB-23-6390	023 - Sub-array junction box installation & Connection																					
	Steel Canopy																						
	RAB-23-6240	023 - Install Secondary Steelwork																					
	RAB-23-6290	023 - Install Metal Cladding Panels																					
	RAB-23-6310	023 - Install Misc Metalworks																					
	Utilities and Drainage																						
	RAB-23-7975	023 - Construct Permanent Drainage, Manholes & Draw Pits																					
	RAB-23-7985	023 - Utilites and Common Telecom Ducting																					
	RAB-23-7995	023 - Install Flushing Water Mains																					
	RAB-23-8005	023 - Install Fresh Water Mains																					
	RAB-23-8015	023 - Install FS Water Mains																					
	Testing & Commissioning																						
	RAB-TC23-1000	023 - T&C (HVAC, FS, P&D, OTHERS)																					
	RAB-TC23-1010	023 - T&C (Lift)																					
	Statutory Submissions & Approvals (Day 610 Completion)																						
	BBEO																						
	RAB-BEE-150	023 - Registered Energy Assessor Inspection & Certification																					
	EMSD - Building 023 Lift Inspection																						
	RAB-FSD-170	023 - Submit EMSD Form 3 (Commencement of Lift Installation)																					
	RAB-FSD-180	023 - Submit EMSD Form 5 (Completion of Lift Installation)																					
	RAB-FSD-190	023 - EMSD Lift Inspection																					
	Water Supplies Department (WSD)																						
Commencement																							
Completion																							
RAB-WSD-774	023 - Submit WWO 46 Pt. IV for Building 023																						
RAB-WSD-107	023 - WSD Inspection/Meter Connection																						
Fire Servives Department (VAC)																							
RAB-FSD-890	023 - Submit Form 314																						
RAB-FSD-900	023 - Submit Form 501																						
Fire Services Department (FSD)																							
Commencement																							
Completion																							
RAB-FSD-108	023 - Submit WWO 46 Pt. IV for Building 023																						
RAB-FSD-112	023 -Issue WWO 46 Part V																						
Engineer (AECOM)																							
RAB-23-2250	023 - Submit Building 023 As Built Drawings to Engineer																						
Building 025 - Inbound Private Car Annexure																							
Excavation																							
Raft Foundations																							
Structure																							
Walls & Columns																							
Roof Slab																							
Cure and Strip																							
ABWF/E&M INTERNAL FINISHES																							
INTERNAL FINISHING WORKS																							
Degree 1																							
RAB-25-7400	025 - MEP 1st Fix																						

RAB6			
Date	Revision	Checked	Approved
01-Sep-17	3-Month Rolling Programme, 01 Sep-17 Update	SGJ	

 Remaining Level of Effort  Actual Work  Critical Remaining ...		3-Month Rolling Programme Update, 01 Sep. 2017	RAB6			
 Actual Level of Effort  Remaining Work  Finish Constraint			Date	Revision	Checked	Approved
			01-Sep-17	3-Month Rolling Programme, 01 Sep-17 Update	SGJ	

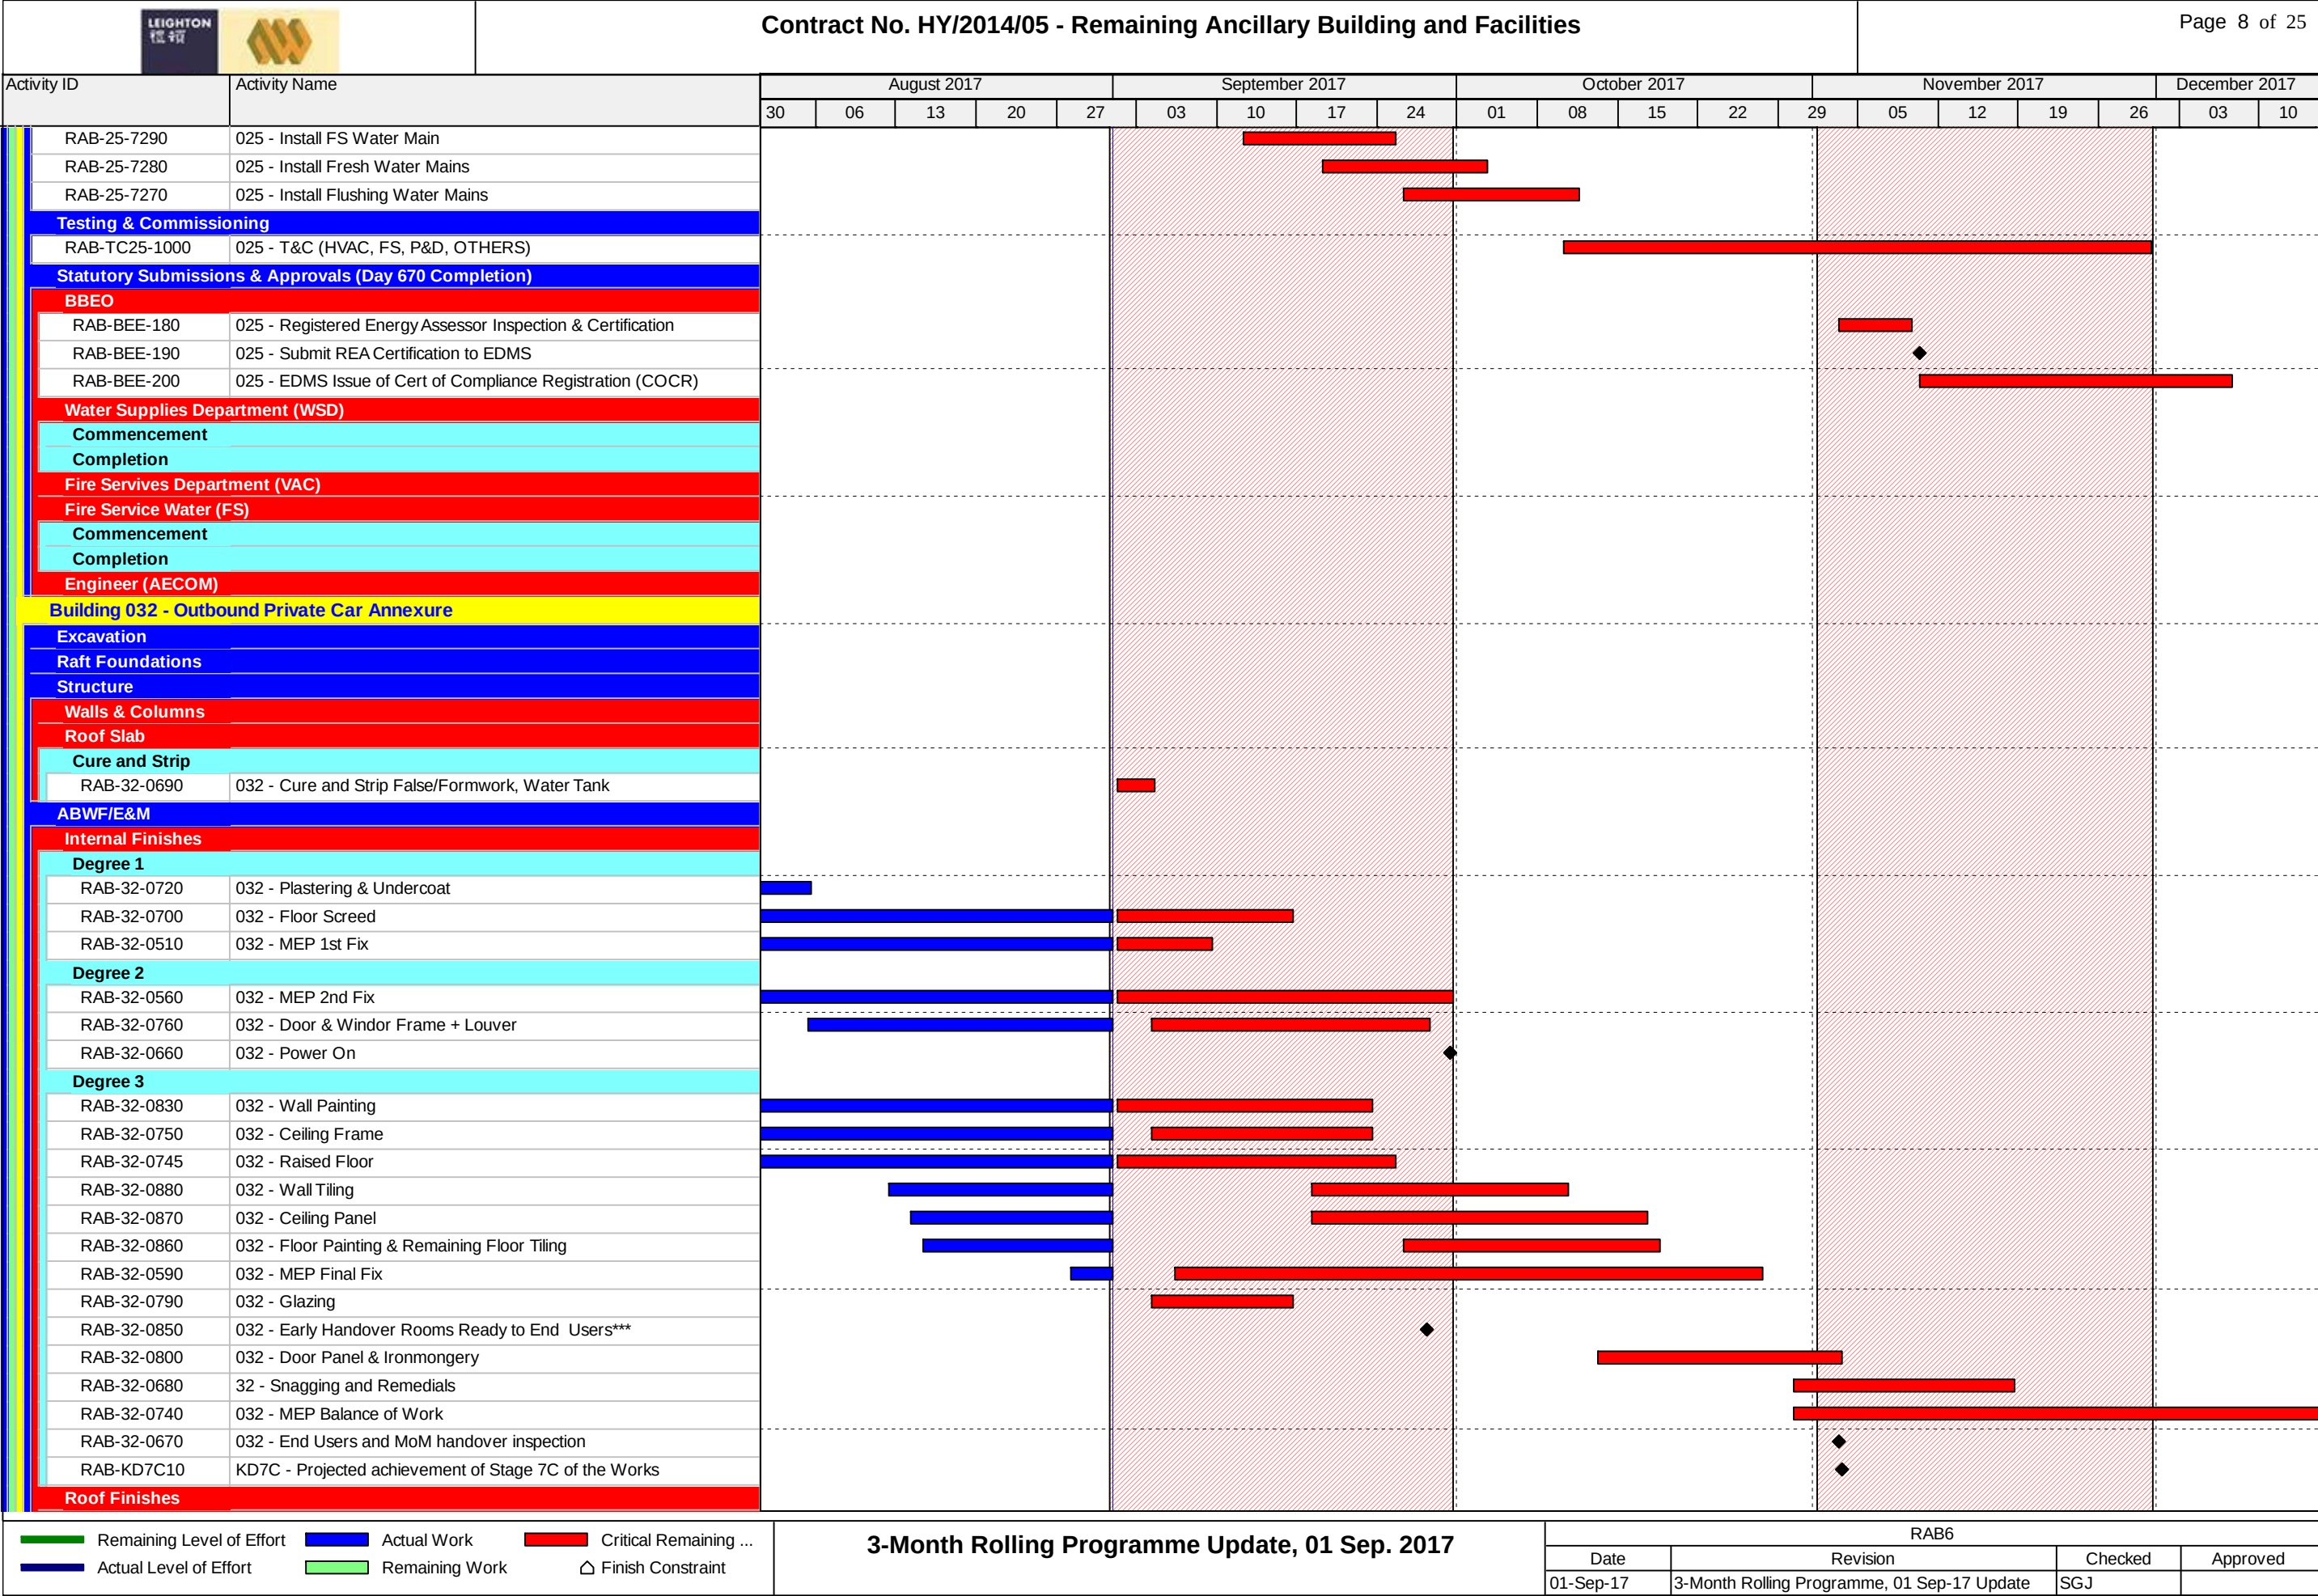


Activity ID	Activity Name	August 2017					September 2017				October 2017				November 2017				December 2017	
		30	06	13	20	27	03	10	17	24	01	08	15	22	29	05	12	19	26	03
	RAB-44-9485	044 - Glazing - 1/F																		
	RAB-44-9475	044 - Floor Paint Finish - 1/F																		
Second Floor																				
Degree 1																				
	RAB-44-9525	044 - Construct Blockwork Walls - 2/F																		
	RAB-44-9545	044 - Plastering & Undercoat - 2/F																		
	RAB-44-9515	044 - MEP 1st Fix - 2/F																		
	RAB-44-9535	044 - Screed - 2/F																		
Degree 2																				
	RAB-44-9575	044 - MEP 2nd Fix - 2/F																		
	RAB-44-9665	044 - Door & Windor Frame + Louver - 2/F																		
	RAB-44-9605	044 - Power On - 2/F																		
	RAB-44-0610	KD8B - Projected achievement of Stage 8B of the Works - 2/F																		
Degree 3																				
	RAB-44-9595	044 - Wall Finish, Paint & Tile - 2/F																		
	RAB-44-9635	044 - Ceiling Paint Finish - 2/F																		
	RAB-44-9725	044 - Ceiling Plaster Board Frame - 2/F																		
	RAB-44-9735	044 - Ceiling Plaster Board																		
	RAB-44-9585	044 - MEP Final Fix - 2/F																		
	RAB-44-9675	044 - Glazing - 2/F																		
	RAB-44-9715	044 - Door Panel & Ironmongery - 2/F																		
	RAB-44-9795	044 - MEP Balance of Works																		
	RAB-44-9685	044 - Floor Tile Finish & Floor Finish to Early handover Rooms - 2/F																		
	RAB-44-9645	044 - Ceiling Panel Frame - 2/F																		
	RAB-44-9745	044 - Ceiling Panel - 2/F																		
Roof Finishes																				
	RAB-44-0420	044 - Leveling screed - (242m²)																		
	RAB-44-0450	044 - Waterproof membrane - (242m²)																		
	RAB-44-1150	044 - Insulation Board - (242m²)																		
	RAB-44-0480	044 - Top Screed - (242m²)																		
	RAB-44-0520	044 - Install Roof Tiles - (242m²)																		
	RAB-44-0540	044 - Install Railing																		
	RAB-44-0550	044 - Install Cat Ladder and Roof Hatch																		
Green Roof																				
	RAB-44-0350	044 - Leveling screed - (242m²)																		
	RAB-44-0360	044 - Waterproof membrane - (242m²)																		
	RAB-44-0390	044 - Top Screed - (242m²)																		
	RAB-44-0400	044 - Install green Roof Irrigation Systems																		
External Finishes																				
Facade																				
	RAB-44-0470	044 - External Render																		
	RAB-44-0530	044 - External Painting																		
	RAB-44-0490	044 - External Tiling																		
	RAB-44-0430	044 - Install External Louvers /Windows/Doors																		
	RAB-44-0570	044 - Dismantle Scaffolding																		
At Grade																				
	RAB-44-6520	044 - Prepare Sub Grade																		
	RAB-44-6510	044 - Laying Geo Textile																		
	RAB-44-6530	044 - Lay Granular Sub-Base																		
	RAB-44-6540	044 - Laying Course																		

RAB6			
Date	Revision	Checked	Approved
01-Sep-17	3-Month Rolling Programme, 01 Sep-17 Update	SGJ	

Activity ID		Activity Name	August 2017					September 2017					October 2017					November 2017					December 2017					
			30	06	13	20	27	03	10	17	24	01	08	15	22	29	05	12	19	26	03	10						
	Building 045 - Highways Depot & Administration Building																											
	Raft Foundation																											
	Diesel Fuel Chamber																											
	Structure G/F to R/F																											
	G/F to 1/F Walls & Columns																											
	1/F Slab																											
	Cure and Strip																											
	1/F to 2/F Walls & Columns																											
	2/F Slab																											
	Cure and Strip																											
	2/f to R/F Walls & Columns																											
	Roof Level Slab																											
	Cure and Strip																											
	ABWF/E&M																											
	Ground Floor, South - G/F																											
	Degree 1, G/F																											
	RAB-45-9725		045 - MEP 1st Fix - G/F																									
	RAB-45-9765		045 - Screed - G/F																									
	Degree 2, G/F																											
	RAB-45-9805		045 - MEP 2nd Fix - G/F																									
	RAB-45-9895		045 - Door & Windor Frame + Louver - G/F																									
	RAB-45-9905		045 - Access for C3 to Install Equipment																									
	RAB-45-10075		045 - Projeted achievement of Stage 8B of the Works - G/F																									
	Degree 3, G/F																											
	RAB-45-9935		045 - Wall Finish, Paint & Tile - G/F																									
	RAB-45-10005		045 - Ceiling Paint - G/F																									
	RAB-45-9915		045 - Floor Finish (Paint & Tile) - G/F																									
	RAB-45-9945		045 - Door Panel & Ironmongery - G/F																									
	RAB-45-10035		045 - Ceiling Plaster Board Frame & Ceiling Panel Frame - G/F																									
	RAB-45-9815		045 - MEP Final Fix - G/F																									
	RAB-45-9925		045 - Glazing - G/F																									
	RAB-45-10055		045 - Ceiling Plaster Board & Ceiling Panel- G/F																									
	First Floor, 1/F																											
	Degree 1, 1/F																											
	RAB-45-9975		045 - Screed - 1/F																									
	RAB-45-9955		045 - MEP 1st Fix - 1/F																									
	Degree 2, 1/F																											
	RAB-45-10015		045 - MEP 2nd Fix - 1/F																									
	RAB-45-10105		045 - Door & Windor Frame + Louver - 1/F																									
	RAB-45-10065		045 - Access to C3 Equipment Instalaltion***																									
	Degree 3, 1/F																											
	RAB-45-10175		045 - Ceiling Paint - 1/F																									
	RAB-45-10145		045 - Wall Finish, Paint & Tile - 1/F																									
	RAB-45-10125		045 - Floor Finish (Paint & Tile) - 1/F																									
	RAB-45-10155		045 - Door Panel & Ironmongery - 1/F																									
	RAB-45-10205		045 - Ceiling Plaster Board Frame Ceiling Panel Frame- 1/F																									
	RAB-45-10025		045 - MEP Final Fix - 1/F																									
	RAB-45-10245		045 - Ceiling Plaster Board & Ceiling Panel - 1/F																									
	RAB-45-10285		045 - Glazing - 1/F																									
	RAB-45-10275		045 - Handover to End users***																									
Second Floor, 2/F																												
Degree 1, 2/F																												
Remaining Level of Effort Actual Level of Effort			Actual Work Remaining Work			Critical Remaining ... Finish Constraint			3-Month Rolling Programme Update, 01 Sep. 2017										RAB6									
									Date					Revision					Checked		Approved							
									01-Sep-17					3-Month Rolling Programme, 01 Sep-17 Update					SGJ									


3-Month Rolling Programme Update, 01 Sep. 2017

RAB6			
Date	Revision	Checked	Approved
01-Sep-17	3-Month Rolling Programme, 01 Sep-17 Update	SGJ	

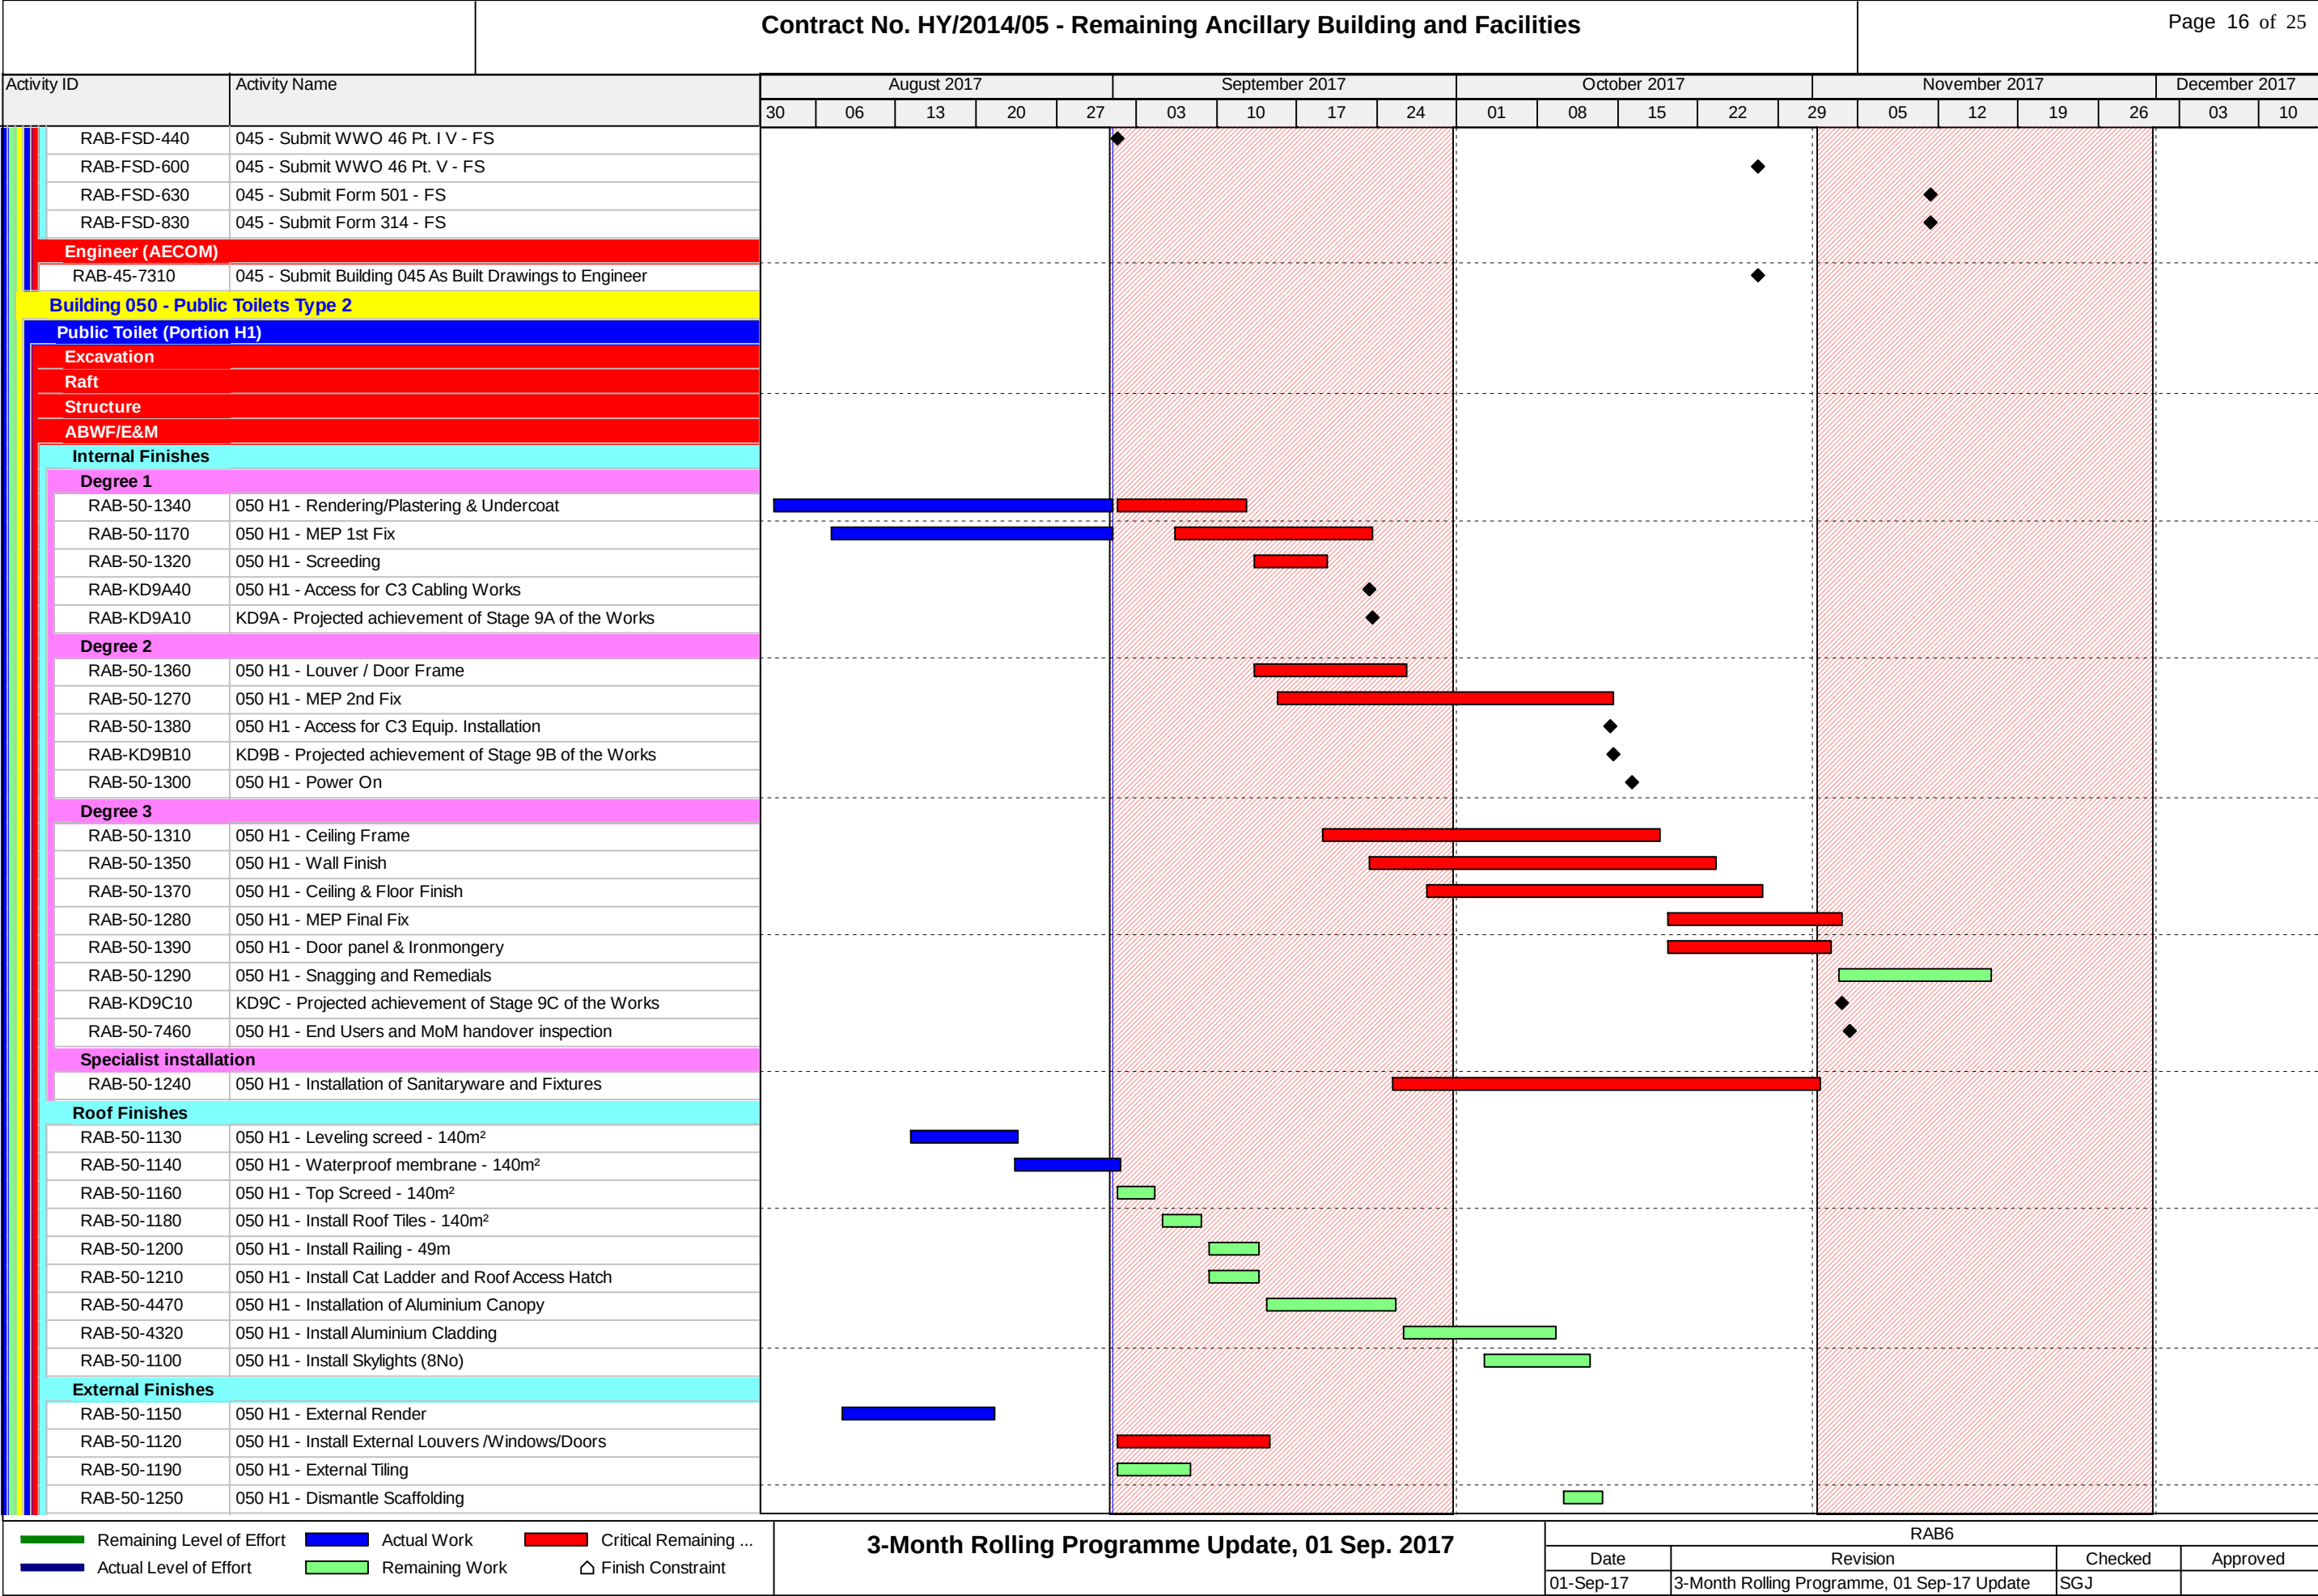


3-Month Rolling Programme Update, 01 Sep. 2017

RAB6			
Date	Revision	Checked	Approved
01-Sep-17	3-Month Rolling Programme, 01 Sep-17 Update	SGJ	

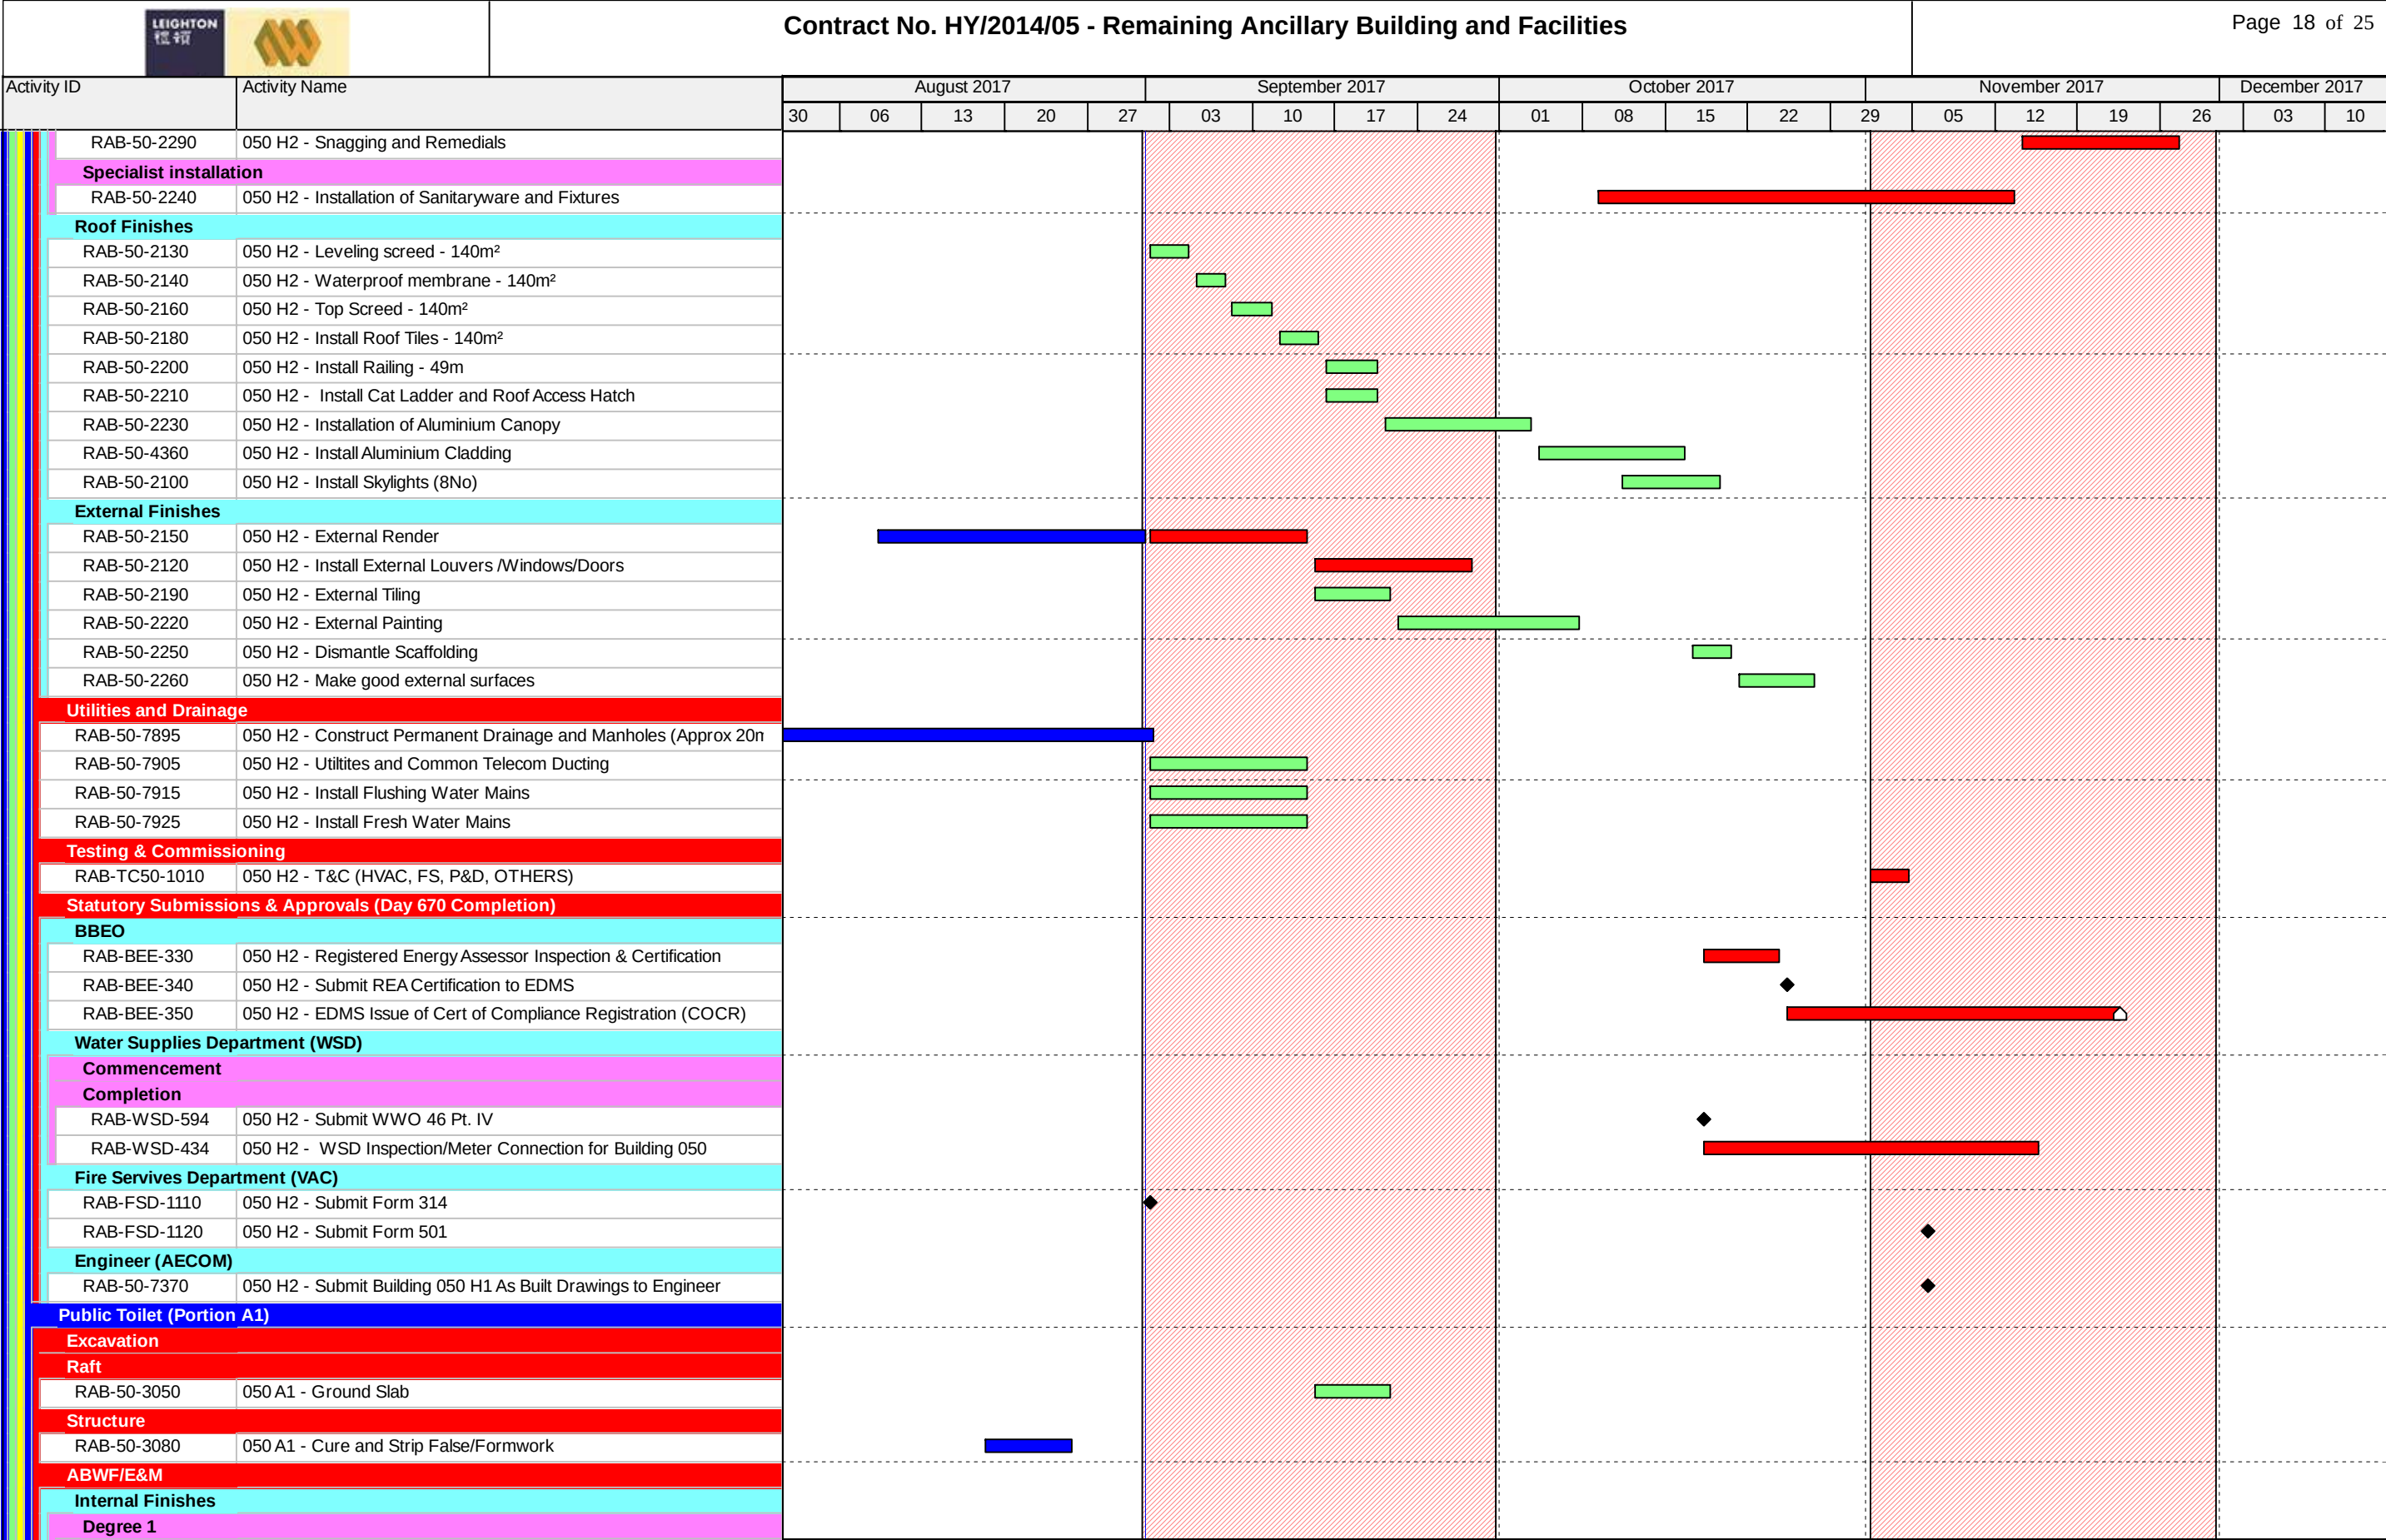

 Remaining Level of Effort  Actual Work  Critical Remaining ...  Actual Level of Effort  Remaining Work  Finish Constraint	3-Month Rolling Programme Update, 01 Sep. 2017	RAB6			
		Date	Revision	Checked	Approved
		01-Sep-17	3-Month Rolling Programme, 01 Sep-17 Update	SGJ	

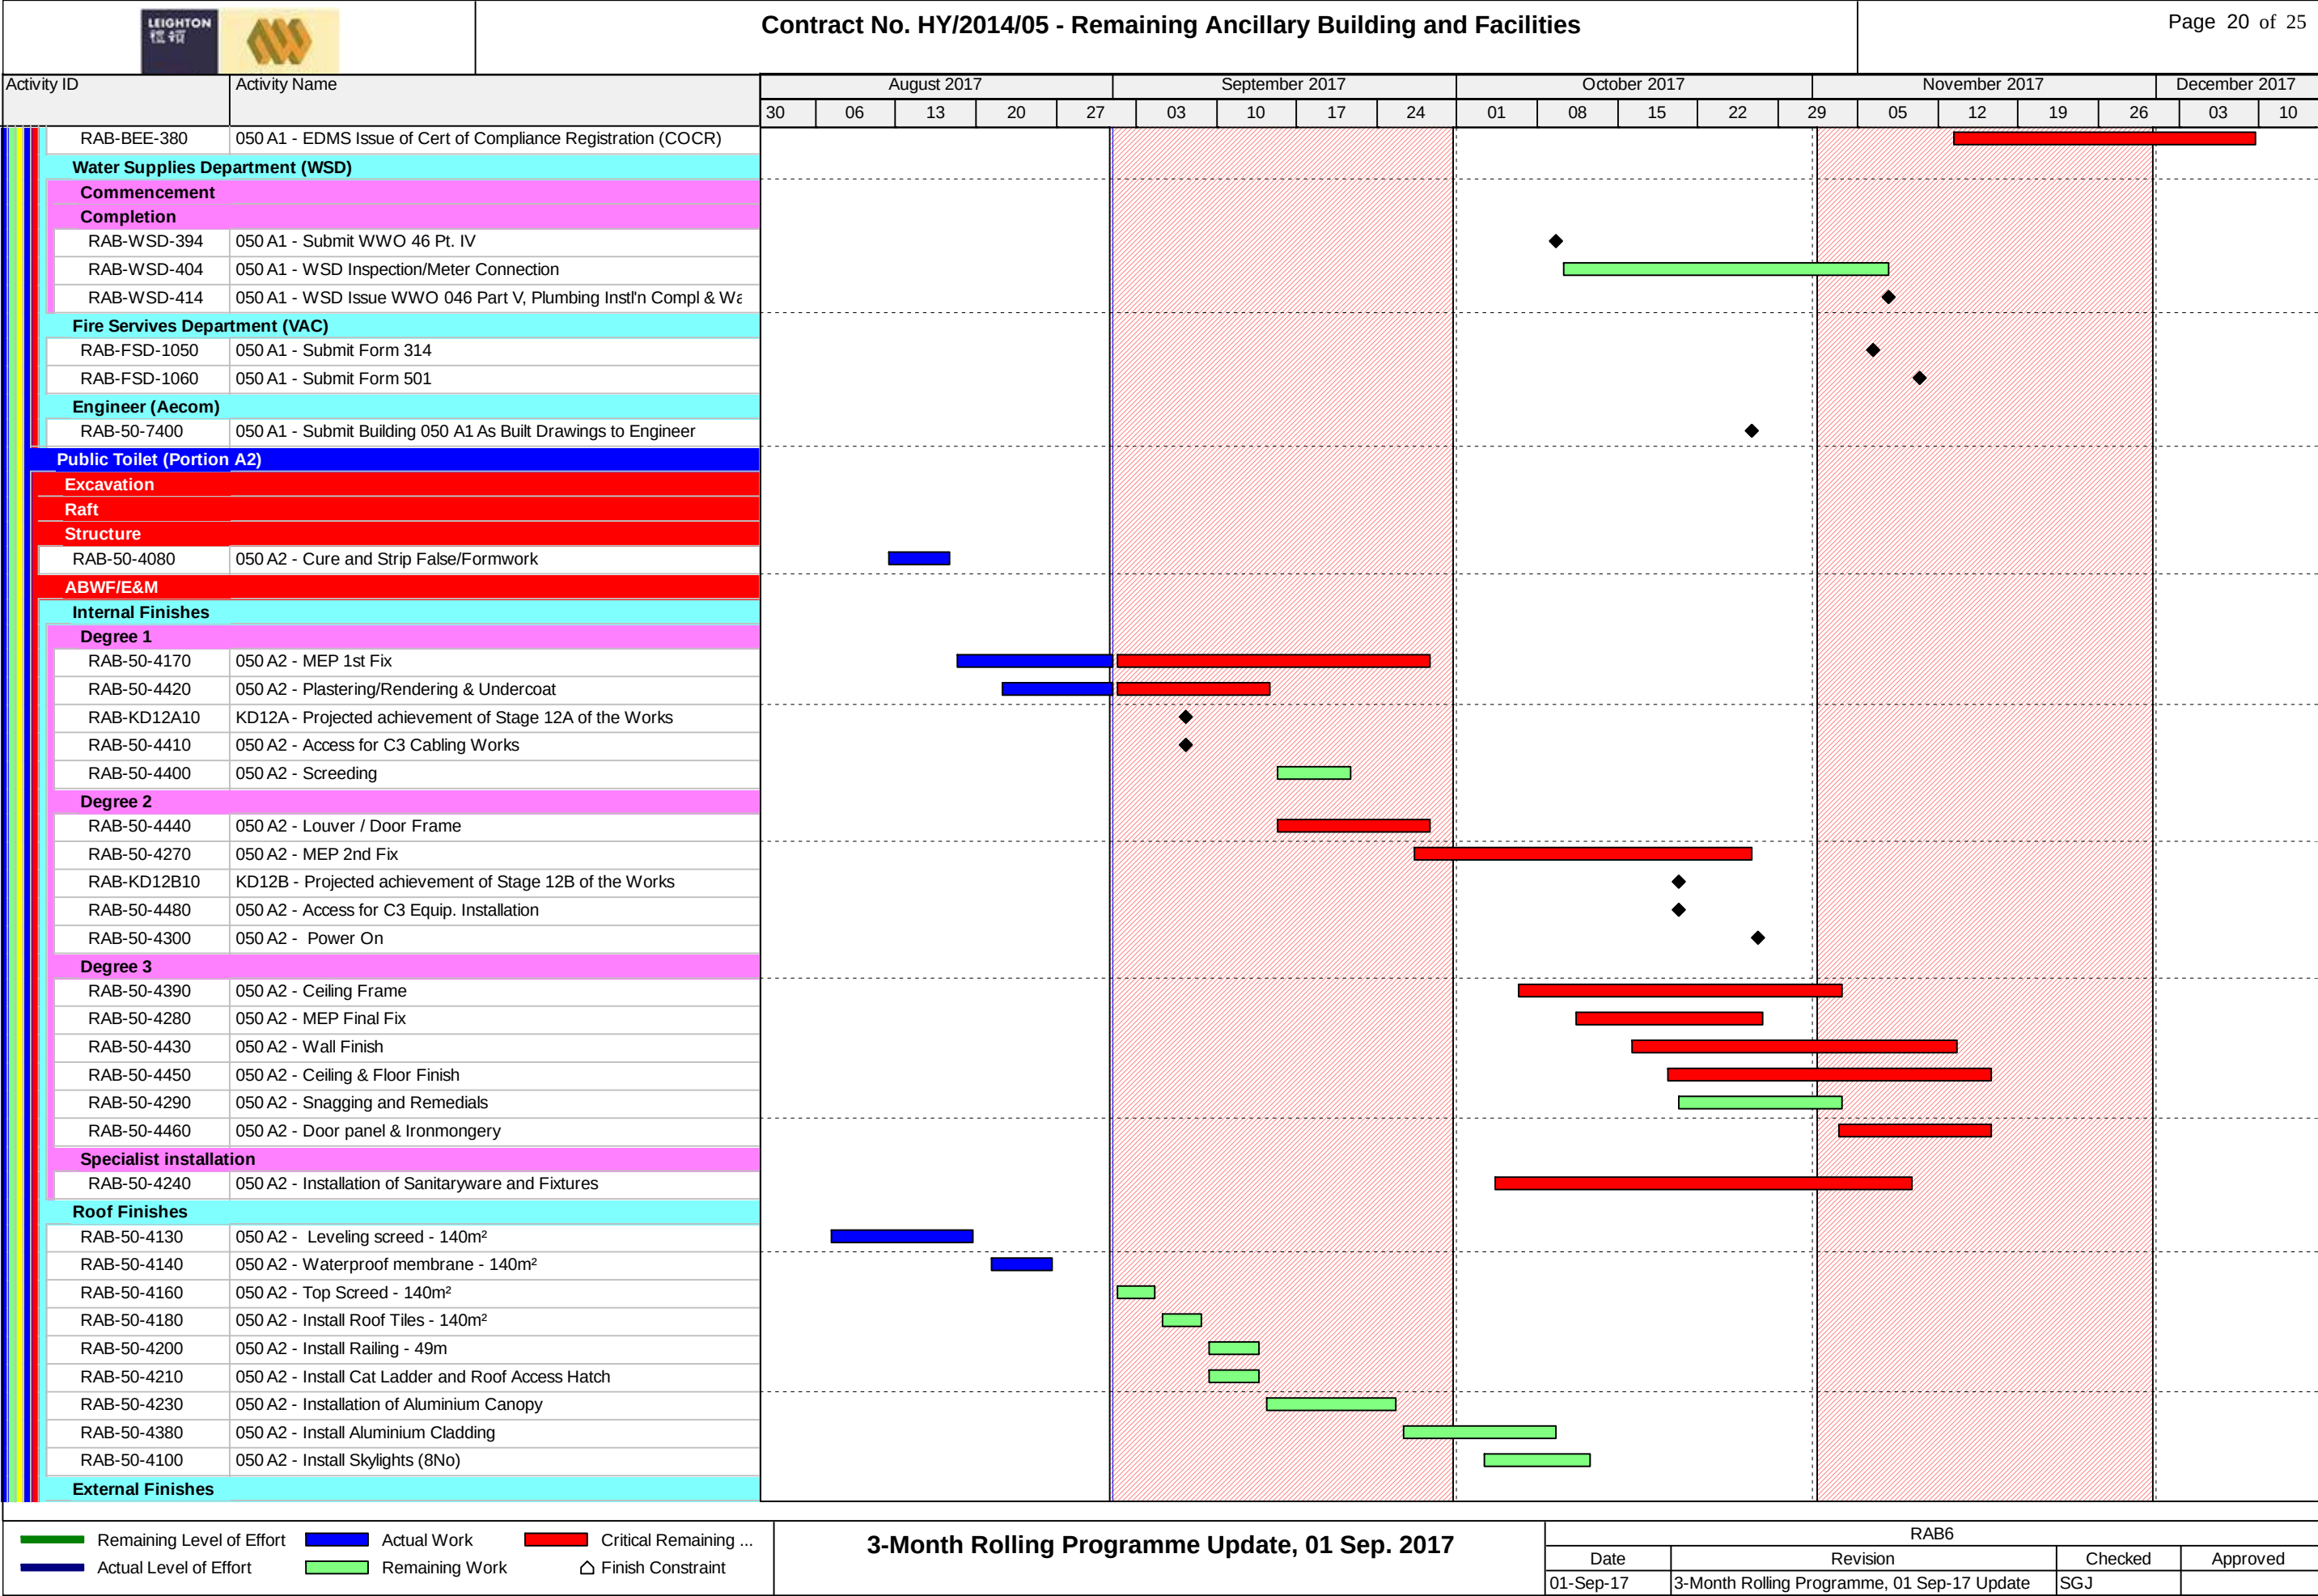 Critical Remaining ...

3-Month Rolling Programme Update, 01 Sep. 2017

RAB6


Date	Revision	Checked	Approved
01-Sep-17	3-Month Rolling Programme, 01 Sep-17 Update	SGJ	


Contract No.: HY/2013/06			Page 3 of 8																																		
Activity ID		Activity Name																																			
Detailed Design Specification Contruction Design and Management Supply/Manufacture Mock-up items Supply/Manufacture prototypes Software Design, Coding and Testing Coding Software System Inetgration Prototype & Software Simulation Tests Procurement - Phase 1 / Section I Supply/Manufacture products for FAT Factory Acceptance Test (FAT) Supply/Manufacture Equipment Delivery and Bench Acceptance Test for Phase 1/ Section I Installation - Phase 1 / Section I Location 1(PCB (001) Basement) EM1920 L1(001)B/F - Cable Laying and termination at Location 1 and Location 2 Location 1(PCB (001) ELV Room (Grid Line E3)) EM1940 L1(001)ELV Rm - Cable Laying and termination at Location 1 and Location 2 Location 2(PCB (001) Ground Floor ELV Room (Grid Line E3)) EM1960 L2(001)ELV Rm - Cable Laying and termination at Location 1 and Location 2 Location 2(PCB (001) Ground Floor DOH Port Health Control Room (Grid Line BD5)) EM1080 L2(001)Heath Ctrl Rm - Cable Laying and termination at Location 1 and Location 2 EM1100 L2(001)Heath Ctrl Rm - Cable Splicing and Testing and Labeling EM1120 L2(001)Health Ctrl Rm - Intercom and PA system Installation EM1140 L2(001)Heath Ctrl Rm - Intercom and PA system tuning Location 2(PCB (001) First Floor Main Server Room) EM1000 L2(001)Main Server Rm - Cable Laying and termination at Location 1 and Location 2 EM1020 L2(001)Main Server Rm - Cable Splicing and Testing and Labeling EM1040 L2(001)Main Server Rm - AVCSS Network and Server Installation EM1060 L2(001)Main Server Rm - AVCSS Network and Server Tuning Location 3(Inbd Cargo Exam Bldg (037) MDF Room) Location 3(Inbd Cargo Exam Bldg (037) ELV Room) Location 3(Inbd Cargo Exam Bldg (037) Inspector Offices 128,129,130,131,128,129,141 EM2020 L3(037)Inspec Offices - Cable Laying and termination in Location 3 and Location 3a EM2040 L3(037)Inspec Offices - Cable Splicing and Testing and Labeling EM2060 L3(037)Inspec Offices - AVCSS SURCON WS and 55" LCD Installation EM2080 L3(037)Inspec Offices - VTS WS Installation EM2100 L3(037)Inspec Offices - SURCON and WS Tuning Location 3(Inbd Cargo Exam Bldg (037) Platform Control Room) EM1160 L3(037)PLF Ctrl Rm - Cable Laying and termination in Location 3 and Location 3a EM1180 L3(037)PLF Ctrl Rm - Cable Splicing and Testing and Labeling EM1200 L3(037)PLF Ctrl Rm - AVCSS SYSCON WS and 55" TV Wall Installation EM1220 L3(037)PLF Ctrl Rm - AVCSS SYSCON WS Tuning																																					
Programme No.: HZMB-DWP		Actual Level of Effort Primary Baseline Actual Work Remaining Work Critical Remaining Work Baseline Milestone Milestone																		Hong Kong-Zhuhai-Macao Bridge Hong Kong Boundary Crossing Facilities - Automatic Vehicle Clearance Support System (AVCSS)																	
Data Date: 14-Aug-15																				Date		Revision		Checked		Approved											
																				14-Nov-16		Rev.: 0		WC		LC											
																				10-Mar-17		Rev.: 1.0a		WC		LC											
																				5-May-17		Rev.: 1.0b		WC		LC											


Contract No.: HY/2013/06			Page 4 of 8											
Activity ID		Activity Name												
</														

Contract No.: HY/2013/06				Page 6 of 8											
Activity ID		Activity Name													

Contract No.: HY/2013/06				Page 7 of 8											
Activity ID		Activity Name													

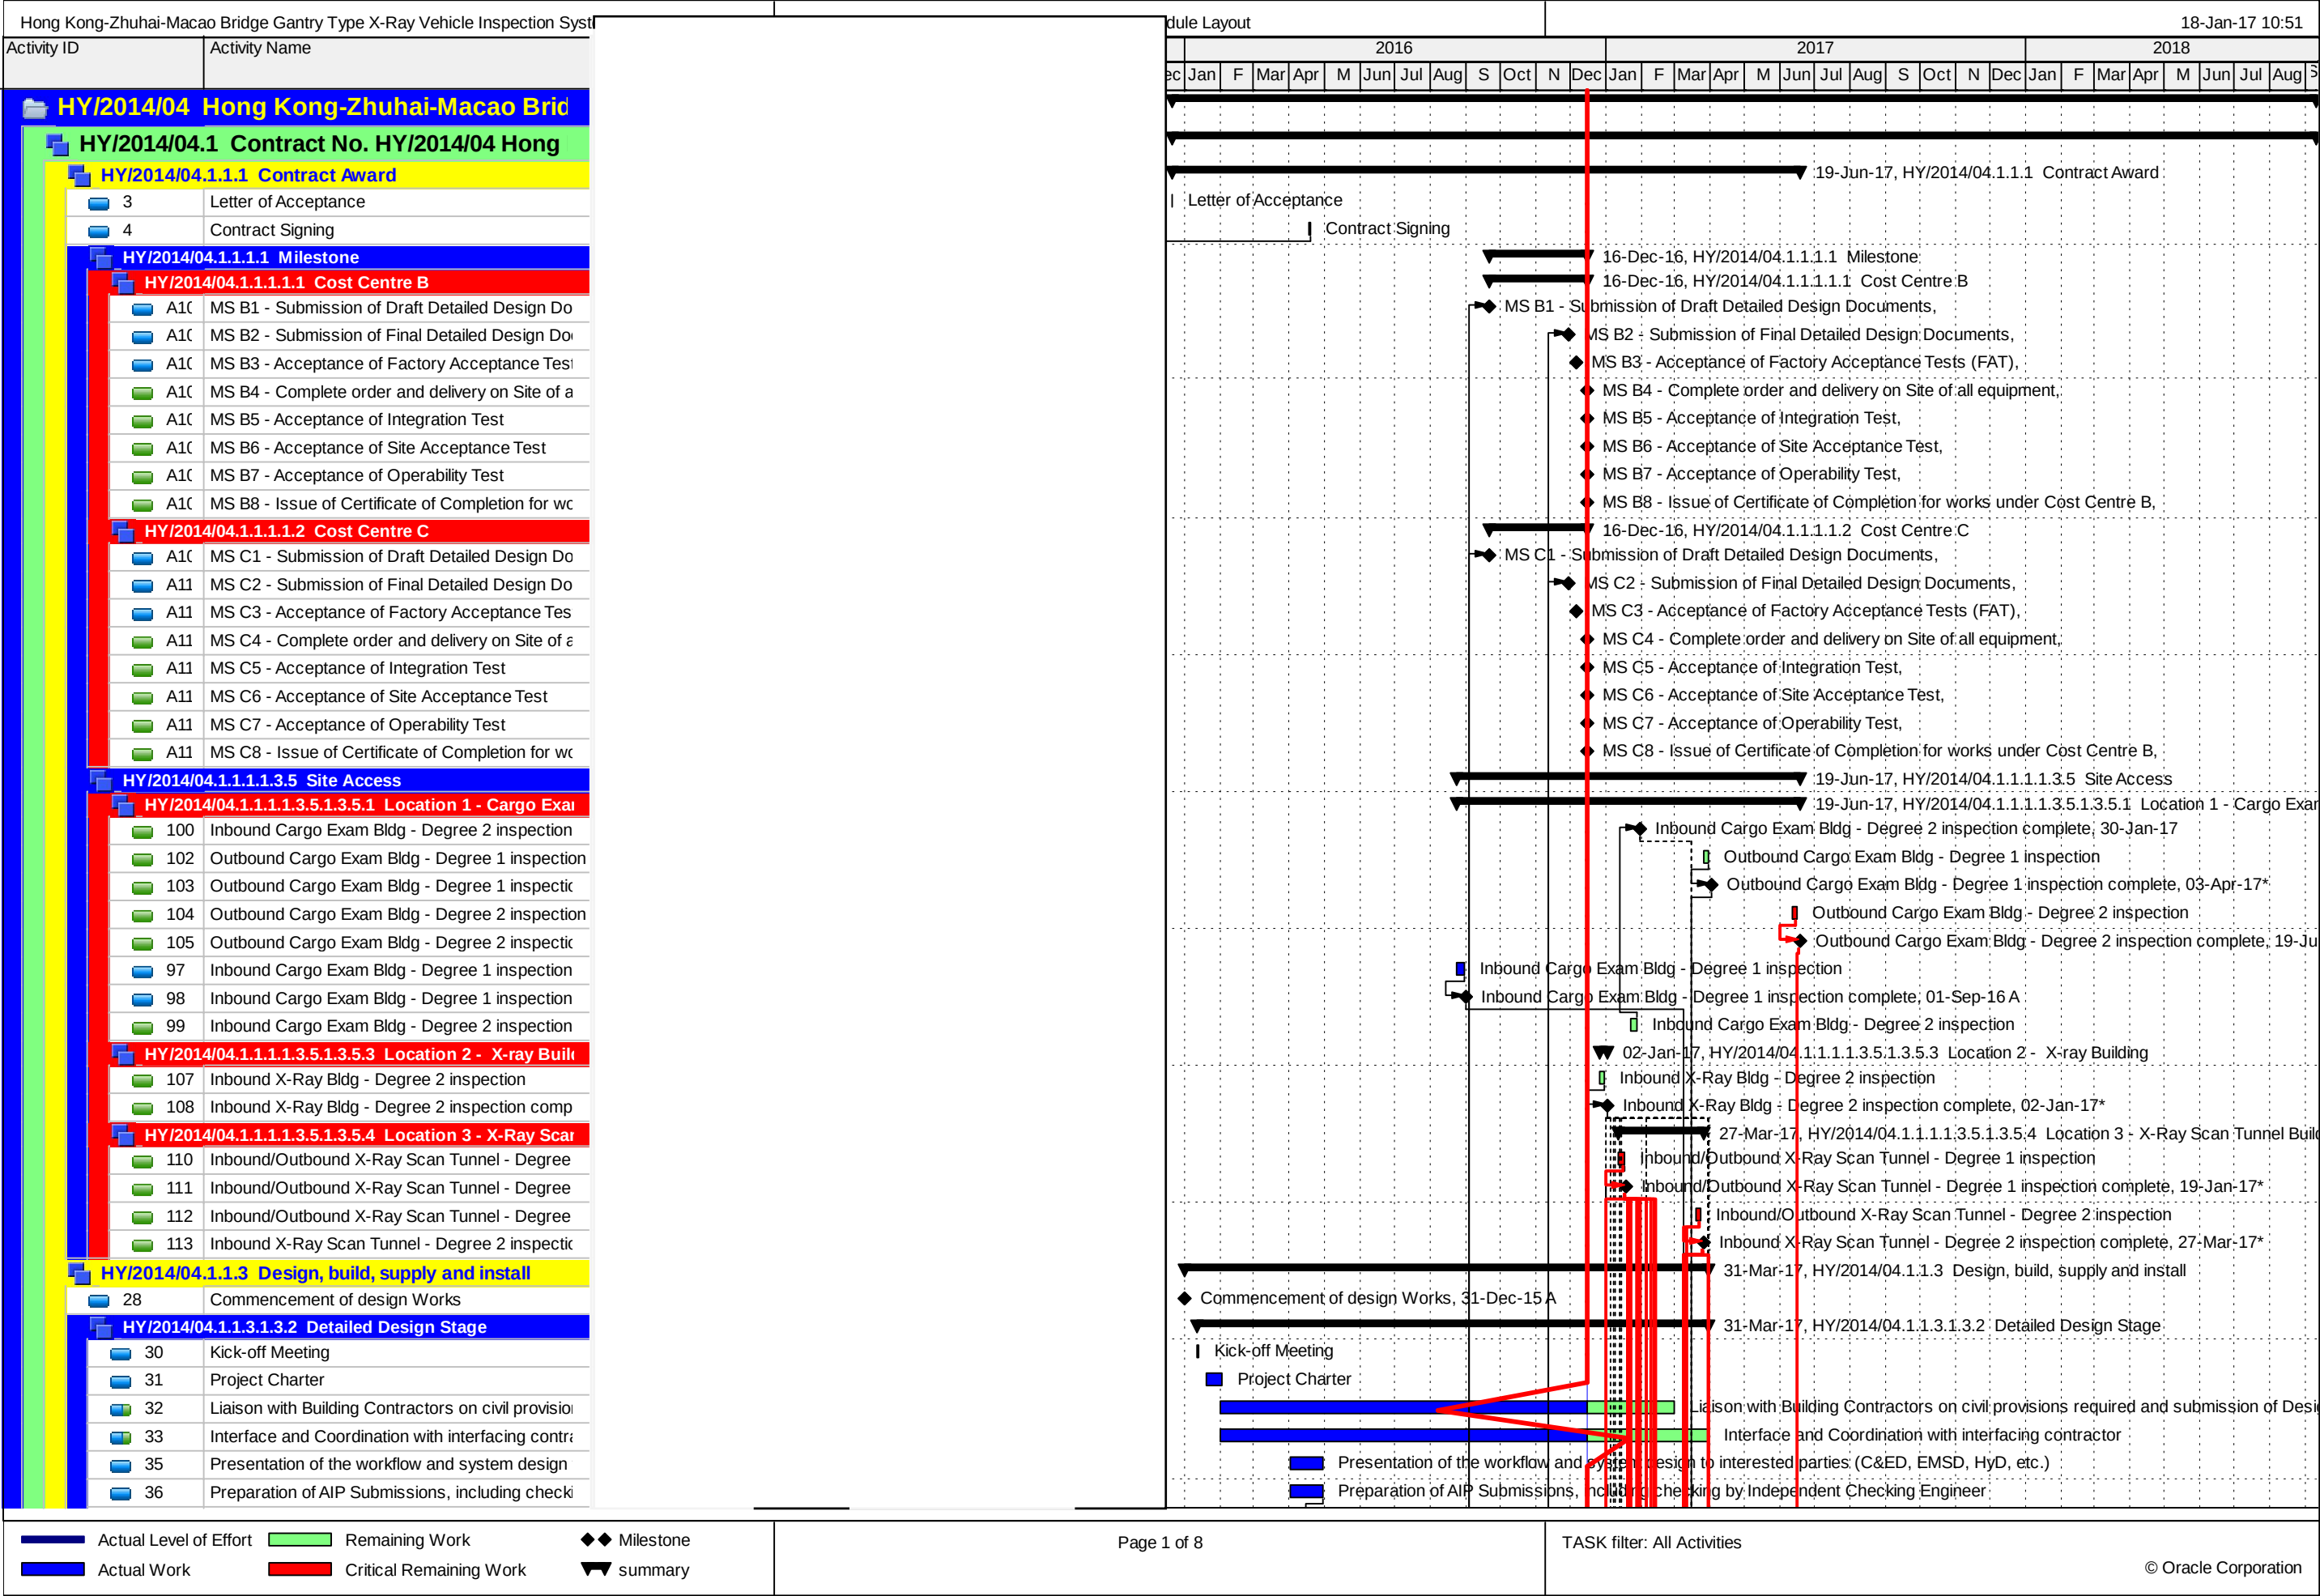

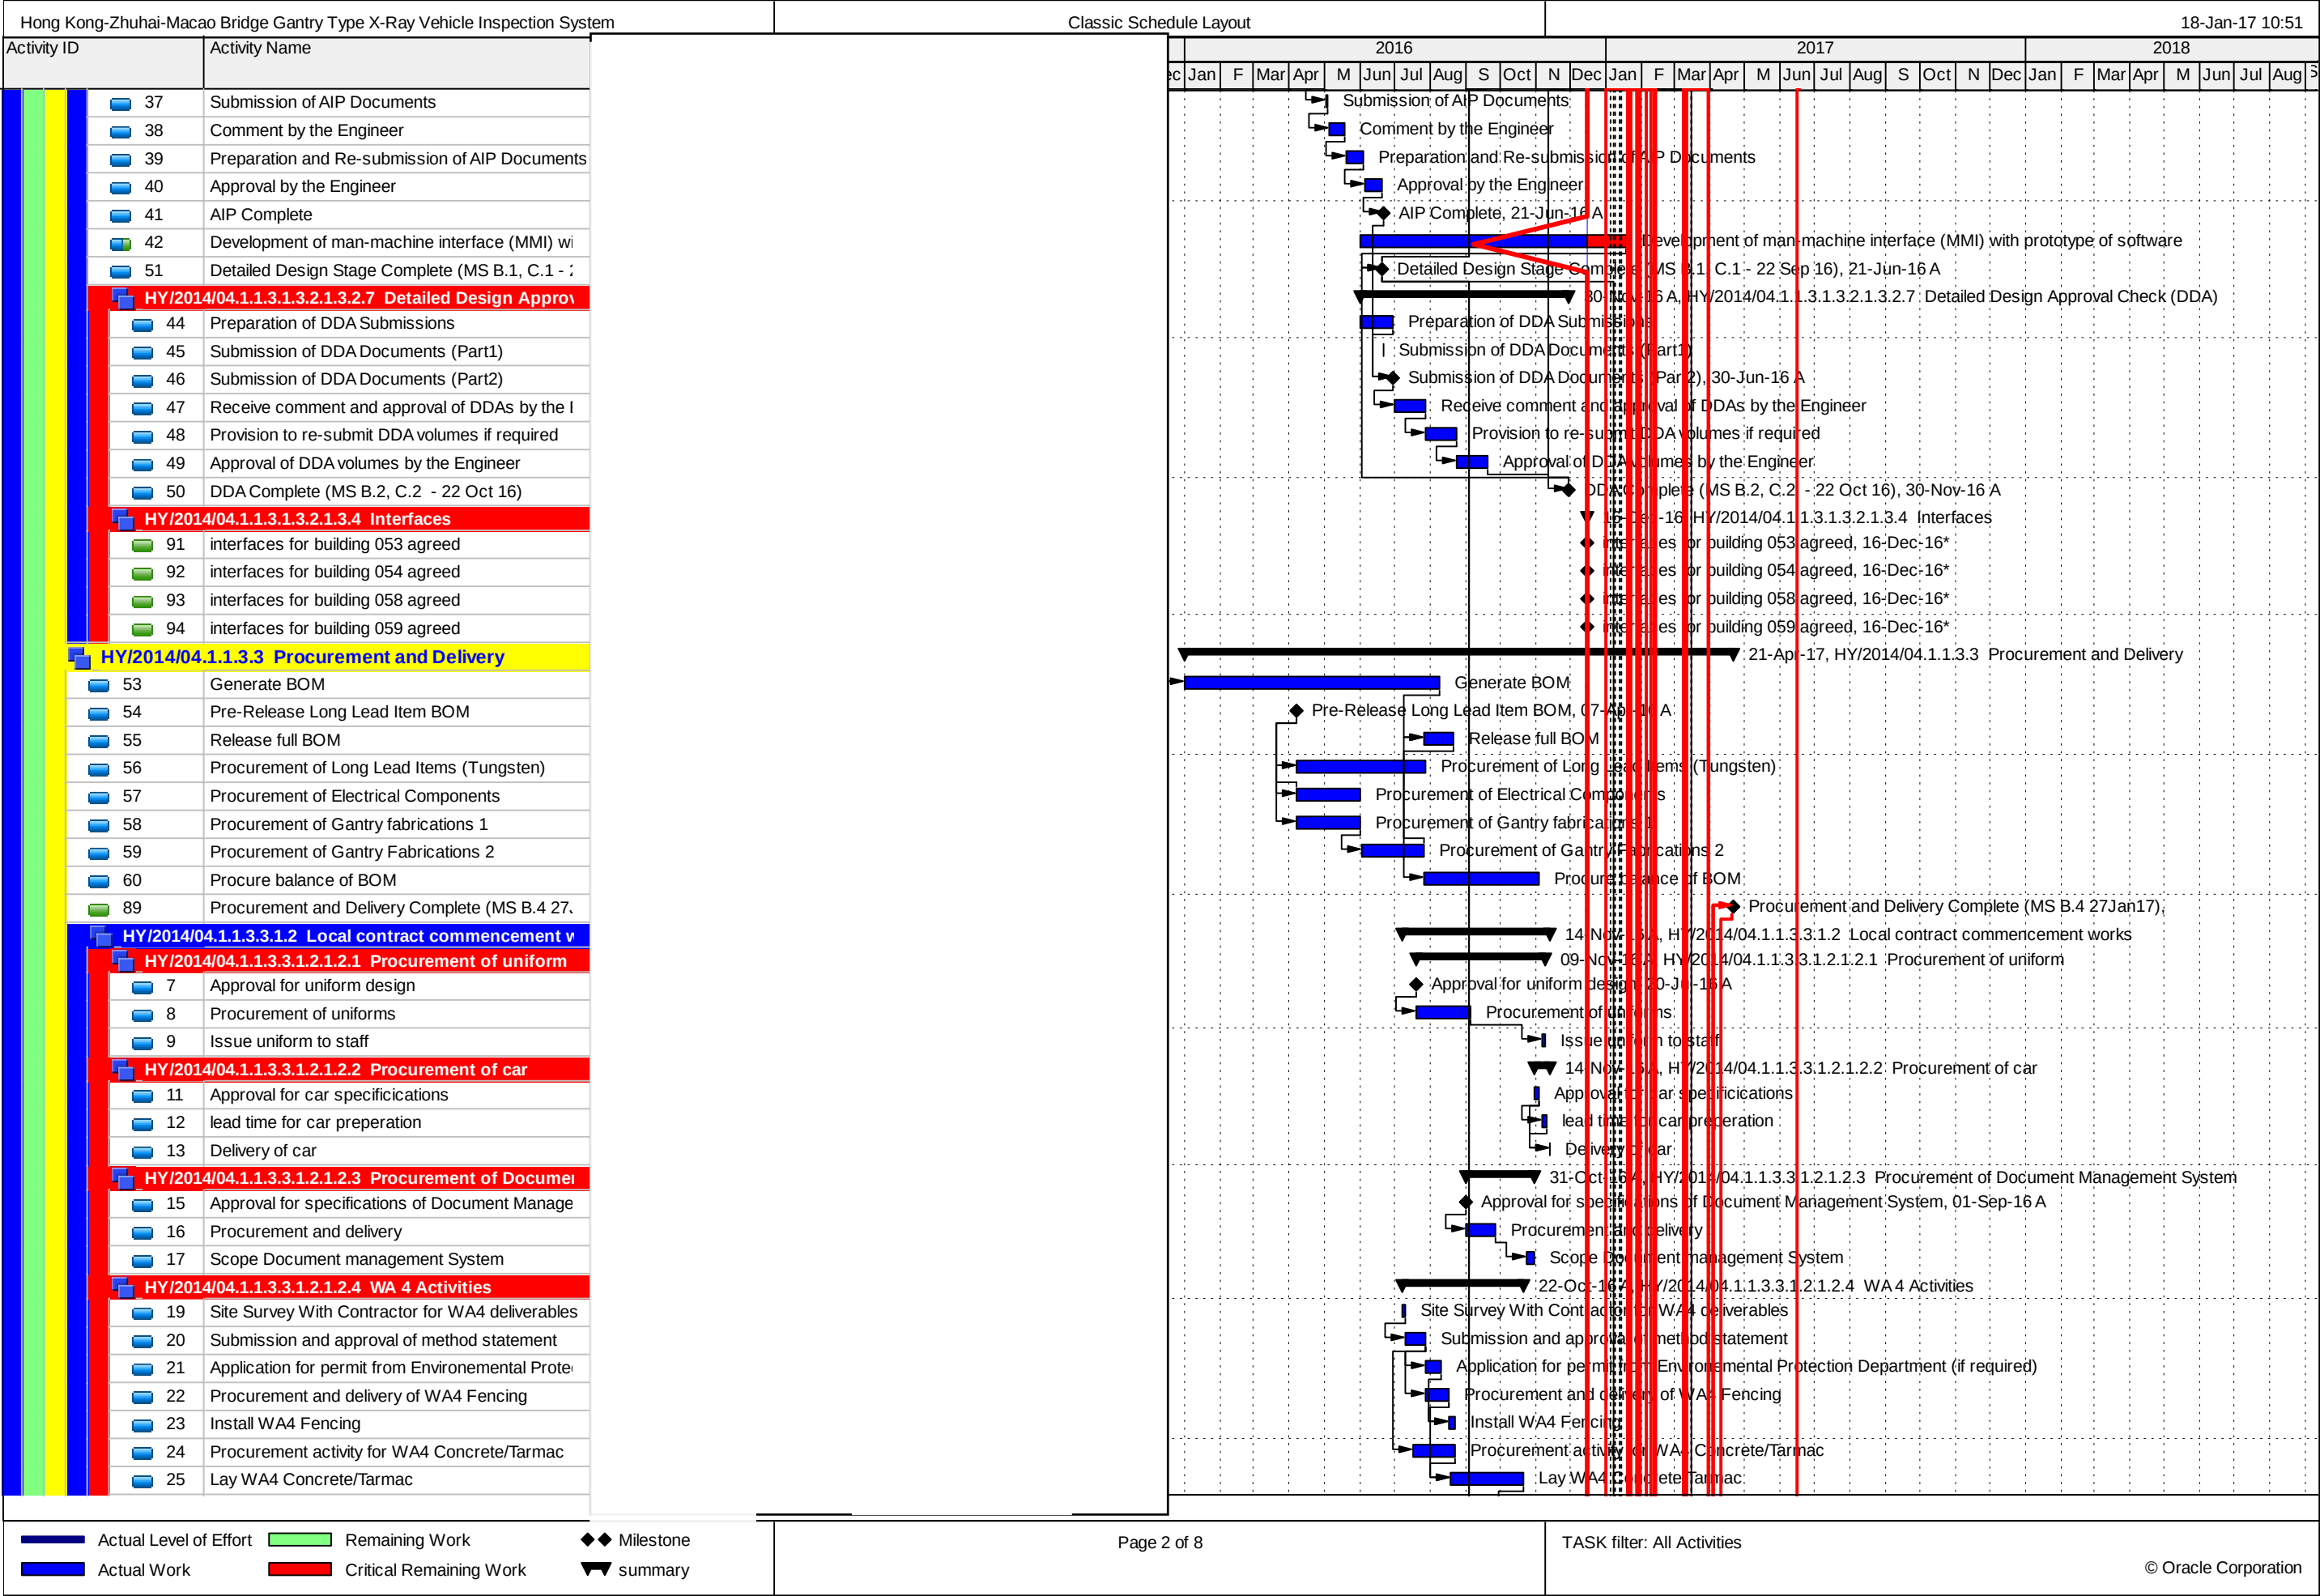

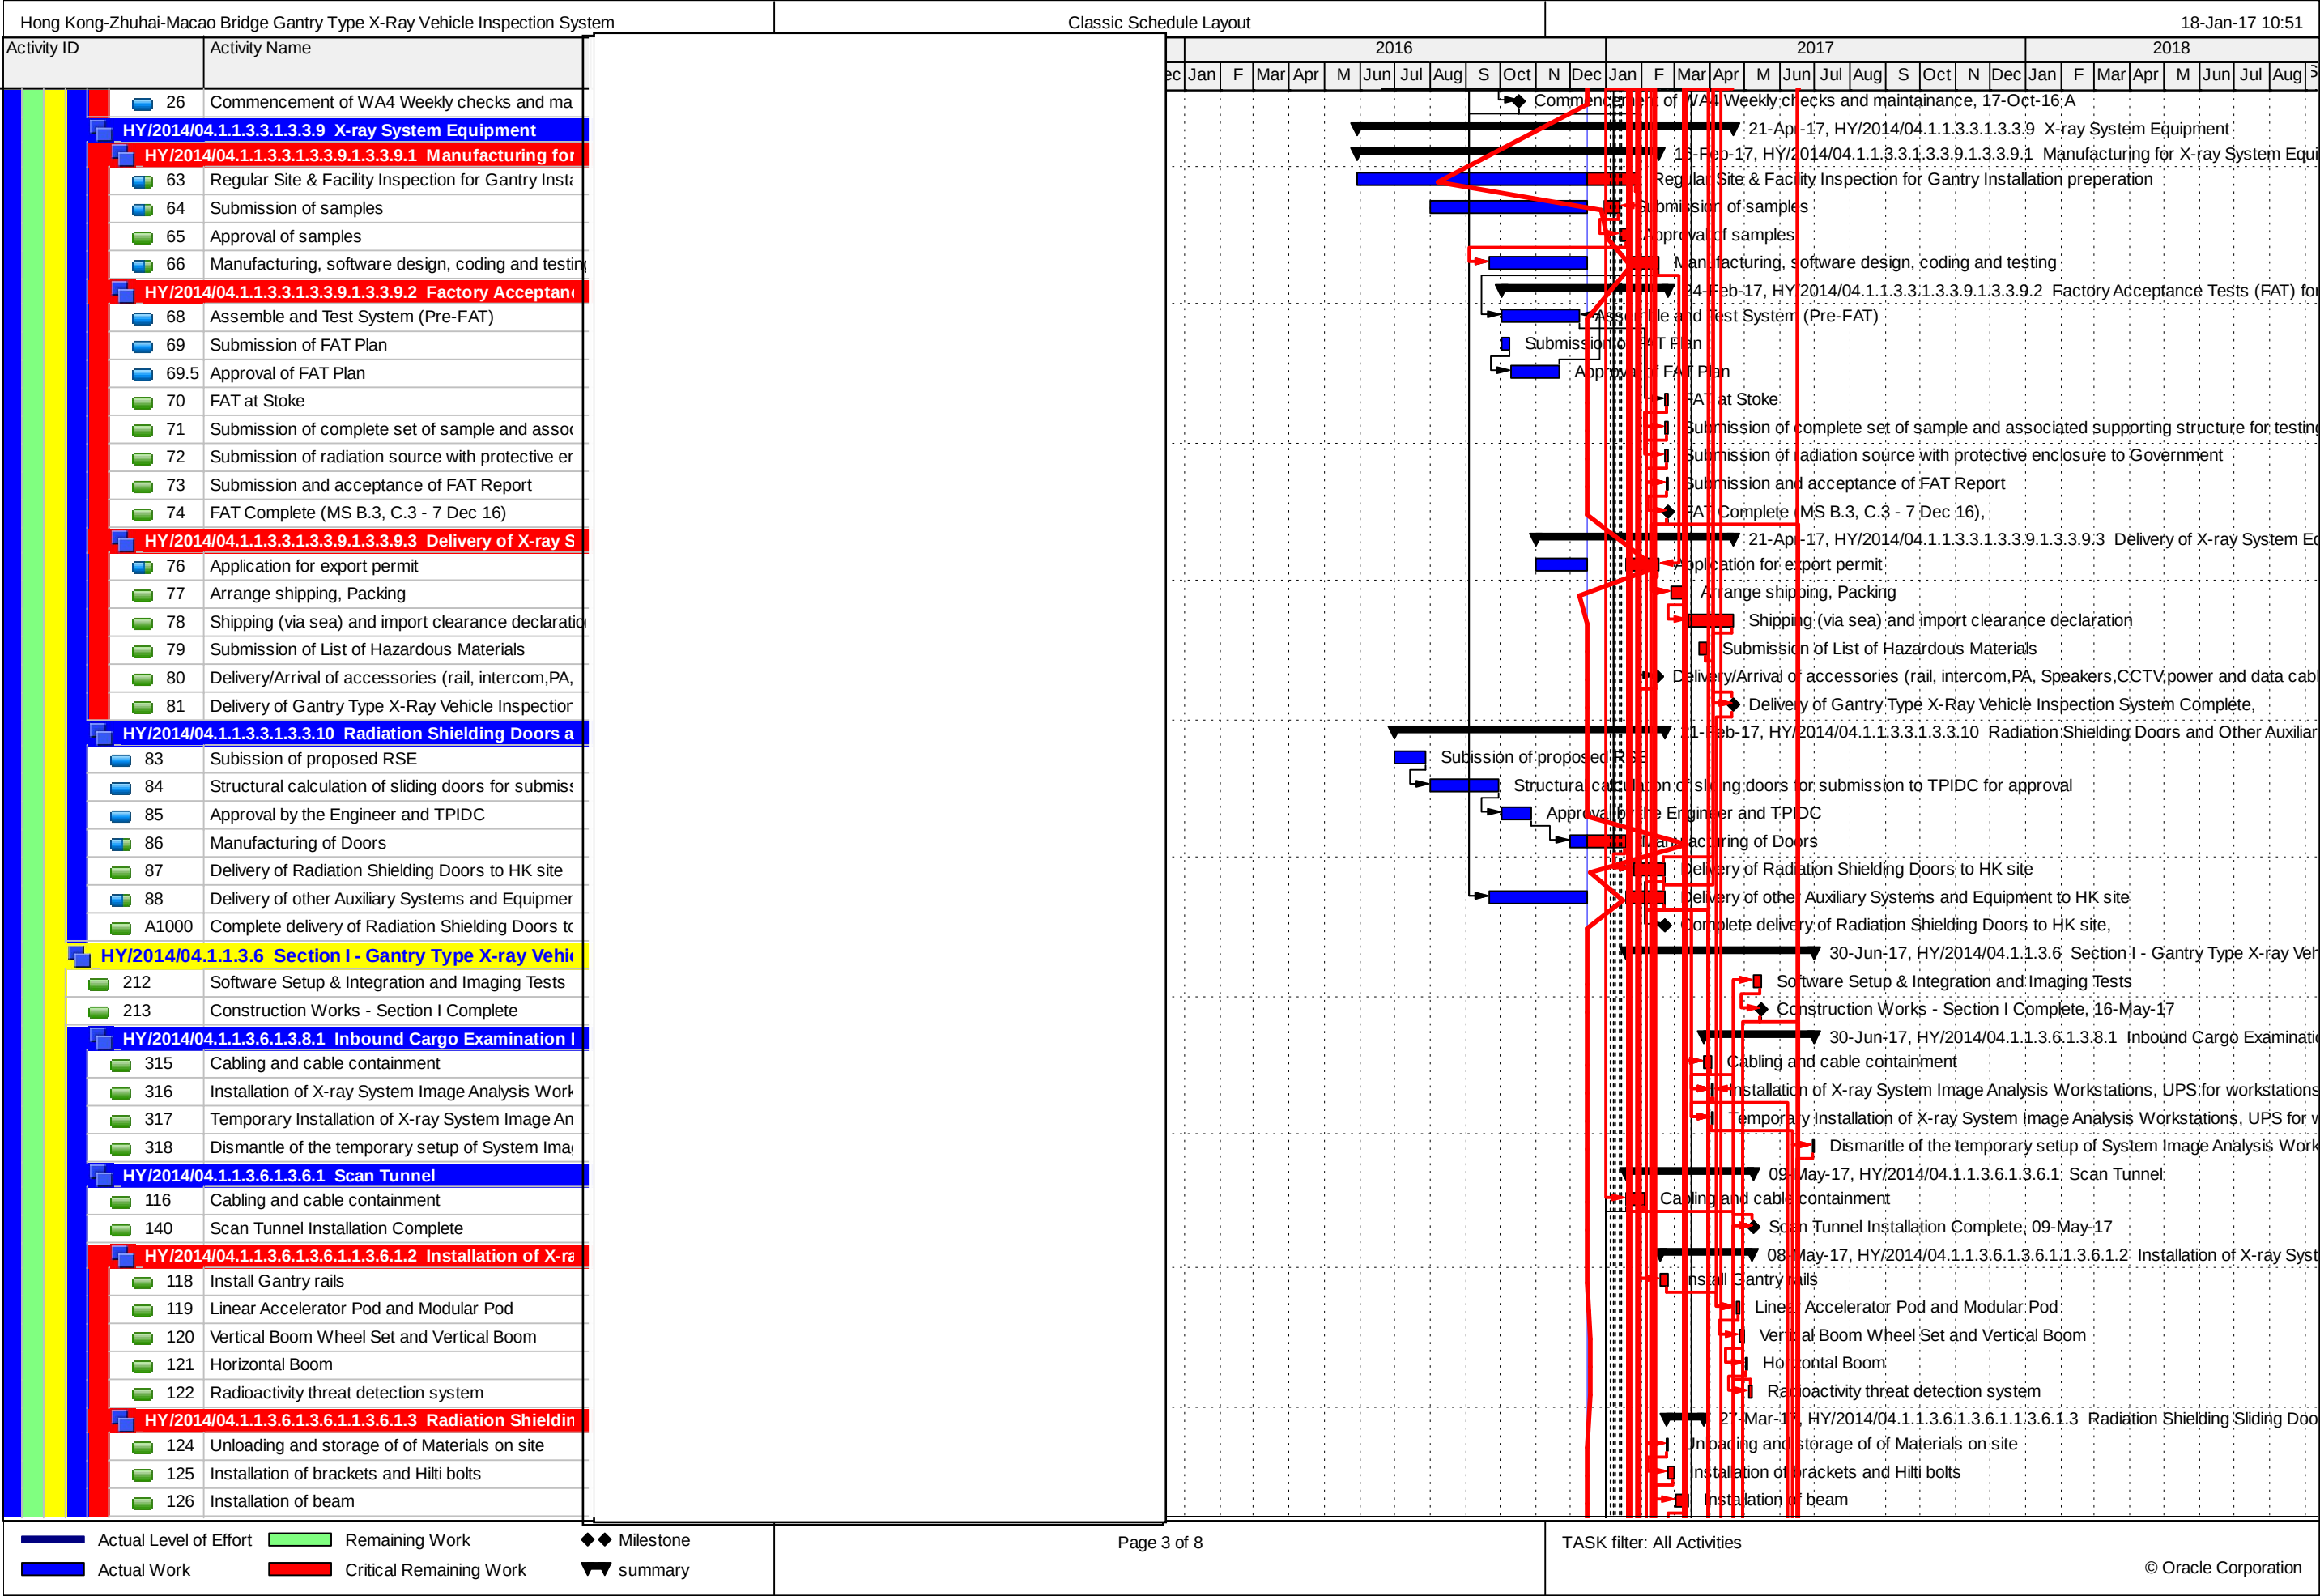

[illegible]

[illegible]

Hong Kong-Zhuhai-Macao Bridge Gantry Type X-Ray Vehicle Inspection System										Classic Schedule Layout										18-Jan-17 10:51																																										
Activity ID		Activity Name													2016												2017												2018																							
															c Jan F Mar Apr M Jun Jul Aug S Oct N Dec												Jan F Mar Apr M Jun Jul Aug S Oct N Dec												Jan F Mar Apr M Jun Jul Aug S Oct N Dec																							
		X-ray System Image Analysis Workstation																																																												
		Radiation shielding sliding door controller																																																												
		CCTV System																																																												
		Public Address System																																																												
		UPS for workstations, equipment and system																																																												
		HY/2014/04.1.1.3.7.1.3.7.2.1.3.7.2.2.1.3.7.2.2.4 Image Interpretation Workstation																																																												
		Intercom System																																																												
		Radiation Monitoring and Alarm System																																																												
		X-ray System Image Analysis Workstation																																																												
		Printer																																																												
		UPS for workstations, equipment and system																																																												
		HY/2014/04.1.1.3.7.1.3.7.2.1.3.7.2.2.1.3.7.2.2.5 X-ray Examination System																																																												
		Server																																																												
		Server rack																																																												
		UPS for workstations, equipment and system																																																												
		HY/2014/04.1.1.3.7.1.3.7.2.1.3.7.2.2.1.3.7.2.2.6 Driver's Waiting Room																																																												
		CCTV System																																																												
		Intercom System																																																												
		Radiation Monitoring and Alarm System																																																												
		Speaker																																																												
		UPS for workstations, equipment and system																																																												
		HY/2014/04.1.1.3.7.1.3.7.2.1.3.7.2.2.1.3.7.2.2.7 Training room																																																												
		Projector screen (Screen size 106")																																																												
		Ceilling mounted projector																																																												
		X-ray System Training Workstation																																																												
		Radiation Monitoring and Alarm System																																																												
		UPS for workstations, equipment and system																																																												
		Training aids																																																												
		Printer																																																												
		HY/2014/04.1.1.3.8 Section III - Cargo Examination Building																																																												
		322 Construction Works - Section III Complete																																																												
		HY/2014/04.1.1.3.8.1.3.8.2 Outbound Cargo Examination Building																																																												
		320 Cabling and cable containment																																																												
		321 Installation of X-ray System Image Analysis Workstations, UPS for workstations, equipment and system																																																												
		HY/2014/04.1.1.3.9 On-Site Testing & Commissioning																																																												
		335 Operability Test																																																												
		336 T&C Complete and Issurance of Certificate of Acceptance, Construction Works Complete, 05-Sep-17																																																												
		345 Contruction Works Complete																																																												
		HY/2014/04.1.1.3.9.1.3.10 Defect Liability Period for Construction Works																																																												
		359 Defect Liability Period																																																												
		360 Submission of Warranty Completion Test Plan																																																												
		361 Warranty Completion Test																																																												
		362 DLP Complete and issuance of Defect Liability Certificate																																																												
		363 Commencement of Maintenance Services																																																												
		HY/2014/04.1.1.3.9.1.3.9.1 Integration Test																																																												
		325 Submission of Integration Test Plan																																																												
		326 Integration Test																																																												
		327 Preparation, submission and acceptance of Integration Test report																																																												
		327.5 Complete Inegration Test (MS B.5 - 3 Mar 17)																																																												
		HY/2014/04.1.1.3.9.1.3.9.2 Site Acceptance Test																																																												
		329 Submission of SAT Plan																																																												

Actual Level of Effort

Actual Work

Remaining Work

Critical Remaining Work

Milestone

summary

Page 7 of 8

TASK filter: All Activities

© Oracle Corporation

 Actual Level of Effort
  Remaining Work
  Milestone
 Actual Work
 Critical Remaining Work
 summary

Page 8 of 8

TASK filter: All Activities

© Oracle Corporation
