

Activity ID		Activity Name		December 2017							January 2018					February 2018					March 2018		
				19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	04	11			
C8 - 3 Month Rolling Programme, Statused 01 January 2018																							
PROGRAMME SUMMARY																							
Fire Service Inspection Schedule Summary																							
GENERAL/PRELIMINARIES																							
DESIGN AND ENGINEERING																							
PROCUREMENT, MANUFACTURING & DELIVERIES																							
CONSTRUCTION																							
Building 021 - C&ED Dangerous Goods Store																							
Raft																							
Structure																							
ABWF/E&M																							
Internal Finishes																							
Degree 1																							
Degree 2																							
RAB-21-0410		021 - Power On																					
Degree 3																							
RAB-21-0345		KD4C - Projected achievement of Stage 4C of the Works																					
RAB-KD4C10		021 - End Users and MoM handover inspection																					
Roof Finishes																							
RAB-21-0270		021 - Install Railing 50m																					
External Finishes																							
Facade																							
RAB-21-0320		021 - Snagging and Remedials (External)																					
At Grade																							
RAB-21-380		021 - Prepare Sub Grade																					
RAB-21-390		021 - Lay Granular Sub-Base																					
RAB-21-360		021 - Concrete Block Paving																					
Utilities and Drainage																							
Testing & Commissioning																							
Statutory Submissions & Approvals (Day 670 Completion)																							
Dangerous Goods Licence																							
RAB-21-0350		021 - DG Licence Iprocessing & Inspection																					
RAB-21-0360		021 - Issue DG Licence																					
Fire Servives Department (VAC)																							
RAB-FSD-300		021 - FS Inspection Period																					
RAB-FSD-310		021 - Fire Certificate Obtained (Form 172) Handover																					
Engineer (AECOM)																							
RAB-21-2190		021 - Submit As-Built Drawings to the Engineer																					
RAB-21-2200		021 - Engineer Inspection Period																					
RAB-21-2210		021 - Engineer Issue Occupation Permit																					
RAB-KD154		KD4 - Projected completion of Section IV of the Works (670 days) Building 0																					
Building 022 - Customs Detective Dog Base Building																							
Excavation																							
Raft Foundations																							
Structure																							
Walls & Columns																							
Roof Slab																							
North Structure																							
Cure and Strip																							
Middle Structure																							

Remaining Level of Effort

Actual Work

Critical Remaining ...

Actual Level of Effort

Remaining Work

Finish Constraint

3-Month Rolling Programme Update, 01 Jan. 2018

Date

01-Jan-18

Revision

3-Month Rolling Programme, 01 Jan-18 Update

Checked

Approved

LEIGHTON 恒耀		Contract No. HY/2014/05 - Remaining Ancillary Building and Facilities												Page 2 of 20					
Activity ID	Activity Name	er 2017			December 2017				January 2018					February 2018				March 2018	
			19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	04	11
	Cure and Strip																		
	South Structure																		
	Cure and Strip																		
	ABWF/E&M																		
	Internal Finishes																		
	North																		
	Degree 1																		
	Degree 2																		
	RAB-22-0910	022 - Power On							◆										
	Degree 3																		
	RAB-22-0865	022- Ceiling Frame & Board Panel																	
	RAB-22-8395	022 - Wall Tiling & Painting																	
	RAB-22-8275	022 - MEP Final Fix																	
	RAB-22-8365	022 - Floor Finish Other Than Early Handovr Rooms																	
	RAB-22-8265	022 - Door Panel & Ironmongery																	
	RAB-22-8295	022 - Snagging and Remedials (Bldg. Internal)																	
	RAB-22-0870	022 - MEP Balance of Works																	
	RAB-22-0980	022 - End Users and MOM Handover Inspection																	
	RAB-22-0950	022 - ABWF and MEP works to Degree 3 (KD5C)																	
	External Finishes																		
	Facade																		
	RAB-22-0470	022 - External Painting, Tiling & Cladding																	
	RAB-22-0710	Snag Listing - Bldg. External & External Works																	
	At Grade																		
	RAB-22-2100	022 - Prepare Sub Grade																	
	RAB-22-2120	022 - Lay Granular Sub-Base																	
	RAB-22-2140	022 - Concrete Block Paving																	
	RAB-22-2170	022 - Landscaping for Outdoor Excise Lawn																	
	Roof Finishes - North																		
	RAB-22-0720	022 - Make good external surfaces																	
	Specialist Installations																		
	Window Wall																		
	Dog Swimming Pool																		
	RAB-22-0600	022 - Tiling to Dog Swimming Pool																	
	RAB-22-0490	022 - Backfill to ground level at Dog Swimming Pool																	
	RAB-22-0640	022 - Plumbing and filtration systems																	
	RAB-22-0630	022 - Metalworks and Railings																	
	RAB-22-0700	022 - Snagging and Remedials - Dog Pool																	
	Utilities and Drainage																		
	Testing & Commissioning																		
	RAB-TC22-1000	022 - T&C (HVAC, FS, P&D, OTHERS)																	
	Statutory Submissions & Approvals (Day 670 Completion)																		
	BEE0																		
	RAB-BEE-120	022 - Registered Energy Assessor Inspection & Certification																	
	RAB-BEE-130	022 - Submit REA Certification to EDMS																	
	RAB-BEE-140	022 - EDMS Issue of Cert of Compliance Registration (COCR)																	
	Water Supplies Department (WSD)																		
	Commencement																		
	Completion																		
	RAB-WSD-804	022 - Submit WWO 46 Pt. IV																	
	RAB-WSD-254	022 - WSD's Processing/Inspection/Meter Connection																	
	RAB-WSD-264	022 - Permanent Water ON/WSD Issue WWO 46 Part V Cert & Water Cor																	
Remaining Level of Effort Actual Level of Effort Actual Work Remaining Work Critical Remaining ... Finish Constraint		3-Month Rolling Programme Update, 01 Jan. 2018								Date	Revision				Checked	Approved			
										01-Jan-18	3-Month Rolling Programme, 01 Jan-18 Update								

[illegible]

LEIGHTON 位頓 		Contract No. HY/2014/05 - Remaining Ancillary Building and Facilities												Page 4 of 20				
Activity ID	Activity Name	November 2017			December 2017				January 2018				February 2018				March 2018	
		19	26		03	10	17	24	31	07	14	21	28	04	11	18	25	04
</																		

Activity ID		Activity Name		er 2017		December 2017				January 2018					February 2018				March 2018	
				19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	04	11
	RAB-BEE-170	023 - EDMS Issue of Cert of Compliance Registration (COCR)																		
	EMSD - Building 023 Lift Inspection																			
	RAB-FSD-190	023 - EMSD Lift Inspection																		
	RAB-FSD-106	023 - EMSD Lift Certificate Issued - Building 023																		
	Water Supplies Department (WSD)																			
	Commencement																			
	Completion																			
	RAB-WSD-774	023 - Submit WWO 46 Pt. IV for Building 023																		
	RAB-WSD-107	023 - WSD Inspection/Meter Connection																		
	RAB-WSD-109	023 - Permanent Water ON/WSD Issue WWO 46 Part V - Water Certificate																		
	Fire Servives Department (VAC)																			
	RAB-FSD-110	023 - FS Inspection Period For Building 023																		
	RAB-FSD-290	023 - Issuance of FS 172, FS Certificate of Compliance																		
	Engineer (AECOM)																			
	RAB-23-2250	023 - Submit Building 023 As Built Drawings to Engineer																		
	RAB-23-2260	023 - Engineer Inspection Period																		
	RAB-23-2270	023 - Engineer Issue Occupation Permit																		
	RAB-KD134	KD3 - Projected completion of Section III of the Works (610 days)																		
	Building 025 - Inbound Private Car Annexure																			
	Excavation																			
	Raft Foundations																			
	Structure																			
	Walls & Columns																			
	Roof Slab																			
	Cure and Strip																			
	ABWF/E&M INTERNAL FINISHES																			
	INTERNAL FINISHING WORKS																			
	Degree 1																			
	Degree 2																			
	Degree 3																			
	RAB-25-7620	025 - Ceiling Panel																		
	RAB-25-7580	025 - Floor Painting																		
	RAB-25-7590	025 - Floor Carpet																		
	RAB-25-7550	025 - MEP Balance of Works																		
	RAB-25-7370	025 - Snagging and Remedials																		
	RAB-25-7375	KD6C - Projected achievement of Stage 6C of the Works																		
	RAB-KD6C10	025 - End Users and MoM handover inspection																		
	RAB-25-7630	025 - Early Handover Rooms Ready to End Users***, Target to Achieve KDI																		
	External Finishes																			
	Facade																			
	RAB-25-0580	025 - Make good external surfaces																		
At Grade																				
RAB-25-6400	025 - Prepare Sub Grade																			
RAB-25-6390	025 - Laying Geo Textile																			
RAB-25-6410	025 - Lay Granular Sub-Base																			
RAB-25-6420	025 - Laying Course																			
RAB-25-6380	025 - Concrete Block Paving																			
RAB-25-0600	025 - Snagging and Remedials																			
Roof Finishes																				
RAB-25-0550	025 - Install Railing (222m)																			
Green Roof																				
Specialist Installations																				

Remaining Level of Effort Actual Work Critical Remaining ... Actual Level of Effort Remaining Work Finish Constraint

3-Month Rolling Programme Update, 01 Jan. 2018

Date	Revision	Checked	Approved
01-Jan-18	3-Month Rolling Programme, 01 Jan-18 Update		

Activity ID	Activity Name		December 2017					January 2018					February 2018					March 2018	
			19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	04	11
</																			

Remaining Level of Effort Actual Work Critical Remaining ... Actual Level of Effort Remaining Work Finish Constraint	3-Month Rolling Programme Update, 01 Jan. 2018	Date 01-Jan-18	Revision 3-Month Rolling Programme, 01 Jan-18 Update	Checked	Approved
---	---	--------------------------------------	--	--------------------	---------------------

Activity ID		Activity Name		er 2017							December 2017					January 2018					February 2018					March 2018	
					19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	04	11						
RAB-32-7250		032 - Submit Building 032 As Built Drawings to Engineer																									
Building 044 - E&M Maintenance Building																											
Excavation																											
Raft																											
Structure																											
Walls & Columns																											
Ground to First Floor																											
First Floor																											
Cure and Strip																											
First Floor to Second Floor																											
Second Floor																											
Cure and Strip																											
Second Floor to Roof																											
Roof Level																											
Cure and Strip																											
ABWF/E&M																											
Ground Floor																											
Degree 1																											
Degree 2																											
RAB-44-9175		044 - MEP 2nd Fix - G/F																									
RAB-44-0760		044 - Door & Windor Frame + Louver - G/F																									
Degree 3																											
RAB-44-9285		044 - Wall Finish, Paint & Tile - G/F																									
RAB-44-9255		044 - Ceiling Paint - G/F																									
RAB-44-9185		044 - MEP Final Fix - G/F																									
RAB-44-9265		044 - Floor Tile Finish - G/F																									
RAB-44-9235		044 - Ceiling Panel Frame - G/F																									
RAB-44-9275		044 - Glazing - G/F																									
RAB-44-9345		044 - Ceiling Panel - G/F																									
RAB-44-9245		044 - Ceiling Plaster Board Frame																									
RAB-44-9295		044 - Door Panel & Ironmongery - G/F																									
RAB-44-9355		044 - Floor Paint Finish - G/F																									
RAB-44-9395		044 - Ceiling Plaster Board																									
First Floor																											
Degree 1																											
Degree 2																											
RAB-44-9365		044 - MEP 2nd Fix - 1/F																									
RAB-44-9455		044 - Door & Windor Frame + Louver - 1/F																									
Degree 3																											
RAB-44-9555		044 - Wall Finish, Paint & Tile - 1/F																									
RAB-44-9465		044 - Ceiling Paint Finish - 1/F																									
RAB-44-9565		044 - Floor Tile Finish - 1/F																									
RAB-44-9375		044 - MEP Final Fix - 1/F																									
RAB-44-9385		044 - Ceiling Panel Frame - 1/F																									
RAB-44-9485		044 - Glazing - 1/F																									
RAB-44-9505		044 - Door Panel & Ironmongery - 1/F																									
RAB-44-9695		044 - Ceiling Plaster Board Frame																									
RAB-44-9495		044 - Ceiling Panel - 1/F																									
RAB-44-9705		044 - Ceiling Plaster Board																									
RAB-44-9475		044 - Floor Paint Finish - 1/F																									
Second Floor																											
Degree 1																											
Remaining Level of Effort		Actual Work		Critical Remaining ...																							
Actual Level of Effort		Remaining Work		△ Finish Constraint																							
3-Month Rolling Programme Update, 01 Jan. 2018												Date		Revision					Checked		Approved						
												01-Jan-18		3-Month Rolling Programme, 01 Jan-18 Update													

LEIGHTON 位頓		Contract No. HY/2014/05 - Remaining Ancillary Building and Facilities												Page 9 of 20							
Activity ID	Activity Name	November 2017			December 2017				January 2018					February 2018				March 2018			
			19	26		03	10	17	24		31	07	14	21	28		04	11	18	25	

Activity ID		Activity Name		er 2017			December 2017			January 2018					February 2018				March 2018					
				19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	04	11				
	RAB-45-10015	045 - MEP 2nd Fix - 1/F																						
	RAB-45-10105	045 - Door & Windor Frame + Louver - 1/F																						
	Degree 3, 1/F																							
	RAB-45-10145	045 - Wall Finish, Paint & Tile - 1/F																						
	RAB-45-10125	045 - Floor Finish (Paint & Tile) - 1/F																						
	RAB-45-10205	045 - Ceiling Plaster Board Frame Ceiling Panel Frame- 1/F																						
	RAB-45-10025	045 - MEP Final Fix - 1/F																						
	RAB-45-10155	045 - Door Panel & Ironmongery - 1/F																						
	RAB-45-10285	045 - Glazing - 1/F																						
	RAB-45-10245	045 - Ceiling Plaster Board & Ceiling Panel - 1/F																						
	RAB-45-10275	045 - Handover to End users***																						
	Second Floor, 2/F																							
	Degree 1, 2/F																							
	Degree 2, 2/F																							
	RAB-45-10225	045 - MEP 2nd Fix - 2/F																						
	RAB-45-10315	045 - Door & Windor Frame + Louver - 2/F																						
	RAB-45-10295	045 - Access for C3 Equip. Installation, 2/F***																						
	RAB-45-0950	KD8B - Projected achievement of Stage 8B of the Works - 2/F, 045																						
	RAB-45-10255	045 - Power On - 2/F																						
	Degree 3, 2/F																							
	RAB-45-10355	045 - Wall Finish, Paint & Tile - 2/F																						
	RAB-45-10235	045 - MEP Final Fix - 2/F																						
	RAB-45-10345	045 - Glazing - 2/F																						
	RAB-45-10335	045 - Floor Finish (Paint & Tile) - 2/F																						
	RAB-45-10365	045 - Door Panel & Ironmongery - 2/F																						
	RAB-45-10375	045 - Ceiling Plaster Board Frame & Ceiling Panel Frame - 2/F																						
	RAB-45-10385	045 - Ceiling Plaster Board & Ceiling Panel - 2/F																						
	RAB-45-0980	045 - Snagging and Remedials - 2/F																						
	RAB-45-10305	045 - MEP Balance of Works																						
	RAB-45-10265	045 - End Users and MoM handover inspection																						
	RAB-45-0970	KD8C - Projected achievement of Stage 8C of the Works - 2/F, 045																						
	External Finishes																							
	Bldg. External Finishes																							
	Facade																							
	RAB-45-0620	045 - Install External Louvers /Windows/Doors																						
	RAB-45-0760	045 - Make good external surfaces																						
	At Grade																							
	RAB-45-6580	045 - Prepare Sub Grade																						
	RAB-45-6570	045 - Laying Geo Textile																						
	RAB-45-6590	045 - Lay Granular Sub-Base																						
RAB-45-6600	045 - Laying Course																							
RAB-45-6560	045 - Concrete Block Paving																							
RAB-45-6620	045 - Snag Listing, External																							
Roof Finishes -																								
RAB-45-0910	045 - Install Roof Tiles																							
RAB-45-0930	045 - Install Cat Ladder and Roof Hatch																							
RAB-45-0920	045 - Install Railing																							
Green Roof - Noth Side, 2/F Level																								
RAB-45-0680	045 - Install green Roof Irrigation Systems																							
RAB-45-0740	045 - Complete Green Roofing Works																							
Specialist Installations																								
Remaining Level of Effort		Actual Work		Critical Remaining ...		3-Month Rolling Programme Update, 01 Jan. 2018										Date		Revision			Checked		Approved	
Actual Level of Effort		Remaining Work		Finish Constraint												01-Jan-18		3-Month Rolling Programme, 01 Jan-18 Update						

Activity ID	Activity Name	er 2017		December 2017				January 2018					February 2018					March 2018	
			19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	04	11
045 - Building 045	Window Wall																		
	East																		
	RAB-45-6960	045 - Install Primary Steelwork for Window Wall																	
	RAB-45-6970	045 - Install Secondary Steelwork for Window Wall																	
	RAB-45-6980	045 - Glazing to Window Wall																	
	West																		
	RAB-45-6990	045 - Install Primary Steelwork for Window Wall																	
	RAB-45-7000	045 - Install Secondary Steelwork for Window Wall																	
	RAB-45-7010	045 - Glazing to Window Wall																	
	Utilities and Drainage																		
	RAB-45-7945	045 - Utilites and Common Telecom Ducting																	
	RAB-45-7955	045 - Install Flushing Water Mains																	
	RAB-45-7965	045 - Install Fresh Water Mains																	
	RAB-45-7975	045 - Install FS Water Main																	
	Testing & Commissioning																		
	RAB-TC45-1020	045 - T&C (HVAC, FS, P&D, OTHERS)																	
	Statutory Submissions & Approvals (Day 670 Completion)																		
	BEE0																		
	RAB-BEE-270	045 - Registered Energy Assessor Inspection & Certification																	
	RAB-BEE-280	045 - Submit REA Certification to EDMS																	
	RAB-BEE-290	045 - EDMS Issue of Cert of Compliance Registration (COCR)																	
	EMSD - Building 045 Lift Inspection																		
	RAB-FSD-250	045 - EMSD Lift Inspection																	
	RAB-FSD-130	045 - EMSD Lift Certificate Issued - Building 045																	
	Fuel Tank - DG License																		
	RAB-FSD-680	045 - FSD Issue License																	
	Generator Set - EPD Permit																		
	Water Supplies Department (WSD)																		
	Commencement																		
	Completion																		
	RAB-WSD-654	045 - Submit WWO 46 Pt. IV																	
	RAB-WSD-284	045 - WSD's Processing/Inspection/Meter Connection																	
	RAB-WSD-294	045 - WSD Issue WWO 046 Part V, Plumbing Instl'n Cert & Connect Water																	
	HVAC																		
	RAB-FSD-1000	045 - Submit Form 501																	
FSD																			
RAB-FSD-630	045 - Submit Form 501 - FS																		
RAB-FSD-830	045 - Submit Form 314 - FS																		
RAB-FSD-450	045 - FS Inspection Period - FS																		
Engineer (AECOM)																			
RAB-45-7310	045 - Submit Building 045 As Built Drawings to Engineer																		
Building 050 - Public Toilets Type 2																			
Public Toilet (Portion H1)																			
Excavation																			
Raft																			
Structure																			
ABWF/E&M																			
Internal Finishes																			
Degree 1																			
RAB-50-1170	050 H1 - MEP 1st Fix																		
RAB-KD9A40	050 H1 - Access for C3 Cabling Works																		
RAB-KD9A10	KD9A - Projected achievement of Stage 9A of the Works																		

Remaining Level of Effort

Actual Work

Critical Remaining ...

Actual Level of Effort

Remaining Work

Finish Constraint

3-Month Rolling Programme Update, 01 Jan. 2018

Date

01-Jan-18

Revision

3-Month Rolling Programme, 01 Jan-18 Update

Checked

Approved

LEIGHTON 禮頓 		Contract No. HY/2014/05 - Remaining Ancillary Building and Facilities													Page 13 of 20						
Activity ID	Activity Name	November 2017			December 2017				January 2018					February 2018				March 2018			
			19	26		03	10	17	24		31	07	14	21	28		04	11	18	25	

LEIGHTON		Contract No. HY/2014/05 - Remaining Ancillary Building and Facilities												Page 14 of 20					
Activity ID	Activity Name	November 2017			December 2017				January 2018					February 2018				March 2018	
			19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	04	11

Activity ID	Activity Name	November 2017		December 2017				January 2018				February 2018				March 2018			
		19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	04	11	
	Structure																		
	ABWF/E&M																		
	Internal Finishes																		
	Degree 1																		
	RAB-50-3310	050 A1 - Plastering/Rendering & Undercoat																	
	RAB-50-3170	050 A1 - MEP 1st Fix																	
	RAB-50-3320	050 A1 - Screeding																	
	RAB-50-3330	050 A1 - Access for C3 for Cabling Works																	
	RAB-KD11A10	KD11A - Projected achievement of Stage 11A of the Works																	
	Degree 2																		
	RAB-50-3270	050 A1 - MEP 2nd Fix																	
	RAB-50-3360	050 A1 - Louver / Door Frame																	
	RAB-50-3390	050 A1 - Access for C3 for Equip. Installation																	
	RAB-KD11B10	KD11B - Projected achievement of Stage 11B of the Works																	
	RAB-50-3300	050 A1 - Power On																	
	Degree 3																		
	RAB-50-3350	050 A1 - Wall Finish																	
	RAB-50-3370	050 A1 - Floor Finish																	
	RAB-50-3380	050 A1 - Door panel & Ironmongery																	
	RAB-50-3340	050 A1 - Ceiling Frame																	
	RAB-50-3280	050 A1 - MEP Final Fix																	
	RAB-KD11C10	KD11C - Projected achievement of Stage 11C of the Works																	
	RAB-50-3290	050 A1 - Snagging and Remedials																	
	Specialist installation																		
	RAB-50-3240	050 A1 - Installation of Sanitaryware and Fixtures																	
	Roof Finishes																		
	RAB-50-3210	050 A1 - Install Cat Ladder and Roof Access Hatch																	
	RAB-50-3200	050 A1 - Install Railing - 49m																	
	RAB-50-3230	050 A1 - Installation of Aluminium Canopy																	
	RAB-50-4370	050 A1 - Install Aluminium Cladding																	
	RAB-50-3100	050 A1 - Install Skylights (8No)																	
	External Finishes																		
	RAB-50-3120	050 A1 - Install External Louvers /Windows/Doors																	
	RAB-50-3190	050 A1 - External Tiling																	
	RAB-50-3260	050 A1 - Make good external surfaces																	
	Utilities and Drainage																		
	RAB-50-7955	050 A1 - Install Flushing Water Mains																	
	RAB-50-7965	050 A1 - Install Fresh Water Mains																	
	Testing & Commissioning																		
	RAB-TC50-1020	050 A1 - T&C (HVAC, FS, P&D, OTHERS)																	
	Statutory Submissions & Approvals (Day 670 Completion)																		
	Water Supplies Department (WSD)																		
	Commencement																		
	Completion																		
	RAB-WSD-394	050 A1 - Submit WWO 46 Pt. IV																	
	RAB-WSD-404	050 A1 - WSD Inspection/Meter Connection																	
	RAB-WSD-414	050 A1 - WSD Issue WWO 046 Part V, Plumbing Inst'n Compl & Water Co																	
	Fire Services Department (VAC)																		
	RAB-FSD-1050	050 A1 - Submit Form 314																	
	RAB-FSD-1060	050 A1 - Submit Form 501																	
RAB-FSD-1180	050 A1 - FS Inspection																		

Remaining Level of Effort

Actual Work

Critical Remaining ...

Actual Level of Effort

Remaining Work

Finish Constraint

3-Month Rolling Programme Update, 01 Jan. 2018

Date

01-Jan-18

Revision

3-Month Rolling Programme, 01 Jan-18 Update

Checked

Approved

[illegible]

Activity ID	Activity Name	er 2017						December 2017					January 2018					February 2018				March 2018	
			19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	04	11				
Building 053 - Outbound X-Ray Scan Tunnel	RAB-53-0620	053 - Construct high level Canopy at +9.95mPD																					
	Utilities and Drainage																						
	Testing & Commissioning																						
	RAB-TC53-1050	053 - T&C, Lift																					
	Statutory Submissions & Approvals (Day 470 Completion)																						
	BEE0																						
	RAB-BEE-420	053 - Registered Energy Assessor Inspection & Certification																					
	RAB-BEE-430	053 - Submit REA Certification to EDMS																					
	RAB-BEE-440	053 - EDMS Issue of Cert of Compliance Registration (COCR)																					
	EMSD - Building 053 Lift Inspection																						
	RAB-FSD-160	053 - EMSD Lift Inspection																					
	RAB-FSD-090	053 - EMSD Lift Certificate Issued (Fire Lift)																					
	Water Supplies Department (WSD)																						
	Commencement																						
	Completion																						
	RAB-WSD-100	053 - Submit WWO 46 Pt. IV																					
	RAB-WSD-102	053 - WSD's Processing/Inspection/Meter Connection																					
	RAB-WSD-104	053 - WSD Issue WWO 046 Part V, Plumbing Compl. Cert & Water Conne																					
	VAC																						
	FSD																						
	RAB-FSD-430	053 - Issue Form 172, FS Compliance Cert.																					
	Engineer (AECOM)																						
	RAB-53-7460	053 - Submit Building 053 As Built Drawings to Engineer																					
	RAB-53-7470	053 - Engineer Inspection Period																					
	RAB-53-7480	053 - Engineer Issue Occupation Permit																					
	RAB-53-KD1	KD1 - Projected Completion of Section I of the Works (470 days) Building 05																					
	Building 058 - Outbound X-Ray Scan Tunnel																						
	Excavation																						
	Raft																						
	Structure																						
	Walls																						
	South																						
	North																						
Roof Slabs																							
Cure and Strip																							
ABWF/E&M																							
Internal Finishes																							
Degree 1																							
Degree 2																							
Degree 3																							
RAB-58-0700	058 - Floor Finish (Epoxy Paint)																						
RAB-58-0660	058 - Snagging and Remedials, Bldg. Internal																						
RAB-58-7520	058 - End Users and MoM handover inspection																						
Roof Finishes																							
RAB-58-0540	058 - Install Railing - 152m																						
External Finishes																							
Facade																							
RAB-58-0470	058 - External Painting																						
At Grade																							
RAB-58-6760	058 - Prepare Sub Grade																						
RAB-58-6750	058 - Laying Geo Textile																						
RAB-58-6770	058 - Lay Granular Sub-Base																						

Date	Revision	Checked	Approved
01-Jan-18	3-Month Rolling Programme, 01 Jan-18 Update		

LEIGHTON 恒耀		Contract No. HY/2014/05 - Remaining Ancillary Building and Facilities														Page 19 of 20			
Activity ID	Activity Name	November 2017			December 2017				January 2018					February 2018				March 2018	
			19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	04	11
	RAB-58-6780	058 - Laying Course																	
	RAB-58-6740	058 - Concrete Block Paving																	
	RAB-58-6800	058 - Snagging and Remedials																	
Glazed Canopy																			
RAB-58-0600	058 - Construct high level canopy at +13.231mPD																		
Utilities and Drainage																			
Testing & Commissioning																			
Statutory Submissions & Approvals (Day 470 Completion)																			
VAC (FSD)																			
RAB-FSD-104	058 - Fire Certificate Obtained (Form 172) Handover For Building 058																		
Engineer (AECOM)																			
RAB-58-7490	058 - Submit Building 058 As Built Drawings to Engineer																		
RAB-58-7500	058 - Engineer Inspection Period																		
RAB-58-7510	058 - Engineer Issue Occupation Permit																		
RAB-KD34	KD1 - Projected Completion of Section I of the Works (470 days) Building 058																		
Building 059 - Inbound X-Ray Scan Tunnel																			
Excavation																			
Raft Foundations																			
Structure																			
Walls																			
West																			
East																			
Roof Slabs																			
Cure and Strip																			
ABWF/E&M																			
Internal Finishes																			
Degree 1																			
Degree 2																			
Degree 3																			
RAB-59-7550	059 - End Users and MoM handover inspection																		
Roof Finishes																			
External Finishes																			
Facade																			
RAB-59-0480	059 - External Painting																		
RAB-59-0650	059 - Make good external surfaces																		
At Grade																			
RAB-59-6700	059 - Prepare Sub Grade																		
RAB-59-6690	059 - Laying Geo Textile																		
RAB-59-6710	059 - Lay Granular Sub-Base																		
RAB-59-6720	059 - Laying Course																		
RAB-59-6680	059 - Concrete Block Paving																		
RAB-59-0670	059 - Snagging and Remedials																		
Glazed Canopy																			
RAB-59-0610	059 - Construct high level glazed canopy at +13.406mPD North																		
Utilities and Drainage																			
Testing & Commissioning																			
Statutory Submissions & Approvals (Day 470 Completion)																			
VAC																			
Fire Services Department (FSD)																			
Commencement																			
Completion																			
Bldg. 059 Ready for FS Inspection (C8 Requirement)																			
RAB-FSD-750	059 - Fire Certificate Obtained (Form 172) Handover For Building 059																		
Remaining Level of Effort Actual Level of Effort Actual Work Remaining Work Critical Remaining ... Finish Constraint		3-Month Rolling Programme Update, 01 Jan. 2018										Date	Revision				Checked	Approved	
												01-Jan-18	3-Month Rolling Programme, 01 Jan-18 Update						

Activity ID	Activity Name	er 2017	December 2017					January 2018					February 2018					March 2018	
			19	26	03	10	17	24	31	07	14	21	28	04	11	18	25	04	11
	Bldg. 059 for FS Inspection (Due to C3 Work Interface)																		
	RAB-FSD-490	059 - Fire Certificate Obtained (Form 172) Handover For Building 059							◆										
	Engineer (AECOM)																		
	RAB-59-7520	059 - Submit Building 059 As Built Drawings to Engineer							◆										
	Bldg. 059 Ready for Engineer Inspection (C8 Requirement)																		
	RAB-59-7570	059 - Engineer Inspection Period																	
	RAB-59-7580	059 - Engineer Issue Occupation Permit										◆							
	RAB-59-7590	KD2 - Projected Completion of Section II of the Works (470 days) Building 0										◆							
	Bldg. 059 Ready for Engineer Inspection (Due to C3 Work Interface)																		
	RAB-59-7530	059 - Engineer Inspection Period																	
	RAB-59-7540	059 - Engineer Issue Occupation Permit										◆							
	RAB-KD24	KD2 - Projected Completion of Section II of the Works (470 days) Building 0										◆							

Remaining Level of Effort Actual Work Critical Remaining ... Actual Level of Effort Remaining Work △ Finish Constraint	3-Month Rolling Programme Update, 01 Jan. 2018	Date Revision Checked Approved
		01-Jan-18 3-Month Rolling Programme, 01 Jan-18 Update

Contract No.: HY/2013/06		Detail Work Programme										Page 1 of 8									
Activity ID	Activity Name	2015			2016				2017				2018				2019				
		Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3		
Hong Kong-Zhuhai_Macao Bridge Hong Kong Boundary Crossing F																					
Key Dates																					
Interface Activities																					
Site and Facility Inspection																					
JS1200	Pre Site and Facility Inspection by Contractor at Location 4 - Deg2																				
JS1210	Joint Site and Facility Inspection with Interface Contractor at Location 4 - Deg2																				
JS1620	Pre Site and Facility Inspection by Contractor at Location 14 - Deg2																				
JS1630	Joint Site and Facility Inspection with Interface Contractor at Location 14 - Deg2																				
JS1760	Pre Site and Facility Inspection by Contractor at Location 18 - Deg1																				
JS1770	Joint Site and Facility Inspection with Interface Contractor at Location 18 - Deg1																				
JS1780	Pre Site and Facility Inspection by Contractor at Location 18 - Deg2																				
JS1790	Joint Site and Facility Inspection with Interface Contractor at Location 18 - Deg2																				
Access Dates																					
AD1000	Location 1(PCB (001) Basement)-Deg1 (270d)																				
AD1010	Location 1(PCB (001) Basement)-Deg2 (380d)																				
AD1020	Location 1(PCB (001) ELV Room (Grid Line E3))-Deg1 (270d)																				
AD1030	Location 1(PCB (001) ELV Room (Grid Line E3))-Deg2 (380d)																				
AD1040	Location 2(PCB (001) First Floor Main Server Room)-Deg1 (330d)																				
AD1050	Location 2(PCB (001) First Floor Main Server Room)-Deg2 (380d)																				
AD1060	Location 2(PCB (001) First Floor Main Server Room) - For Server Installation - Deg2 (380d)																				
AD1070	Location 2(PCB (001) Ground Floor ELV Room (Grid Line E3)) - Deg1 (330d)																				
AD1080	Location 2(PCB (001) Ground Floor DOH Port Health Control Room (Grid Line BD5)) - Deg1 (330d)																				
AD1090	Location 2(PCB (001) Ground Floor DOH Port Health Control Room (Grid Line BD5)) - Deg2 (380d)																				
AD1130	Location 3(Inbd Cargo Exam Bldg (037) Platform Control Room)-Deg2 (500d)																				
AD1150	Location 3(Inbd Cargo Exam Bldg (037) Inspector Offices 128,129,130,131,128,129,14132)-Deg2 (500d)																				
AD1170	Location 3a(Inbd Cargo Exam Bldg (037) ROCARS Room)-Deg2 (480d)																				
AD1190	Location 3a(Inbd Cargo Exam Bldg (037) Main Server Room)-Deg2 (480d)																				
AD1200	Location 3a(Inbd Cargo Exam Bldg (037) Main Server Room) - For Server installation - Deg2 (480d)																				
AD1220	Location 4(Outbd Cargo Exam Bldg (023))-Deg2 (680d)																				
AD1240	Location 4a(Outbd Cargo Exam Bldg (023))-Deg2 (630d)																				
AD1270	Location 6(Common Utility Enclosure & Staff Subway)-Deg1 (400d)																				
AD1290	Location 7(Common Utility Enclosure & Staff Subway)-Deg1 (270d)																				
AD1300	Location 8(Inbd Private Car Annex (025))-Deg1 (430d)																				
AD1310	Location 8(Inbd Private Car Annex (025))-Deg2 (580d)																				
AD1320	Location 8(Inbd Private Car Annex (025) Canopy)-Deg1 (430d)																				
AD1330	Location 8(Inbd Private Car Annex (025) Canopy)-Deg2 (580d)																				
AD1340	Location 9(Outbd Private Car Annex (032))-Deg1 (520d)																				
AD1350	Location 9(Outbd Private Car Annex (032))-Deg2 (660d)																				
AD1360	Location 9(Outbd Private Car Annex (032) Canopy)-Deg1 (520d)																				
AD1370	Location 9(Outbd Private Car Annex (032) Canopy)-Deg2 (660d)																				
AD1501	Location 12(Inbd Private Car Kiosks(027))-Deg1 (400d) Phase 2																				
AD1510	Location 12(Inbd Private Car Kiosks(027))-Deg2 (480d) Phase 1																				
AD1511	Location 12(Inbd Private Car Kiosks(027))-Deg2 (480d) Phase 2																				
AD1521	Location 12(Inbd Private Car Kiosks(027) Canopy)-Deg1 (400d) Phase 2																				

Programme No.: HZMB-DWP

Data Date: 14-Aug-15

Actual Level of Effort

Primary Baseline

Actual Work

Remaining Work

Critical Remaining Work

Baseline Milestone

Milestone

summary

Hong Kong-Zhuhai-Macao Bridge

Hong Kong Boundary Crossing

Facilities - Automatic Vehicle

Clearance Support System (AVCSS)

Date

Revision

Checked

Approved

14-Nov-16

Rev.: 0

WC

LC

10-Mar-17

Rev.: 1.0a

WC

LC

5-May-17

Rev.: 1.0b

WC

LC

Contract No.: HY/2013/06			Detail Work Programme										Page 2 of 8												
Activity ID	Activity Name			2015			2016				2017				2018				2019						
				Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3				
		AD1530	Location 12(Inbd Private Car Kiosks(027) Canopy)-Deg2 (480d) Phase 1													Location 12(Inbd Private Car Kiosks(027) Canopy)-Deg2 (480d) Phase 1									
		AD1531	Location 12(Inbd Private Car Kiosks(027) Canopy)-Deg2 (480d) Phase 2													Location 12(Inbd Private Car Kiosks(027) Canopy)-Deg2 (480d) Phase 2									
		AD1540	Location 12(Inbd GV Kiosks (028))-Deg1 (400d) Phase 1													Location 12(Inbd GV Kiosks (028))-Deg1 (400d) Phase 1									
		AD1541	Location 12(Inbd GV Kiosks (028))-Deg1 (400d) Phase 2													Location 12(Inbd GV Kiosks (028))-Deg1 (400d) Phase 2									
		AD1550	Location 12(Inbd GV Kiosks (028))-Deg2 (480d) Phase 1													Location 12(Inbd GV Kiosks (028))-Deg2 (480d) Phase 1									
		AD1551	Location 12(Inbd GV Kiosks (028))-Deg2 (480d) Phase 2													Location 12(Inbd GV Kiosks (028))-Deg2 (480d) Phase 2									
		AD1560	Location 12(Inbd GV Kiosks (028) Canopy)-Deg1 (400d) Phase 1													Location 12(Inbd GV Kiosks (028) Canopy)-Deg1 (400d) Phase 1									
		AD1561	Location 12(Inbd GV Kiosks (028) Canopy)-Deg1 (400d) Phase 2													Location 12(Inbd GV Kiosks (028) Canopy)-Deg1 (400d) Phase 2									
		AD1570	Location 12(Inbd GV Kiosks (028) Canopy)-Deg2 (480d) Phase 1													Location 12(Inbd GV Kiosks (028) Canopy)-Deg2 (480d) Phase 1									
		AD1571	Location 12(Inbd GV Kiosks (028) Canopy)-Deg2 (480d) Phase 2													Location 12(Inbd GV Kiosks (028) Canopy)-Deg2 (480d) Phase 2									
		AD1580	Location 12(Outbd GV Kiosks (029))-Deg1 (400d) Phase 1													Location 12(Outbd GV Kiosks (029))-Deg1 (400d) Phase 1									
		AD1581	Location 12(Outbd GV Kiosks (029))-Deg1 (400d) Phase 2													Location 12(Outbd GV Kiosks (029))-Deg1 (400d) Phase 2									
		AD1590	Location 12(Outbd GV Kiosks (029))-Deg2 (480d) Phase 1													Location 12(Outbd GV Kiosks (029))-Deg2 (480d) Phase 1									
		AD1591	Location 12(Outbd GV Kiosks (029))-Deg2 (480d) Phase 2													Location 12(Outbd GV Kiosks (029))-Deg2 (480d) Phase 2									
		AD1600	Location 12(Outbd GV Kiosks (029) Canopy)-Deg1 (400d) Phase 1													Location 12(Outbd GV Kiosks (029) Canopy)-Deg1 (400d) Phase 1									
		AD1601	Location 12(Outbd GV Kiosks (029) Canopy)-Deg1 (400d) Phase 2													Location 12(Outbd GV Kiosks (029) Canopy)-Deg1 (400d) Phase 2									
		AD1610	Location 12(Outbd GV Kiosks (029) Canopy)-Deg2 (480d) Phase 1													Location 12(Outbd GV Kiosks (029) Canopy)-Deg2 (480d) Phase 1									
		AD1611	Location 12(Outbd GV Kiosks (029) Canopy)-Deg2 (480d) Phase 2													Location 12(Outbd GV Kiosks (029) Canopy)-Deg2 (480d) Phase 2									
		AD1620	Location 13(Outbd Private Car Kiosks (030))-Deg1 (480d) Phase 1													Location 13(Outbd Private Car Kiosks (030))-Deg1 (480d) Phase 1									
		AD1630	Location 13(Outbd Private Car Kiosks (030))-Deg2 (550d) Phase 1													Location 13(Outbd Private Car Kiosks (030))-Deg2 (550d) Phase 1									
		AD1640	Location 13(Outbd Private Car Kiosks (030) Canopy)-Deg1 (480d) Phase 1													Location 13(Outbd Private Car Kiosks (030) Canopy)-Deg1 (480d) Phase 1									
		AD1650	Location 13(Outbd Private Car Kiosks (030) Canopy)-Deg2 (550d) Phase 1													Location 13(Outbd Private Car Kiosks (030) Canopy)-Deg2 (550d) Phase 1									
		AD1660	Location 14(Future-Outbd/Inbd Private Car Kiosks)-Deg1 (610d)													Location 14(Future-Outbd/Inbd Private Car Kiosks)-Deg1 (610d)									
		AD1670	Location 14(Future-Outbd/Inbd Private Car Kiosks)-Deg2 (680d)													Location 14(Future-Outbd/Inbd Private Car Kiosks)-Deg2 (680d)									
		AD1700	Location 16(Outbd Traffic Control Kiosk (101))-Deg1 (400d)													Location 16(Outbd Traffic Control Kiosk (101))-Deg1 (400d)									
		AD1710	Location 16(Outbd Traffic Control Kiosk (101))-Deg2 (480d)													Location 16(Outbd Traffic Control Kiosk (101))-Deg2 (480d)									
		AD1740	Location 18(Outbd Private Car Exam Bldg(024))-Deg1 (-)													Location 18(Outbd Private Car Exam Bldg(024))-Deg1 (-)									
		AD1750	Location 18(Outbd Private Car Exam Bldg(024))-Deg2 (670d)													Location 18(Outbd Private Car Exam Bldg(024))-Deg2 (670d)									
		AD1780	(by C03) Underground Ducting (UUD1.1) between CUE and Inbd Cargo Exam Bldg (023)													(by C03) Underground Ducting (UUD1.1) between CUE and Inbd Cargo Exam Bldg (023)									
		AD1790	(by C03) (UUD1.2) between Inbd Cargo Exam Bldg South (037[S]) and DOH Cargo Exam Bldg (023)													(by C03) (UUD1.2) between Inbd Cargo Exam Bldg South (037[S]) and DOH Cargo Exam Bldg (023)									
		AD1800	(by C03) (UUD2) between Inbd Cargo Exam Bldg North (037[N]) and Inbd Vehicle Clearance Plaza (023)													(by C03) (UUD2) between Inbd Cargo Exam Bldg North (037[N]) and Inbd Vehicle Clearance Plaza (023)									
		AD1810	(by C03) (UUD9.1) btw Inbd Cargo Exam Bldg S.(037[S]) & Inbd PC Exam Bldg(033) and Inbd Vehicle Clearance Plaza (023)													(by C03) (UUD9.1) btw Inbd Cargo Exam Bldg S.(037[S]) & Inbd PC Exam Bldg(033) and Inbd Vehicle Clearance Plaza (023)									
		AD1820	(by C03) (UUD9.3) between Inbd Private Car Exam Bldg (033) and Inbd Vehicle Clearance Plaza (023)													(by C03) (UUD9.3) between Inbd Private Car Exam Bldg (033) and Inbd Vehicle Clearance Plaza (023)									
		AD1830	(by C03) (UUD9.2) between Inbd Private Car Exam Bldg (033) and Inbd Vehicle Clearance Plaza (023)													(by C03) (UUD9.2) between Inbd Private Car Exam Bldg (033) and Inbd Vehicle Clearance Plaza (023)									
		AD1840	(by C03) Underground Ducting (UUD3.1) between CUE to Outbd Cargo Exam Bldg (023)													(by C03) Underground Ducting (UUD3.1) between CUE to Outbd Cargo Exam Bldg (023)									
		AD1850	(by C03) (UUD3.2) btw Outbd Car Exam Bldg (023) and Outbd PC Exam Bldg (024) and Inbd Vehicle Clearance Plaza (023)													(by C03) (UUD3.2) btw Outbd Car Exam Bldg (023) and Outbd PC Exam Bldg (024) and Inbd Vehicle Clearance Plaza (023)									
		AD1860	(byC03) (UUD4.1) between Outbd Private Car Exam Bldg (024) and Outbd Vehicle Clearance Plaza (023)													(byC03) (UUD4.1) between Outbd Private Car Exam Bldg (024) and Outbd Vehicle Clearance Plaza (023)									
		AD1870	(byC03) (UUD5) between Outbd Car Exam Bldg South (023[S]) and Outbd Vehicle Clearance Plaza (023)													(byC03) (UUD5) between Outbd Car Exam Bldg South (023[S]) and Outbd Vehicle Clearance Plaza (023)									
		AD1880	(by C03) Underground Ducting (UUD8) between CUE and Outbd PCA (032)													(by C03) Underground Ducting (UUD8) between CUE and Outbd PCA (032)									
		AD1910	(by C03) Inbound Vehicle Clearance Plaza													(by C03) Inbound Vehicle Clearance Plaza									
		AD1920	(by C03) Outbound Vehicle Clearance Plaza				</																		

Contract No.: HY/2013/06			Detail Work Programme										Page 3 of 8																		
Activity ID		Activity Name											2015			2016				2017				2018				2019			
													Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	

Contract No.: HY/2013/06			Detail Work Programme										Page 4 of 8																											
Activity ID		Activity Name													2015			2016				2017				2018				2019										
															Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3								
		 Location 3a(Inbdcargo Exam Bldg (037) ROCARS Room)																																						
		 EM1240 L3a(037) ROCARS Rm - Cable Laying and termination in Location 3 and Location 3a																																						
		 EM1260 L3a(037) ROCARS Rm - Cable Splicing and Testing and Labeling																																						
		 EM1280 L3a(037) ROCARS Rm - AVCSS SYSCON and SURCON and Intercom Installation																																						
		 EM1300 L3a(037) ROCARS Rm - VTS WS Installation																																						
		 EM1320 L3a(037) ROCARS Rm - VID WS Installation																																						
		 EM1340 L3a(037) ROCARS Rm - SURCON and SYSCON and WS Tuning																																						
		 Location 3a(Inbdcargo Exam Bldg (037) Main Server Room)																																						
		 EM2120 L3a(037)Main Server Rm - Cable Laying and termination in Location 3 and Location 3a																																						
		 EM2140 L3a(037)Main Server Rm - Cable Splicing and Testing and Labeling																																						
		 EM2160 L3a(037)Main Server Rm - AVCSS Server Installation																																						
		 EM2180 L3a(037)Main Server Rm - VTS Server Installation																																						
		 EM2200 L3a(037)Main Server Rm - Servers Tuning																																						
		 Location 4(Outbdcargo Exam Bldg (023) MDF Room)																																						
		 Location 4a(Outbdcargo Exam Bldg (023) ROCARS Room)																																						
		 EM2240 L4a(023)ROCARS Rm - Cable Splicing and Testing and Labeling																																						
		 EM2260 L4a(023)ROCARS Rm - AVCSS SYSCON and SURCON and Intercom Installation																																						
		 EM2280 L4a(023)ROCARS Rm - VTS WS Installation																																						
		 EM2300 L4a(023)ROCARS Rm - SYSCON and SURCON and WS Tuning																																						
		 Location 5(Common Utility Enclosure & Staff Subway)																																						
		 EM2341 L5(CUE) - Cable Laying between Location 5 and Location 6																																						
		 EM2361 L5(CUE) - Cable Laying between Location 5 and Location 7																																						
		 EM2380 L5(CUE) - Cable Splicing and Testing and Labeling																																						
		 Location 6(Common Utility Enclosure & Staff Subway)																																						
		 EM2400 L6(CUE) - Cable Laying between Location 5 and Location 6																																						
		 EM2420 L6(CUE) - Cable Splicing and Testing and Labeling																																						
		 Location 7(Common Utility Enclosure & Staff Subway)																																						
		 EM2440 L7(CUE) - Cable Laying between Location 5 and Location 7																																						
		 EM2460 L7(CUE) - Cable Splicing and Testing and Labeling																																						
		 Location 12(Inbdcargo Private Car Kiosks,GV Kiosks (027,028,029))																																						
		 Inbdcargo Private Car Kiosks(027) - 9 nos (Phase 1)																																						
		 EM1500 L12(027)(9nos P1) - Cable Splicing and Testing and Labeling																																						
		 EM1520 L12(027)(9nos P1) - AVCSS/MOM Kiosk Equipment Installation (9 nos)																																						
		 EM1541 L12(027)(9nos P1) - XDB installation (18 nos)																																						
		 EM1542 L12(027)(9nos P1) - ODB installation (5 nos)																																						
		 EM1543 L12(027)(9nos P1) - ODB installation (2 nos)																																						
		 EM1544 L12(027)(9nos P1) - ODB installation (2 nos)																																						
		 EM1560 L12(027)(9nos P1) - Loop installation (45 nos)																																						
		 Inbdcargo Goods Vehicle Kiosks(028) - 5 nos (Phase 1)																																						
		 EM1620 L12(028)(5nos P1) - Cable Laying and termination																																						
		 EM1640 L12(028)(5nos P1) - Cable Splicing and Testing and Labeling																																						
		 EM1660 L12(028)(5nos P1) - AVCSS/MOM Kiosk Equipment Installation (5 nos)																																						
		 EM1681 L12(028)(5nos P1) - XDB installation (10 nos)																																						
		 EM1682 L12(028)(5nos P1) - ODB installation (3 nos)																																						
		 EM1683 L12(028)(5nos P1) - ODB installation (2 nos)																																						
Programme No.: HZMB-DWP Data Date: 14-Aug-15			 Actual Level of Effort  summary  Primary Baseline  Actual Work  Remaining Work  Critical Remaining Work  Baseline Milestone  Milestone										Hong Kong-Zhuhai-Macao Bridge Hong Kong Boundary Crossing Facilities - Automatic Vehicle Clearance Support System (AVCSS)								<table><tr><th>Date</th><th>Revision</th><th>Checked</th><th>Approved</th></tr><tr><td>14-Nov-16</td><td>Rev.: 0</td><td>WC</td><td>LC</td></tr><tr><td>10-Mar-17</td><td>Rev.: 1.0a</td><td>WC</td><td>LC</td></tr><tr><td>5-May-17</td><td>Rev.: 1.0b</td><td>WC</td><td>LC</td></tr></table>				Date	Revision	Checked	Approved	14-Nov-16	Rev.: 0	WC	LC	10-Mar-17	Rev.: 1.0a	WC	LC	5-May-17	Rev.: 1.0b	WC	LC
Date	Revision	Checked	Approved																																					
14-Nov-16	Rev.: 0	WC	LC																																					
10-Mar-17	Rev.: 1.0a	WC	LC																																					
5-May-17	Rev.: 1.0b	WC	LC																																					

Contract No.: HY/2013/06			Detail Work Programme												Page 5 of 8																	
Activity ID		Activity Name													2015			2016				2017				2018				2019		
															Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3

Contract No.: HY/2013/06			Detail Work Programme												Page 7 of 8																															
Activity ID		Activity Name													2015			2016				2017				2018				2019																
															Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3														
		 Location 8(Inbd Private Car Annex (025)) (Phase 2)																																												
		 EM3370 L8(025) - Cable Containment in Kiosks																																												
		 EM3380 L8(025) - Cable Laying and termination																																												
		 EM3400 L8(025) - Cable Splicing and Testing and Labeling																																												
		 Location 9(Outbd Private Car Annex (032)) (Phase 2)																																												
		 EM3500 L9(032) - Cable Containment in Kiosks																																												
		 EM3520 L9(032) - Cable Laying and termination																																												
		 Initial On-Site Test and Commissioning / Pre-SAT (Phase 2 / Section II)																																												
		 Site Acceptance Test (Phase 2 / Section II)																																												
		 Operability Period Test (Phase 2 / Section II)																																												
		 Completion (Phase 2 / Section II)																																												
		 Engineering Support for Phase 2 / Section II																																												
		 Procurement for Phase2 / Section III																																												
		 Delivery and Bench Acceptance Test for Phase2 / Section III																																												
		 Installation - Phase 2 / Section III																																												
		 Location 10,11,12,13 (Vehicle Clearance Kiosks)																																												
		 Location 12 Inbd Private Car Kiosks (027) - 12 nos (Phase 2)																																												
		 EM4440 L12(027)(12nos P2) - Cable Laying and termination																																												
		 EM4460 L12(027)(12nos P2) - Cable Splicing and Testing and Labeling																																												
		 EM4480 L12(027)(12nos P2) - AVCSS/DOH/MOM Kiosk Equipment Installation (12 nos)																																												
		 Location 13 Outbd Private Car Kiosks (030) - 12 nos (Phase 2)																																												
		 EM4560 L13(030)(12nos P2) - Cable Containment in Kiosks																																												
		 Location 12 Outbd Goods Vehicle Kiosks (029) - 3 nos (Phase 2)																																												
		 EM4880 L12(029)(3nos P2) - Cable Laying and termination																																												
		 EM4900 L12(029)(3nos P2) - Cable Splicing and Testing and Labeling																																												
		 EM4920 L12(029)(3nos P2) - AVCSS/DOH/MOM Kiosk Equipment Installation (3 nos)																																												
		 EM4940 L12(029)(3nos P2) - ODB & XDB Installation (3 nos)																																												
		 EM4960 L12(029)(3nos P2) - AIOP Installation (3 nos)																																												
		 EM4980 L12(029)(3nos P2) - Loop Installation (15 nos)																																												
		 Location 11 Outbd Coach Kiosks (009) - 4 nos (Phase 2)																																												
		 Location 12 Inbd Goods Vehicle Kiosks (028) - 3 nos (Phase 2)																																												
		 EM4720 L12(028)(3nos P2) - Cable Laying and termination																																												
		 EM4740 L12(028)(3nos P2) - Cable Splicing and Testing and Labeling																																												
		 EM4760 L12(028)(3nos P2) - AVCSS/DOH/MOM Kiosk Equipment Installation (3 nos)																																												
		 EM4780 L12(028)(3nos P2) - ODB & XDB Installation (3 nos)																																												
		 EM4800 L12(028)(3nos P2) - AIOP Installation (3 nos)																																												
		 EM4820 L12(028)(3nos P2) - Loop Installation (15 nos)																																												
		 EM4840 L12(028)(3nos P2) - Kiosk Equipment Configuration (3 nos)																																												
		 EM5120 L12(028)(3nos P2) - Inbd Goods Vehicle Kiosks Installation Complete																																												
		 Location 10 Shuttle Bus Kiosks (006) - 4 nos (Phase 2)																																												
		 EM4000 L10(006)(4nos P2) - Cable Containment in Kiosks																																												
		 Location 11 Inbd Coach Kiosks (010) - 2 nos (Phase 2)-1																																												
		 Location 11 Inbd Coach Kiosks (010) - 2 nos (Phase 2)-2																																												
		 Initial On-Site Test and Commissioning / Pre-SAT (Phase 2 / Section III)																																												
Programme No.: HZMB-DWP Data Date: 14-Aug-15			 Actual Level of Effort	 Primary Baseline	 Actual Work	 Remaining Work	 Critical Remaining Work	 Baseline Milestone	 Milestone	 summary	Hong Kong-Zhuhai-Macao Bridge Hong Kong Boundary Crossing Facilities - Automatic Vehicle Clearance Support System (AVCSS)										<table><tr><th>Date</th><th>Revision</th><th>Checked</th><th>Approved</th></tr><tr><td>14-Nov-16</td><td>Rev.: 0</td><td>WC</td><td>LC</td></tr><tr><td>10-Mar-17</td><td>Rev.: 1.0a</td><td>WC</td><td>LC</td></tr><tr><td>5-May-17</td><td>Rev.: 1.0b</td><td>WC</td><td>LC</td></tr></table>										Date	Revision	Checked	Approved	14-Nov-16	Rev.: 0	WC	LC	10-Mar-17	Rev.: 1.0a	WC	LC	5-May-17	Rev.: 1.0b	WC	LC
Date	Revision	Checked	Approved																																											
14-Nov-16	Rev.: 0	WC	LC																																											
10-Mar-17	Rev.: 1.0a	WC	LC																																											
5-May-17	Rev.: 1.0b	WC	LC																																											

[illegible]

Programme No.: HZMB-DWP

Data Date: 14-Aug-15

Actual Level of Effort

Primary Baseline

Actual Work

Remaining Work

Critical Remaining Work

Baseline Milestone

Milestone

summary


Hong Kong-Zhuhai-Macao Bridge


Hong Kong Boundary Crossing


Facilities - Automatic Vehicle

Clearance Support System (AVCSS)


Date	Revision	Checked	Approved
14-Nov-16	Rev.: 0	WC	LC
10-Mar-17	Rev.: 1.0a	WC	LC
5-May-17	Rev.: 1.0b	WC	LC

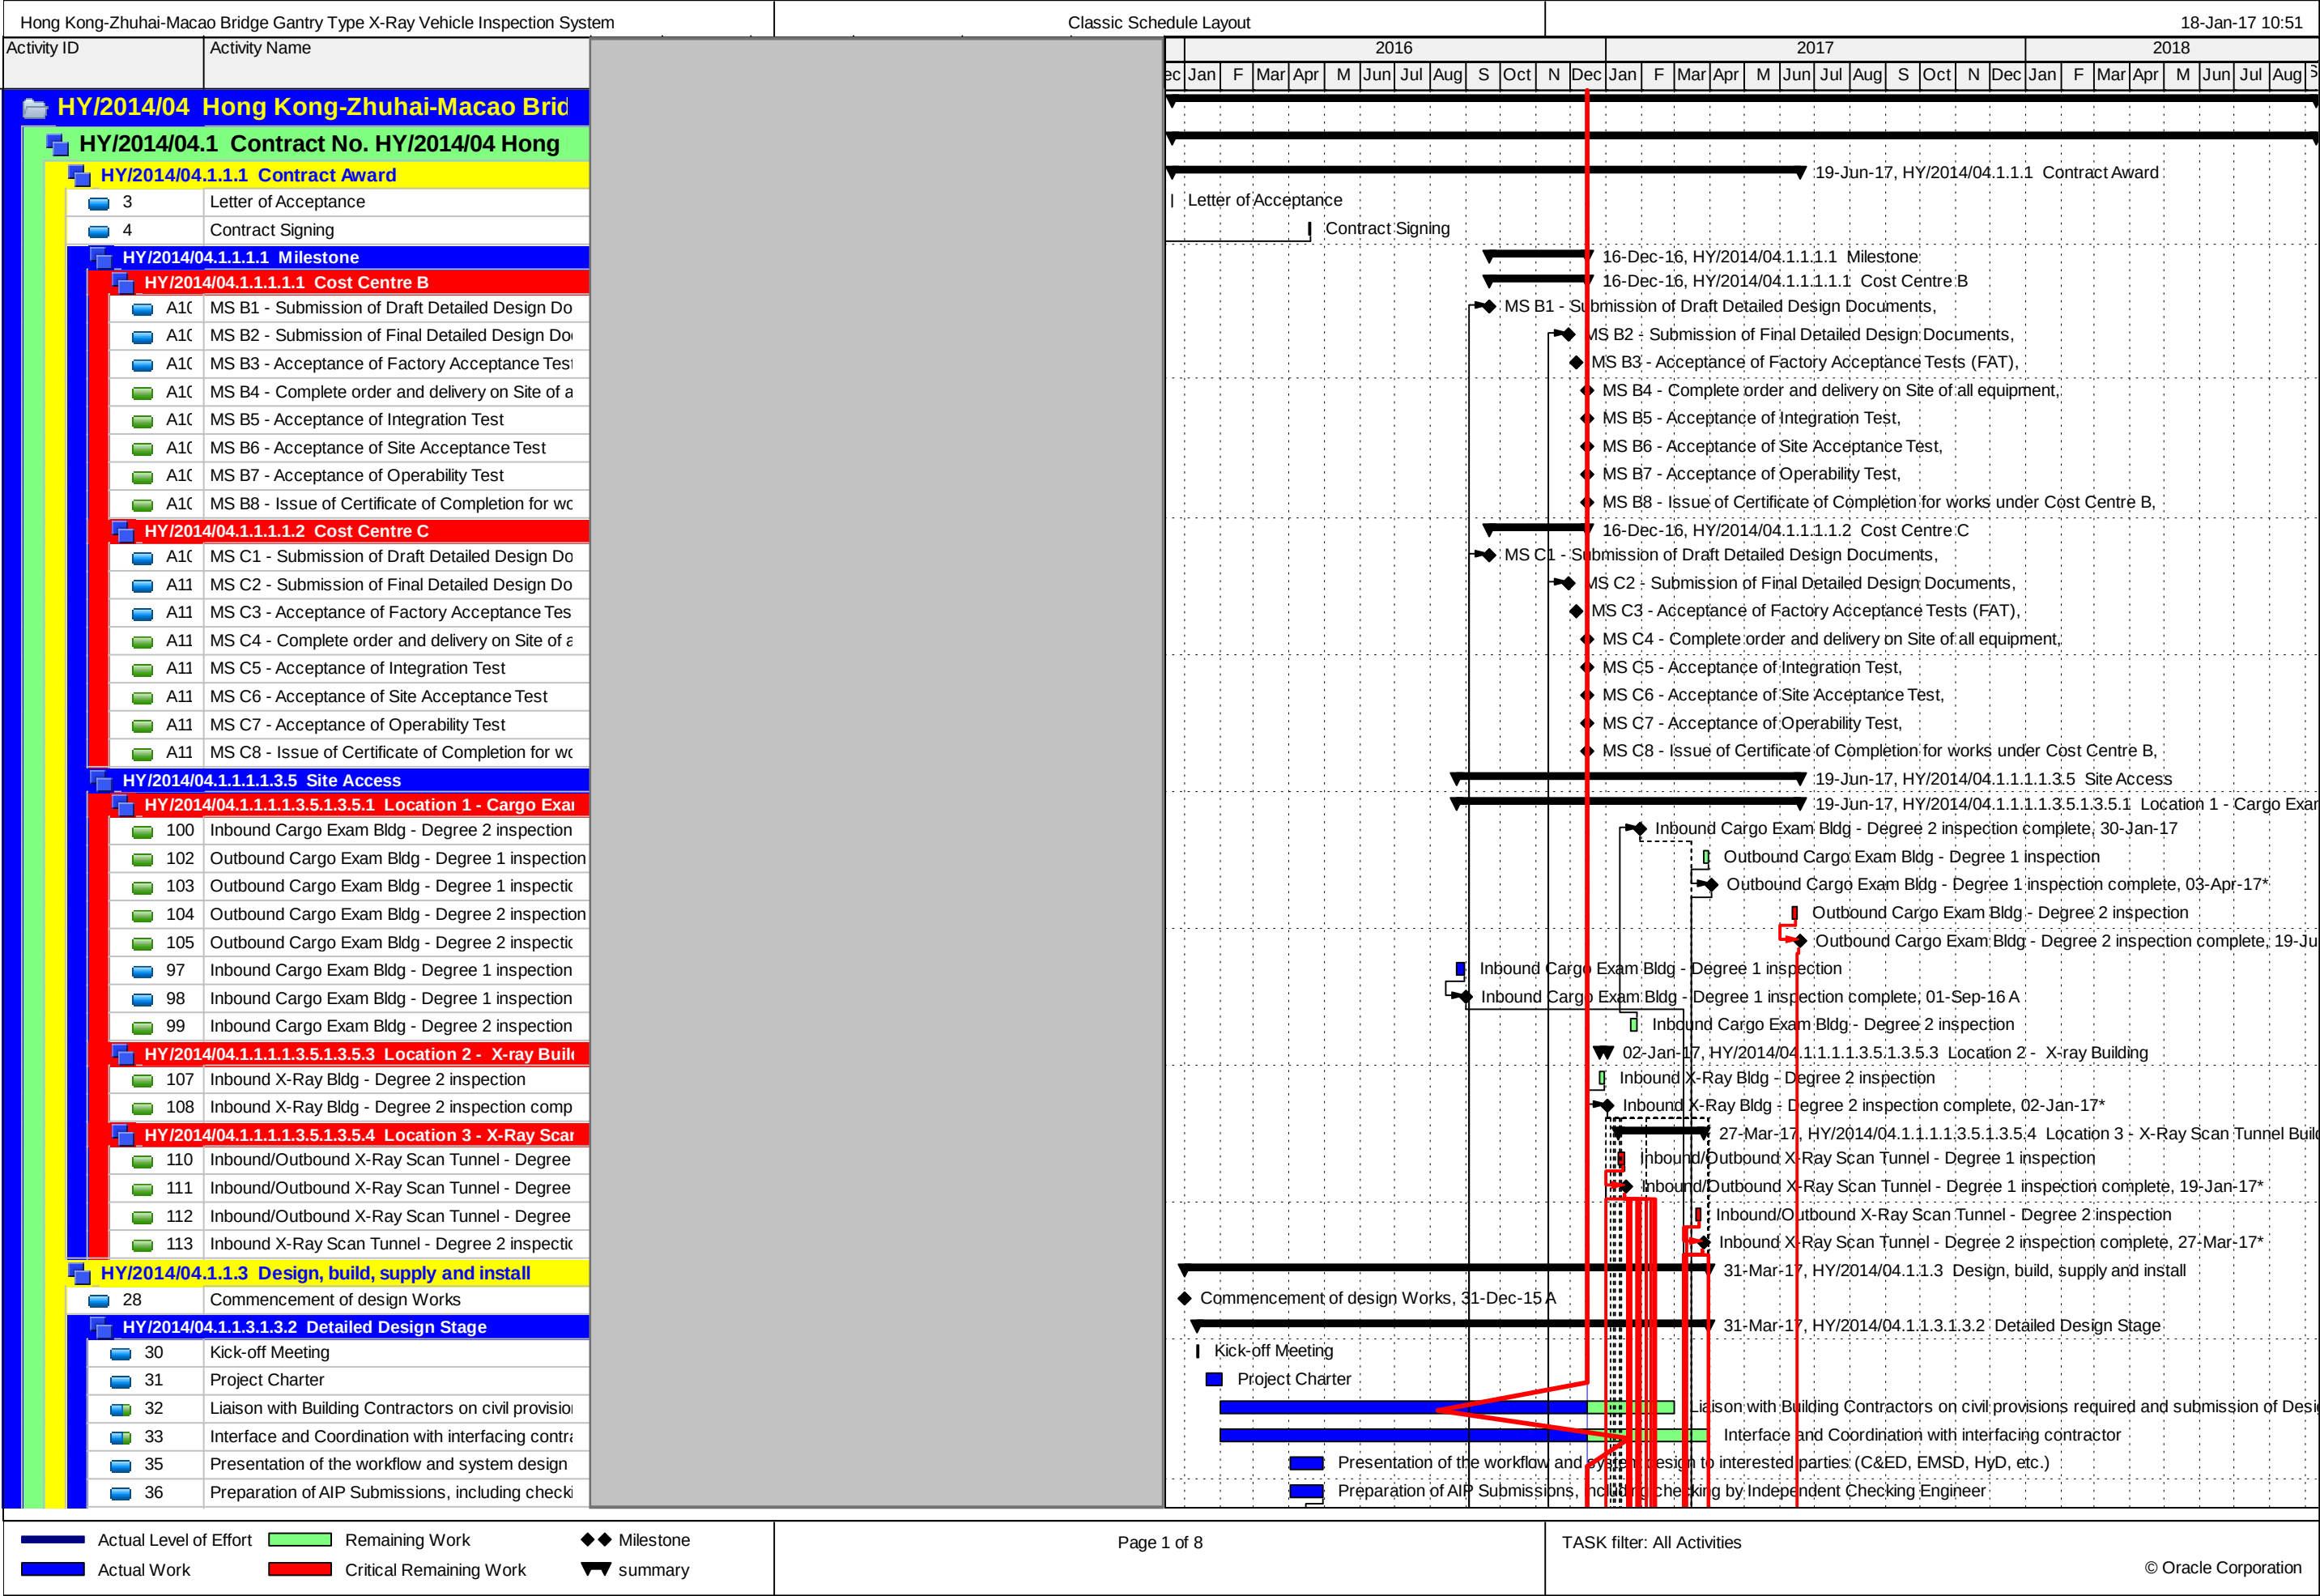

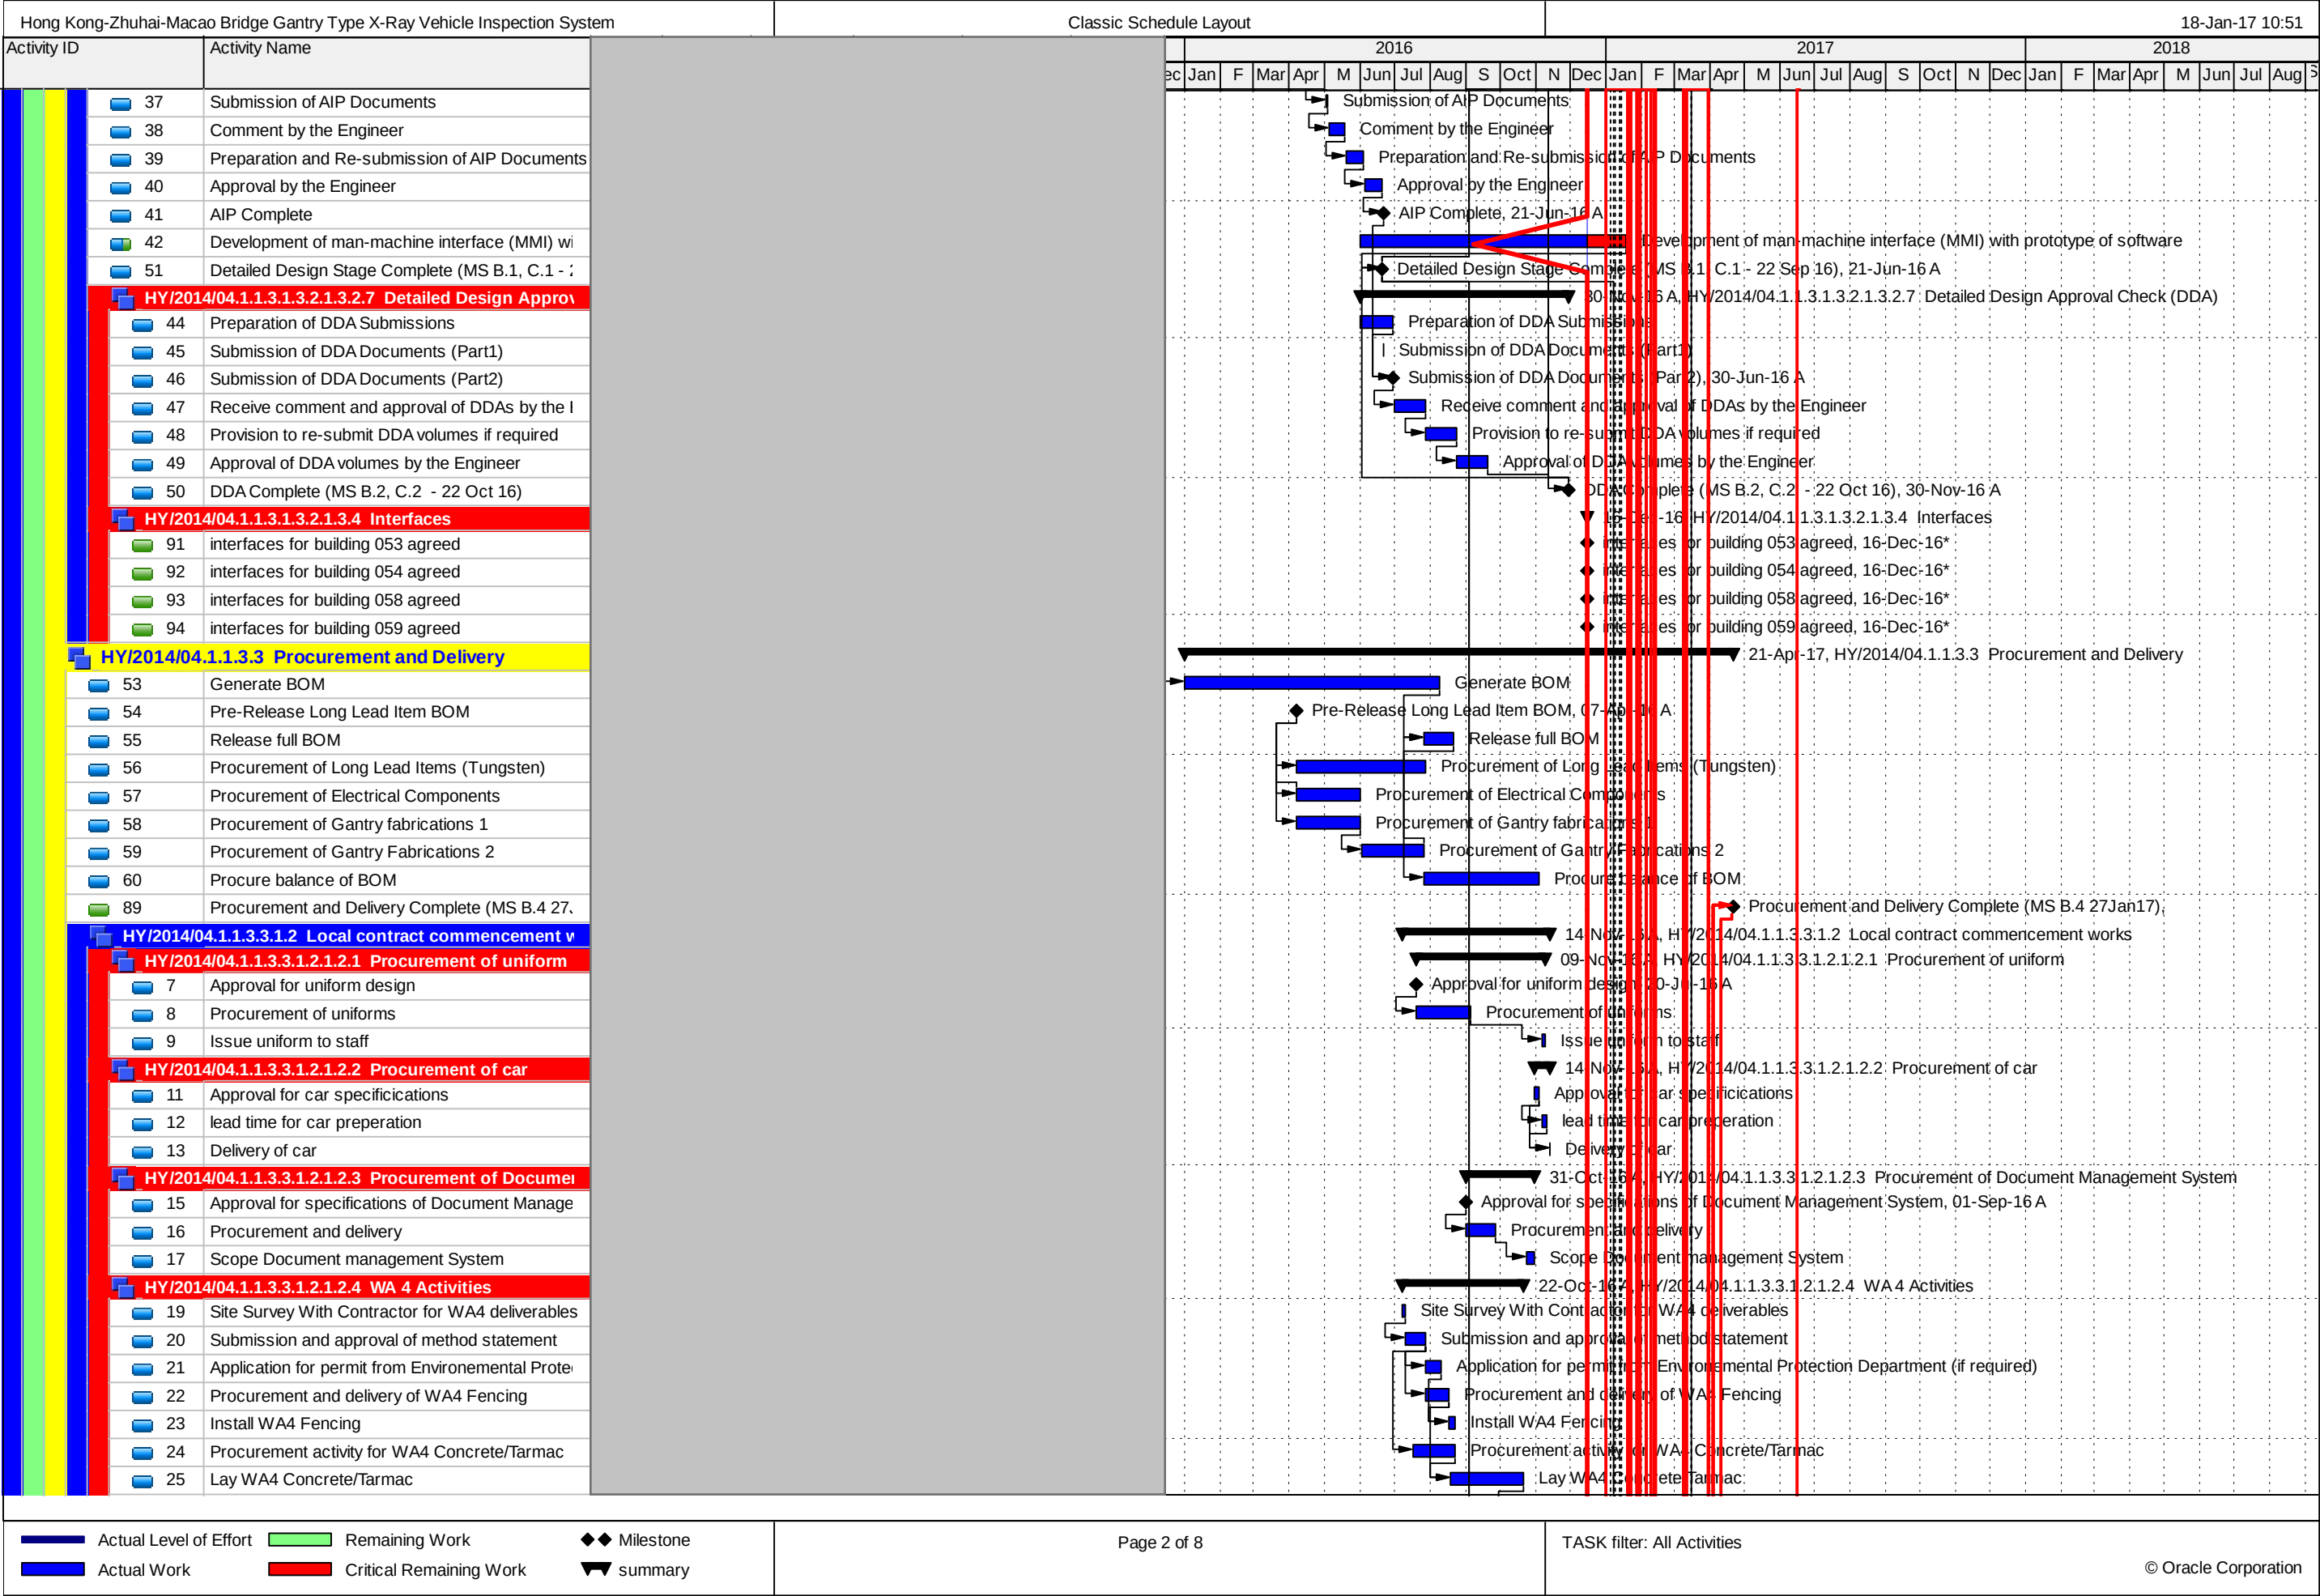

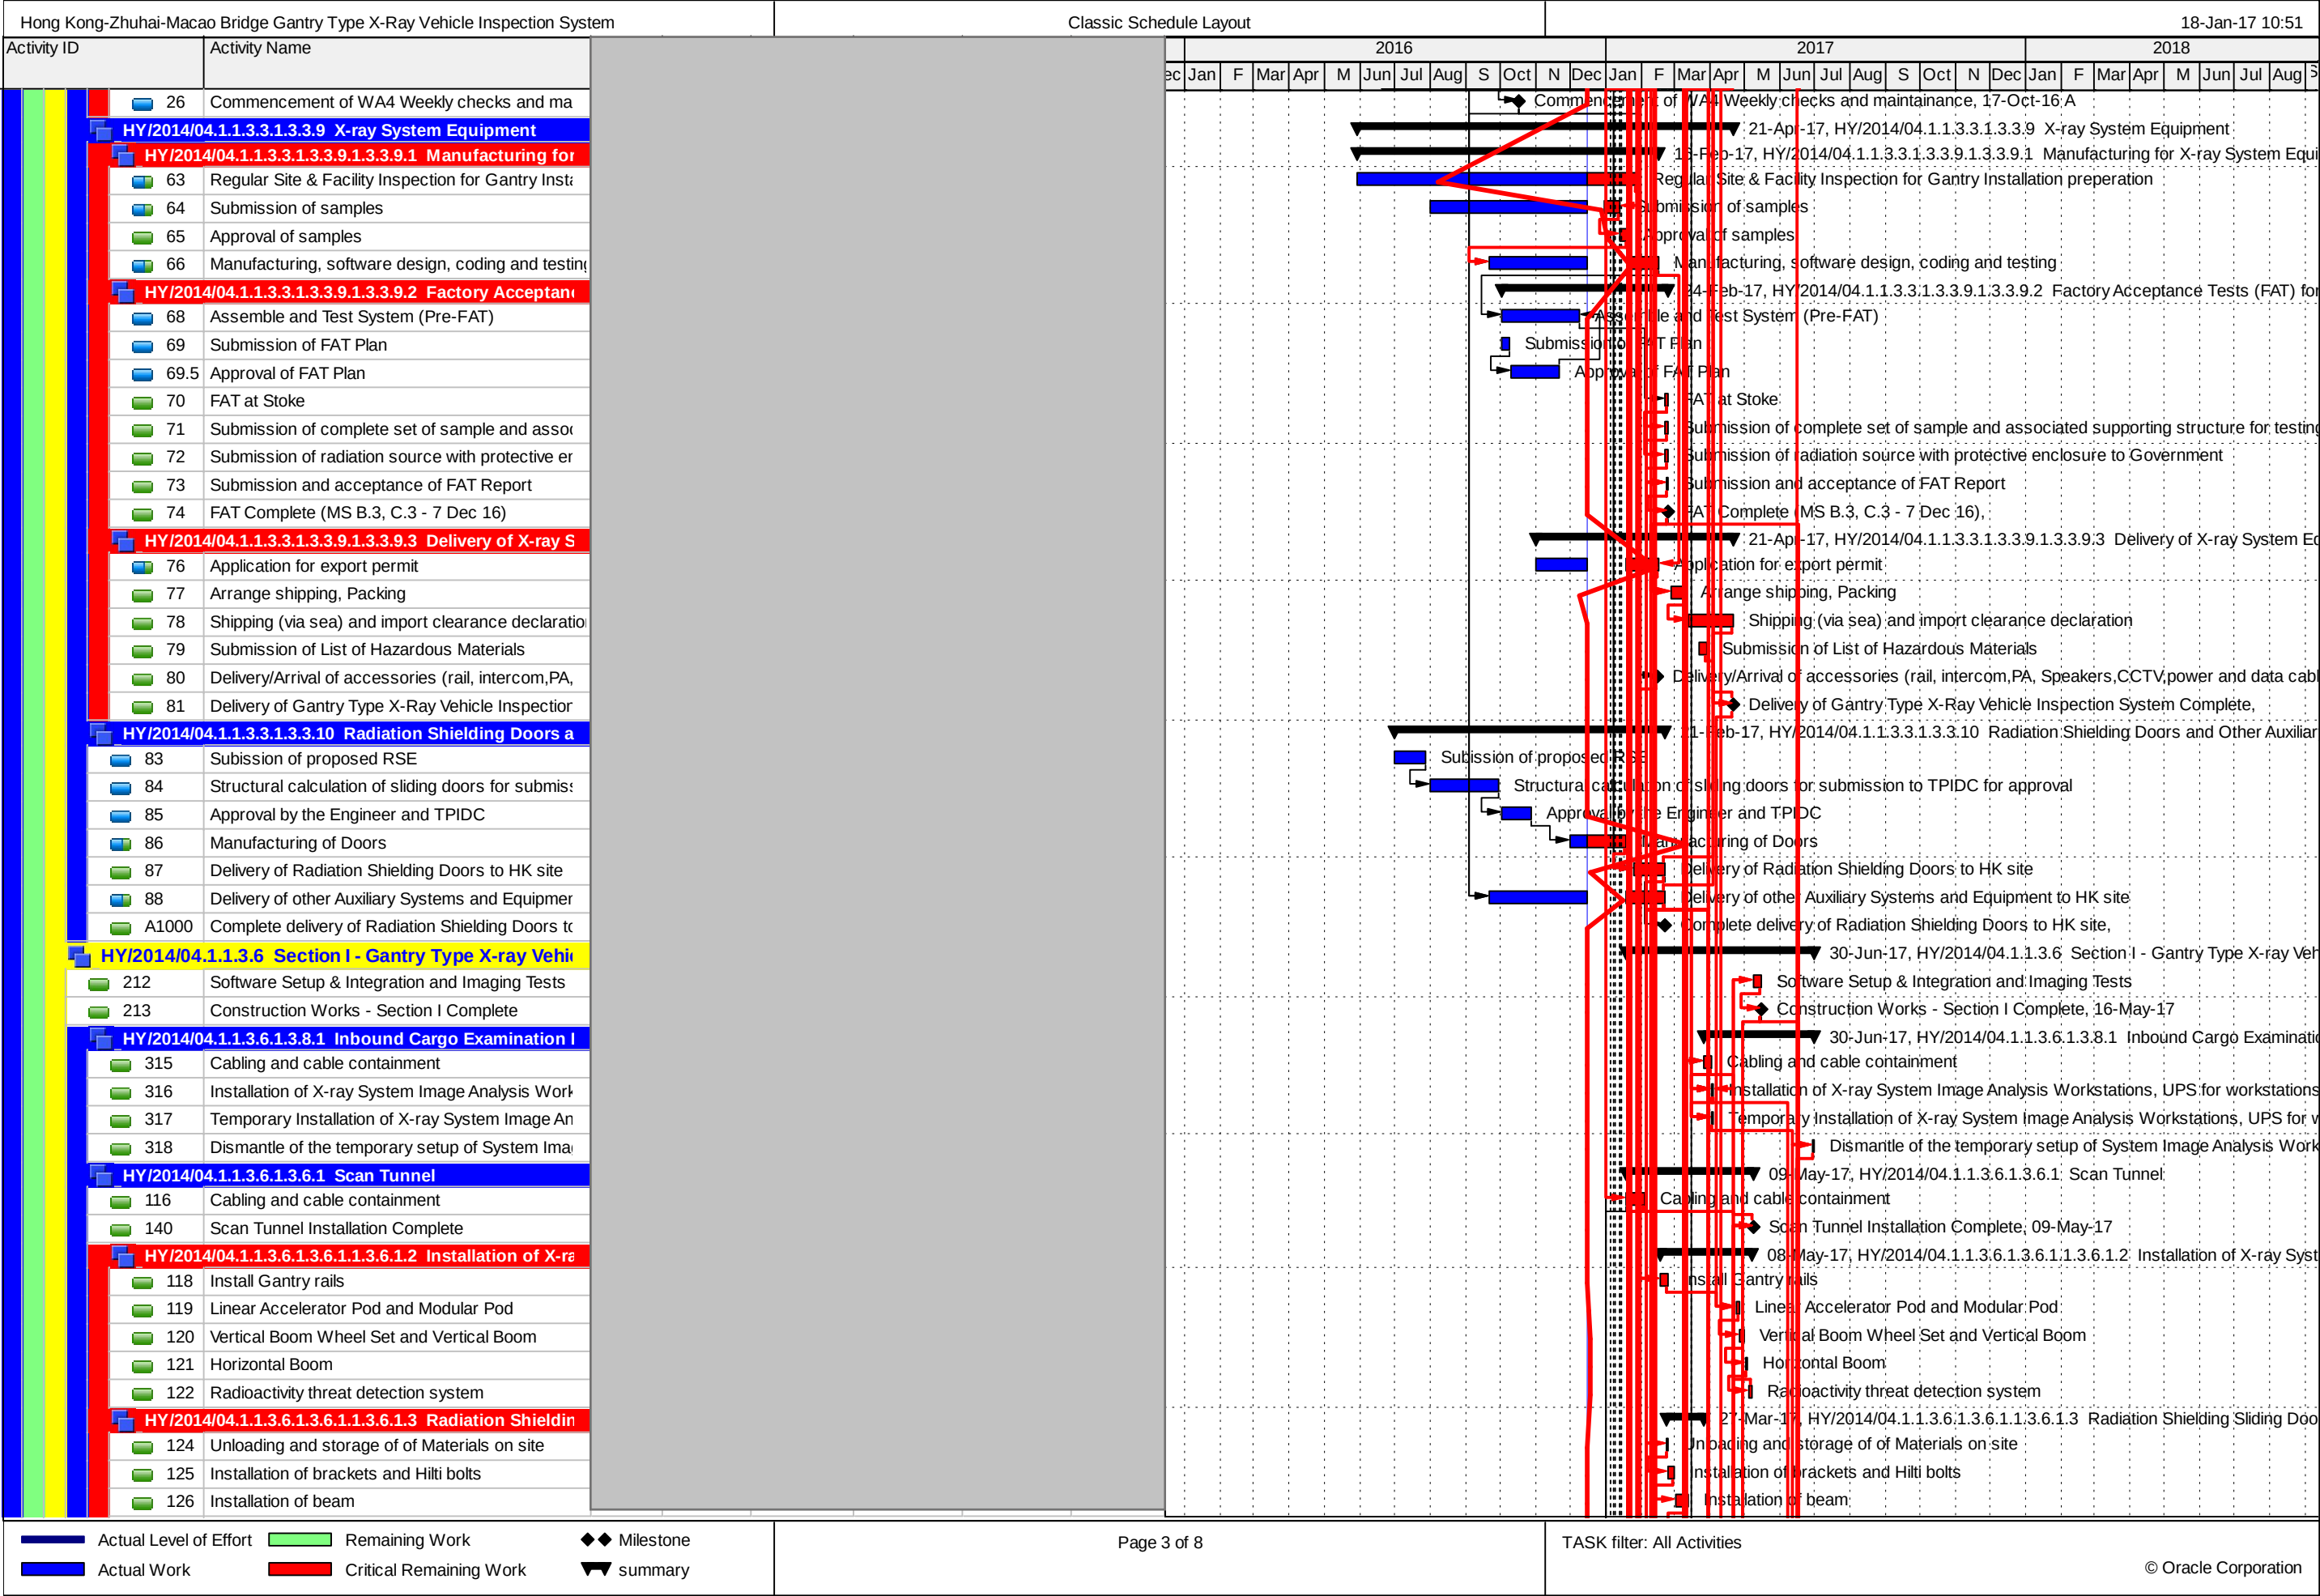

[illegible]

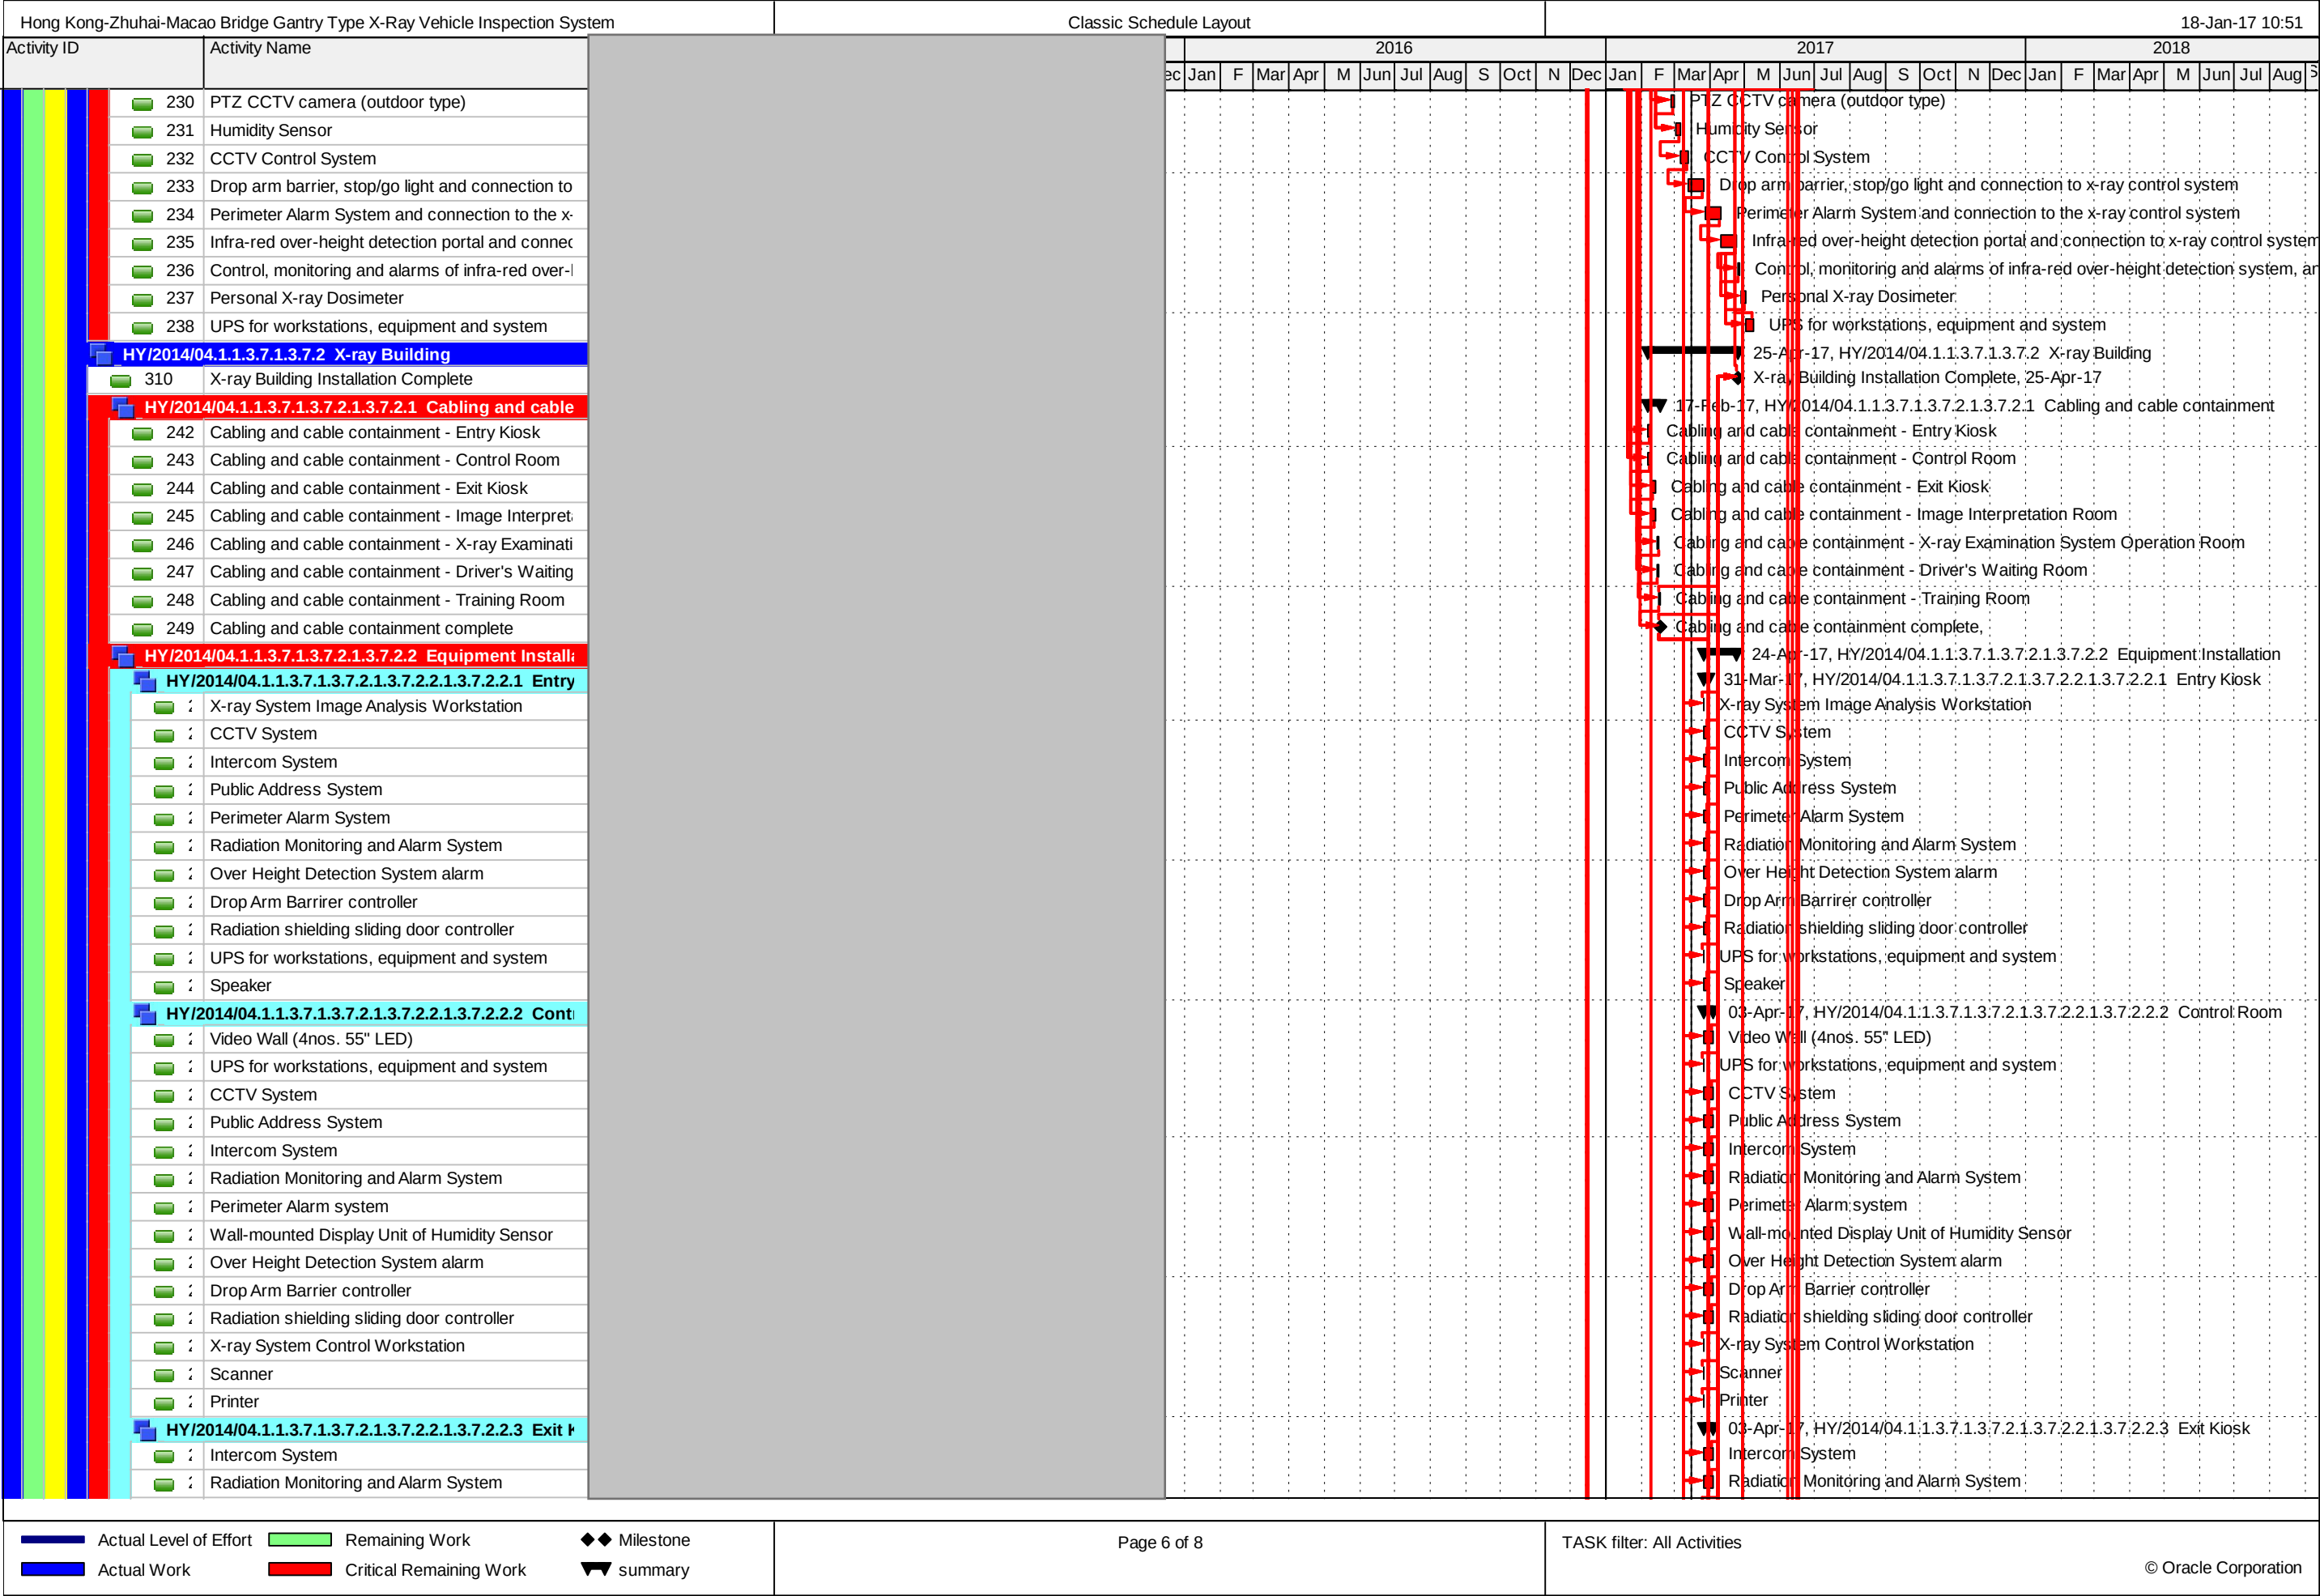

■ Actual Level of Effort
 ■ Remaining Work
 ◆◆ Milestone
 Page 8 of 8
 TASK filter: All Activities
 © Oracle Corporation
