
3-Months Rolling Programme (ER Part 5 & SCC 27(9))

Layout ZMB - Layout 1 (3M Rolling Prog)(3M46)

3-Months Rolling Programme (ER Part 5 & SCC 27(9)) Sheet 2 of 12 TASK filters: 3M46, HZMB No Level Effort (March 2016 to May 2016) Activity ID (days) SHT7530 SHT T002 Bay 48 lining [469m/485m] - Waterproofing, rebar fixing, formworks, concreting 6d 14-Mar-16 19-Mar-16 0% SHT T002 Bay 48 lining [469m/485m] - Waterproofing, rebar fixing, formworks, concreting SHT7540 SHT T002 Bay 49 lining [479m/485m] - Waterproofing, rebar fixing, formworks, concreting 6d 18-Mar-16 23-Mar-16 0% SHT T002 Bay 49 lining [479m/485m] - Waterproofing, rebar fixing, formworks, concreting SHT T002 Bay 50 lining [485m/485m] - Waterproofing, reban fixing, formworks, concreting SHT7550 SHT T002 Bay 50 lining [485m/485m] - Waterproofing, rebar fixing, formworks, concreting 6d 22-Mar-16 27-Mar-16 0% T002 Kicker Wall SHT T002 kicker wall [450m/485m] - Drained (150mm thk slab) -Waterproofing, rebar, fwk, 26-Jan-16 A 100% SHT6500-22 29-Sep-15 A 0% SHT6500-23 SHT T002 kicker wall [485m/485m] - Drained (150mm thk slab) - Waterproofing, rebar, fwk, SHT T002 kicker wall [485m/485m] - Drained (150mm thk slab) - Waterproofing, rebar, fwk, concrete SHT T002 OHVD - Shutter assembly works 04-Jan-16 A 23-Jan-16 A 100% SHT7510-05 15d SHT T002 OHVD [20m/485m] - Formworks, rebar fixing, concreting SHT7510-1 4d 23-Jan-16 A 30-Jan-16 A 100% SHT7510-2 SHT T002 OHVD [40m/485m] - Formworks, rebar fixing, concreting 4d 01-Feb-16 A 20-Feb-16 A 100% SHT7510-3 SHT T002 OHVD [60m/485m] - Formworks, rebar fixing, concreting 4d 22-Feb-16 A 23-Feb-16 0% SHT T002 OHVD [60m/485m] - Formworks, rebar fixing, concreting SHT T002 OHVD [80m/485m] - Formworks, rebar fixing, concreting SHT T002 OHVD [80m/485m] - Formworks, rebar fixing, concreting SHT7510-4 4d 24-Feb-16 27-Feb-16 0% SHT T002 OHVD [100m/485m] - Formworks, rebar fixing, concreting SHT7510-5 SHT T002 OHVD [100m/485m] - Formworks, rebar fixing, concreting 4d 28-Feb-16 02-Mar-16 0% SHT T002 OHVD [120m/485m] - Formworks, rebar fixing, concreting 06-Mar-16 SHT T002 OHVD [120m/485m] - Formworks, rebar fixing, concreting SHT7510-7 SHT T002 OHVD [140m/485m] - Formworks, rebar fixing, concreting 4d 07-Mar-16 10-Mar-16 0% SHT T002 OHVD [140m/485m] - Formworks, rebar fixing, concreting 4d SHT T002 OHVD [160m/485m] - Formworks, rebar fixing, concreting SHT7510-8 SHT T002 OHVD [160m/485m] - Formworks, rebar fixing, concreting 11-Mar-16 14-Mar-16 0% SHT T002 OHVD [180m/485m] - Formworks, rebar fixing, concreting 4d 18-Mar-16 SHT T002 OHVD [180m/485m] - Formworks, rebar fixing, concreting SHT7510-9 15-Mar-16 0% SHT T002 OHVD [200m/485m] - Formworks, rebar fixing, concreting 4d SHT7510-10 SHT T002 OHVD [200m/485m] - Formworks, rebar fixing, concreting 19-Mar-16 22-Mar-16 0% SHT T002 OHVD [220m/485m] - Formworks, rebar fixing, concreting SHT7510-11 SHT T002 OHVD [220m/485m] - Formworks, rebar fixing, concreting 4d 23-Mar-16 26-Mar-16 SHT7510-12 SHT T002 OHVD [240m/485m] - Formworks, rebar fixing, concreting 4d 27-Mar-16 30-Mar-16 0% SHT T002 OHVD [240m/485m] - Formworks, rebar fixing, concreting SHT T002 OHVD [260m/485m] - Formworks, rebar fixing, concreting SHT T002 OHVD [260m/485m] - Formworks, rebar fixing, concreting 4d SHT7510-13 31-Mar-16 0% 03-Apr-16 SHT T002 OHVD [280m/485m] Formworks, rebar fixing, concreting SHT7510-14 SHT T002 OHVD [280m/485m] - Formworks, rebar fixing, concreting 4d 04-Apr-16 07-Apr-16 0% SHT T002 OHVD [300m/485m] - Formworks, rebar fixing, concreting SHT7510-15 4d 11-Apr-16 SHT T002 OHVD [300m/485m] - Formworks, rebar fixing concreting 08-Apr-16 0% SHT7510-16 SHT T002 OHVD [320m/485m] - Formworks, rebar fixing, concreting 4d 12-Apr-16 SHT T002 OHVD [320m/485m] - Formworks, rebair fixing, concreting 15-Apr-16 0% SHT7510-17 SHT T002 OHVD [340m/485m] - Formworks, rebar fixing, concreting 16-Apr-16 19-Apr-16 SHT T002 OHVD [340m/485m] - Formworks, rebar fixing, concre SHT T002 OHVD [360m/485m] - Formworks, rebar fixing, SHT7510-18 SHT T002 OHVD [360m/485m] - Formworks, rebar fixing, concreting 4d 20-Apr-16 23-Apr-16 0% 4d SHT T002 OHVD [380m/485m] - Formworks, rebar f SHT7510-19 SHT T002 OHVD [380m/485m] - Formworks, rebar fixing, concreting 24-Apr-16 27-Apr-16 0% SHT T002 OHVD [400m/485m] - Formworks, rebar fixing, concreting 4d 01-May-16 SHT T002 OHVD [400m/485m] - Formworks, SHT7510-20 28-Apr-16 0% SHT T002 OHVD [420m/485m] - Formw SHT T002 OHVD [420m/485m] - Formworks, rebar fixing, concreting 4d SHT7510-21 02-May-16 05-May-16 SHT 7002 OHVD [440m/485m] - F SHT7510-22 SHT T002 OHVD [440m/485m] - Formworks, rebar fixing, concreting 4d 09-May-16 06-May-16 = SHT T002 OHVD [460m/485r SHT T002 OHVD [460m/485m] - Formworks, rebar fixing, concreting SHT7510-23 4d 10-May-16 13-May-16 0% SHT T002 OHVD 480n SHT T002 OHVD [480m/485m] - Formworks, rebar fixing, concreting 4d SHT7510-24 17-May-16 0% 14-May-16 SHT T002 OHVD [485m/485m] - Formworks, rebar fixing, concreting SHT T002 OHVD SHT7510-25 3d 18-May-16 20-May-16 0% SHT T002 Bay 3 base slab [60m/480m], 150mm thk, drained section - Waterproofing, rebar, fwk, SHT T002 Bay 3 base slab [60m/480m], 150mm thk, drained section - Waterproofing, rebar, fwk, concrete 0% SHT6510 9d 07-Mar-16 15-Mar-16 SHT6520 SHT T002 Bay 4 base slab [90m/480m], 150mm thk, drained section - Waterproofing, rebar, fwk, concre SHT T002 Bay 4 base slab [90m/480m], 150mm thk, drained section - Waterproofing, rebar, fwk, 9d 24-Mar-16 0% 16-Mar-16 SHT T002 Bay 5 base slab [120m/480m],150mm thk, drained section - Waterproofing, rebar, SHT T002 Bay 5 base slab [120m/480m], 150mm thk, drained section - Waterproofing, reb SHT6530 9d 25-Mar-16 02-Apr-16 0% SHT T002 Bay 6 base slab [150m/480m], 150mm thk, drained section -Waterproofing, rebar, SHT6540 0% SHT T002 Bay 6 base slab [150m/480m], 150mm thk, drained section - Wate 9d 03-Apr-16 11-Apr-16 SHT6550 SHT T002 Bay 7 base slab [180m/480m], 150mm thk, drained section - Waterproofing, rebar, 9d 12-Apr-16 20-Apr-16 0% SHT T002 Bay 7 base slab [180m/480m], 150mm thk, drained s SHT6560 SHT T002 Bay 8 base slab [210m/480m], 150mm thk, drained section - Waterproofing, rebar 9d 21-Apr-16 29-Apr-16 0% SHT T002 Bay 8 base slab [210m/480m], 150mn SHT T002 Bay 8 base slab [240m/48 SHT6570 SHT T002 Bay 8 base slab [240m/480m] - Waterproofing, rebar, fwk, concrete 9d 30-Apr-16 08-May-16 0% SHT6580 SHT T002 Bay 9 base slab [270m/480m] - Waterproofing, rebar, fwk, concrete SHT T002 Bay 9 base 9d 17-May-16 0% 09-May-16 SHT T002 SHT6590 SHT T002 Bay 10 base slab [300m/480m] -Waterproofing, rebar, fwk, concrete 9d 18-May-16 26-May-16 **Cross Passages** Civil & Structural and E&M Works Cross Passage At Mined Tunnel - 5 nos. Cross Passage - CP2 SHT9060-9 SHT CP2 Base slab - Formworks, rebars, concreting & formworks removal 28-Feb-16 08-Mar-16 SHT QP2 Base slab - Formworks, rebars, concreting & formworks removal SHT9060-30 SHT CP3 Lining - 1st stage, (Formworks, rebars, concreting & formworks removal) 09-Dec-15 A 15-Feb-16 A 100% SHT CP3 Lining - 2nd stage, (Formworks, rebars, concreting & formworks removal) SHT9060-40 0% SHT CP3 Lining - 2nd stage, (Formworks, rebars, concreting & formworks removal) 16-Feb-16 A 25-Feb-16 SHT9060-50 SHT CP3 Lining - 3rd stage, (Formworks, rebars, concreting & formworks removal) 0% SHT CP3 Lining - 3rd stage, (Formworks, rebars, concreting & formworks removal) 6d 26-Feb-16 02-Mar-16 SHT CP3 Lining - 4th stage, (Formworks, rebars, concreting & formworks removal) 0% SHT CP3 Lining - 4th stage, (Formworks, rebars, concreting & formworks removal) SHT9060-60 6d 03-Mar-16 08-Mar-16 SHT CP3 Base slab Formworks, rebars, concreting & formworks removal SHT9060-10 SHT CP3 Base slab - Formworks, rebars, concreting & formworks removal 10d 09-Mar-16 18-Mar-16 0% SHT9060-100 SHT CP4 Lining - 3rd stage, (Formworks, rebars, concreting & formworks removal) 7d 08-Dec-15 A 13-Jan-16 A 100% SHT9060-110 SHT CP4 Lining - 4th stage, (Formworks, rebars, concreting & formworks removal) 100% 7d 14-Jan-16 A 19-Jan-16 A SHT9060-120 SHT CP4 Base slab - Formworks, rebars, concreting & formworks removal 10d 0% SHT CP4 Base slab - Formworks, rebars, concreting & formworks removal 19-Mar-16 28-Mar-16 **Ventilation Building RC Works RC Walls** Wall W2 - Grid Line D SHT8260 SHT Vent. Bldg. - Wall W2 Upper part(1000mm thk) - Grid D/1-4, (Formworks, rebars, concrete) 12d 05-Jan-16 A 01-Feb-16 A SHT8270 SHT Vent. Bldg. - Wall W2 Upper part(1000mm thk) - Grid D/4-6, (Formworks, rebars, concrete) 09-Jan-16 A 22-Jan-16 A SHT Vent. Bldg. - Wall W1 Upper part(1000mm thk) - Grid A/1-4, (Formworks, rebars, concrete) 29-Dec-15 A 01-Feb-16 A 100% SHT8092 SHT8102 SHT Vent. Bldg. - Wall W1 Upper part(1000mm thk) - Grid A/4-6, (Formworks, rebars, concrete) 09-Jan-16 A 22-Jan-16 A 100% T002 - Area between E-G/1-6 Maintenance corridor SHT Vent. Bldg. - Main. Corridor (Grid G/3-4) at +14.456mPD, (Formworks, rebars, concrete) SHT9968 26-Feb-16 02-Mar-16 0% SHT Vent. Bldg. - Main. Corridor (Grid G/3-4) at +14.456mPD, (Formworks, rebars, concrete) SHT Vent. Bldg. - Main. Corridor (Grid G/2-3) at +14.456mPD, (Formworks, rebars, concrete) 08-Mar-16 ent. Bldg. - Main. Corridor (Grid G/2-3) at +14.456mPD, (Formworks, rebars, concrete) SHT9978 03-Mar-16 0% SHT Vent. Bldg. - Main. Corridor (Grid E-F/4-5) at +42.5mPD. (Formworks, rebars, concrete) 0% SHT Vent. Bldg. - Main. Corridor (Grid E-F/4-5) at +42.5mPD, (Formworks, rebars, concrete) SHT9938 09-Mar-16 14-Mar-16 SHT Vent. Bldg. - Main. Corridor (Grid G/2-5) at +19,95mPD, (Formworks SHT Vent. Bldg. - Main. Corridor (Grid G/2-5) at +19.95mPD, (Formworks, rebars, concrete) 27-Mar-16 01-Apr-16 0% SHT Vent. Bldg. - G/F - Ground floor slab(E-G/1-4), (Formworks, rebars, concrete) 21-Jan-16 A 26-Jan-16 A 100% SHT8069 12d SHT Vent, Bldg. - G/F - Ground floor slab(E-G/4-6), (Formworks, rebars, concrete) SHT8068 12d 21-Jan-16 A 26-Jan-16 A 100% 2nd Floor - 3rd Floor SHT Vent. Bldg. - 2/F - 3/F - Walls F2-F3 (F-G/1-4), (Formworks, rebars, concrete) SHT Vent. Bldg. - 2/F - 3/F - Walls F2-F3 (E-G/1-4), (Formworks, rebars, concrete) SHT8340 12-Nov-15 A 02-Mar-16 75% SHT8112 SHT Vent. Bldg. - 2/F - 3/F - Columns F2-F3 (E-G/4-6)-7 nos., (Formworks, rebars, concrete) 25-Feb-16 02-Mar-16 0% SHT Vent. Bldg - 2/F - 3/F - Columns F2-F3 (E-G/4-6)-7 nos., (Formworks, rebars, concrete) 7d SHT8410 SHT Vent. Bldg. - 2/F - 3/F - Walls F2-F3 (E-G/4-6), (Formworks, rebars, concrete) 7d 03-Mar-16 09-Mar-16 0% SHT Vent. Bldg. - 2/F - 3/F - Walls F2-F3 (E-G/4-6), (Formworks, rebars, concrete) 10-Mar-16 Went Bldg_= 4/F = 5/F = Columns C4E, C4F and C5F (E-G/1-4) (Formworks, rebars, concrete) SHT8592 SHT Vent. Bldg. - 4/F - 5/F - Columns C4E,C4F and C5F (E-G/1-4) (Formworks, rebars, 10d 01-Mar-16 0% SHT8602 SHT Vent. Bldg. - 4/F - 5/F - Walls F4-F5 (E-G/1-4), (Formworks, rebars, concrete) 10d 01-Mar-16 10-Mar-16 Vent. Bldg. - 4/F - 5/F - Walls F4-F5 (E-G/1-4), (Formworks, rebars, concrete) 30-Apr-16 SHT8612 SHT Vent. Bldg. - 4/F - 5/F - Temporary works for 5/F slab 05-May-16 0% SHT Vent. Bldg. - 4/F - 5/F - Temporary v SHT8622 SHT Vent. Bldg. - 4/F - 5/F - 5th Floor slab(E-G/1-6) (Formworks, rebars, concrete) 15d 06-May-16 20-May-16 0% SHT Vent. Bldg. Area between D-E/1-6 SHT Vent. Bldg. - G/F -UG/F - Columns C1D and C2Da to UG/F, (Formworks, rebars, concrete) 20-Feb-16 A 0% SHT Vent. Bldg. - G/F - UG/F - Columns C1D and C2Da to UG/F, (Formworks, rebars, concrete) SHT8222 29-Feb-16 SHT8162 SHT Vent. Bldg. - G/F -UG/F - Columns C5Da& C5Db, and Beams UGBD5 (Formworks, rebars, SHT Vent Bldg. - G/F - UG/F - Columns C5Da& C5Db, and Beams UGBD5 (Formworks, rebars, concrete) 6d 01-Mar-16 06-Mar-16 0% SHT8682 SHT Vent. Bldg. - G/F - UGF - Walls (Formworks, rebars, concrete) SHT Vent, Bldg. - G/F - UGF - Walls (Formworks, rebars, concrete) 7d 03-Mar-16 10-Mar-16 0% SHT Vent; Bldg. - G/F - UG/F - Backfilling works, (D-E/1-4) SHT Vent. Bldg. - G/F - UG/F - Backfilling works, (D-E/1-4) 3d 09-Mar-16 11-Mar-16 0% SHT8192 SHT Vent. Bldg. - G/F - UG/F - Temporary work for U/G slab (D-E/1-4) 4d 12-Mar-16 15-Mar-16 0% SHT Vent. Bldg. - G/F UG/F - Temporary work for U/G slab (D E/1-4) SHT8202 SHT Vent. Bldg. - G/F - UG/F - UG slab(D-E/1-4), (Formworks, rebars, concrete) 16-Mar-16 SHT Vent. Bldg.:- G/F -UG/F - UG slab(D-E/1-4), (Formworks, rebats, concrete) 6d 21-Mar-16 0% SHT8232 SHT Vent. Bldg. - G/F - UG/F - Backfilling works, (D-E/4-6) 4d 25-Mar-16 SHT Vent. Bldg. - G/F - UG/F - Backfilling works, (D-E/4-6) 22-Mar-16 0% SHT Vent. Bldg. - G/F - UG/F - Temporary work for U/G slab (D-E/4-6) SHT8242 SHT Vent. Bldg. - G/F -UG/F - Temporary work for U/G slab (D-E/4-6) 6d 26-Mar-16 31-Mar-16 0% SHT Vent. Bldg. - G/F - UG/F - UG slab(D-E/4-6), (Formworks, rebars, concrete) SHT8252 SHT Vent. Bldg. - G/F - UG/F - UG slab(D-E/4-6), (Formworks, rebars, concrete) 8d 01-Apr-16 08-Apr-16 0% Interface Room SHT9908 SHT Vent. Bldg. - Interface Room - Ground Floor Slab 10d 22-Jan-16 A 26-Jan-16 A 100% SHT9888 SHT Vent. Bldg. - Interface Room - Roof Slab and Beam (Formworks, rebars, concrete) 19-Feb-16 A SHT9918 SHT Vent. Bldg. - Interface Room - Wall (Formworks, rebars, concrete) 27-Jan-16 A 19-Feb-16 A SHT Vent. Bldg. - Ground Floor slab (D-E/2-4) (Formworks, rebars, concrete) 12d 16-Jan-16 A 26-Jan-16 A 100% SHT8442 SHT Vent. Bldg. - Ground Floor slab (D-E/4-6) (Formworks, rebars, concrete) , except Water 26-Jan-16 A 100% SHT8422 0% SHT Vent. Bldg. - UG/F - 1/F Columns C1D and C2Da & Beam UGBD1a (Formworks, rebars, 10d 01-Mar-16 11-Mar-16 Vent.∤Bldg. - ŲG/F - 1/F Columns C1D and C2Da & Beam UGBD1a (Formworks, rebars, concrete SHT8692 SHT Vent. Bldg. - UG/F - 1/F - Walls (Formworks, rebars, concrete) 11-Mar-16 18-Mar-16 0% SHT Vent. Bldg. - UG/F - 1/F - Walls (Formworks, rebars, concrete) SHT9928 SHT Vent. Bldg. - 1st Floor slab & Beam (D-E/2-3) (Formworks, rebars, concrete) 7d 11-Mar-16 18-Mar-16 0% SHT Vent. Bldg. - 1st Floor slab & Beam (D-E/2-3) (Formworks, rebars, concrete) SHT8432 SHT Vent. Bldg. - G/F - Backfilling works 10d 17-Mar-16 31-Mar-16 SHT Vent. Bldg. - G/F - Backfilling works 0% SHT Vent. Bldg. - 1/F - 2/F - Walls F1-F2, (D-E/2-4) (Formworks, rebars, concrete) SHT Vent. Bldg. - 1/F - 2/F - Walls F1-F2, (D-E/2-4) (Formworks, rebars, concrete) SHT8462 8d 16-Feb-16 A 25-Feb-16 25% SHT8472 SHT Vent. Bldg. - 1/F - 2/F -Temporary work for 2/F slab (D-E/2-4) 0% SHT Vent. Bldg. - 1/F - 2/F - Temporary work for 2/F slab (D-E/2-4) 20-Feb-16 25-Feb-16

Layout ZMB - Layout 1 (3M Rolling Prog)(3M46)

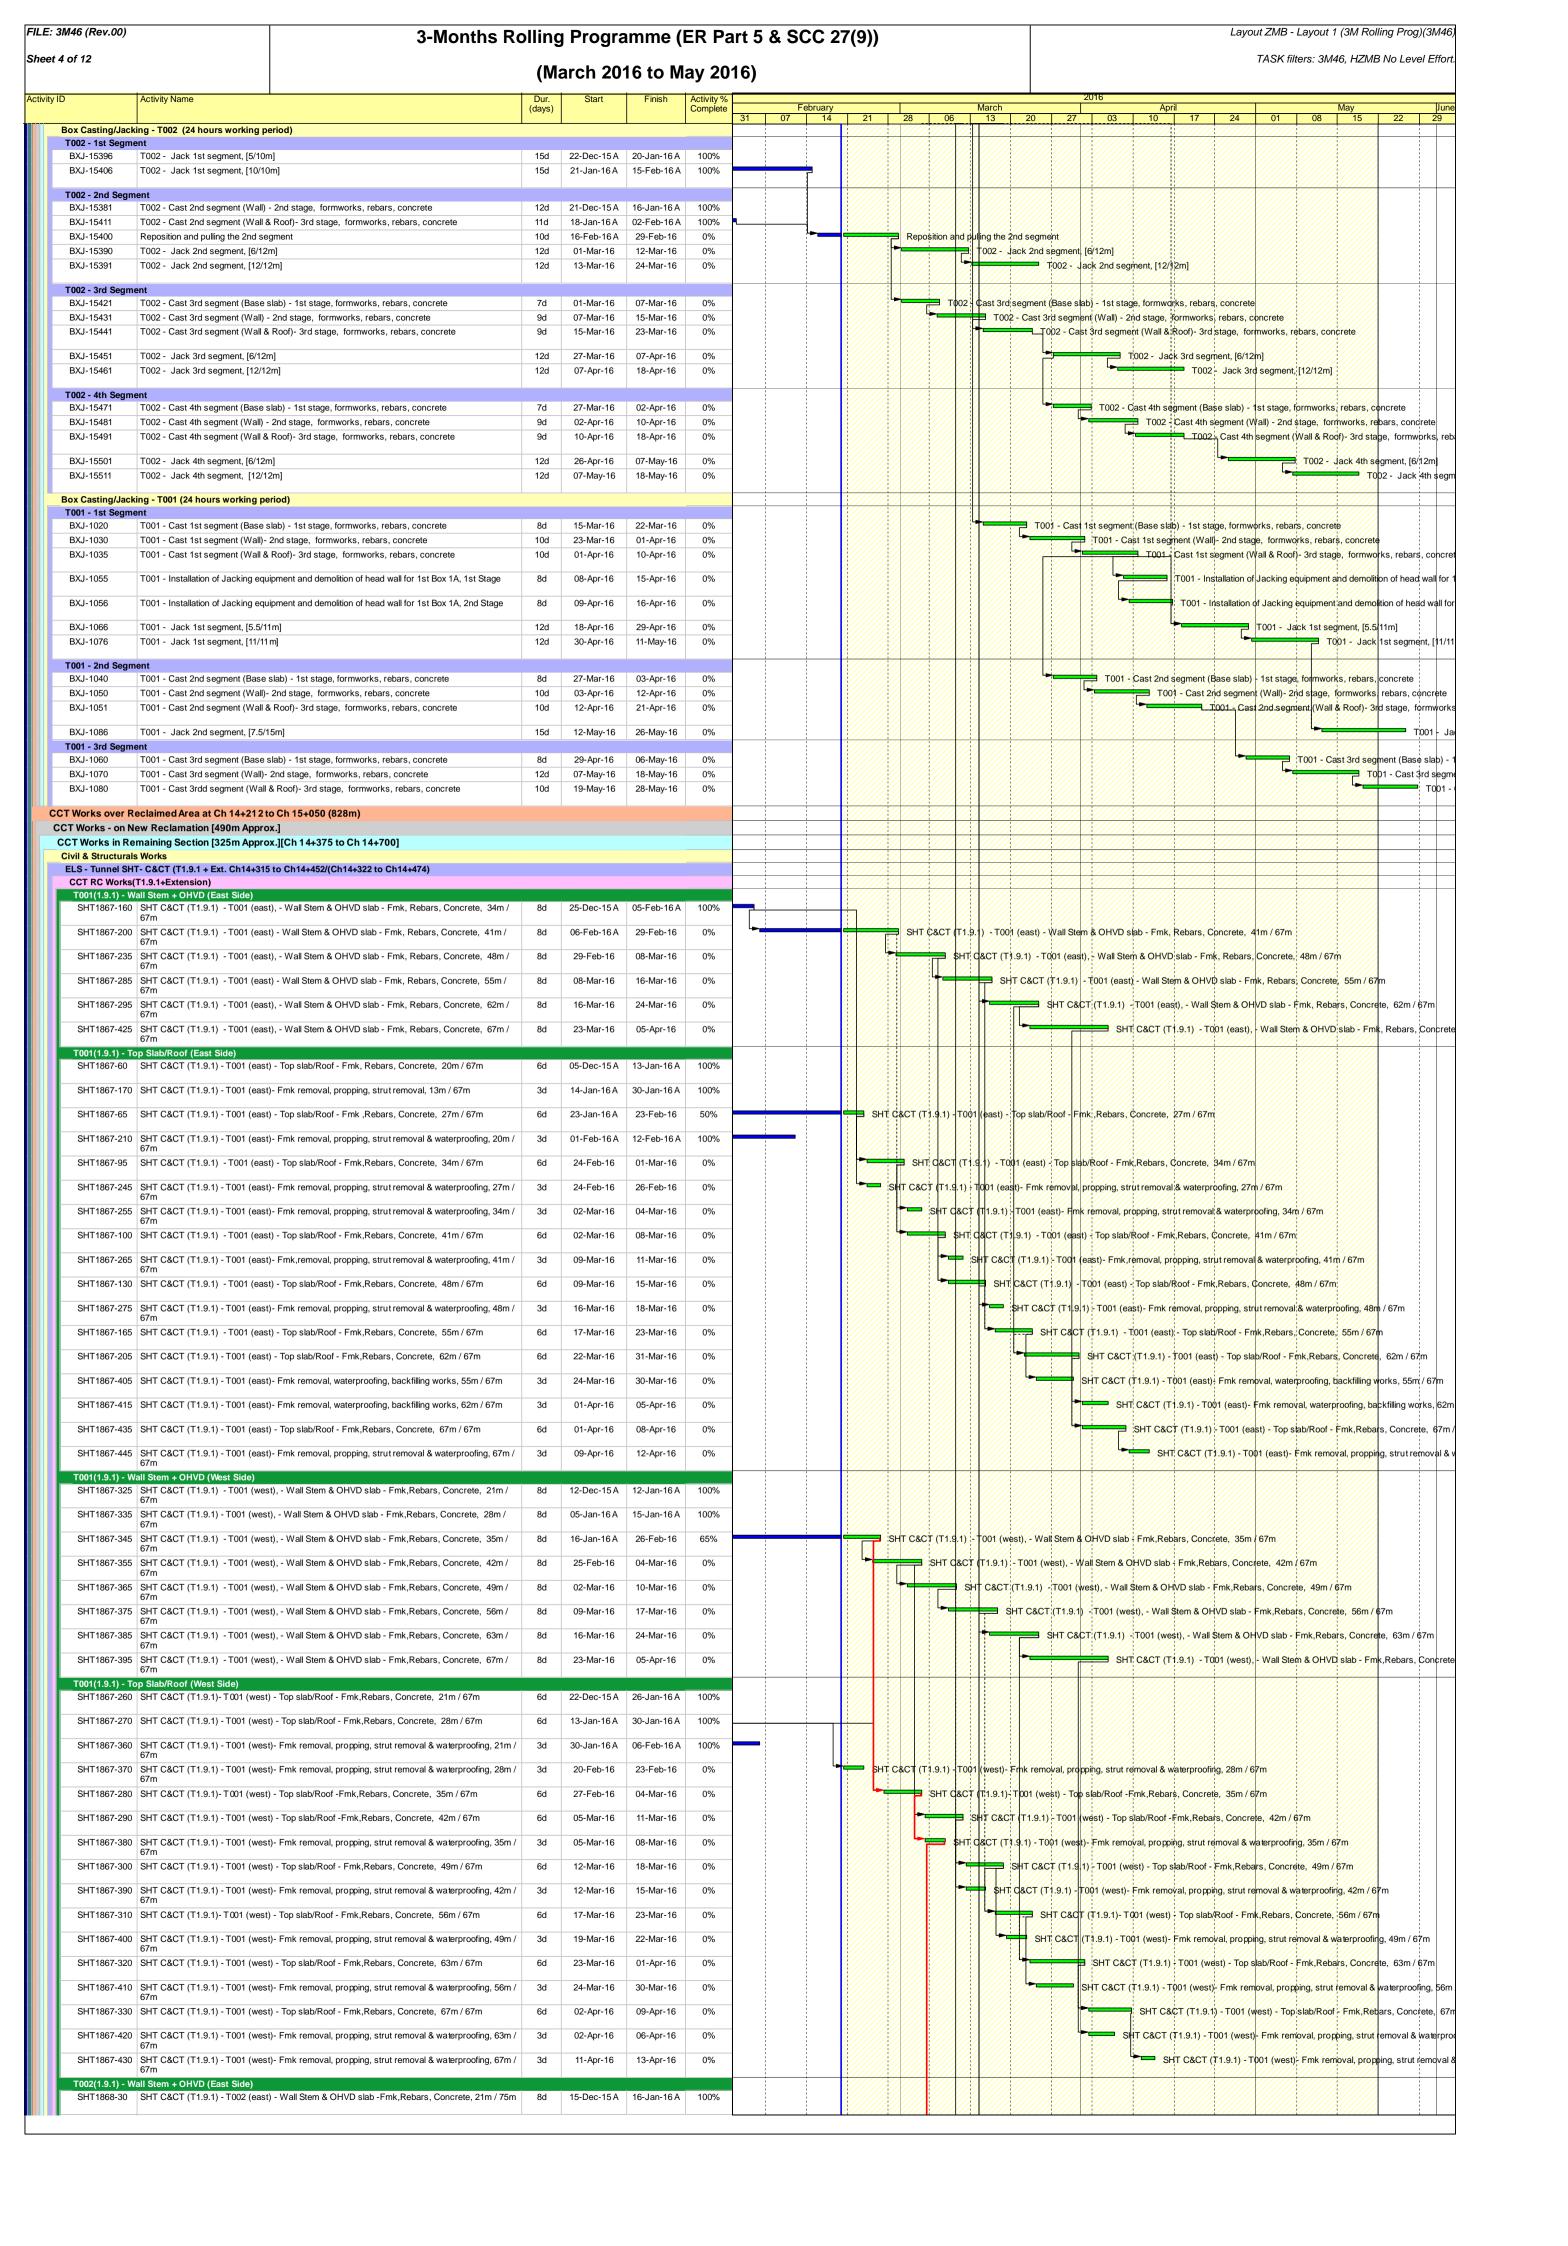

t 10 of 12			(Ma	arch 20	16 to M	ay 20	16)					TASK filters: 3M46, HZMB No Level E
y ID	Activity Name		Dur. (days)	Start	Finish	Activity % Complete	February				March	
MAS1625	Maint. Access Subway Ramp A, B	ay A3 - RC Wall formworks removal	3d	15-Feb-16 A	17-Feb-16 A	100%	31 07 14	21	28	06	13	20 27 03 10 17 24 01 08 15 22 2
MAS1655	concreting)	ay A3 - Top slab (internal falseworks, formworks, rebar fixing,	5d	24-Mar-16	01-Apr-16	0%						Maint. Access Subway Ramp A, Bay A3 Top slab (internal falseworks, formworks, reb
MAS1665 MAS1635		ay A3 - Top Slab formworks removal ay A3 - Staircase (formworks, rebar fixing, concreting)	3d 5d	02-Apr-16 11-Apr-16	06-Apr-16 15-Apr-16	0%						Maint, Access Subway Ramp A, Bay A3 - Top Slab formworks removal Maint, Access Subway Ramp A, Bay A3 - Staircase (formworks, re
MAS1645 Bay A4	Maint. Access Subway Ramp A, B	ay A3 - Staircase formworks removal	3d	16-Apr-16	19-Apr-16	0%						Maint. Access Subway Ramp A, Bay A3 - Staircase formwork
MAS1565	Maint. Access Subway Ramp A, B	ay A4 - RC Wall formworks removal	2d	11-Jan-16 A	13-Jan-16 A	100%						
MAS1575	Maint. Access Subway Ramp A, B	ay A4 - Staircase (formworks, rebar fixing, concreting)	5d	11-Apr-16	15-Apr-16	0%						Maint. Access Subway Ramp A, Bay A4 - Staircase (formworks, re
MAS1585 Bay A5	Maint. Access Subway Ramp A, B	ay A4 - Staircase formworks removal	3d	16-Apr-16	19-Apr-16	0%						Maint. Access Subway Ramp A, Bay A4 - Staircase formwork
MAS1505		ay A5 - RC Wall formworks removal	2d	11-Jan-16 A	13-Jan-16 A	100%						
MAS1515 MAS1525		ay A5 - Staircase (formworks, rebar fixing, concreting) ay A5 - Staircase formworks removal	5d 3d	16-Apr-16 22-Apr-16	21-Apr-16 25-Apr-16	0%						Maint. Access Subway Ramp A, Bay A5 - Staircase (fprm Maint Access Subway Ramp A, Bay A5 - Staircase
Bay A6 MAS1470		ay A6 - Staircase (formworks, rebar fixing, concreting)	5d	16-Apr-16	21-Apr-16	0%						Maint. Access Subway Ramp A, Bay A6 - Staircase (forms
MAS1475		ay A6 - Staircase formworks removal	3d	22-Apr-16	25-Apr-16	0%						Maint Access Subway Ramp A, BayA6 - Staircase
01 / T002 ON GF CSS & E&M	RADE ROADWORKS (Works und	er Section 1]										
CLP BA2.1205-315	CLP - excavation and cable laying	Ch15+540 to Ch15+650)	12d	26-Jan-16 A	05-Feb-16 A	100%						
BA2.1205-325	CLP - excavation and cable laying	·	12d	03-May-16*	17-May-16	0%						CLP - excavation a
BA2.1205-335 terface w/ HY/2	CLP - excavation and cable laying 2010/02- 16+045 to 16+223.24	Ch15+830 to Ch16+160)	12d	17-May-16*	30-May-16	0%						
23730	sheet piles & mobilization work	C] - Temporary work for Pump Sump P/S SPS7, Delivery of	15d	10-Aug-15 A	08-Mar-16	30%				LR	SH-HKB	CF [north area-Portion C] - Temporary work for Pump Sump P/S SPS7, Delivery of sheet piles & mobilization wo
A237301 A237302	installation, Stage 1	C] - Temporary work for Pump Sump P/S SPS7, Sheet piles C] - Temporary work for Pump Sump P/S SPS7, Sheet piles	16d 16d	09-Mar-16 31-Mar-16	30-Mar-16	0%						LR SH-HKBCF [north area-Portion C] - Temporary work for Pump Sump P/S SPS7, Sheet p
N237302 N237401	installation, Stage 2 LR SH-HKBCF [north area-Portion]	C] - Temporary work for Pump Sump P/S SPS7, Sheet piles C] - Temporary work for Pump Sump P/S SPS7, Sheet piles	16d 15d	31-Mar-16 20-Apr-16	19-Apr-16 07-May-16	0%						LR SH-HKBCF [north area-Portion C] - Tempdrary work for F
A237402	installation, Stage 3	C] - Excavation for Pump Sump P/S SPS7, 1st Stage	15d	09-May-16	26-May-16	0%						LR SH
		der Section 2 (Middle to North Area) of SB Airport Rd (Works under Section 2)										
A2- Initial Works BA2.1200-3			12d	30-Dec-15 A	12-Jan-16 A	100%						
A2- Foundation					107							
A2.1200-4	Bridge A2 Piers - Prebored h-piles		12d	13-Jan-16 A	28-Jan-16 A							
8A2.1200-14	Bridge A2 Piers - Prebored h-piles		12d	28-Jan-16 A	18-Feb-16 A					Dria	Diore	Prehared haniles Pile Test
A2.1200-24 A2.1200-34	Bridge A2 Piers - Prebored h-piles Bridge A2 Piers - Prebored h-piles		12d 12d	19-Feb-16 A 05-Mar-16	04-Mar-16 18-Mar-16	0%				uge A		Prebored h-piles Pile Test Bridge A2 Piers - Prebored h-piles Pile Cap, B1 - Excavation
3A2.1200-54 3A2.1200-54	Bridge A2 Piers - Prebored h-piles	• *	12d 12d 7d	05-Mar-16 05-Mar-16	18-Mar-16 30-Mar-16	0% 0%					7//////	Bridge A2 Piers - Prebored h-piles Pile Cab, B1 - Excavation Bridge A2 Piers - Prebored h-piles Pile Cab, B2 - Excavation Bridge A2 Piers - Prebored h-piles Pile Cap, B1 - Fwk, Rebar and Concreting
3A2.1200-64	-	Pile Cap, B2 - Fwk, Rebar and Concreting	7d 7d	19-Mar-16	30-Mar-16	0%						Bridge A2 Piers - Prebored h-piles Pile Cap, B1 - Pwk, Rebar and Concreting Bridge A2 Piers - Prebored h-piles Pile Cap, B2 - Fwk, Rebar and Concreting
A2 -South Abut n 3A2.1205-345 3A2.1205-365	Bridge A2 South Abut - AA approva	I for Demolish extg bridge staircase	0d	07-Mar-16* 07-Mar-16	22-Mar-16	0%				♦ Bridg	e A2 Sout	nth Abut - AA approval for Demolish extg bridge staircase Bridge A2 Sputh Abut - Demolish extg bridge staircase
A2.1205-405	Bridge A2 South Abut - Demolish e. Bridge A2 South Abut - U- Trough F	amp Ch049 - Ch056 - Base Slab	14d 12d	23-Mar-16	09-Apr-16	0%						Bridge A2 South Abut - U- Trough Ramp Ch049 - Ch056 - Base Slab
A2.1205-375 A2.1205-475	Bridge A2 South Abut - Retaining W Bridge A2 South Abut - U- Trough F	amp Ch049 - Ch056 - Wall Stem	8d 14d	11-Apr-16 11-Apr-16	19-Apr-16 26-Apr-16	0%						Bridge A2 South Abut - Retaining Wall Panel 1 - Base Slab Bridge A2 South Abut - Ut Trough Ramp Ch049 - C
A2.1205-415 A2.1205-435	Bridge A2 South Abut - Retaining W Bridge A2 South Abut - Retaining W		10d 8d	20-Apr-16 20-Apr-16	30-Apr-16 28-Apr-16	0% 0%						Bridge A2 South Abut - Retaining Wall Panel 2 Bridge A2 South Abut - Retaining Wall Panel 2- E
3A2.1205-455 3A2.1205-445	Bridge A2 South Abut - Retaining W Bridge A2 South Abut - Retaining W		8d 10d	29-Apr-16 03-May-16	09-May-16 13-May-16	0% 0%						L. Bridge A2 South Abut - Retainin Bridge A2 South Abut - Re
A2.1205-465	Bridge A2 South Abut - Retaining W	all Panel 3 - Well Stem	10d	16-May-16	26-May-16	0%						Bridge
North Abutment				,								
BA2.1205-225 BA2.1205-245	Bridge A2 North Abut - Excavation Bridge A2 North Abut - Pad Footing		24d 15d	14-Mar-16 15-Apr-16	14-Apr-16 03-May-16	0%						Bridge A2 North Abut - Excavation, blinding layer
BA2.1205-285	Bridge A2 North Abut - Pad Footing	•	15d	04-May-16	21-May-16	0%						Bridge A2 North Abut - Pad Footing - 1 b Bridge A2 No
BA2.1205-3	Bridge A2 Ramp - Excavation, bline	ling layer	12d	20-Feb-16	04-Mar-16	0%	 			Bridge A	Ramp -	Excavation, blinding layer
BA2.1205-4 BA2.1205-5	Bridge A2 Ramp - Bas e Slab Bridge A2 Ramp - Wall		7d 12d	05-Mar-16 14-Mar-16	12-Mar-16 30-Mar-16	0%					Bridge	a A2 Ramp - Bas e Slab Bridge A2 Ramp - Wall
Bay 2 BA2.1205-15	Bridge A2 Ramp - Excavation, blin-	lina lavas	12d	05-Mar-16	18-Mar-16	0%						Bridge A2 Ramp - Excavation, blinding layer
BA2.1205-15	Bridge A2 Ramp - Bas e Slab	iling layer	7d	19-Mar-16	30-Mar-16	0%						Bridge A2 Ramp - Bas e Slab
BA2.1205-35 Bay 3	Bridge A2 Ramp - Wall		12d	31-Mar-16	14-Apr-16	0%						Bridge A2 Ramp - Wall
BA2.1205-45	Bridge A2 Ramp - Excavation, bline	ling layer	12d	09-Jan-16 A	26-Jan-16 A	100%						
BA2.1205-55	Bridge A2 Ramp - Bas e Slab		7d	27-Jan-16 A	16-Feb-16 A							
BA2.1205-65	Bridge A2 Ramp - Wall		12d	17-Feb-16 A	04-Mar-16	0%				Bridge A	2 Ramp	Wall
BA2.1205-105	Bridge A2 Ramp - Excavation, bline	ling layer	12d	09-Jan-16 A	26-Jan-16 A	100%						
BA2.1205-115 BA2.1205-125	Bridge A2 Ramp - Bas e Slab Bridge A2 Ramp - Wall		7d 12d	05-Mar-16 14-Mar-16	12-Mar-16 30-Mar-16	0%					Bridge	A2 Ramp - Bas e Slab Bridge A2 Ramp - Wall
Bay 5 BA2.1205-75	Bridge A2 Ramp - Excavation, blin	ling layer	12d	19-Mar-16	06-Apr-16	0%						Bridge A2 Ralmp - Excavation, blinding layer
BA2.1205-85	Bridge A2 Ramp - Bas e Slab		7d	07-Apr-16	14-Apr-16	0%						Bridge A2 Ramp - Bas e Slab
BA2.1205-95 Bay 6	Bridge A2 Ramp - Wall		12d	15-Apr-16	28-Apr-16	0%						Bridge A2 Ramp - Wall
BA2.1205-165	Bridge A2 Ramp - Excavation, blin	ling layer	12d	07-Apr-16	20-Apr-16	0%						Bridge A2 Ramp - Excavation, blinding layer
BA2.1205-175 BA2.1205-185	Bridge A2 Ramp - Bas e Slab Bridge A2 Ramp - Wall		7d 12d	21-Apr-16 29-Apr-16	28-Apr-16 13-May-16	0% 0%						Bridge A2 Ramp - Base Slab Bridge A2 Ramp - Wall
BA2.1205-195	Bridge A2 Ramp - Excavation, bline	ling layer	12d	21-Apr-16	05-May-16	0%						Bridge A2 Ramp - Excavation, blindin
BA2.1205-205	Bridge A2 Ramp - Bas e Slab		7d	06-May-16	13-May-16	0%						Bridge A2 Ramp - Base 9
BA2.1205-215 Bay 8	Bridge A2 Ramp - Wall		12d	16-May-16	28-May-16	0%						Bri
BA2.1205-135	Bridge A2 Ramp - Excavation, bline	ling layer	12d	06-May-16	20-May-16	0%						Bridge A2 Ram
tility Culvert No.		o Cheong Hong Road [48m Approx.]-1										
UC1.1114	ty Diversion inside UC 1 Permanent Utility diversion - teleco		14d	29-Feb-16*	15-Mar-16	0%					77X77	ermanent Utility diversion - telecom cable (by others), Stage 1
UC1.1115 UC1.1116	Permanent Utility diversion - cutting	/jointing/switching ATC/CAD cables(by others) /jointing/switching ATC/CAD cables complete	14d 0d	29-Feb-16*	15-Mar-16 15-Mar-16	0%					///////////////////////////////////////	ermanent Utility diversion - cutting/jointing/switching ATC/CAD cables(by others) ermanent Utility diversion - cutting/jointing/switching ATC/CAD cables complete
UC1.1163 UC1.1173	Permanent Utility diversion - teleco Permanent Utility diversion - teleco		16d 16d	16-Mar-16 08-Apr-16	07-Apr-16 26-Apr-16	0% 0%						Permanent Utility diversion - telecom cable (by others), Stage 2 Permanent Utility diversion - telecom cable (by others)
	p. 2 Ext. near Bridge A2 [15m App	rox.] (Works under Section 2)										
UC2.1058	Permanent Utility Diversion - TCS:	* *	15d	29-Feb-16*	16-Mar-16	0%					///////////	Permanent Utility Diversion - TCSS (by others), Stage 1
UC2.1059 UC2.10591	Permanent Utility Diversion - CAD	ATC cables(by others), Stage 2	10d 10d	29-Feb-16* 11-Mar-16	10-Mar-16 22-Mar-16	0%						ent Utility Diversion - CAD/ATC cables(by others), Stage 1 Permanent Utility Diversion - CAD/ATC cables(by others), Stage 2
UC2.10581 UC2.10592	Permanent Utility Diversion - TCS: Permanent Utility Diversion - CAD		15d 10d	17-Mar-16 23-Mar-16	07-Apr-16 07-Apr-16	0% 0%						Permanent Utility Diversion - TCSS (by others), Stage 2 Permanent Utility Diversion - CAD/ATC cables(by others), Stage 2
UC2.10525 UC2.1061	•	r main (by CSHK), connection works n of CAD/ATC cables(by others) -30 Nov 2013	7d 0d	06-Apr-16*	13-Apr-16 07-Apr-16	0% 0%						Permanent Utility Diversion - sewer main (by CSHK), connection work Complete permanent utility diversion of CAD/ATC cables(by others) -30 Nov 20
UC2.10582 UC2.105241	Permanent Utility Diversion - TCS: Permanent Utility Diversion - TCS:	(by others), Stage 3	15d 15d	08-Apr-16 26-Apr-16	25-Apr-16 13-May-16	0% 0%						Permanent Utility Diversion - TCSS (by others), Star
tility Culvert No.	. 3 and Permanent Utility Divers											
Backfilling and R RET11000	Retaining Structure Bay 1 - Base slab (Formwork, Reb	ar and concreting)	10d	20-Jan-16 A	05-Feb-16 A	100%						
RET11040	Bay 3- Base slab (Formwork, Reba	r and concreting)	10d	20-Jan-16 A	05-Feb-16 A	100%						
RET11010	Bay 1 - Wall Stem (Formwork, Reb	ar and concreting)	12d	05-Feb-16 A	01-Mar-16	65%	-		Ba	y 1 - Wall S	Stem (For	rmwork, Rebar and concreting)
RET11050	Bay 3 - Wall stem(Formwork, Reba	r and concreting)	12d	05-Feb-16 A	01-Mar-16	65%			Ba	y3-Walls	stem(Forn	mwork, Rebar and concreting)
RET11080	Bay 5 - Base slab (Formwork, Reb	ar and concreting)	10d	05-Feb-16 A	01-Mar-16	70%			Ba	y 5 - Base	slab (Fbri	mwork, Rebar and concreting)
RET11070	Bay 4 - Base slab (Formwork, Reb		10d	02-Mar-16	12-Mar-16	0%	1	////////	7/M//	1/1/1/1/	<u> </u>	- Base slab (Formwork, Rebar and concreting)

			(Ma	TASK filters: 3M46, HZMB No Level Effort				
ty ID	Activity Name		Dur. (days)	Start	Finish	Activity % Complete	February March	2016 April May
BA1.1022-4	Retaining Wall C - C4 - Wall, Form	nworks/scaffolding + Steel Bar Fixing	10d	16-May-16	26-May-16	0%	31 07 14 21 28 06 13	20 27 03 10 17 24 01 08 15 22 2 Retain
Retaining Wall D	D(Bay 1 to Bay 4)							
BA1.1021-16	Retaining Wall D - D3 - Excavation		15d	17-Mar-16	07-Apr-16	0%		Retaining Wall D - D3 - Excavation
BA1.1020-21 BA1.1020-22	Retaining Wall D - D3 -Base slab, Retaining Wall D - D3 - Base slab,	Concreting	14d 1d	08-Apr-16 25-Apr-16	23-Apr-16 25-Apr-16	0%		Retaining Wall D - D3 - Base slab, Formwork + Steel Ba
BA1.1020-221 BA1.1020-222	Retaining Wall D - D3 - Wall, Conc	-	10d 1d	26-Apr-16 09-May-16	07-May-16 09-May-16	0%		Retaining Wall D - D3 - Wall, Form Retaining Wall D - D3 - Wall, Co
BA1.1020-223 BA1.1020-293	Retaining Wall D - D3 - Wall, Remo	<u> </u>	2d 4d	10-May-16 12-May-16	11-May-16 17-May-16	0%		Retaining Wall D - D3 - Wall Retaining Wall D - I
Bay D4 BA1.1020-233	Retaining Wall D - D4 - Excavation		15d	18-May-16	03-Jun-16	0%		
Utilitiy Culvert No				05.11 45.4	40.5.1.40.4	1000/		
UC1.11162 UC1.11142		ure extension - Ch18 - Ch36 - Wall and Roof ure extension - Ch00 - Ch17 - Wall and Roof	5d 5d	05-Nov-15 A 11-Jan-16 A	18-Feb-16 A 03-Feb-16 A			
		rt traffic to BA1 & ex. ECR SB RD/ Future M009)	00	Tr dail 1071	00 1 00 1071	10070		
A4350 BA1 - Cantilever	Implement Stage 3 TTA (TBC, inclured Implement Stage 3 TTA (TBC, inclured Implement Stage 3 TTA (TBC, including Implement Stage 3 TTA (TBC, includ	uding exact alignment)	0d		07-Mar-16*	0%	mplement Stage	3 TTA (TBC, including exact alignment)
A3620 A3570	Bridge A1 Deck - cantilever section Bridge A1 Deck - cantilever section	• • •	12d 12d	08-Mar-16 22-Mar-16	21-Mar-16 08-Apr-16	0% 0%		Bridge A1 Deck - cantilever section + parapet, 1st half Bridge A1 Deck - cantilever section + parapet, 2nd half
A4360 A4440		n wearing course and road markings n wearing course and road markings	12d 12d	09-Apr-16 23-Apr-16	22-Apr-16 07-May-16	0%		Bridge A1 Deck - cantilever section wearing course and Bridge A1 Deck - cantilever section
	(except entrance to ex. Tung Fa	iRd)	04	07 May 40*		00/		
A4430 A4411	Start works M006: Drainage works +Undergro	ound utilities (watermain, TCSS, telecoms etc.), 1st half	0d 12d	07-Mar-16* 07-Mar-16	19-Mar-16	0%	Start works	M006: Drainage works +Underground utilities (watermain, TCSS, telecoms etc.), 1st half
A4610		ound utilities (watermain, TCSS, telecoms etc.), 2nd half	12d	21-Mar-16	07-Apr-16	0%		M006: Drainage works +Underground utilities (watermain, TCSS, telecoms etc
A4620 A4621		road base and precast kerbs, road lighting poles	12d	31-Mar-16	14-Apr-16 28-Apr-16	0%		M006: Road formation, subbase, road base and precast kerbs, road
A4630	M006: Final wearing course and ro	road base and precast kerbs, road lighting poles oad marking and traffic signs, road lighting lamps & T&C	12d 12d	15-Apr-16 22-Apr-16	06-May-16			M006: Road formation, subbase, road base and M006: Final wearing course and road
Initial Works A3950	rmanent Soldier Pile Wall along	rincipal setting out stations, 1st half	12d	09-Mar-16	22-Mar-16	0%		Joint condition; survey /Establish principal setting out stations, 1st half
A3939	Erect safety fence along AEL side,		12d	09-Mar-16	22-Mar-16	0%		Erect safety fence along AEL side, 1st half
A3952 A3940	Install ADMS, 1st part Erect safety fence along AEL side,	.2nd half'	12d 12d	09-Mar-16 23-Mar-16	22-Mar-16 09-Apr-16	0% 0%		Install ADMS, 1st part Erect safety fence along AEL side, 2nd half
A3953 A3951		rincipal setting out stations, 2nd half	12d 12d	23-Mar-16 23-Mar-16	09-Apr-16 09-Apr-16	0% 0%		Install ADMS, 2nd part Joint condition survey /Establish principal setting out stations, 2nd half
A3963 Utilities Perman	Install ADMS, 3rd part nent Diversion at BA1/Depresse	d Rd Area	16d	11-Apr-16	28-Apr-16	0%		Install ADM\$, 3rd part
A3880	Permanent utility diversion - fresh	water main (by CSHK), 1st Stage	15d	11-Apr-16	27-Apr-16	0%		Permanent utility diversion - fresh water main (by
A3900 A3840 A3850	Permanent utility diversion - gas m Permanent utility diversion - teleco Permanent utility diversion - TCSS	om cable / CAD cable (by others), 1st Stage	15d 15d 15d	11-Apr-16 11-Apr-16 11-Apr-16	27-Apr-16 27-Apr-16 27-Apr-16	0% 0% 0%		Permanent utility diversion - gas main (by others) Permanent utility diversion - telecom cable / CAD Permanent utility diversion - TCSS cable (by other
A3850 A3870 A3931	Permanent utility diversion - CLP c	cable civil prov. works, 1st stage	15d	11-Apr-16	27-Apr-16	0%		Permanent utility diversion - CLP cable civil prov.
A3891 A3930	Permanent utility diversion - CLP c Permanent utility diversion - fresh Permanent utility diversion - gas m	water main (by CSHK), 1st Stage	15d 15d 15d	28-Apr-16 28-Apr-16 28-Apr-16	17-May-16 17-May-16 17-May-16	0% 0% 0%		Permanent utility die
A3911 A3921		om cable / CAD cable (by others), 1st Stage	15d 15d	28-Apr-16 28-Apr-16	17-May-16 17-May-16	0%		Permanent utility div
A3881 A3901	Permanent utility diversion - fresh Permanent utility diversion - gas m	water main (by CSHK)	30d 30d	18-May-16 18-May-16	22-Jun-16 22-Jun-16	0%		2 Februarien duny di
A3841 A3851	Permanent utility diversion - gas in Permanent utility diversion - teleco Permanent utility diversion - TCSS	om cable / CAD cable (by others)	30d 30d	18-May-16 18-May-16	22-Jun-16 22-Jun-16	0%		
A3871	Permanent utility diversion - CLP c		30d	18-May-16	22-Jun-16	0%		
A4050	Permanent soldier pile wall (AEL si	ide)- site investigation	14d	29-Apr-16	17-May-16	0%		Permanent soldier
A3990 Construct M008,	Permanent soldier pile wall (AEL si , Ch 0+100 to Ch 0+787, L=687m	ide)- piling works, 1st 15nos (incl. pile test) n (except Depressed Rd. Area)	15d	18-May-16	03-Jun-16	0%		
A4370	_	Underground utilities (watermain), 1st 50m	15d	08-Mar-16	24-Mar-16	0%		M008: 1st Half: Drainage works +Underground utilities (watermain), 1st 50m
A4371 A4372	M008: 1st Half: Drainage works +l	Underground utilities (watermain) 2nd 50m Underground utilities (watermain) 3rd 50m	15d 15d	29-Mar-16 16-Apr-16	15-Apr-16 04-May-16	0%		:M008: 1st:Half: Drainage works +Underground utilities (watermain) M008: 1st Half: Drainage works +Underground utilities (watermain)
A4373 Construct M007 A4590	Ch. 0+100 to Ch. 0+483), L=383	Underground utilities (watermain) 4th 50m The reclamation portion (but start early at landside portion)	15d	05-May-16	23-May-16 18-Mar-16*	0%		M008: 1st Start after surcharge removed at reclamation portion (but start early at landside portion)
A4540		Underground utilities (watermain), 1st 50m	0d 15d	19-Mar-16	09-Apr-16	0%		M007: 1st Half: Drainage works +Underground utilities (watermain), 1st 50m
A4720 A4730		Underground utilities (watermain), 2nd 50m Underground utilities (watermain), 3rd 50m	15d 15d	11-Apr-16 28-Apr-16	27-Apr-16 17-May-16	0% 0%		M007: 1st Half: Drainage works + Underground ut
A4900	M007: 1st Half: Drainage works +l	Underground utilities (watermain,), 4th 50m	15d	18-May-16	03-Jun-16	0%		
A4720 A4730	M007: 1st Half: Drainage works +\text{\text{\text{M007:}} 1st Half: Drainage works +\text{\text{\text{\text{\text{V}}}}}	Underground utilities (watermain), 2nd 50m Underground utilities (watermain), 3rd 50m	15d 15d	11-Apr-16 28-Apr-16	27-Apr-16 17-May-16	0% 0%		MQ07: 1st Half: Drainage works + Undergroun
