


Activity ID	Activity Name	Orig Dur	Planned Start	Planned Finish	Current Start	Current Finish	2015									2016					
							May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan						
TMCLK - Northern Connection Sub-Sea Tunnel Section																					
General Submissions																					
General Design Submissions																					
(A19) DDA for Roadworks & Project Alignment																					
DD68370	SO's Review	35	18-Sep-14	22-Oct-14	22-Dec-14A	15-Jul-15A															
(G6) IFA for Tunnel GBP																					
DD70750	SO's Review	35	29-Apr-14	02-Jun-14	03-Jul-14A	30-Aug-15															
DD70760	SO Approval with Condition R eceived	0		03-Jun-14		31-Aug-15															
Construction Supervision Plan																					
GEO1115	2nd GEO Review	28	29-Mar-14	25-Apr-14	01-Feb-14A	11-Jun-15 A															
Construction																					
Northern Landfall																					
North Reclamation (Phase 1)																					
Construction																					
Zone D1																					
Reclamation																					
NRC15160	Surcharge Removal - Zone D1 - (CH205 to 255) to +6mPD	8	09-Nov-15	17-Nov-15	17-Dec-15	19-Dec-15															
NRC15180	Surcharge Removal - Zone D1 - (CH255 to 305) to +6mPD	7	24-Nov-15	01-Dec-15	19-Dec-15A	07-Jan-16															
NRC15190	Surcharge Period - Zone D1 - (CH305 to 355)	180	19-Nov-14	17-May-15	03-Jun-15A	06-Jul-15A															
NRC15200	Surcharge Removal - Zone D1 - (CH305 to 355)	7	18-May-15	26-May-15	03-Jun-15A	06-Jul-15A															
Zone D2																					
Reclamation																					
NRC15210	Surcharge Period - Zone D2 - (CH355 to 405)	180	02-Dec-14	30-May-15	17-Nov-14A	15-May-15A															
NRC15220	Surcharge Removal - Zone D2 - (CH355 to 405)	9	01-Jun-15	10-Jun-15	15-Jun-15A	08-Jul-15A															
NRC15230	Surcharge Period - Zone D2 - (CH405 to 443)	180	12-Dec-14	09-Jun-15	21-Nov-14A	19-May-15A															
NRC15240	Surcharge Removal - Zone D2 - (CH405 to 443)	9	11-Jun-15	22-Jun-15	15-Jun-15A	10-Jul-15A															
Zone C1																					
Reclamation																					
NRC15260	Surcharge Removal - Zone C1 - (CH443 to 493)	10	06-May-17	17-May-17	27-Jun-15A	07-Aug-15A															
NRC15270	Surcharge Period - Zone C1 - (CH493 to 543)	180	13-Nov-14	12-May-15	31-Dec-14A	28-Jun-15A															
NRC15280	Surcharge Removal - Zone C1 - (CH493 to 543)	10	06-May-17	17-May-17	22-Jul-15A	14-Aug-15A															
Zone C2																					
Reclamation																					
NRC15290	Surcharge Period - Zone C2 - (CH543 to 598)	180	05-Nov-14	03-May-15	31-Dec-14A	28-Jun-15A															
Zone B																					
Vertical Seawall																					
NRC11400	VS - Mass Concrete Coping - Zone B - (CH598 to 648)	8	01-Sep-14	10-Sep-14	21-Oct-14A	16-Jul-15A															
NRC11410	VS - Mass Concrete Coping - Zone B - (CH648 to 698)	8	11-Sep-14	19-Sep-14	20-Nov-14A	16-Jul-15A															
NRC11420	VS - Mass Concrete Coping - Zone B - (CH698 to 738)	8	20-Sep-14	29-Sep-14	02-Dec-14A	16-Jul-15A															
Reclamation																					
NRC11990	Public Fill - Zone B - (CH598 to 648) to +10mPD	6	29-Aug-15	04-Sep-15	20-Sep-14A	22-Sep-14A															
NRC15310	Surcharge Period - Zone B - (CH598 to 648)	180	05-Sep-15	02-Mar-16	22-Sep-14A	20-Mar-15A															
NRC15320	Surcharge Removal - Zone B - (CH598 to 648)	10	03-Mar-16	14-Mar-16	29-Aug-15	09-Sep-15															
NRC15360	Surcharge Removal - Zone B - (CH698 to 738)	10	25-Mar-15	10-Apr-15	29-Aug-15	09-Sep-15															
Zone A1																					
Reclamation																					
NRC15380	Surcharge Removal - Zone A1 - (CH738 to 793)	10	26-May-15	06-Jun-15	16-Jul-15A	16-Jul-15A															
Zone A2																					
Sloping Seawall																					
NRC12760	SS - Armour Rock - Zone A2 - (CH843 to 893)	4	14-Jun-14	19-Jun-14	16-Apr-15A	29-Aug-15															
NRC12770	SS - Armour Rock - Zone A2 - (CH893 to 956)	4	19-Jun-14	24-Jun-14	16-Apr-15A	31-Aug-15															
Reclamation																					
NRC15390	Surcharge Period - Zone A2 - (CH793 to 843)	180	10-Dec-14	08-Jun-15	11-Nov-14 A	09-May-15A															
NRC15400	Surcharge Removal - Zone A2 - (CH738 to 956)	10	08-Jun-15	19-Jun-15	08-Jun-15A	02-Sep-15															
Zone F																					
CH184 to CH231																					
A6416230	F - Anchor wall Installation - CH184 to CH231	4	10-Feb-14	13-Feb-14	29-Aug-15	02-Sep-15															
A6416290	F - Backfilling up to 0.0mPD & G2 Installation to Anchor Wall- CH184 to CH231	3	14-Feb-14	16-Feb-14	16-Mar-15A	04-Sep-15															
A6416295	F - Backfilling up to +3.0mPD & G1 Installation to Anchor Wall- CH184 to CH231	2	17-Feb-14	18-Feb-14	16-Mar-15A	05-Sep-15															
A6416300	F - Backfilling up to +6.0mPD to Anchor Wall - CH184 to CH231	2	19-Feb-14	20-Feb-14	06-Sep-15	07-Sep-15															
A6416400	F - Backfilling to +6.0mPD to Existing Seawall - CH184 to CH231	1	21-Feb-14	21-Feb-14	08-Sep-15	08-Sep-15															
CH231 to CH278																					
A6416280	F - Backfilling up to +6.0mPD - CH231 to CH278	2	17-Apr-14	18-Apr-14	03-Sep-15	04-Sep-15															
A6416310	F - Anchor wall Installation - CH231 to CH278	4	22-Apr-14	25-Apr-14	05-Sep-15	09-Sep-15															
A6416480	F - Backfilling up to 0.0mPD & G2 Installation to Anchor Wall- CH231 to CH278	3	26-Apr-14	28-Apr-14	03-Mar-15A	10-Sep-15															
A6416490	F - Backfilling up to +3.0mPD & G1 Installation to Anchor Wall - CH231 to CH278	2	29-Apr-14	30-Apr-14	10-Mar-15A	11-Sep-15															
A6416500	F - Backfilling up to +6.0mPD to Anchor Wall - CH231 to CH278	2	01-May-14	02-May-14	12-Sep-15	13-Sep-15															
A6416510	F - Backfilling to +6.0mPD to Existing Seawall - CH231 to CH278	1	03-May-14	03-May-14	14-Sep-15	14-Sep-15															
CH278 to CH327																					
A6416220	F - Backfilling up to +6.0mPD - CH278 to CH327	2	12-Apr-14	13-Apr-14	01-Sep-15	02-Sep-15															
A6416340	F - Anchor wall Installation - CH278 to CH327	4	26-Apr-14	30-Apr-14	10-Sep-15	14-Sep-15															
A6416520	F - Backfilling up to 0.0mPD & G2 Installation to Anchor Wall - CH278 to CH327	3	01-May-14	03-May-14	03-Mar-15A	15-Sep-15															
A6416530	F - Backfilling up to +3.0mPD & G1 Installation to Anchor Wall - CH278 to CH327	3	04-May-14	06-May-14	10-Mar-15A	16-Sep-15															

Activity ID	Activity Name	Orig Dur	Planned Start	Planned Finish	Current Start	Current Finish	2015								2016
							May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan
A6416540	F - Backfilling up to +6.0mPD to Anchor Wall - CH278 to CH327	3	07-May-14	09-May-14	17-Sep-15	19-Sep-15									
A6416550	F - Backfilling to +6.0mPD to Existing Seawall - CH278 to CH327	1	10-May-14	10-May-14	20-Sep-15	20-Sep-15									
CH327 to CH381															
A6416170	F - Backfilling up to +6.0mPD - CH327 to CH381	3	04-Apr-14	06-Apr-14	29-Aug-15	31-Aug-15									
A6416370	F - Anchor wall Installation - CH327 to CH381	3	02-May-14	05-May-14	15-Sep-15	17-Sep-15									
A6416560	F - Backfilling up to 0.0mPD & G2 Installation to Anchor Wall - CH327 to CH381	3	06-May-14	08-May-14	03-Mar-15A	18-Sep-15									
A6416570	F - Backfilling up to +3.0mPD & G1 Installation to Anchor Wall - CH327 to CH381	3	09-May-14	11-May-14	10-Mar-15A	19-Sep-15									
A6416580	F - Backfilling up to +6.0mPD to Anchor Wall - CH327 to CH381	2	12-May-14	13-May-14	20-Sep-15	21-Sep-15									
A6416590	F - Backfilling to +6.0mPD to Existing Seawall - CH327 to CH381	1	14-May-14	14-May-14	22-Sep-15	22-Sep-15									
Box Culvert Extension															
Construction															
Ch000-010 Culvert Outfall															
A1000	Installation of temporary bulk head	26	10-Aug-15	08-Sep-15	28-Nov-15	30-Dec-15									
A1010	Removal of public fill at outfall area	4	09-Sep-15	12-Sep-15	31-Dec-15	05-Jan-16									
A1020	Cut sheet pile wall below water level by diver	18	14-Sep-15	06-Oct-15	06-Jan-16	26-Jan-16									
A1030	Removal of temporary seawall block	3	07-Oct-15	09-Oct-15	27-Jan-16	29-Jan-16									
A1040	Preparation & pour blinding concrete base of box culvert outfall	8	10-Oct-15	19-Oct-15	30-Jan-16	15-Feb-16									
A1050	Install precast culvert element by barge (5 nos.)	21	20-Oct-15	13-Nov-15	16-Feb-16	10-Mar-16									
A1060	Concreting in-situ Top Slab and sticth joint	12	14-Nov-15	27-Nov-15	11-Mar-16	24-Mar-16									
CH000-150 Land Section															
ELS Foundation															
A6416891	Bored Pile Construction - A33 to A54 (3 Rigs) - 22 out of 22 piles	11	11-Nov-14	22-Nov-14	27-Jul-15A	07-Aug-15A									
A6416891 EOT	Inclement Weather - Bored Pile Construction - A33 to A54 (3 Rigs) - 22 out of 22 piles	5	24-Nov-14	28-Nov-14	08-Aug-15A	13-Aug-15A									
A6418180	Ch010-100 - Pump test for Excavation	24	12-Feb-15	18-Mar-15	27-Jul-15A	22-Aug-15A									
A6418190	Ch010-100 - Toe Grouting (if required)	24	19-Mar-15	20-Apr-15	24-Aug-15A	19-Sep-15A									
ELS & Structure															
Pile A43/A41 CJ to Pile A41/A39 CJ															
ELS															
A1610	Installation of strut S1	5	08-May-15	13-May-15	20-Aug-15A	01-Sep-15									
A1620	Excavation to FEL	5	14-May-15	19-May-15	02-Sep-15	07-Sep-15									
Box Culvert Structure															
A1630	Pile cap construction	10	27-May-15	06-Jun-15	14-Sep-15	24-Sep-15									
A1640	Base slab construction including kicker	6	19-Jun-15	26-Jun-15	09-Oct-15	15-Oct-15									
A1641	Removal of strut S1	4	27-Jun-15	02-Jul-15	16-Oct-15	20-Oct-15									
A1642	System formworks delivery & setup	14	03-Jul-15	18-Jul-15	22-Oct-15	06-Nov-15									
A1650	Walls & top slab construction	6	20-Jul-15	25-Jul-15	07-Nov-15	13-Nov-15									
A1660	Removal of strut S2 & Backfilling up to required level	6	03-Aug-15	08-Aug-15	21-Nov-15	27-Nov-15									
Pile A45/A43 CJ to Pile A43/A41 CJ															
ELS															
A1510	Excavation to 0.5m below strut S1	5	08-May-15	13-May-15	07-Aug-15A	18-Aug-15A									
A1520	Installation of strut S1	5	14-May-15	19-May-15	18-Aug-15A	04-Sep-15									
A1530	Excavation to FEL	5	20-May-15	26-May-15	08-Sep-15	12-Sep-15									
Box Culvert Structure															
A1540	Pile cap construction	10	08-Jun-15	18-Jun-15	25-Sep-15	08-Oct-15									
A1550	Base slab construction including kicker	6	27-Jun-15	04-Jul-15	16-Oct-15	23-Oct-15									
A1551	Removal of strut S1	4	06-Jul-15	09-Jul-15	24-Oct-15	28-Oct-15									
A1560	Walls & top slab construction	6	27-Jul-15	01-Aug-15	14-Nov-15	20-Nov-15									
A1570	Removal of strut S2 & Backfilling up to required level	6	10-Aug-15	15-Aug-15	28-Nov-15	04-Dec-15									
Pile A47/A45 CJ to Pile A45/A43 CJ															
ELS															
A1400	Excavation to 0.5m below strut S2	4	30-Apr-15	05-May-15	21-Jul-15A	25-Jul-15A									
A1410	Installation of strut S2	5	06-May-15	11-May-15	22-Jul-15A	28-Jul-15A									
A1420	Excavation to 0.5m below strut S1	5	14-May-15	19-May-15	29-Aug-15	03-Sep-15									
A1430	Installation of strut S1	5	20-May-15	26-May-15	05-Sep-15	10-Sep-15									
A1440	Excavation to FEL	5	27-May-15	01-Jun-15	14-Sep-15	18-Sep-15									
Box Culvert Structure															
A1450	Pile cap construction	10	19-Jun-15	02-Jul-15	09-Oct-15	20-Oct-15									
A1460	Base slab construction including kicker	6	06-Jul-15	11-Jul-15	24-Oct-15	30-Oct-15									
A1461	Removal of strut S1	4	13-Jul-15	16-Jul-15	31-Oct-15	04-Nov-15									
A1470	Walls & top slab construction	6	03-Aug-15	08-Aug-15	21-Nov-15	27-Nov-15									
A1480	Removal of strut S2 & Backfilling up to required level	6	17-Aug-15	22-Aug-15	05-Dec-15	11-Dec-15									
Pile A49/A47 CJ to Pile A47/A45 CJ															
ELS															
A1310	Excavation to 0.5m below strut S2	4	06-May-15	09-May-15	18-Jul-15A	25-Jul-15A									
A1320	Installation of strut S2	5	11-May-15	15-May-15	21-Jul-15A	21-Jul-15A									
A1330	Excavation to 0.5m below strut S1	5	20-May-15	26-May-15	04-Sep-15	09-Sep-15									
A1340	Installation of strut S1	5	27-May-15	01-Jun-15	11-Sep-15	16-Sep-15									
A1350	Excavation to FEL	5	02-Jun-15	06-Jun-15	19-Sep-15	24-Sep-15									
Box Culvert Structure															
A1360	Pile cap construction	10	03-Jul-15	14-Jul-15	22-Oct-15	02-Nov-15									
A1370	Base slab construction including kicker	6	15-Jul-15	21-Jul-15	03-Nov-15	09-Nov-15									

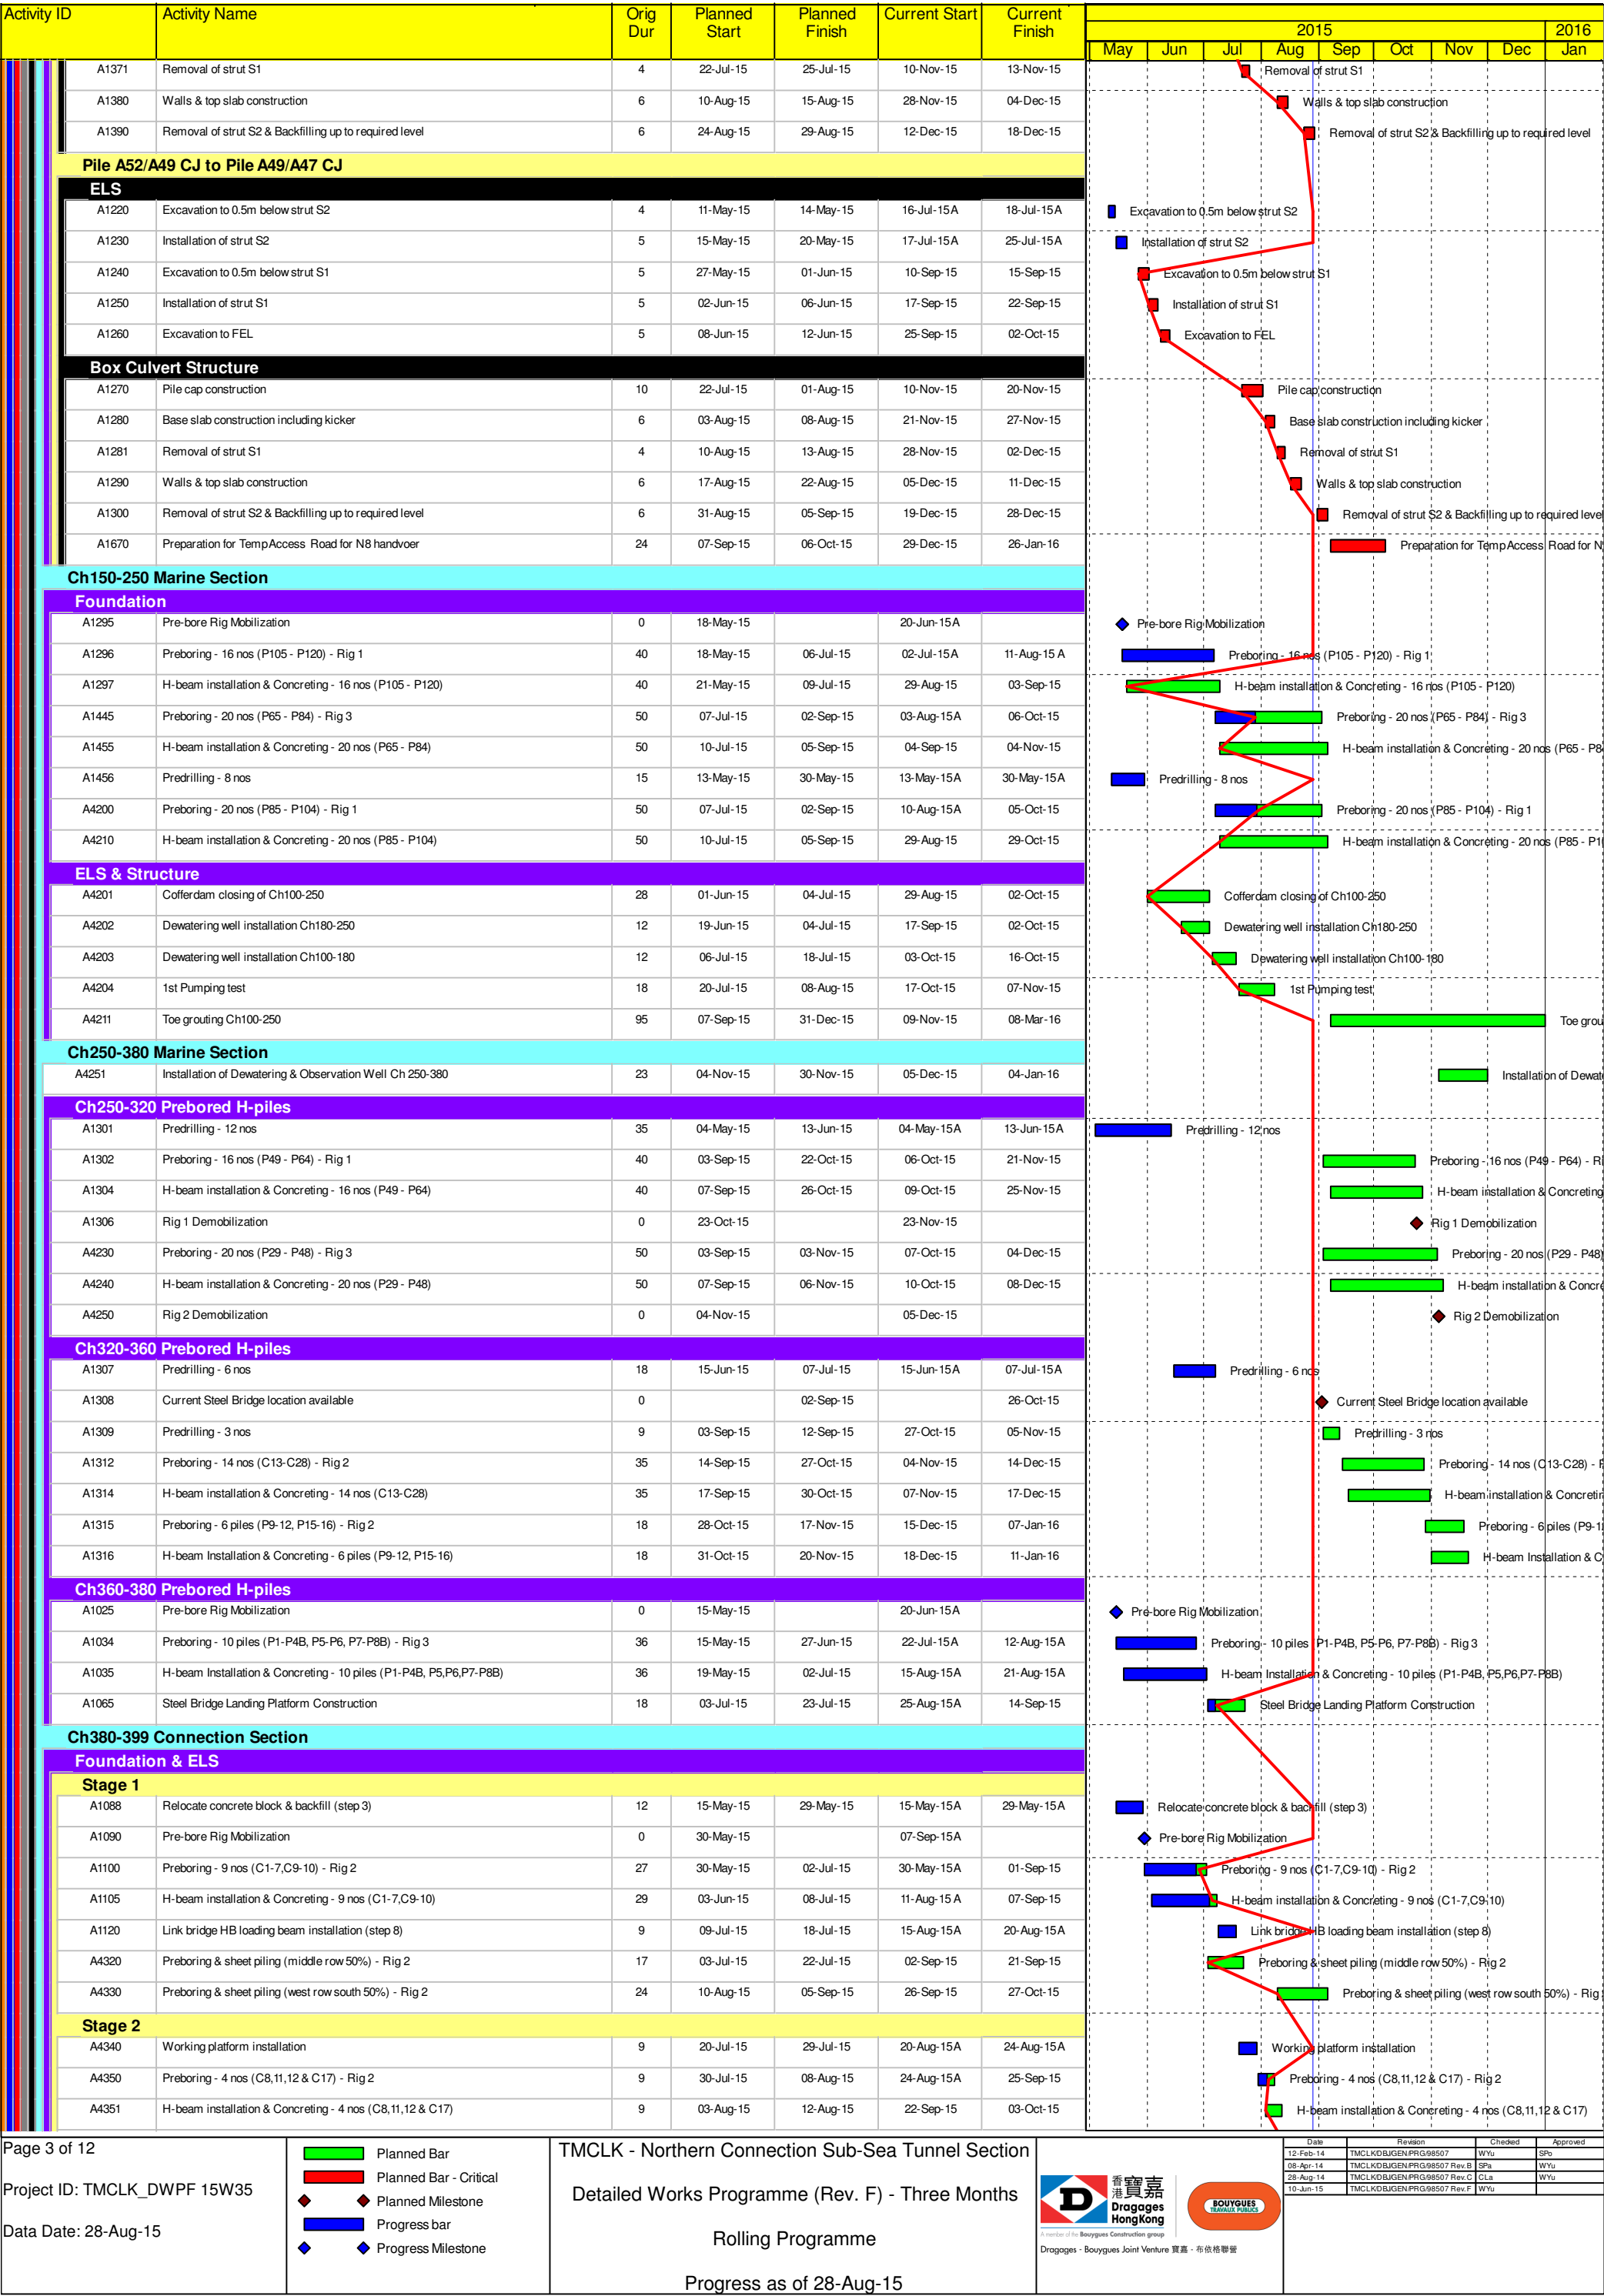

[illegible]

Activity ID	Activity Name	Orig Dur	Planned Start	Planned Finish	Current Start	Current Finish										
							2015									2016
							May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	
TBM10495	SB - North TBM Tunnel - Back-up Gnatry G3 & G4 Assembly	15	10-Jul-15	26-Jul-15	25-Oct-15A	08-Nov-15A										
TBM10500	SB - North TBM Tunnel - CDG with Trimix (Ch7176 to 7126 - 50m)	10	26-Jul-15	05-Aug-15	15-Jun-15A	22-Jul-15A										
TBM10510	SB - North TBM Tunnel - CDG with Trimix (Ch7126 to 7021 - 105m)	17	05-Aug-15	23-Aug-15	23-Jul-15A	16-Aug-15A										
TBM10520	SB - North TBM Tunnel - CDG with Trimix (Ch7021 to 6891 - 130m)	12	23-Aug-15	04-Sep-15	17-Aug-15A	05-Sep-15										
TBM10530	SB - North TBM Tunnel - CDG+Boulder with Saturation (Ch6891 to 6861 - 30m)	9	04-Sep-15	13-Sep-15	06-Sep-15	14-Sep-15										
TBM10540	SB - North TBM Tunnel - Transition with Saturation (Ch6861 to 6729 - 132m)	63	13-Sep-15	15-Nov-15	15-Sep-15	16-Nov-15										
TBM10550	SB - North TBM Tunnel - Transition with Saturation (Ch6729 to 6709 - 20m)	5	15-Nov-15	20-Nov-15	17-Nov-15	21-Nov-15										
TBM11030	SB - North TBM Tunnel - Thrust Frame Removal	12	04-Sep-15	18-Sep-15	07-Sep-15	19-Sep-15										
TBM11040	SB - North TBM Tunnel - Transition with Saturation (Ch6709 to 6661 - 48m)	11	20-Nov-15	01-Dec-15	22-Nov-15	02-Dec-15										
North Approach Tunnel Internal Structure - NB																
ISIG0990	NB - North TBM Tunnel - Invert Backfilling (Ch7205 to 7175 - 30m) Stage 1	8	19-Aug-15	26-Aug-15	26-Sep-15	03-Oct-15										
ISIG1000	NB - North TBM Tunnel - Invert Backfilling (Ch7175 to 6870 - 305m) Stage 1	87	27-Aug-15	21-Nov-15	04-Oct-15	29-Dec-15										
ISIG1015	NB - North TBM Tunnel - Invert Backfilling (Ch6870 to 6688 - 182m) Stage 1	77	22-Nov-15	06-Feb-16	30-Dec-15	18-Mar-16										
ISIG1020	NB - North TBM Tunnel - Preparation for Invert Gallery Installation	14	27-Aug-15	09-Sep-15	04-Oct-15	17-Oct-15										
ISIG1030	NB - North TBM Tunnel - Invert Precast Gallery Installation (Ch7205 to 6870 - 335m)	96	10-Sep-15	14-Dec-15	18-Oct-15	21-Jan-16										
ISIG1045	NB - North TBM Tunnel - Invert Backfilling (Ch7205 to 7175 - 30m) Stage 2	9	01-Oct-15	09-Oct-15	08-Nov-15	16-Nov-15										
ISIG1050	NB - North TBM Tunnel - Invert Backfilling (Ch7175 to 7125 - 50m) Stage 2	15	10-Oct-15	24-Oct-15	17-Nov-15	01-Dec-15										
ISIG1060	NB - North TBM Tunnel - Invert Backfilling (Ch7125 to 7075 - 50m) Stage 2	15	25-Oct-15	08-Nov-15	02-Dec-15	16-Dec-15										
ISIG1070	NB - North TBM Tunnel - Invert Backfilling (Ch7075 to 7025 - 50m) Stage 2	15	09-Nov-15	23-Nov-15	17-Dec-15	31-Dec-15										
ISIG1080	NB - North TBM Tunnel - Invert Backfilling (Ch7025 to 6975 - 50m) Stage 2	14	24-Nov-15	07-Dec-15	01-Jan-16	14-Jan-16										
North Approach Tunnel Internal Structure - SB																
ISIG1115	SB - North TBM Tunnel - Invert Backfilling (Ch7205 to 7175 - 30m)	8	18-Sep-15	26-Sep-15	20-Sep-15	27-Sep-15										
ISIG1120	SB - North TBM Tunnel - Invert Backfilling (Ch7175 to 7125 - 50m)	13	26-Sep-15	09-Oct-15	28-Sep-15	10-Oct-15										
ISIG1130	SB - North TBM Tunnel - Invert Backfilling (Ch7125 to 7075 - 50m)	13	09-Oct-15	22-Oct-15	11-Oct-15	23-Oct-15										
ISIG1140	SB - North TBM Tunnel - Invert Backfilling (Ch7075 to 7025 - 50m)	13	22-Oct-15	04-Nov-15	24-Oct-15	05-Nov-15										
ISIG1150	SB - North TBM Tunnel - Invert Backfilling (Ch7025 to 6975 - 50m)	12	04-Nov-15	16-Nov-15	06-Nov-15	17-Nov-15										
ISIG1160	SB - North TBM Tunnel - Invert Backfilling (Ch6975 to 6925 - 50m)	12	16-Nov-15	28-Nov-15	18-Nov-15	29-Nov-15										
North Approach Cross Passage																
CP55 - Traditional Method																
A6418390	CP55 Platform Available from ML03 North Approach Tunnel Backfilling	0	10-Oct-15		17-Nov-15											
A6418440	CP55 Platform Available from ML02 North Approach Tunnel Backfilling	0	09-Oct-15		12-Oct-15											
CP54 - Traditional Method																
A6418380	CP54 Platform Available from ML03 North Approach Tunnel Backfilling	0	24-Nov-15		02-Jan-16											
A6418450	CP54 Platform Available from ML02 North Approach Tunnel Backfilling	0	04-Nov-15		06-Nov-15											
North Ventilation Building																
Design Submission																
(A10) ACABAS Submissions																
GS01650	ACABAS Approval	28	16-Mar-14	12-Apr-14	27-Aug-15A	23-Sep-15										
(A11) Submissons to Design Advisory Panel of ArchSD																
GS01730	Prepare Re-submission	18	19-May-14	09-Jun-14	22-Jul-14 A	31-Aug-15										
GS01740	ArchSD's comment	30	10-Jun-14	09-Jul-14	01-Sep-15	30-Sep-15										
(I1) DDA for North Vent.Bldgs. GBP & Arch.Submission																
DD01235	Designer to Reply RTC + Update Submission	21	28-Jul-14	20-Aug-14	02-May-15A	30-Sep-15										
DD01240	Submit Updated DDAto SO/ ICE/ IPs	0	21-Aug-14		02-Oct-15											
DD01245	ICE Approval & Issue Check Cert	12	21-Aug-14	03-Sep-14	02-Oct-15	15-Oct-15										
DD01250	Submit ICE Check Cert to SO	6	04-Sep-14	11-Sep-14	16-Oct-15	23-Oct-15										
DD01255	IPs Review	28	21-Aug-14	17-Sep-14	02-Oct-15	29-Oct-15										
DD01260	IP's No Objection Received	0		17-Sep-14		29-Oct-15										
DD01265	SO's Review	35	21-Aug-14	24-Sep-14	02-Oct-15	05-Nov-15										
DD01270	SO Approval with Condition Received	0		24-Sep-14		05-Nov-15										
(I1) DDA for North & South Vent.Bldg. ABWF works																
DD67638	Preparation of DDANorth & SouthABWF	18	25-Sep-14	17-Oct-14	06-Nov-15	26-Nov-15										
DD67648	Review & Comment by JV	24	18-Oct-14	14-Nov-14	27-Nov-15	24-Dec-15										
(I2) DDA for North Vent.Bldgs.Foundation Design																
DD01355	IPs Review	28	03-Dec-14	30-Dec-14	30-Jan-15A	17-Jun-15A										
DD01360	IP's No Objection Received	0		30-Dec-14		17-Jun-15A										
DD01380	SO's Review	35	03-Dec-14	06-Jan-15	30-Jan-15A	17-Jun-15A										
DD01385	SO Approval with Condition Received	0		06-Jan-15		17-Jun-15A										
(I2) DDA for North Vent.Bldgs.Structural Design incl.Vent.Connections																
DD68018	Review & Comment by JV	18	27-Sep-14	20-Oct-14	02-Apr-15A	03-Aug-15A										
DD68020	Designer prepare DDA	10	21-Oct-14	31-Oct-14	04-Aug-15A	10-Aug-15A										
DD68028	Formal Submission of DDAto ICE/ IPs	0		31-Oct-14		10-Aug-15A										
DD68030	Advanced Submission to SO	0		31-Oct-14		10-Aug-15A										
DD68038	IPs/ SO's Advance Comments/ ICE Comments	28	01-Nov-14	28-Nov-14	10-Aug-15A	07-Sep-15										
DD68040	Comments Received	0		28-Nov-14		07-Sep-15										
DD68048	Designer to Reply RTC + Update Submission	21	29-Nov-14	23-Dec-14	08-Sep-15	03-Oct-15										
DD68058	Submit Updated DDAto SO/ ICE/ IPs	0	24-Dec-14		05-Oct-15											
DD68068	ICE Approval & Issue Check Cert	12	24-Dec-14	09-Jan-15	05-Oct-15	17-Oct-15										
DD68078	Submit ICE Check Cert to SO	6	10-Jan-15	16-Jan-15	19-Oct-15	26-Oct-15										

Activity ID	Activity Name	Orig Dur	Planned Start	Planned Finish	Current Start	Current Finish	2015										2016
							May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan		
DD68088	IPs Review	28	24-Dec-14	20-Jan-15	05-Oct-15	01-Nov-15											
DD68098	IP's No Objection Received	0		20-Jan-15		01-Nov-15											
DD68210	SO's Review	35	24-Dec-14	27-Jan-15	05-Oct-15	08-Nov-15											
DD68220	SO Approval with Condition Received	0		27-Jan-15		09-Nov-15											
(I3) DDA for North & South Vent.Bldgs. Service and E&M Provision																	
DD01600	Preparation of DDANth VB Service and E&MS Provision	18	12-Sep-14	04-Oct-14	01-Jul-15A	31-Aug-15											
DD01605	Review & Comment by JV	24	06-Oct-14	01-Nov-14	01-Sep-15	29-Sep-15											
DD01610	Designer prepare DDA	15	03-Nov-14	19-Nov-14	30-Sep-15	17-Oct-15											
DD01615	Formal Submission of DDAto ICE/ IPs	0		19-Nov-14		17-Oct-15											
DD01620	Advanced Submission to SO	0		19-Nov-14		17-Oct-15											
DD01625	IPs/ SO's Advance Comments/ ICE Comments	28	20-Nov-14	17-Dec-14	18-Oct-15	14-Nov-15											
DD01630	Comments Received	0		17-Dec-14		14-Nov-15											
DD01635	Designer to Reply RtC + Update Submission	21	18-Dec-14	14-Jan-15	16-Nov-15	09-Dec-15											
(J1) DDA Temp.works for Construction of Nth.Vent.Bldg.																	
DD04390	Review & Comment by JV	18	13-Oct-14	01-Nov-14	08-May-15A	31-Aug-15											
DD04400	Designer prepare DDA	10	03-Nov-14	13-Nov-14	01-Sep-15	11-Sep-15											
DD04410	Formal Submission of DDAto ICE/ IPs	0		13-Nov-14		11-Sep-15											
DD04420	Advanced Submission to SO	0		13-Nov-14		11-Sep-15											
DD04430	IPs/ SO's Advance Comments/ ICE Comments	28	14-Nov-14	11-Dec-14	12-Sep-15	09-Oct-15											
DD04440	Comments Received	0		11-Dec-14		09-Oct-15											
DD04450	Designer to Reply RtC + Update Submission	21	12-Dec-14	08-Jan-15	10-Oct-15	04-Nov-15											
DD04460	Submit Updated DDAto SO/ ICE/ IPs	0	09-Jan-15		05-Nov-15												
DD04470	ICEApproval & Issue Check Cert	12	09-Jan-15	22-Jan-15	05-Nov-15	18-Nov-15											
DD04480	Submit ICE Check Cert to SO	6	23-Jan-15	29-Jan-15	19-Nov-15	25-Nov-15											
DD04490	IPs Review	28	09-Jan-15	05-Feb-15	05-Nov-15	02-Dec-15											
DD04540	SO's Review	35	09-Jan-15	12-Feb-15	05-Nov-15	09-Dec-15											
(J2) Tower Crane Foundation for Ventilation Building																	
DD70480	Preparation of DDA Tower Crane Foundation for Vent Bldg Construction	18	01-Jun-15	22-Jun-15	01-Jul-15A	06-Jul-15A											
DD70490	Review & Comment by JV	18	23-Jun-15	14-Jul-15	06-Jul-15A	09-Jul-15A											
DD70500	Designer prepare DDA	10	15-Jul-15	25-Jul-15	09-Jul-15A	09-Jul-15A											
DD70510	Formal Submission of DDAto ICE/ IPs	0		25-Jul-15		09-Jul-15A											
DD70520	Advanced Submission to SO	0		25-Jul-15		09-Jul-15A											
DD70530	IPs/ SO's Advance Comments/ ICE Comments	28	26-Jul-15	22-Aug-15	09-Jul-15A	22-Jul-15A											
DD70540	Comments Received	0		22-Aug-15		22-Jul-15A											
DD70550	Designer to Reply RtC + Update Submission	21	24-Aug-15	16-Sep-15	22-Jul-15A	22-Jul-15A											
DD70560	Submit Updated DDAto SO/ ICE/ IPs	0	17-Sep-15		22-Jul-15A												
DD70570	ICEApproval & Issue Check Cert	12	17-Sep-15	02-Oct-15	22-Jul-15A	22-Jul-15A											
DD70580	Submit ICE Check Cert to SO	6	03-Oct-15	09-Oct-15	22-Jul-15A	22-Jul-15A											
DD70590	IPs Review	28	17-Sep-15	14-Oct-15	22-Jul-15A	22-Jul-15A											
DD70600	IP's No Objection Received	0		14-Oct-15		22-Jul-15A											
DD70640	SO's Review	35	17-Sep-15	21-Oct-15	22-Jul-15A	22-Jul-15A											
DD70650	SO Approval with Condition Received	0		22-Oct-15		22-Jul-15A											
(C3) DDA for North Vent Shaft & Duct Permanent Structure																	
DD67278	Review & Comment by JV	18	28-Aug-14	18-Sep-14	08-Apr-15A	31-Aug-15											
DD67280	Designer prepare DDA	10	19-Sep-14	30-Sep-14	01-Sep-15	11-Sep-15											
DD67288	Formal Submission of DDAto ICE/ IPs	0		30-Sep-14		11-Sep-15											
DD67290	Advanced Submission to SO	0		30-Sep-14		11-Sep-15											
DD67298	IPs/ SO's Advance Comments/ ICE Comments	28	01-Oct-14	28-Oct-14	12-Sep-15	09-Oct-15											
DD67300	Comments Received	0		28-Oct-14		09-Oct-15											
DD67308	Designer to Reply RtC + Update Submission	21	29-Oct-14	21-Nov-14	10-Oct-15	04-Nov-15											
DD67318	Submit Updated DDAto SO/ ICE/ IPs	0	22-Nov-14		05-Nov-15												
DD67328	ICEApproval & Issue Check Cert	12	22-Nov-14	05-Dec-14	05-Nov-15	18-Nov-15											
DD67338	Submit ICE Check Cert to SO	6	06-Dec-14	12-Dec-14	19-Nov-15	25-Nov-15											
DD67348	IPs Review	28	22-Nov-14	19-Dec-14	05-Nov-15	02-Dec-15											
DD67368	SO's Review	35	22-Nov-14	26-Dec-14	05-Nov-15	09-Dec-15											
North Surface Roadworks, Utility & Drainage works																	
Design Submission																	
(A20) DDA for Traffic Sign, Road Marking, Street Furnitures, Sign Gantry & etc																	
DD01755	SO's Review	35	11-Dec-14	14-Jan-15	10-Apr-15A	31-Aug-15											
DD01760	SO Approval with Condition Received	0		14-Jan-15		31-Aug-15											
(C2) DDA for Sewerage, Drainage, Waterworks & Utility works for North Landfall																	
DD02135	Designer to Reply RtC + Update Submission	21	15-Oct-14	07-Nov-14	09-Feb-15A	31-Aug-15											
DD02140	Submit Updated DDAto SO/ ICE/ IPs	0	08-Nov-14		01-Sep-15												
DD02145	ICEApproval & Issue Check Cert	12	08-Nov-14	21-Nov-14	01-Sep-15	14-Sep-15											
DD02150	Submit ICE Check Cert to SO	6	22-Nov-14	28-Nov-14	15-Sep-15	21-Sep-15											
DD02155	IPs Review	28	08-Nov-14	05-Dec-14	01-Sep-15	28-Sep-15											
DD02160	IP's No Objection Received	0		05-Dec-14		28-Sep-15											
DD02165	SO's Review	35	08-Nov-14	12-Dec-14	01-Sep-15	05-Oct-15											

Activity ID	Activity Name	Orig Dur	Planned Start	Planned Finish	Current Start	Current Finish	2015								2016
							May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan
DD02170	SO Approval with Condition Received	0		12-Dec-14		05-Oct-15									
Sub-sea Tunnel															
Sub-sea TBM Tunnelling															
Major Procurement															
S881 -															
PO103360	S881 - 13.6m dia - TBM - Manufacturing - Cutterhead	257	18-Jul-14	03-Jun-15	18-Jul-14 A	12-Sep-15									
PO103430	S881 - 13.6m dia - TBM - Workshop Assembly	70	02-Feb-15	06-May-15	10-Mar-15 A	03-Sep-15									
PO103440	S881 - 13.6m dia - TBM - Workshop Acceptance Test	0		06-May-15		03-Sep-15									
PO103450	S881 - 13.6m dia - TBM - Disassembly and Packing for Transport	16	07-May-15	26-May-15	10-Jul-15 A	12-Sep-15									
PO103460	S881 - 13.6m dia - TBM - Delivery	20	27-May-15	15-Jun-15	13-Sep-15	02-Oct-15									
PO103470	S881 - 13.6m dia - TBM - Arrival to site	0		15-Jun-15		02-Oct-15									
Design Submission															
(B6) Risk Assessment of Submarine Cable - Tunnelling Works															
GS01460	CLP Review (4 weeks)	28	17-Mar-15	13-Apr-15	08-May-15 A	30-Aug-15									
GS01465	CLP Comment Received	0		13-Apr-15		31-Aug-15									
GS01467	SO's Condition Approval	35	12-Mar-15	15-Apr-15	08-May-15 A	01-Sep-15									
(G1) IFA for Structural Health Monitoring System for TBM Tunnel															
DD71050	IPs Review	28	31-May-14	27-Jun-14	23-Dec-14 A	22-Jun-15 A									
DD71060	IPs No Objection Received	0		27-Jun-14		22-Jun-15 A									
DD71070	SO's Review	35	31-May-14	04-Jul-14	23-Dec-14 A	22-Jun-15 A									
DD71080	SO Approval with Condition Received	0		04-Jul-14		22-Jun-15 A									
DD71200	TBM Segment Mould Acceptance & Trial	0	11-Jul-14		22-Jun-15 A										
(G1) DDA for TBM Tunnel Lining Structural Design - Sub-sea tunnel															
DD6670	Sub-sea TBM Tunnel Segment - Fabrication	265	06-Oct-14	29-Aug-15	29-Nov-14 A	23-Apr-16									
(G1) DDA for TBM Tunnel Lining Settlement Anlysis & Confinement Pressure - Sub-sea tunnel															
DD6720	IPs/ SO's Advance Comments/ ICE Comments	28	25-Oct-14	21-Nov-14	10-May-15 A	23-Jul-15 A									
DD67258	Comments Received	0		21-Nov-14		23-Jul-15 A									
DD6730	Designer to Reply RtC + Update Submission	21	22-Nov-14	16-Dec-14	23-Jul-15 A	28-Jul-15 A									
DD6740	Submit Updated DDA to SO/ ICE/ IPs	0	17-Dec-14		28-Jul-15 A										
DD6750	ICE Approval & Issue Check Cert	12	17-Dec-14	02-Jan-15	28-Jul-15 A	28-Jul-15 A									
DD6760	Submit ICE Check Cert to SO	6	03-Jan-15	09-Jan-15	28-Jul-15 A	28-Jul-15 A									
DD6770	IPs Review	28	17-Dec-14	13-Jan-15	28-Jul-15 A	30-Aug-15									
DD6780	IPs No Objection Received	0		13-Jan-15		30-Aug-15									
DD6830	SO's Review	35	17-Dec-14	20-Jan-15	28-Jul-15 A	05-Sep-15									
DD6840	SO Approval with Condition Received	0		20-Jan-15		05-Sep-15									
(G3) DDA for TBM Tunnel Internal Structures (Sub-sea)															
DD00955	IPs Review	28	17-Nov-14	14-Dec-14	05-May-15 A	26-Jun-15 A									
DD00960	IPs No Objection Received	0		14-Dec-14		26-Jun-15 A									
DD00980	SO's Review	35	17-Nov-14	21-Dec-14	05-May-15 A	26-Jun-15 A									
DD00985	SO Approval with Condition Received	0		22-Dec-14		26-Jun-15 A									
Sub-sea Tunnel Cross Passage & Internal Structure															
Design Submission															
(G4) DDA for Cross Passage - Permanent works - incl. Geotechnical Assessment - Sub-sea tunnel															
AN1180	Early DDASub-sea Cross Passage Lining & CPOpening	151	03-Jun-14	29-Nov-14	03-Jun-14 A	13-Jul-15 A									
DD01100	Preparation of DDACross Passage incl. Detailed Geotechnical Assessment	0	01-Dec-14	01-Dec-14	13-Jul-15 A	13-Jul-15 A									
DD01105	Review & Comment by JV	6	01-Dec-14	06-Dec-14	13-Jul-15 A	29-Aug-15									
DD01110	Designer prepare DDA	12	08-Dec-14	20-Dec-14	31-Aug-15	12-Sep-15									
DD01115	Formal Submission of DDA to ICE/ IPs	0		20-Dec-14		12-Sep-15									
DD01120	Advanced Submission to SO	0		20-Dec-14		12-Sep-15									
DD01125	IPs/ SO's Advance Comments/ ICE Comments	28	21-Dec-14	17-Jan-15	13-Sep-15	10-Oct-15									
DD01130	Comments Received	0		17-Jan-15		10-Oct-15									
DD01135	Designer to Reply RtC + Update Submission	21	19-Jan-15	11-Feb-15	12-Oct-15	05-Nov-15									
DD01140	Submit Updated DDA to SO/ ICE/ IPs	0	12-Feb-15		06-Nov-15										
DD01145	ICE Approval & Issue Check Cert	12	12-Feb-15	04-Mar-15	06-Nov-15	19-Nov-15									
DD01150	Submit ICE Check Cert to SO	6	05-Mar-15	11-Mar-15	20-Nov-15	26-Nov-15									
DD01155	IPs Review	28	12-Feb-15	11-Mar-15	06-Nov-15	03-Dec-15									
DD01180	SO's Review	35	12-Feb-15	18-Mar-15	06-Nov-15	10-Dec-15									
ETWB TCW No 15/2005 - Cross Passage Ground Treatment for Sub-sea TBM Tunnel															
GEO1270	1st Submission to GEO - ETWB TCW No 15/2005 - Cross Passage Ground Treatment for Sub-sea TBM Tunnel	0		13-Jul-15		28-Aug-15									
GEO1275	1st Submission GEO Review	28	14-Jul-15	10-Aug-15	29-Aug-15	25-Sep-15									
GEO1280	Received GEO Comment	0		10-Aug-15		25-Sep-15									
GEO1285	Prepare Response to Comment	12	11-Aug-15	24-Aug-15	26-Sep-15	12-Oct-15									
GEO1290	2nd Submission to GEO	0		24-Aug-15		12-Oct-15									
GEO1295	2nd GEO Review	28	25-Aug-15	21-Sep-15	13-Oct-15	09-Nov-15									
GEO1490	Received 2nd GEO Comment	0		21-Sep-15		09-Nov-15									
GEO1495	Prepare Respond to 2nd Comment	12	22-Sep-15	07-Oct-15	10-Nov-15	23-Nov-15									
GEO1500	3rd Submission to GEO	0		07-Oct-15		23-Nov-15									
GEO1505	3rd GEO Review	28	08-Oct-15	04-Nov-15	24-Nov-15	21-Dec-15									
Method Statement Submission															
Method Statement of Cross Passage Formwork															

Planned Bar

Planned Bar - Critical

Planned Milestone

Progress bar

Progress Milestone

香港寶嘉

Dragages HongKong

A member of the Bouygues Construction group

BOUYGUES

TRAVAUX PUBLICS

Bouygues Construction group

Date

Revision

Cheded

Approved

12-Feb-14

TMCLKDBUGENPRG98507

WYu

SPa

08-Apr-14

TMCLKDBUGENPRG98507 Rev.B

SPa

WYu

28-Aug-14

TMCLKDBUGENPRG98507 Rev.C

CLa

WYu

10-Jun-15

TMCLKDBUGENPRG98507 Rev.F

WYu

Activity ID	Activity Name	Orig Dur	Planned Start	Planned Finish	Current Start	Current Finish	2015										2016
							May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan		
MS2630	Re-submission	18	20-May-15	10-Jun-15	15-Feb-16	05-Mar-16											
MS2640	SO's Review	28	11-Jun-15	08-Jul-15	06-Mar-16	02-Apr-16											
MS2650	SO's Approval	0		08-Jul-15		02-Apr-16											
Southern Landfall																	
South Cut & Cover Tunnel																	
Design Submission																	
(E2) DDA for South C&C Box & Approach Ramp																	
DD00460	Preparation DDA Sth C&C Box and Approach Ramp	18	18-Nov-14	08-Dec-14	02-Jul-15A	31-Jul-15A											
DD00470	Review & Comment by JV	18	09-Dec-14	31-Dec-14	31-Jul-15A	31-Aug-15											
DD00480	Designer prepare DDA	10	02-Jan-15	13-Jan-15	01-Sep-15	11-Sep-15											
DD00490	Formal Submission of DDA to ICE/ IPs	0		13-Jan-15		11-Sep-15											
DD00500	Advanced Submission to SO	0		13-Jan-15		11-Sep-15											
DD00510	IPs/ SO's Advance Comments/ ICE Comments	28	14-Jan-15	10-Feb-15	12-Sep-15	09-Oct-15											
DD00520	Comments Received	0		10-Feb-15		09-Oct-15											
DD00530	Designer to Reply RtC + Update Submission	21	11-Feb-15	13-Mar-15	10-Oct-15	04-Nov-15											
DD00540	Submit Updated DDA to SO/ ICE/ IPs	0	14-Mar-15		05-Nov-15												
DD00550	ICE Approval & Issue Check Cert	18	14-Mar-15	08-Apr-15	05-Nov-15	25-Nov-15											
DD00560	Submit ICE Check Cert to SO	6	09-Apr-15	15-Apr-15	26-Nov-15	02-Dec-15											
DD00570	IPs Review	28	14-Mar-15	10-Apr-15	05-Nov-15	02-Dec-15											
DD00620	SO's Review	35	14-Mar-15	17-Apr-15	05-Nov-15	09-Dec-15											
ETWB TCW No. 15/2005 - Geotechnical Risk Assessment C&C Tunnels at Southern Landfall																	
GEO1300	1st Submission to GEO - ETWB TCW No. 15/2005 - Geotechnical Risk Assessment C&C Tunnels at Southern Landfall	0		11-Jun-15		05-Dec-15											
GEO1305	1st Submission GEO Review	28	12-Jun-15	09-Jul-15	06-Dec-15	02-Jan-16											
GEO1310	Received GEO Comment	0		09-Jul-15		02-Jan-16											
GEO1315	Prepare Response to Comment	12	10-Jul-15	23-Jul-15	04-Jan-16	16-Jan-16											
GEO1320	2nd Submission to GEO	0		23-Jul-15		16-Jan-16											
GEO1325	2nd GEO Review	28	24-Jul-15	20-Aug-15	17-Jan-16	13-Feb-16											
(F3) AIP Temp.Support for South.C&C, Portal & ELS																	
DD69660	Designer to Reply RtC + Update Submission	21	13-Dec-14	09-Jan-15	10-May-15A	04-Jun-15A											
DD69670	Submit Updated AIP to SO/ ICE/ IPs	0	10-Jan-15		04-Jun-15A												
DD69680	ICE Approval & Issue Check Cert	12	10-Jan-15	23-Jan-15	04-Jun-15A	04-Jun-15A											
DD69690	IPs Review	28	10-Jan-15	06-Feb-15	04-Jun-15A	30-Aug-15											
DD69700	IPs No Objection Received	0		06-Feb-15		30-Aug-15											
DD69710	SO's Review	35	10-Jan-15	13-Feb-15	04-Jun-15A	01-Sep-15											
DD69720	SO Approval with Condition Received	0		13-Feb-15		01-Sep-15											
(F3) DDA Temp.Support for South.C&C, Portal & ELS																	
DD04000	Preparation of DDA South C&C ELS	18	01-Apr-15	25-Apr-15	02-Sep-15	22-Sep-15											
DD04010	Review & Comment by JV	18	27-Apr-15	18-May-15	23-Sep-15	15-Oct-15											
DD04020	Designer prepare DDA	10	19-May-15	30-May-15	16-Oct-15	28-Oct-15											
DD04030	Formal Submission of DDA to ICE/ IPs	0		30-May-15		28-Oct-15											
DD04040	Advanced Submission to SO	0		30-May-15		28-Oct-15											
DD04050	IPs/ SO's Advance Comments/ ICE Comments	28	31-May-15	27-Jun-15	29-Oct-15	25-Nov-15											
DD04060	Comments Received	0		27-Jun-15		25-Nov-15											
DD04070	Designer to Reply RtC + Update Submission	21	29-Jun-15	23-Jul-15	26-Nov-15	19-Dec-15											
DD04080	Submit Updated DDA to SO/ ICE/ IPs	0	24-Jul-15		21-Dec-15												
DD04090	ICE Approval & Issue Check Cert	12	24-Jul-15	06-Aug-15	21-Dec-15	06-Jan-16											
DD04100	Submit ICE Check Cert to SO	6	07-Aug-15	13-Aug-15	07-Jan-16	13-Jan-16											
DD04110	IPs Review	28	24-Jul-15	20-Aug-15	21-Dec-15	17-Jan-16											
DD04120	IPs No Objection Received	0		20-Aug-15		17-Jan-16											
DD04160	SO's Review	35	24-Jul-15	27-Aug-15	21-Dec-15	24-Jan-16											
DD04170	SO Approval with Condition Received	0		27-Aug-15		25-Jan-16											
ETWB TCW No 15/2005 - ELS Design for C&C Tunnel at Southern Landfall																	
GEO1390	1st Submission to GEO - ETWB TCW No 15/2005 - ELS Design for C&C Tunnel at Southern Landfall	0		06-Aug-15		06-Jan-16											
GEO1395	1st Submission GEO Review	28	07-Aug-15	03-Sep-15	07-Jan-16	03-Feb-16											
GEO1400	Received GEO Comment	0		03-Sep-15		03-Feb-16											
GEO1405	Prepare Response to Comment	12	04-Sep-15	17-Sep-15	04-Feb-16	24-Feb-16											
GEO1410	2nd Submission to GEO	0		17-Sep-15		24-Feb-16											
GEO1415	2nd GEO Review	28	18-Sep-15	15-Oct-15	25-Feb-16	23-Mar-16											
Method Statement Submission																	
Method Statement of Construction Methodology of C&C Tunnels																	
MS1700	Preparation Method Statement for C&C Tunnels	25	28-Mar-15	30-Apr-15	29-Aug-15	26-Sep-15											
MS1710	Submit Method Statement to SO	0		30-Apr-15		26-Sep-15											
MS1720	SO Reviews & Comments	28	01-May-15	28-May-15	27-Sep-15	24-Oct-15											
MS1730	Re-submission	18	29-May-15	18-Jun-15	26-Oct-15	14-Nov-15											
MS1740	SO's Review	28	19-Jun-15	16-Jul-15	15-Nov-15	12-Dec-15											
MS1750	SO's Approval	0		16-Jul-15		12-Dec-15											
Construction																	
DDP11520	South C&C Tunnel - Diaphragm Wall	120	03-Oct-15	02-Mar-16	07-Mar-16	02-Aug-16											
South Retrieval Shaft																	

Activity ID		Activity Name	Orig Dur	Planned Start	Planned Finish	Current Start	Current Finish	2015								2016
								May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan
Design Submission																
(B5) AIP Construction Risk Assessment - Impact on South Landfall																
GS01215	Prepare Re-submission	10	15-Jan-15	26-Jan-15	11-May-15 A	03-Jun-15A										
GS01220	2nd Submission	0		26-Jan-15		03-Jun-15A										
GS01225	ICE Cert. Issue	6	27-Jan-15	02-Feb-15	03-Jun-15A	10-Jun-15A										
GS01250	SO's ConditionApproval	35	27-Jan-15	02-Mar-15	03-Jun-15A	30-Aug-15										
(B5) DDA Construction Risk Assessment - Impact on South Landfall																
DD68500	Preparation of Construction Risk Assessment - Impact onSouth Landfall	36	03-Mar-15	17-Apr-15	31-Aug-15	13-Oct-15										
DD68510	1st Submission	0		17-Apr-15		13-Oct-15										
DD68520	SO's Comments for 1st Submission	35	18-Apr-15	22-May-15	14-Oct-15	17-Nov-15										
DD68530	Prepare Re-submission	10	23-May-15	04-Jun-15	18-Nov-15	28-Nov-15										
DD68540	2nd Submission	0		04-Jun-15		28-Nov-15										
DD68550	ICE Cert. Issue	6	05-Jun-15	11-Jun-15	30-Nov-15	05-Dec-15										
DD68600	SO's ConditionApproval	35	05-Jun-15	09-Jul-15	29-Nov-15	02-Jan-16										
(F1) AIP Temp.works - Retrieval Shaft on Southern Landfall inc. break-out																
AP01635	Designer to Prepare RitC & Updated AIP	18	25-Nov-14	15-Dec-14	28-Apr-15A	31-Aug-15										
AP01640	Submission ofAIP to SO/ ICE together with Reply To Comment (RTC)	0		15-Dec-14		31-Aug-15										
AP01645	Reply to IPs Comments in RTC	0		15-Dec-14		31-Aug-15										
AP01650	ICEApproval & Issue of Design Check Cert.	18	16-Dec-14	08-Jan-15	01-Sep-15	21-Sep-15										
AP01655	Check Cert to SO	0		08-Jan-15		21-Sep-15										
AP01660	No Objection or Further Minor Comments from IPs Received	0		08-Jan-15		21-Sep-15										
AP01680	SO Review (35 Days)	35	17-Dec-14	20-Jan-15	03-Sep-15	05-Oct-15										
AP01685	SOApproval with Condition Received	0		20-Jan-15		05-Oct-15										
(F1) DDA Temp.works - Retrieval Shaft on Southern Landfall inc. break-out																
DD03510	Preparation of DDA Temp Support for Sth Retrieval Shaft	18	01-Apr-15	25-Apr-15	06-Oct-15	27-Oct-15										
DD03520	Review & Comment by JV	18	27-Apr-15	18-May-15	28-Oct-15	17-Nov-15										
DD03530	Designer prepare DDA	6	19-May-15	26-May-15	18-Nov-15	24-Nov-15										
DD03540	Formal Submission of DDAto ICE/ IPs	0		26-May-15		24-Nov-15										
DD03550	Advanced Submission to SO	0		26-May-15		24-Nov-15										
DD03560	IPs/ SO's Advance Comments/ ICE Comments	28	27-May-15	23-Jun-15	25-Nov-15	22-Dec-15										
DD03570	Comments Received	0		23-Jun-15		22-Dec-15										
DD03580	Designer to Reply RitC + Update Submission	21	24-Jun-15	18-Jul-15	23-Dec-15	19-Jan-16										
DD03590	Submit Updated DDAto SO/ ICE/ IPs	0	20-Jul-15		20-Jan-16											
DD03600	ICEApproval & Issue Check Cert	12	20-Jul-15	01-Aug-15	20-Jan-16	02-Feb-16										
DD03610	Submit ICE Check Cert to SO	6	03-Aug-15	08-Aug-15	03-Feb-16	16-Feb-16										
DD03620	IPs Review	28	20-Jul-15	16-Aug-15	20-Jan-16	16-Feb-16										
DD03630	IP's No Objection Received	0		16-Aug-15		16-Feb-16										
DD03670	SO's Review	35	20-Jul-15	23-Aug-15	20-Jan-16	23-Feb-16										
DD03680	SOApproval with Condition Received	0		24-Aug-15		23-Feb-16										
ETWB TCW No 15/2005 - ELS Design for TBM Retrieval Shaft at Southern Landfall																
GEO1330	1st Submission to GEO - ETWB TCW No 15/2005 - ELS Design for TBM Retrieval Shaft at Southern Landfall	0		24-Aug-15		23-Feb-16										
GEO1335	1st Submission GEO Review	28	24-Aug-15	20-Sep-15	24-Feb-16	22-Mar-16										
GEO1340	Received GEO Comment	0		21-Sep-15		22-Mar-16										
GEO1345	Prepare Response to Comment	12	21-Sep-15	06-Oct-15	23-Mar-16	09-Apr-16										
GEO1350	2nd Submission to GEO	0		06-Oct-15		09-Apr-16										
GEO1355	2nd GEO Review	28	07-Oct-15	03-Nov-15	10-Apr-16	07-May-16										
(F2) AIP Temp works of Ground Treatment for TBMs passing under Southern Landfall																
AP01905	Review & Comment by JV	18	23-Sep-14	15-Oct-14	29-Aug-15	18-Sep-15										
AP01910	Designer PrepareAIP	12	16-Oct-14	29-Oct-14	19-Sep-15	05-Oct-15										
AP01915	Formal Submission of AIP to ICE/IPs	0		29-Oct-14		05-Oct-15										
AP01920	Advanced Submission of AIP to SO	0		29-Oct-14		05-Oct-15										
AP01925	Review & Comment by SO/ ICE/ IPs	28	30-Oct-14	26-Nov-14	06-Oct-15	02-Nov-15										
AP01930	Advance Commants from SO/ Comments from ICE/ IPs Received	0		26-Nov-14		02-Nov-15										
AP01935	Designer to Prepare RitC & Updated AIP	18	27-Nov-14	17-Dec-14	03-Nov-15	23-Nov-15										
AP01940	Submission ofAIP to SO/ ICE together with Reply To Comment (RTC)	0		17-Dec-14		23-Nov-15										
AP01945	Reply to IPs Comments in RTC	0		17-Dec-14		23-Nov-15										
AP01950	ICEApproval & Issue of Design Check Cert.	18	18-Dec-14	10-Jan-15	24-Nov-15	14-Dec-15										
AP01980	SO Review (35 Days)	35	19-Dec-14	22-Jan-15	24-Nov-15	28-Dec-15										
(F2) DDA Temp works of Ground Treatment for TBMs passing under Southern Landfall																
DD04750	Review & Comment by JV	18	27-Apr-15	18-May-15	15-Apr-15A	30-Dec-15										
DD04790	IPs/ SO's Advance Comments/ ICE Comments	28	27-May-15	23-Jun-15	08-Jan-16	04-Feb-16										
DD04800	Comments Received	0		23-Jun-15		04-Feb-16										
DD04810	Designer to Reply RitC + Update Submission	21	24-Jun-15	18-Jul-15	05-Feb-16	07-Mar-16										
DD04820	Submit Updated DDAto SO/ ICE/ IPs	0	20-Jul-15		08-Mar-16											
DD04830	ICEApproval & Issue Check Cert	12	20-Jul-15	01-Aug-15	08-Mar-16	21-Mar-16										
DD04840	Submit ICE Check Cert to SO	6	03-Aug-15	08-Aug-15	22-Mar-16	31-Mar-16										
DD04850	IPs Review	28	20-Jul-15	16-Aug-15	08-Mar-16	04-Apr-16										
DD04860	IP's No Objection Received	0		16-Aug-15		04-Apr-16										

Page 11 of 12

Project ID: TMCLK_DWPF 15W35

Data Date: 28-Aug-15

Planned Bar

Planned Bar - Critical

Planned Milestone

Progress bar

Progress Milestone

TMCLK - Northern Connection Sub-Sea Tunnel Section

Detailed Works Programme (Rev. F) - Three Months

Rolling Programme

Progress as of 28-Aug-15

香港寶嘉

Dragages HongKong

A member of the Bouygues Construction group

Dragages - Bouygues Joint Venture 寶嘉 - 布依格聯營

Bouygues Business Partner

Date	Revision	Checked	Approved
12-Feb-14	TMCLKDBJUGENPRG/98507	WYu	SPa
08-Apr-14	TMCLKDBJUGENPRG/98507 Rev.B	SPa	WYu
28-Aug-14	TMCLKDBJUGENPRG/98507 Rev.C	CLa	WYu
10-Jun-15	TMCLKDBJUGENPRG/98507 Rev.F	WYu	

Activity ID	Activity Name	Orig Dur	Planned Start	Planned Finish	Current Start	Current Finish	2015										2016
							May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan		
DD67888	IPs Review	28	22-May-15	18-Jun-15	05-Mar-16	01-Apr-16	IPs Review										
DD67898	IP's No Objection Received	0		18-Jun-15		01-Apr-16	IP's No Objection Received										
DD67940	SO's Review	35	22-May-15	25-Jun-15	05-Mar-16	08-Apr-16	SO's Review										
DD67950	SO Approval with Condition Received	0		25-Jun-15		08-Apr-16	SO Approval with Condition Received										
(J1) DDA Temp.works for Construction of Sth.Vent.Bldg.																	
DD04560	Preparation of DDASouth VB ELS	18	01-Jun-15	22-Jun-15	10-Dec-15	02-Jan-16	Preparation of DDASouth VB ELS										
DD04570	Review & Comment by JV	18	23-Jun-15	14-Jul-15	04-Jan-16	23-Jan-16	Review & Comment by JV										
DD04580	Designer prepare DDA	10	15-Jul-15	25-Jul-15	25-Jan-16	04-Feb-16	Designer prepare DDA										
DD04590	Formal Submission of DDAto ICE/ IPs	0		25-Jul-15		04-Feb-16	Formal Submission of DDAto ICE/ IPs										
DD04600	Advanced Submission to SO	0		25-Jul-15		04-Feb-16	Advanced Submission to SO										
DD04610	IPs/ SO's Advance Comments/ ICE Comments	28	26-Jul-15	22-Aug-15	05-Feb-16	03-Mar-16	IPs/ SO's Advance Comments/ ICE Comments										
DD04620	Comments Received	0		22-Aug-15		03-Mar-16	Comments Received										
DD04630	Designer to Reply RtC + Update Submission	21	24-Aug-15	16-Sep-15	04-Mar-16	31-Mar-16	Designer to Reply RtC + Update Submission										
DD04640	Submit Updated DDAto SO/ ICE/ IPs	0	17-Sep-15		01-Apr-16		Submit Updated DDAto SO/ ICE/ IPs										
DD04650	ICEApproval & Issue Check Cert	12	17-Sep-15	02-Oct-15	01-Apr-16	15-Apr-16	ICEApproval & Issue Check Cert										
DD04660	Submit ICE Check Cert to SO	6	03-Oct-15	09-Oct-15	16-Apr-16	22-Apr-16	Submit ICE Check Cert to SO										
DD04670	IPs Review	28	17-Sep-15	14-Oct-15	01-Apr-16	28-Apr-16	IPs Review										
DD04680	IP's No Objection Received	0		14-Oct-15		28-Apr-16	IP's No Objection Received										
DD04720	SO's Review	35	17-Sep-15	21-Oct-15	01-Apr-16	05-May-16	SO's Review										
DD04730	SO Approval with Condition Received	0		22-Oct-15		05-May-16	SO Approval with Condition Received										
Construction																	
DDP11930	Mobilization & Setting Up Piling Rigs	64	06-Aug-15	22-Oct-15	29-Aug-15	14-Nov-15	Mobilization & Setting Up Piling Rigs										
DDP11940	S - Piling (Socket H-piles)	132	23-Oct-15	08-Apr-16	06-May-16	13-Oct-16	S - Piling (Socket H-piles)										
DDP11960	S - Sheet Piling	48	23-Oct-15	17-Dec-15	16-Nov-15	13-Jan-16	S - Sheet Piling										
South Surface Roadworks, Utility & Drainage works																	
Design Submission																	
(E1) AIP - Southern Landfall Seawall Modification																	
AP00900	Designer Prepare AIP - Southern Landfall Seawall Modification	36	08-Nov-16	19-Dec-16	08-Jun-15A	08-Jul-15A											
AP00905	Review & Comment by JV	12	20-Dec-16	05-Jan-17	08-Jul-15A	13-Jul-15A											
AP00910	Designer prepare AIP	6	06-Jan-17	12-Jan-17	13-Jul-15A	16-Jul-15A											
AP00915	Formal Submission of AIP to ICE/IPs	0		12-Jan-17		16-Jul-15A											
AP00920	Advanced Submission of AIP to SO	0		12-Jan-17		16-Jul-15A											
AP00925	Review & Comment by SO/ ICE/ IPs	28	13-Jan-17	09-Feb-17	16-Jul-15A	30-Aug-15											
AP00930	Advance Commants from SO/ Comments from ICE/ IPs Received	0		09-Feb-17		31-Aug-15											
AP00935	Designer to Prepare RtC & Updated AIP	18	10-Feb-17	02-Mar-17	31-Aug-15	19-Sep-15											
AP00940	Submisson of AIP to SO/ ICE together with Reply To Comment (RTC)	0		02-Mar-17		19-Sep-15											
AP00945	Reply to IPs Comments in RTC	0		02-Mar-17		19-Sep-15											
AP00950	ICEApproval & Issue of Design Check Cert.	18	03-Mar-17	23-Mar-17	21-Sep-15	13-Oct-15											
AP00955	Check Cert to SO	0		23-Mar-17		13-Oct-15											
AP00960	No Objection or Further Minor Comments from IPs Received	0		23-Mar-17		13-Oct-15											
AP00980	SO Review (35 Days)	35	03-Mar-17	06-Apr-17	22-Sep-15	26-Oct-15											
AP00985	SO Approval with Condition Received	0		06-Apr-17		26-Oct-15											
(E1) DDA - Southern Landfall Seawall Modification																	
DD01900	Preparation of DDAModification of Seawall at Sth Landfall	18	07-Apr-17	02-May-17	27-Oct-15	16-Nov-15											
DD01905	Review & Comment by JV	18	04-May-17	24-May-17	17-Nov-15	07-Dec-15											
(E3) DDA for Sewerage, Drainage, Waterworks & Utility works for South Landfall																	
DD05860	IPs/ SO's Advance Comments/ ICE Comments	28	04-Jan-15	31-Jan-15	27-Mar-15A	02-Sep-15	ICE Comments										
DD05870	Comments Received	0		31-Jan-15		02-Sep-15	Comments Received										
DD05880	Designer to Reply RtC + Update Submission	21	02-Feb-15	04-Mar-15	03-Sep-15	26-Sep-15	RtC + Update Submission										
DD05890	Submit Updated DDAto SO/ ICE/ IPs	0	05-Mar-15		29-Sep-15		DDAto SO/ ICE/ IPs										
DD05900	ICEApproval & Issue Check Cert	12	05-Mar-15	18-Mar-15	29-Sep-15	13-Oct-15	ICE Approval & Issue Check Cert										
DD05910	Submit ICE Check Cert to SO	6	19-Mar-15	25-Mar-15	14-Oct-15	20-Oct-15	ICE Check Cert to SO										
DD05920	IPs Review	28	05-Mar-15	01-Apr-15	29-Sep-15	26-Oct-15	Review										
DD05930	IP's No Objection Received	0		01-Apr-15		26-Oct-15	Objection Received										
DD05940	SO's Review	35	05-Mar-15	08-Apr-15	29-Sep-15	02-Nov-15	Review										
DD05950	SO Approval with Condition Received	0		08-Apr-15		02-Nov-15	approval with Condition Received										
Method Statement Submission																	
Method Statement of Ground Treatment for TBMs Passing under Southern Landfall Seawall																	
MS2700	Preparation Method Statement for Ground Improvement in South Landfall	9	20-Jul-15	29-Jul-15	08-Mar-16	17-Mar-16	Preparation Method Statement for Ground Improvement in South La										
MS2710	Submit Method Statement to SO	0		29-Jul-15		17-Mar-16	Submit Method Statement to SO										
MS2720	SO Reviews & Comments	28	30-Jul-15	26-Aug-15	18-Mar-16	14-Apr-16	SO Reviews & Comments										
MS2730	Re-submission	6	27-Aug-15	02-Sep-15	15-Apr-16	21-Apr-16	Re-submission										
MS2740	SO's Review	28	03-Sep-15	30-Sep-15	22-Apr-16	19-May-16	SO's Review										
MS2750	SO's Approval	0		30-Sep-15		19-May-16	SO's Approval										
Construction																	
DDP11435	Temporary Platform for Ground Treatment for TBM passing under Southern Seawall	48	06-Aug-15	02-Oct-15	29-Aug-15	27-Oct-15	Temporary Platform for Ground Treatment										
DDP11440	Grouting Treatment for TBM passing under Southern Seawall	339	03-Oct-15	25-Nov-16	20-May-16	14-Jul-17	Grouting Treatment for TBM passing under Southern Seawall										
