



## WPD011-MRP19

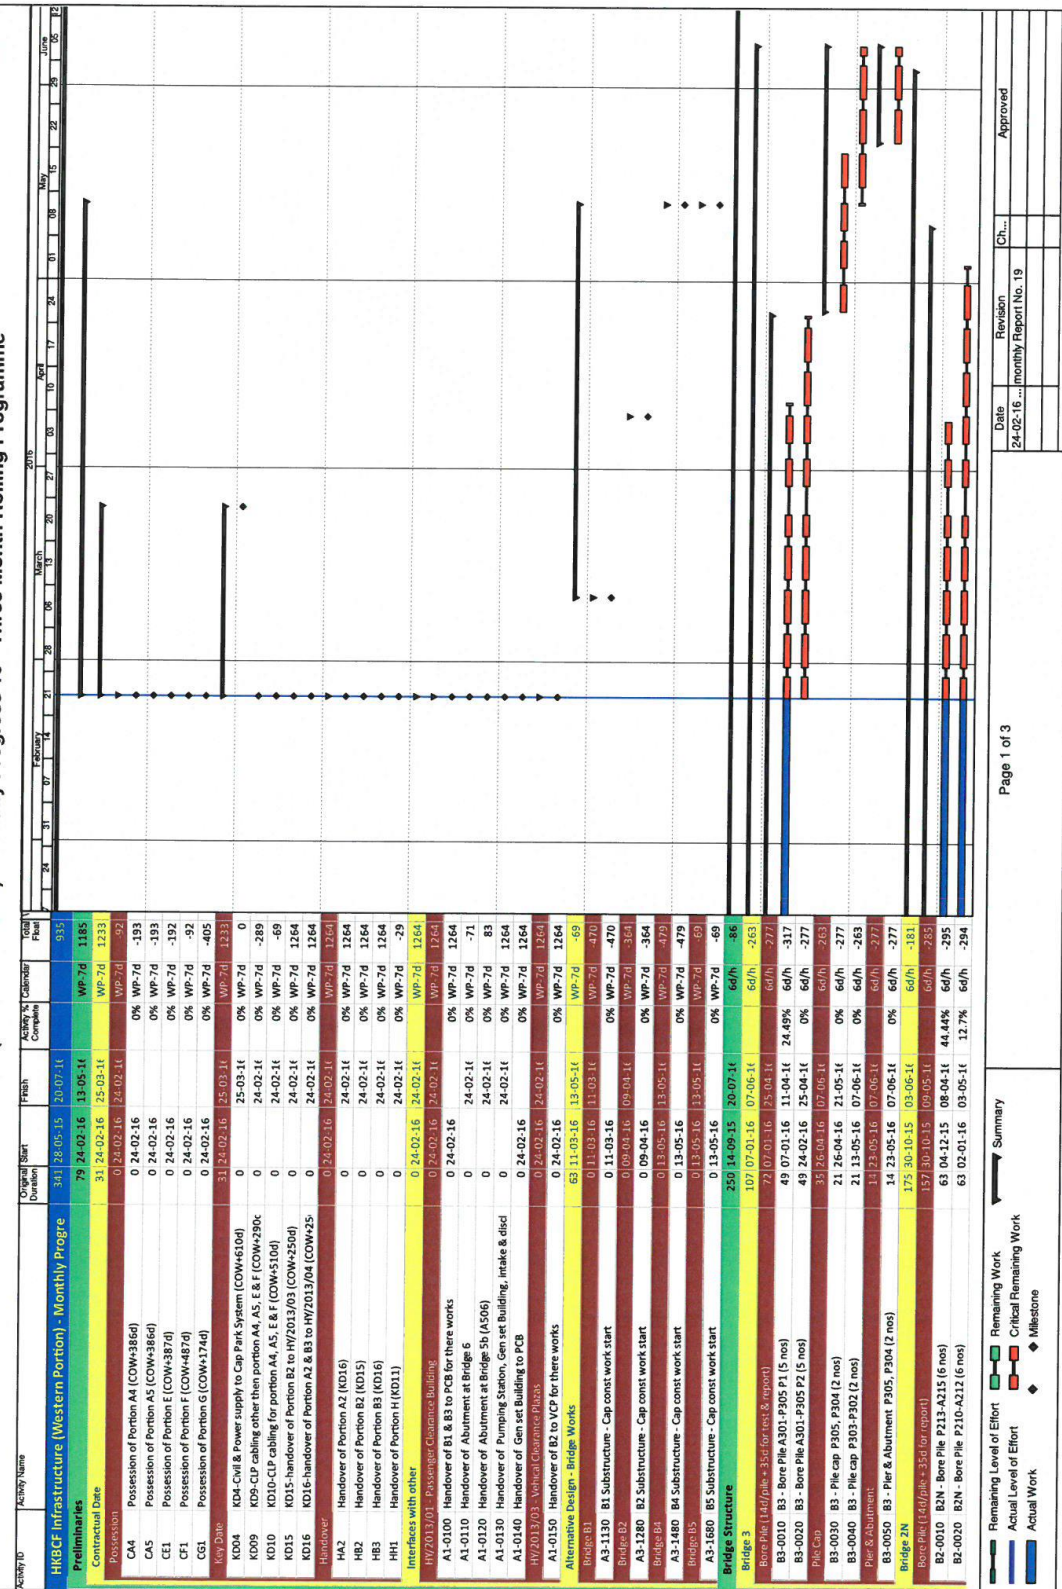

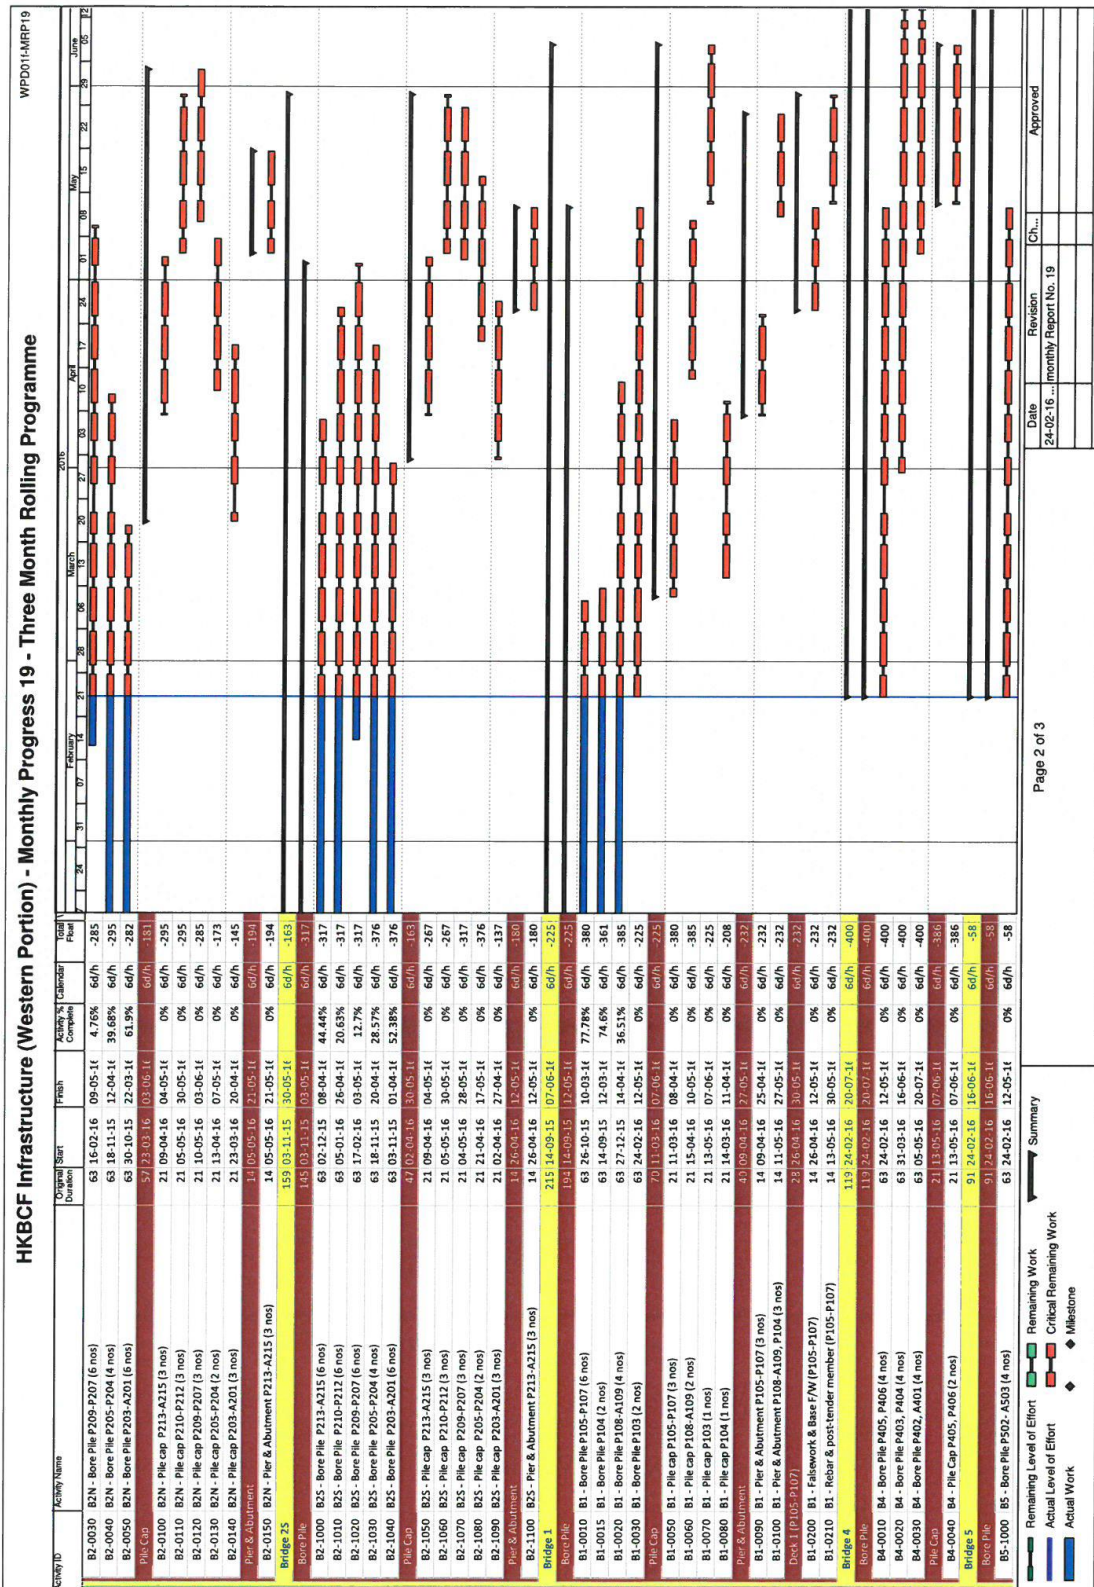

## WPD011-MRP19

| Activity ID                       | Activity Name                                                  | Original Duration     | Finish | Activity % Complete | Calendar | Total |
|-----------------------------------|----------------------------------------------------------------|-----------------------|--------|---------------------|----------|-------|
| B5-1020                           | B5 - Bore Pile P504 (P505) (4 nos)                             | 63 24-02-16 12:05-11  | 0%     | 6d/h                | 58       |       |
| B5-1030                           | B5 - Bore Pile P507 (A508) (4 nos)                             | 63 31-03-16 16:06-11  | 0%     | 6d/h                | 58       |       |
| Pile Cap                          |                                                                | 14 13-05-16 30:05-11  | 0%     | 6d/h                | 54       |       |
| B5-1040                           | B5 - Pile Cap P502, A503 (2 nos)                               | 14 13-05-16 30:05-11  | 0%     | 6d/h                | 54       |       |
| B5-1060                           | B5 - Pile Cap P504, P505 (2 nos)                               | 14 13-05-16 30:05-11  | 0%     | 6d/h                | 54       |       |
| Storm & Sewer Drainage Works      |                                                                |                       |        |                     |          |       |
| Storm Drain below +1.3m (2m/day)  |                                                                | 31 24-02-16 18:06-11  | 6d/h   | 144                 |          |       |
| U16 - convert CS into RI and      |                                                                | 31 11-05-16 18:05-11  | 6d/h   | 144                 |          |       |
| D1-0010                           | Box C3.2 - M3E2.5 (8m) 1050mm                                  | 23 11-05-16 17:06-11  | 6d/h   | 385                 |          |       |
| D1-0020                           | M42E.5 - M3E3.1 (25m) 900mm                                    | 10 11-05-16 23:05-11  | 0%     | 6d/h                | 385      |       |
| D1(a) - between B1 & B2           |                                                                | 10 18-05-16 28:05-11  | 6d/h   | 376                 |          |       |
| D1-0070                           | Box C3.1 - M3AE.8 (2.65m) 1200mm                               | 10 18-05-16 28:05-11  | 0%     | 6d/h                | 376      |       |
| F(a) - Sewall Side                |                                                                | 22 24-05-16 18:06-11  | 6d/h   | 313                 |          |       |
| D1-0490                           | M76A.23 - M53A.9 (44m) 1200mm                                  | 22 24-05-16 18:06-11  | 0%     | 6d/h                | 313      |       |
| Storm Drain about +1.3m (7m/day)  |                                                                | 73 24-02-16 25:05-11  | 6d/h   | 326                 |          |       |
| A1(1) - several feet to B2        |                                                                | 73 24-02-16 18:03-11  | 6d/h   | 326                 |          |       |
| D2-0010                           | M4E.8 - M4E.3 (183m) 750mm                                     | 25 24-02-16 24:03-11  | 0%     | 6d/h                | 361      |       |
| D2-0020                           | M4E.3 - M4E.1 (71m) 600mm                                      | 11 29-03-16 11:04-11  | 0%     | 6d/h                | 326      |       |
| D2-0600                           | M4E.7 - M1E.1 (35m) 300mm                                      | 5 12-04-16 18:04-11   | 0%     | 6d/h                | 326      |       |
| B(1) - CIP for RACE               |                                                                | 38 24-02-16 06:05-11  | 6d/h   | 328                 |          |       |
| D2-0030                           | M31C.A8 - M31C.7 (66m) 900mm                                   | 10 24-02-16 05:03-11  | 0%     | 6d/h                | 361      |       |
| D2-0040                           | M31C.7 - M31C.5 (70m) 750mm                                    | 10 07-03-16 17:03-11  | 0%     | 6d/h                | 361      |       |
| D2-0050                           | M31C.5 - M31C.2 (105m) 600mm                                   | 15 18-03-16 08:04-11  | 0%     | 6d/h                | 361      |       |
| D2-0060                           | M12E.4 - M12E.1 (35m) 750mm                                    | 5 09-04-16 10:04-11   | 0%     | 6d/h                | 361      |       |
| D2-0070                           | M12E.3 - M12E.2 (35m) 600mm                                    | 5 15-04-16 20:04-11   | 0%     | 6d/h                | 361      |       |
| D2-0080                           | M12E.2 - M12E.1 (41m) 450mm                                    | 6 21-04-16 27:04-11   | 0%     | 6d/h                | 328      |       |
| D2-0085                           | M12E.2 - M12E.A2 (8m) 450mm                                    | 2 28-04-16 29:04-11   | 0%     | 6d/h                | 328      |       |
| D2-0090                           | M31C.2 - M31C.1 (35m) 450mm                                    | 5 30-04-16 06:05-11   | 0%     | 6d/h                | 328      |       |
| A(4) - after B2                   |                                                                | 38 12-04-16 25:05-11  | 6d/h   | 326                 |          |       |
| D2-0100                           | M81A.1 - M81A.4 (130m) 300mm                                   | 19 12-04-16 04:05-11  | 0%     | 6d/h                | 326      |       |
| D2-0110                           | M66A.1 - M66A.B1 (66m) 450mm                                   | 10 07-05-16 19:05-11  | 0%     | 6d/h                | 328      |       |
| D2-0120                           | M66A.1 - M66A.C1 (35m) 600mm                                   | 5 20-05-16 25:05-11   | 0%     | 6d/h                | 328      |       |
| Utilities                         |                                                                |                       |        |                     |          |       |
| CIP Cable trench & duct           |                                                                | 335 28-05-15 13:07-11 | 941    |                     |          |       |
| Portion A1 & A3                   |                                                                | 141 24-02-16 13:07-11 | WP-7d  | -309                |          |       |
| UT-1000                           | CIP trench & Duct - bridge 2 to Sub-station                    | 60 16-03-16 14:05-11  | 0%     | WP-7d               | -309     |       |
| UT-1010                           | CIP trench & Duct - bridge 2 to South Portion                  | 60 15-05-16 13:07-11  | 0%     | WP-7d               | -309     |       |
| UT-1080                           | CHEC cross road duct for CIP works                             | 21 24-02-16 15:03-11  | 0%     | WP-7d               | -309     |       |
| Cable Duct (TCS5, EUV & UV)       |                                                                | 45 28-05-15 05:03-11  | 6d/h   | 1044                |          |       |
| Reinforcement                     |                                                                | 45 28-05-15 05:03-11  | 6d/h   | 1044                |          |       |
| UT-1170                           | Cable duct for TCS5, EUV, UV & other department (I)            | 45 28-05-15 05:03-11  | 77.78% | 6d/h                | 1044     |       |
| Road Works                        |                                                                |                       |        |                     |          |       |
| Road Furniture & Fit out          |                                                                | 105 24-02-16 04:07-11 | 201    |                     |          |       |
| Road Lighting Design & Submission |                                                                | 105 24-02-16 04:07-11 | 6d/h   | -240                |          |       |
| RW-2050                           | Submit & approval of road lighting system sub-contractor       | 60 24-02-16 09:05-11  | 0%     | 6d/h                | -240     |       |
| RW-2060                           | Prepare, submit & approval of road lighting system design      | 60 21-04-16 04:07-11  | 0%     | 6d/h                | -240     |       |
| Landscape                         |                                                                | 120 24-02-16 22:06-11 | WP-7d  | -239                |          |       |
| RW-2070                           | Submit & design of irrigation system                           | 120 24-02-16 22:06-11 | WP-7d  | -239                |          |       |
| RW-2070                           | Prepare, submit & approval of irrigation system sub-contractor | 120 24-02-16 22:06-11 | 0%     | WP-7d               | -239     |       |
