

Appendix B


Construction Programme

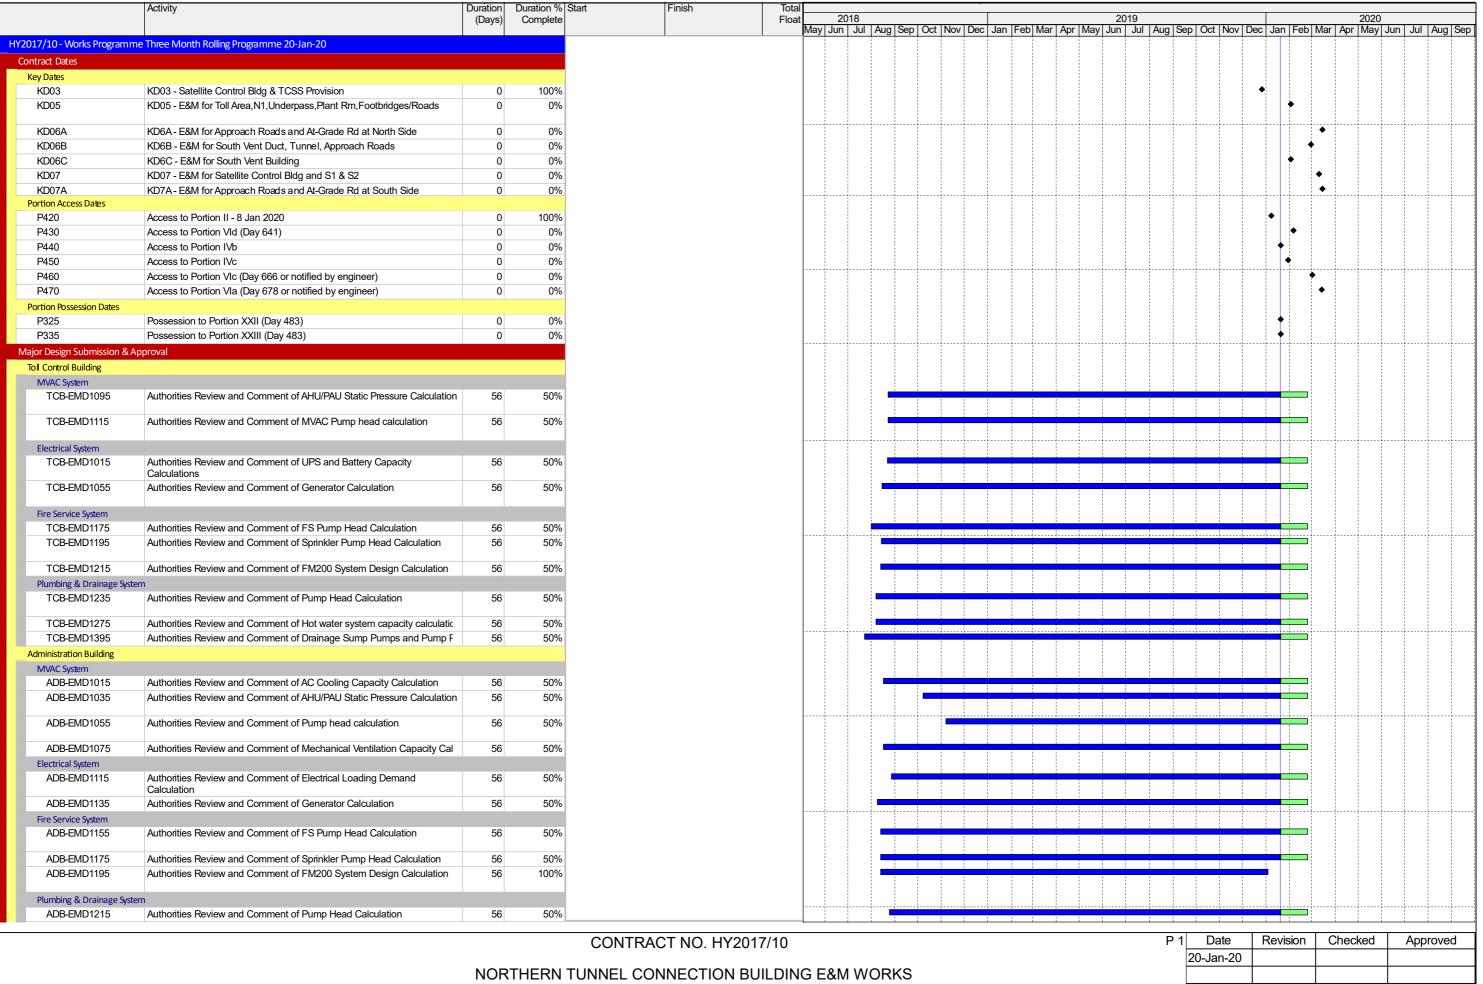



² 1	Date	Revision	Checked	Approved
	20-Jan-20			

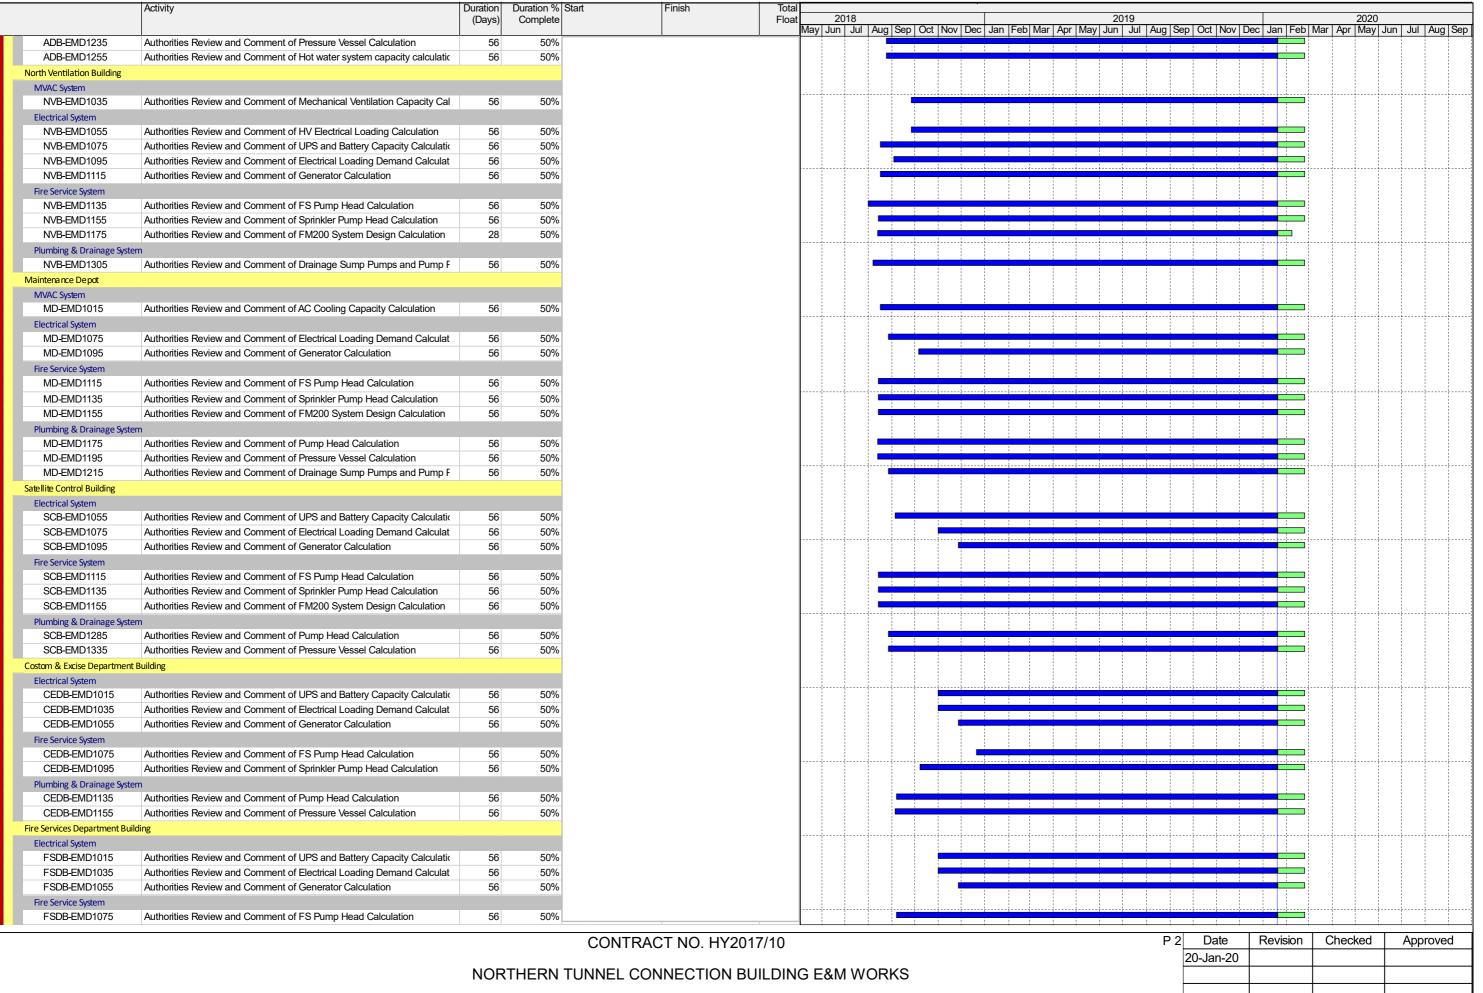



2	Date	Revision	Checked	Approved
	20-Jan-20			

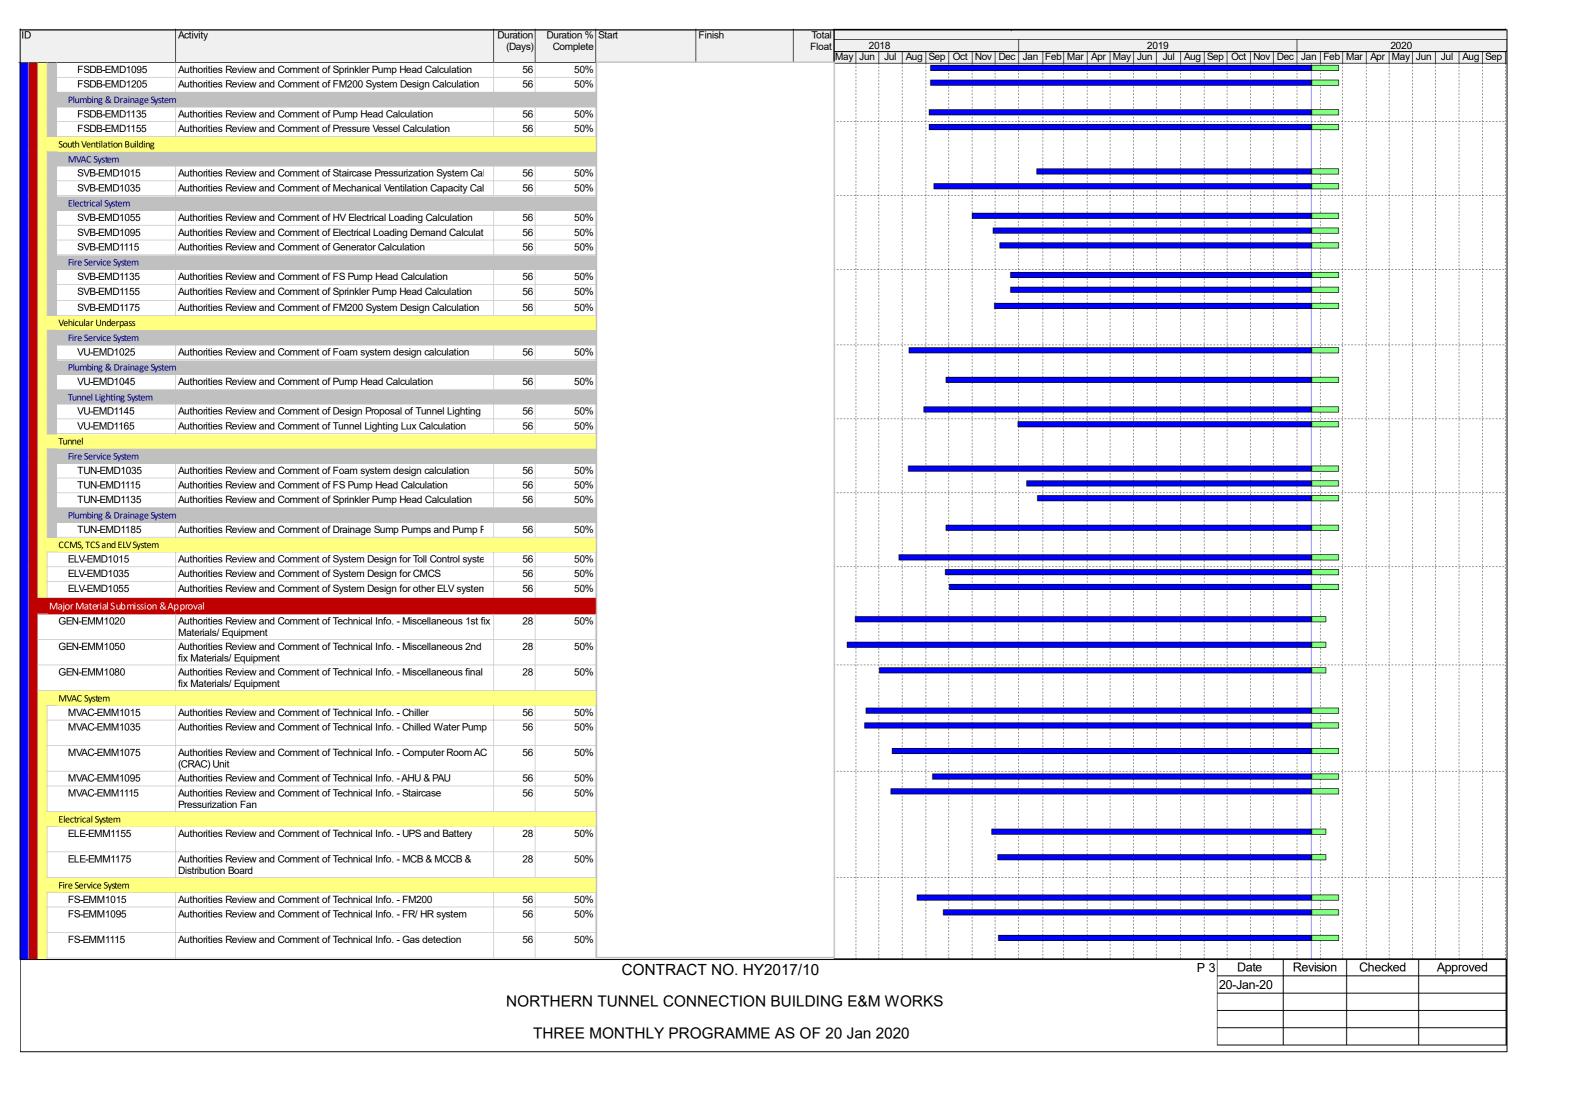


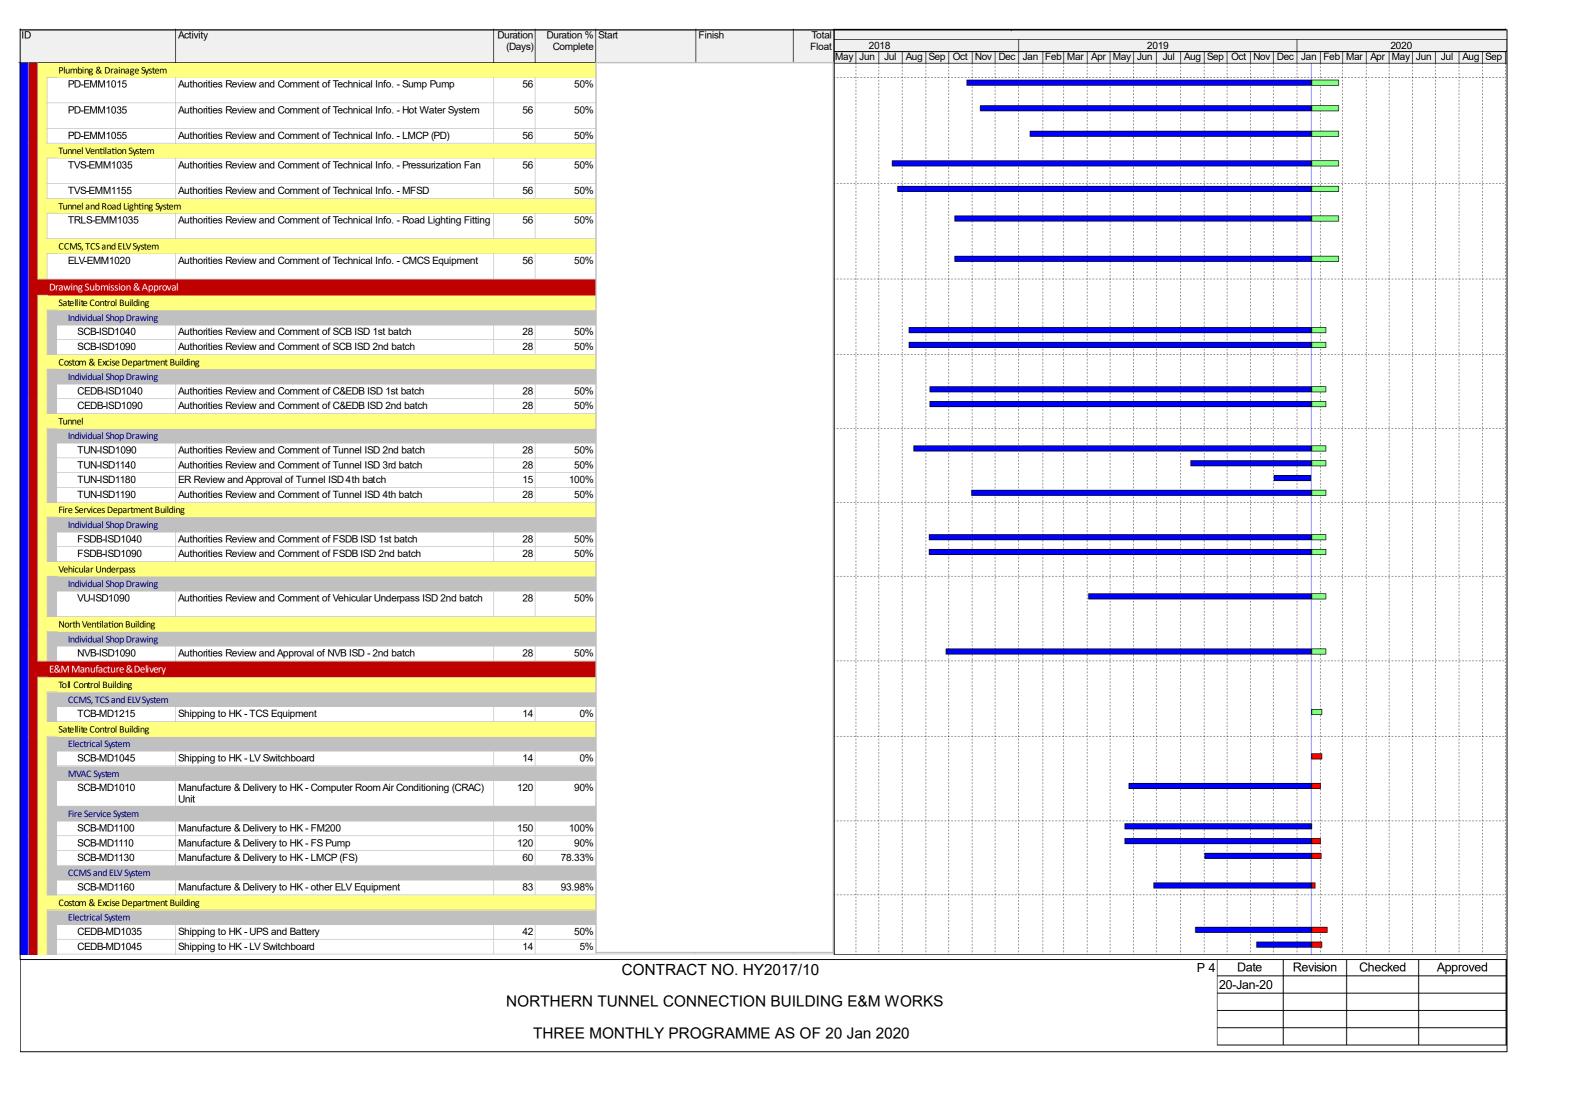


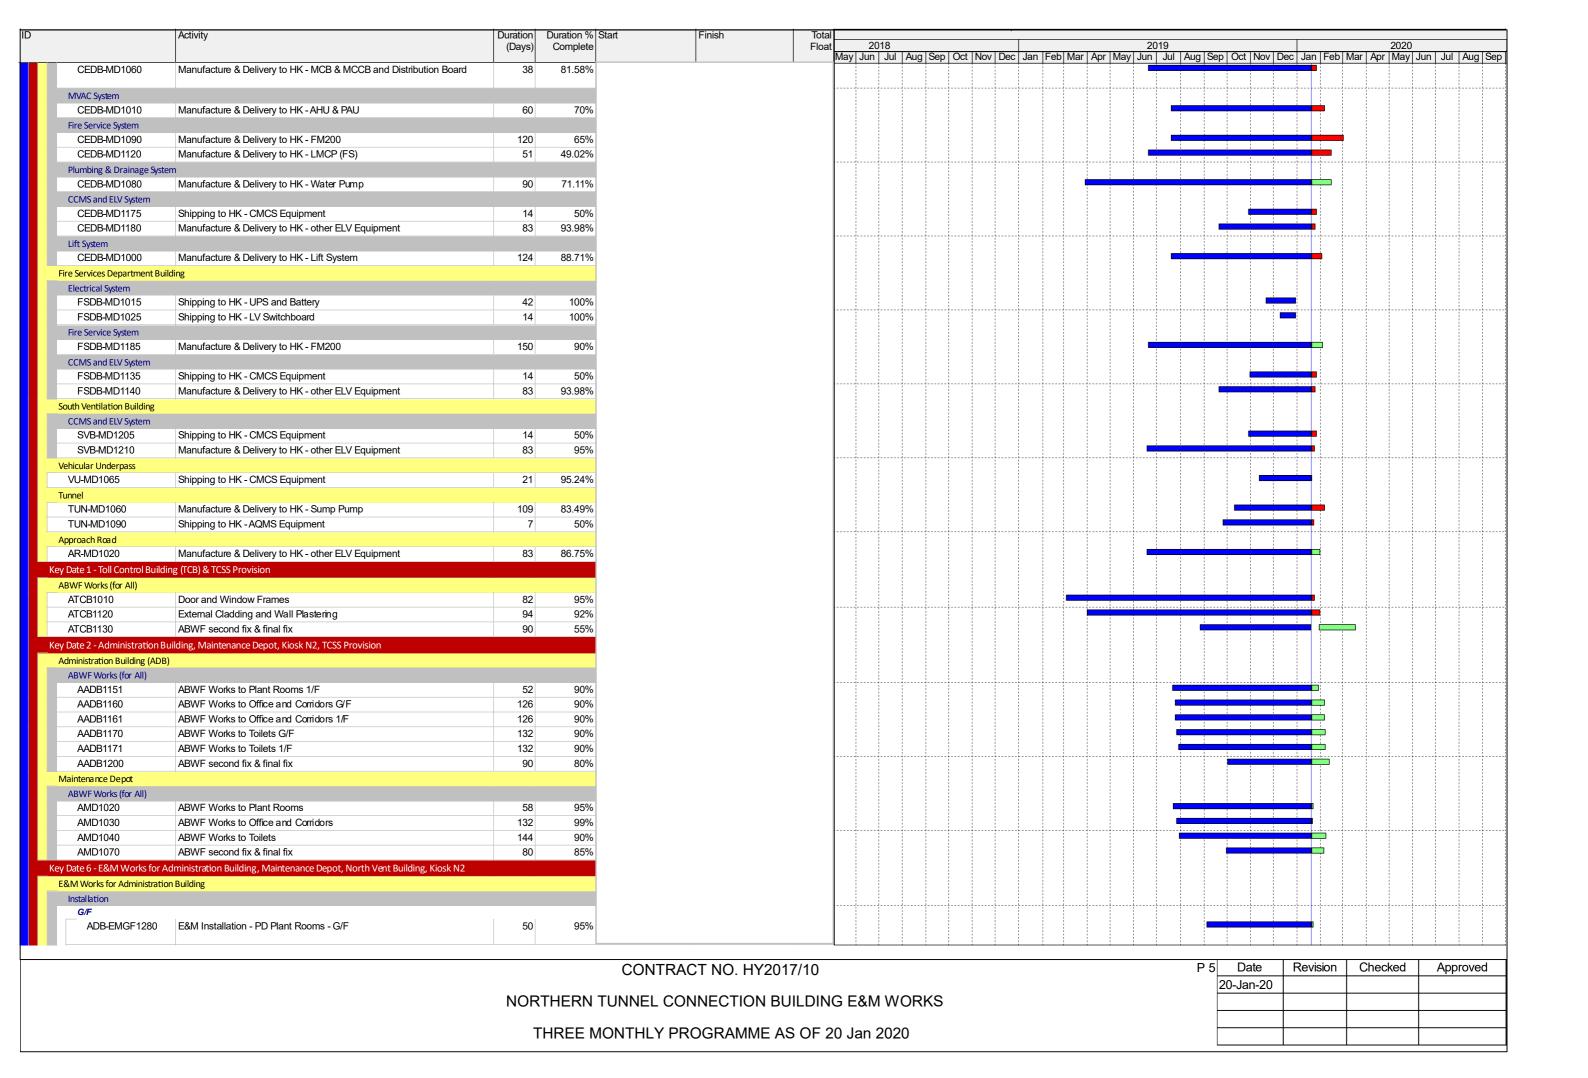


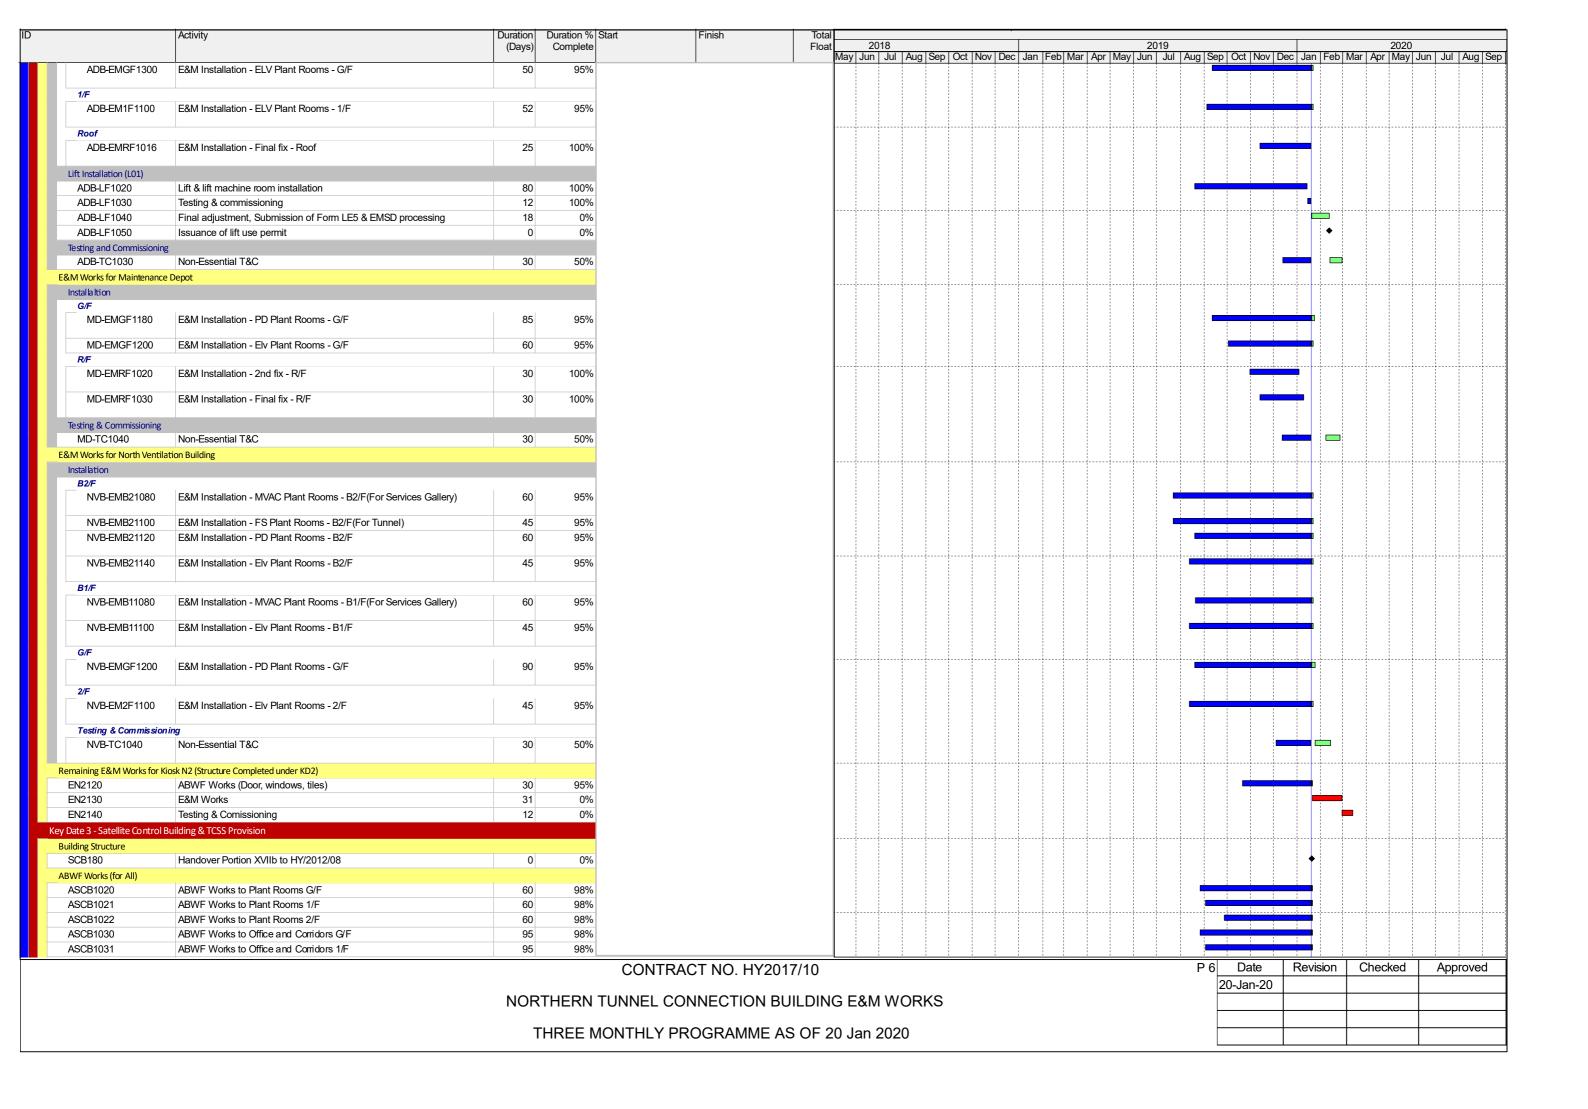


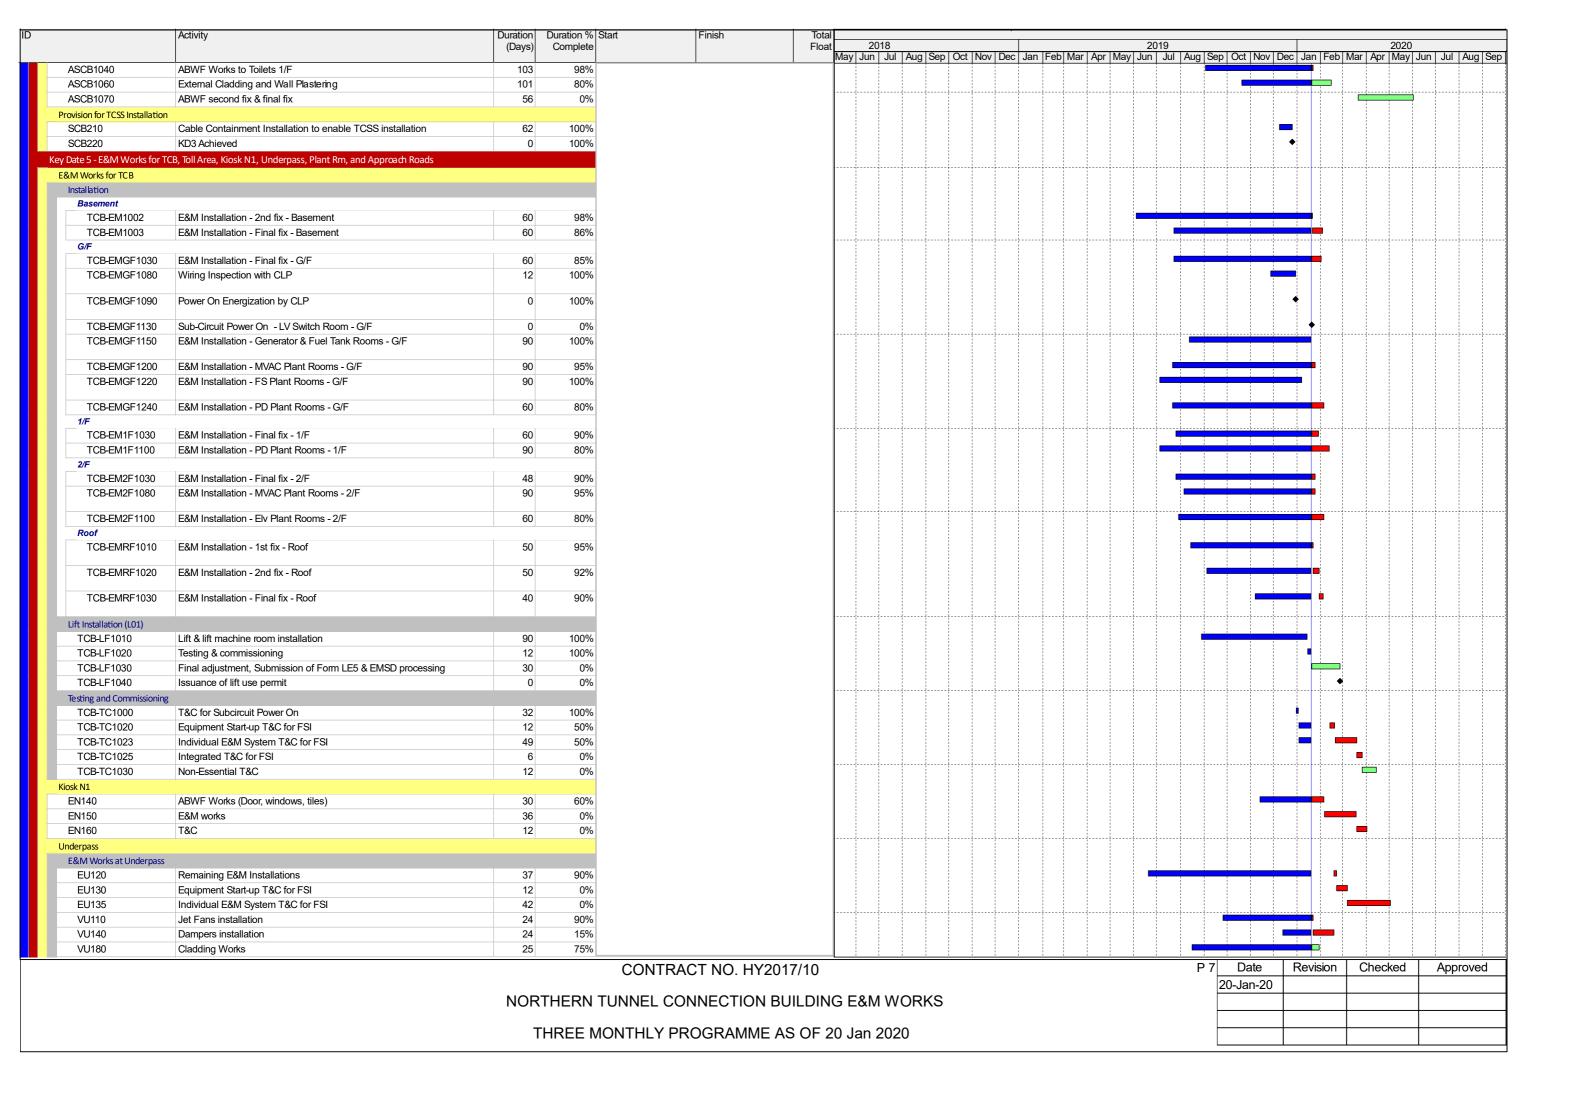


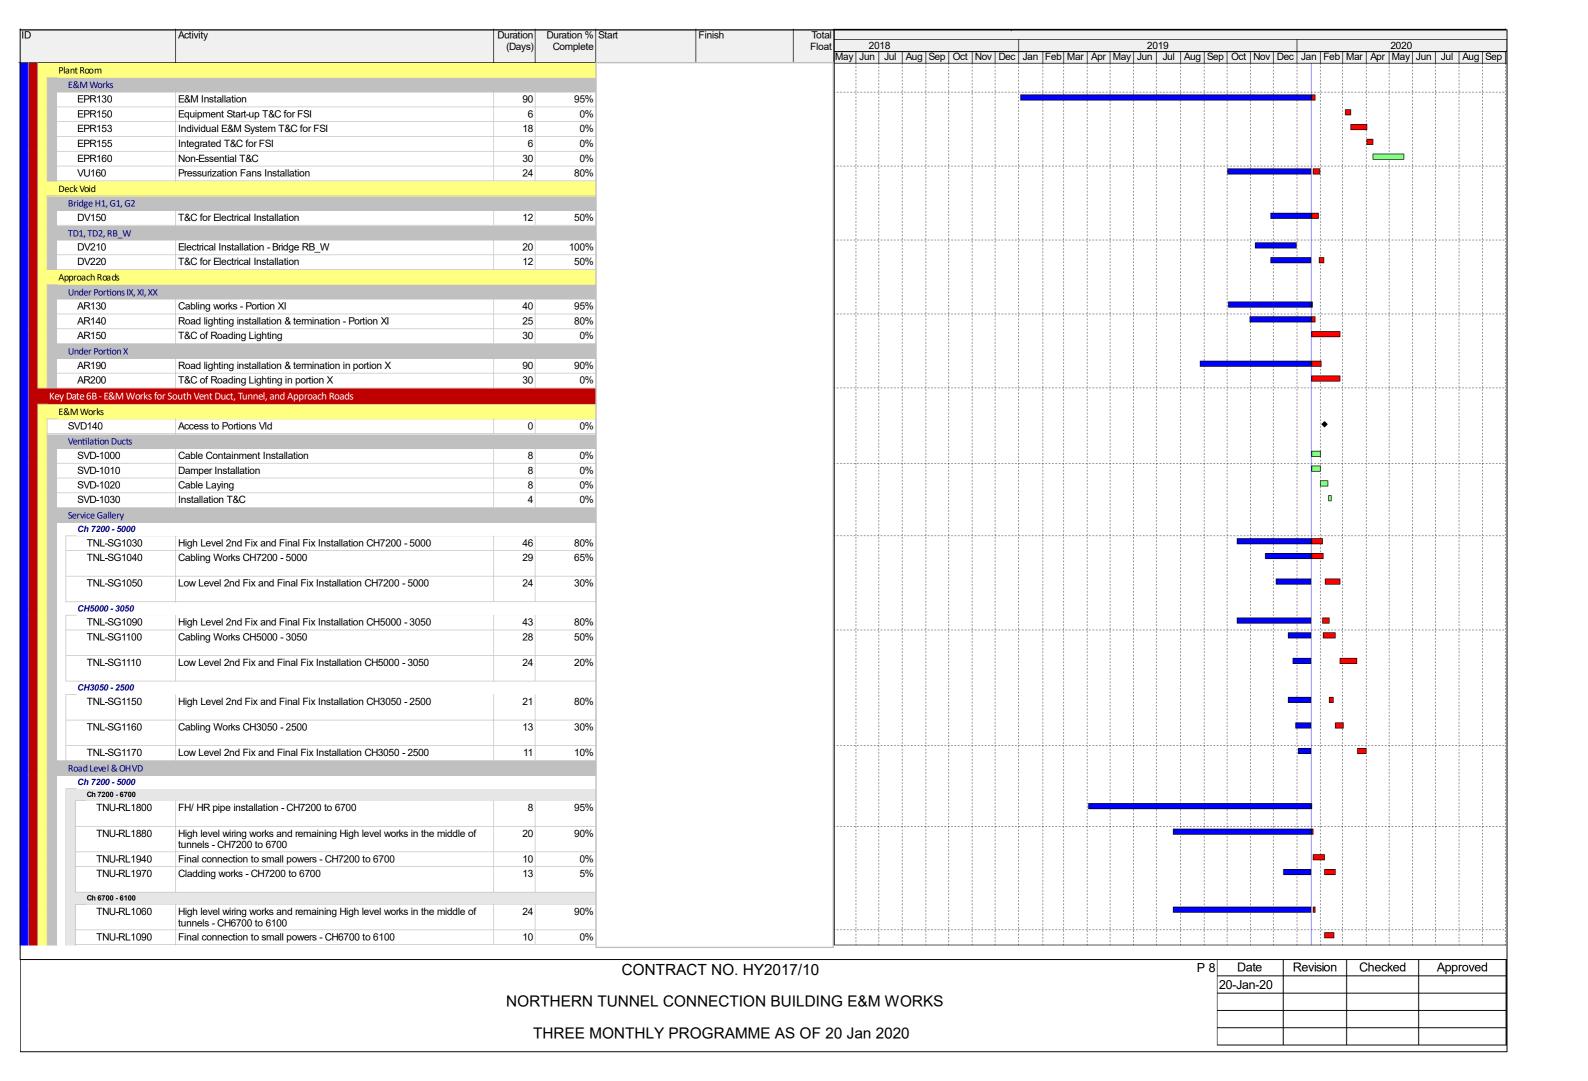


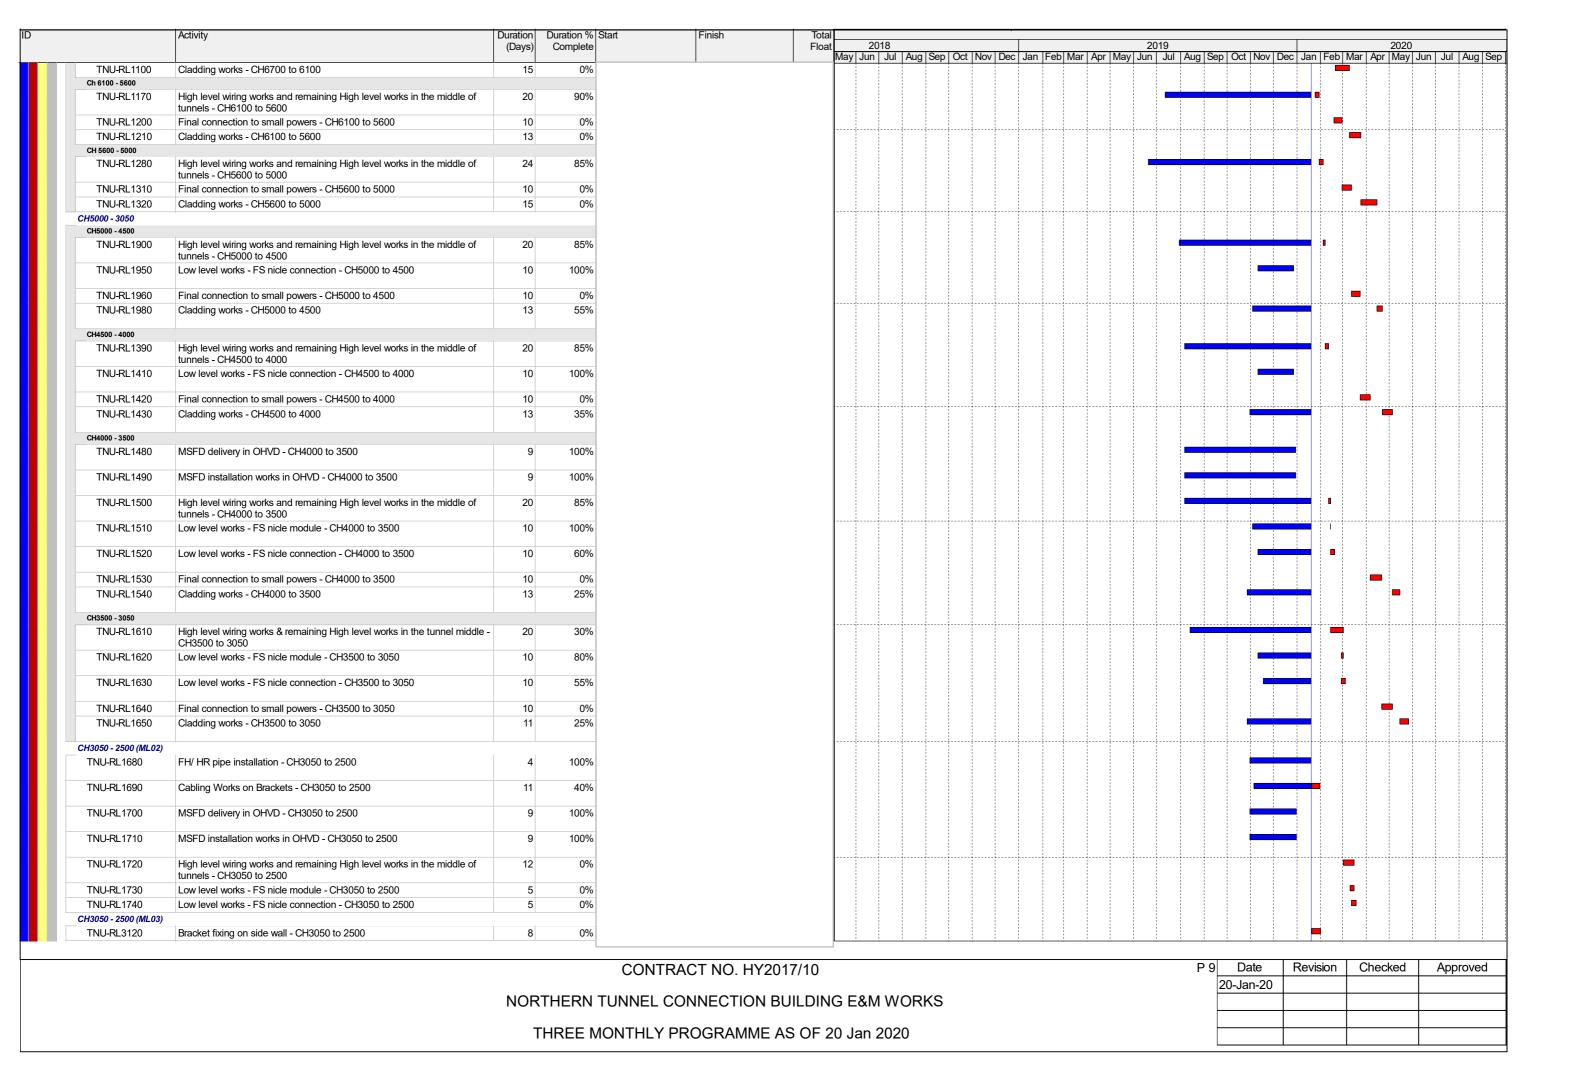

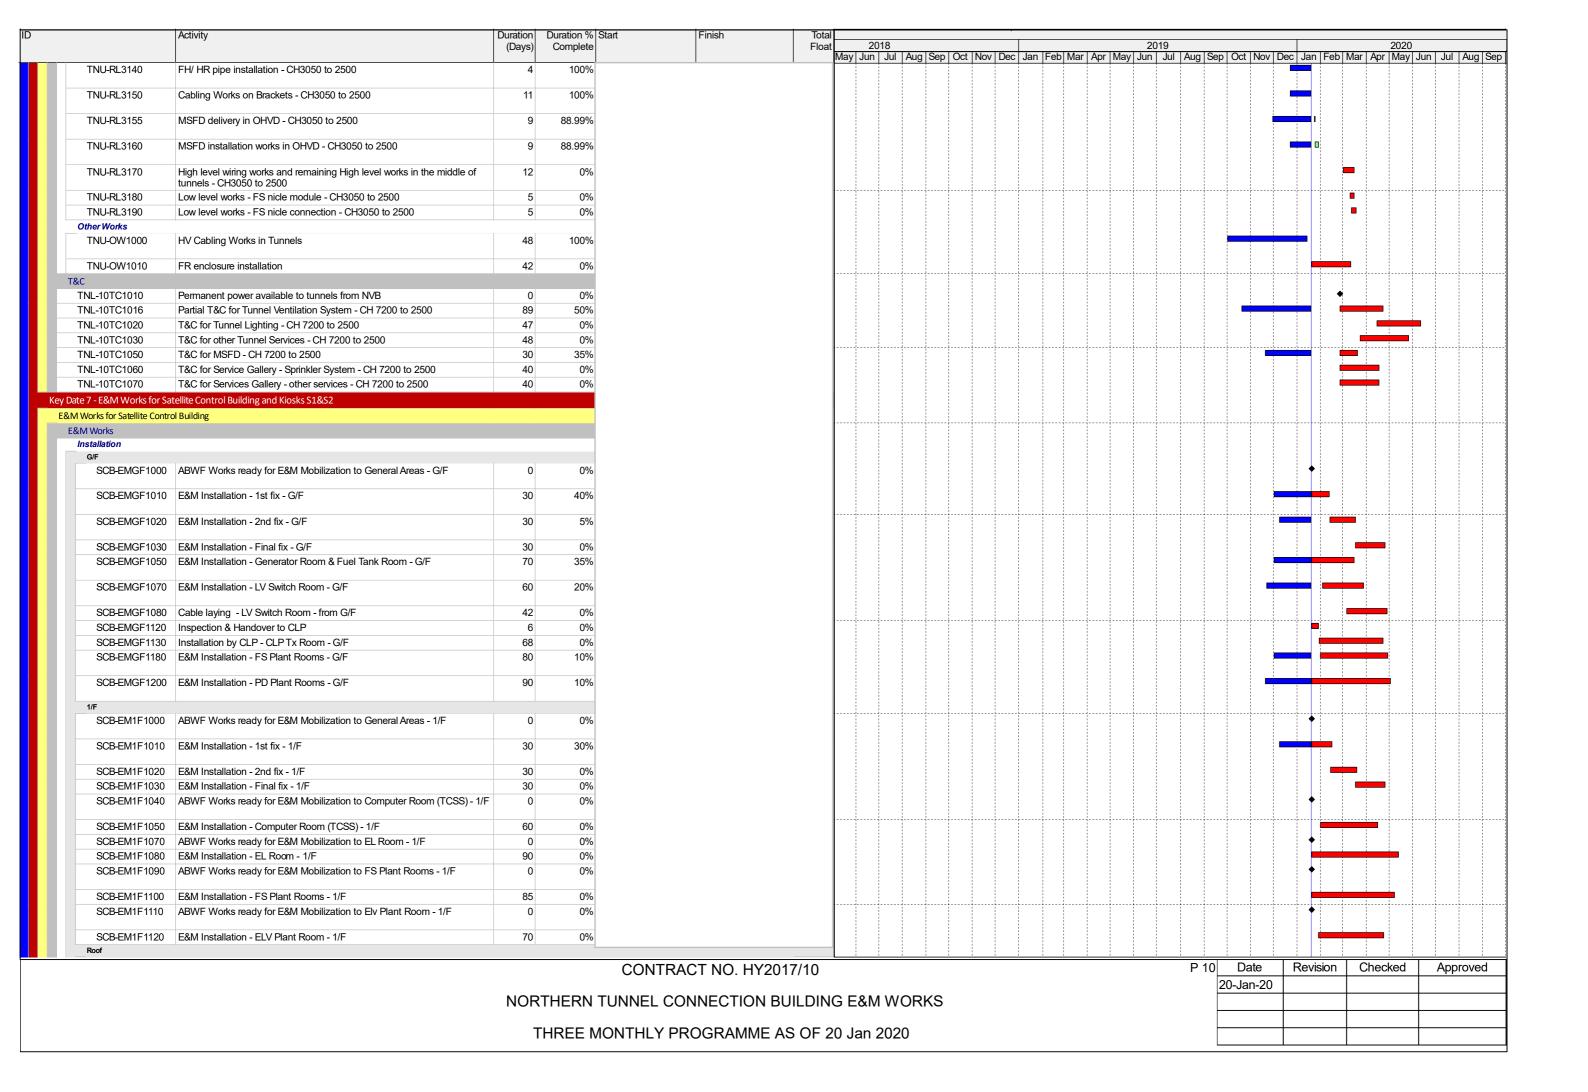


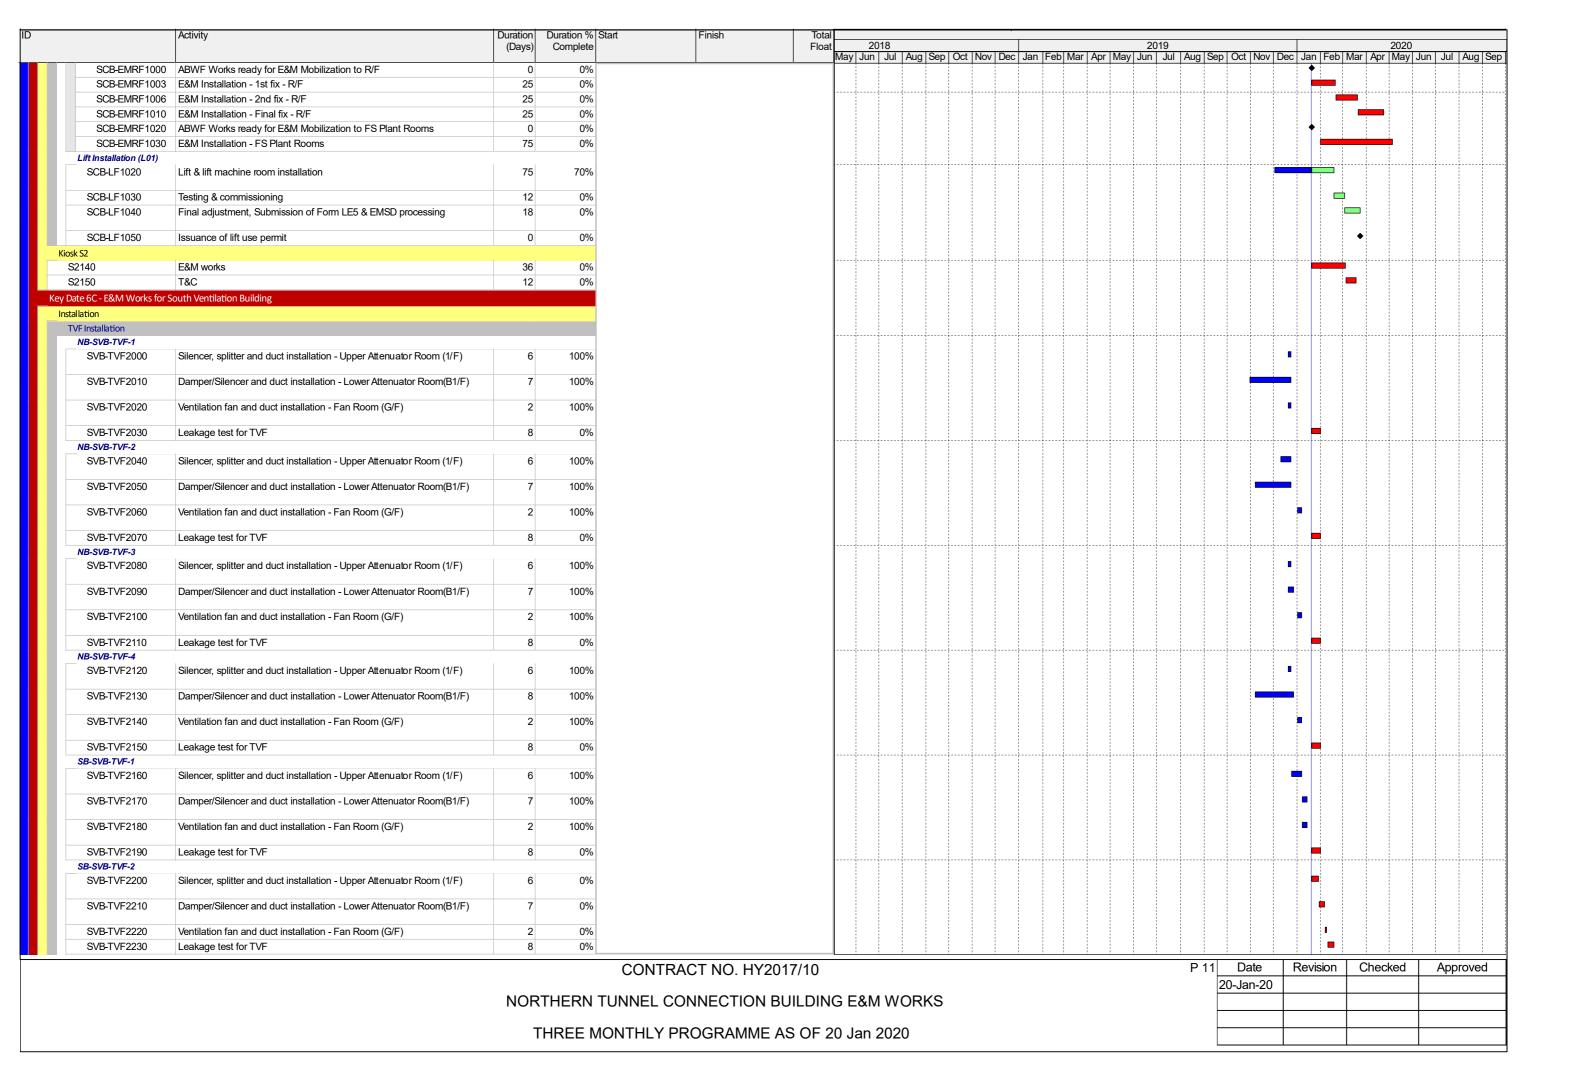

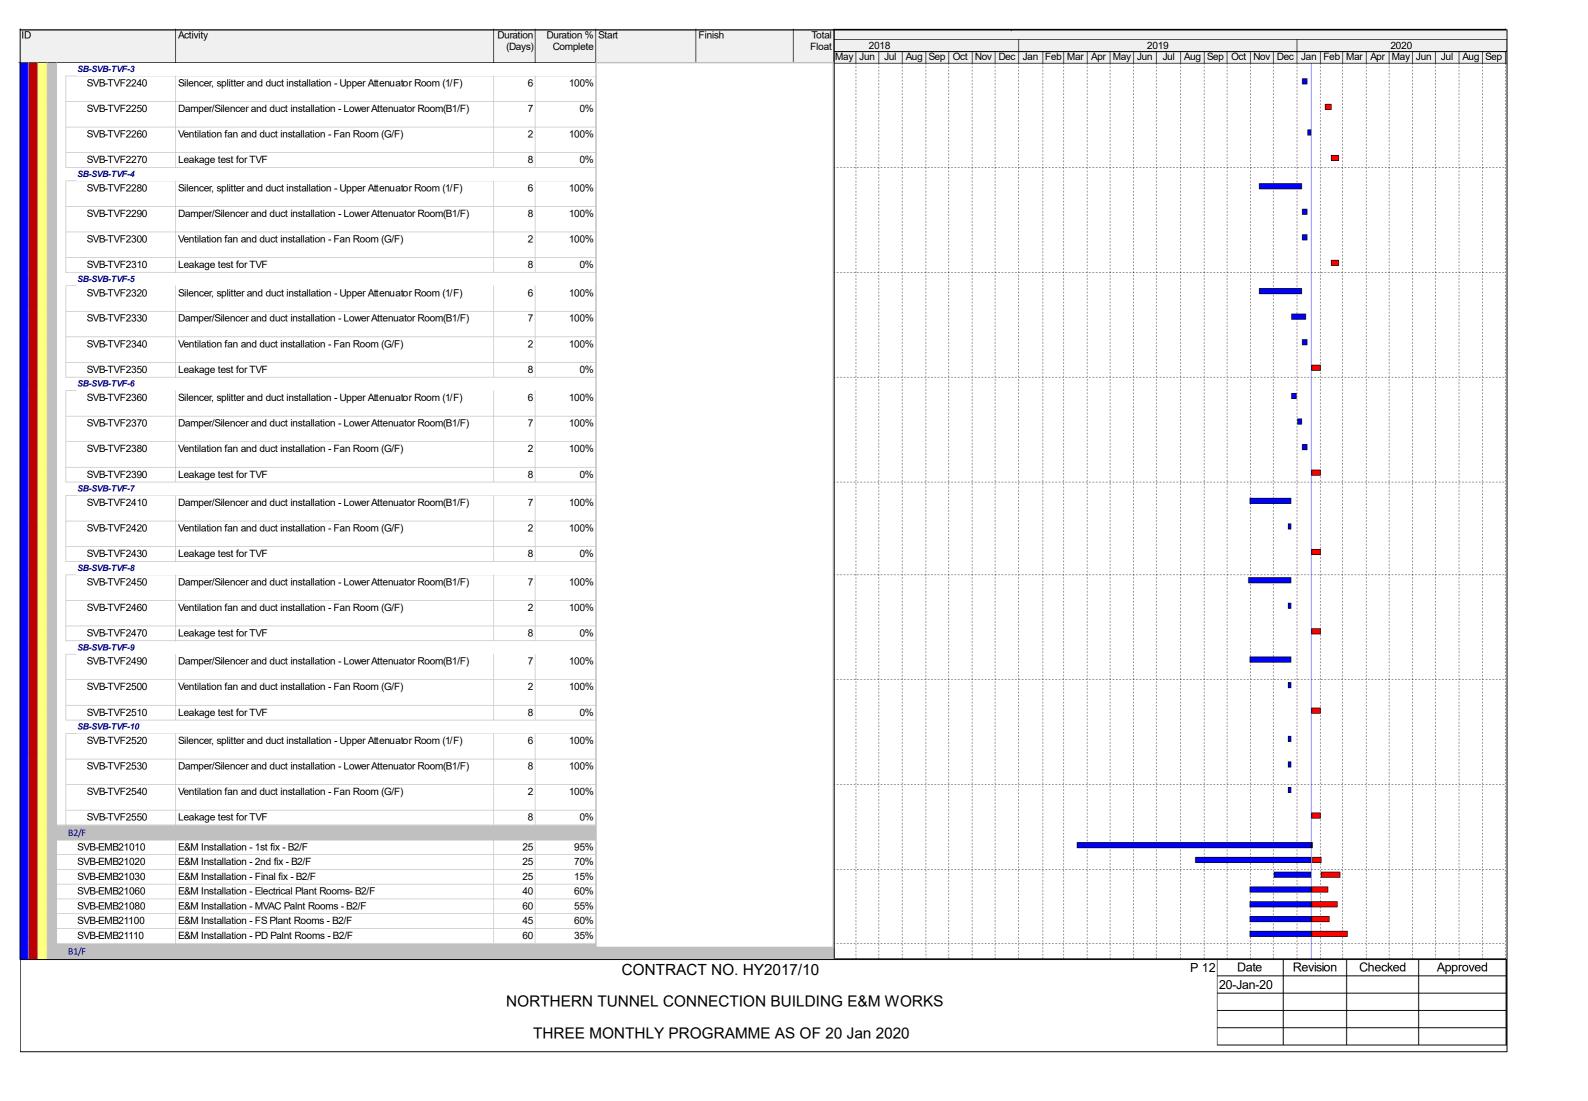


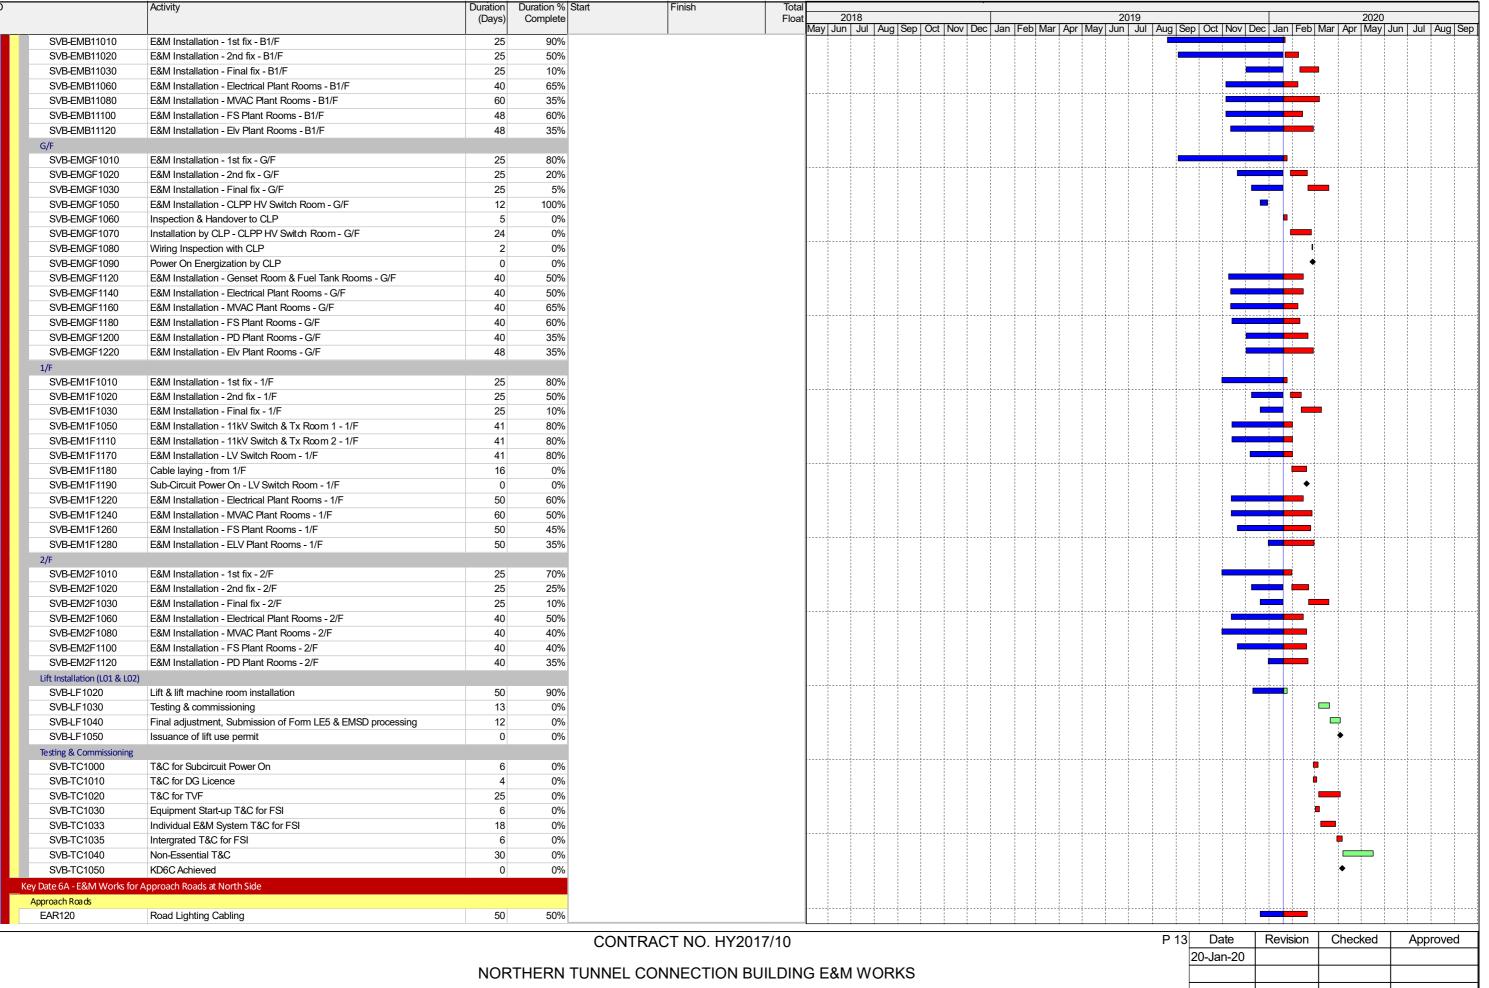



3	Date	Revision	Checked	Approved
	20-Jan-20			

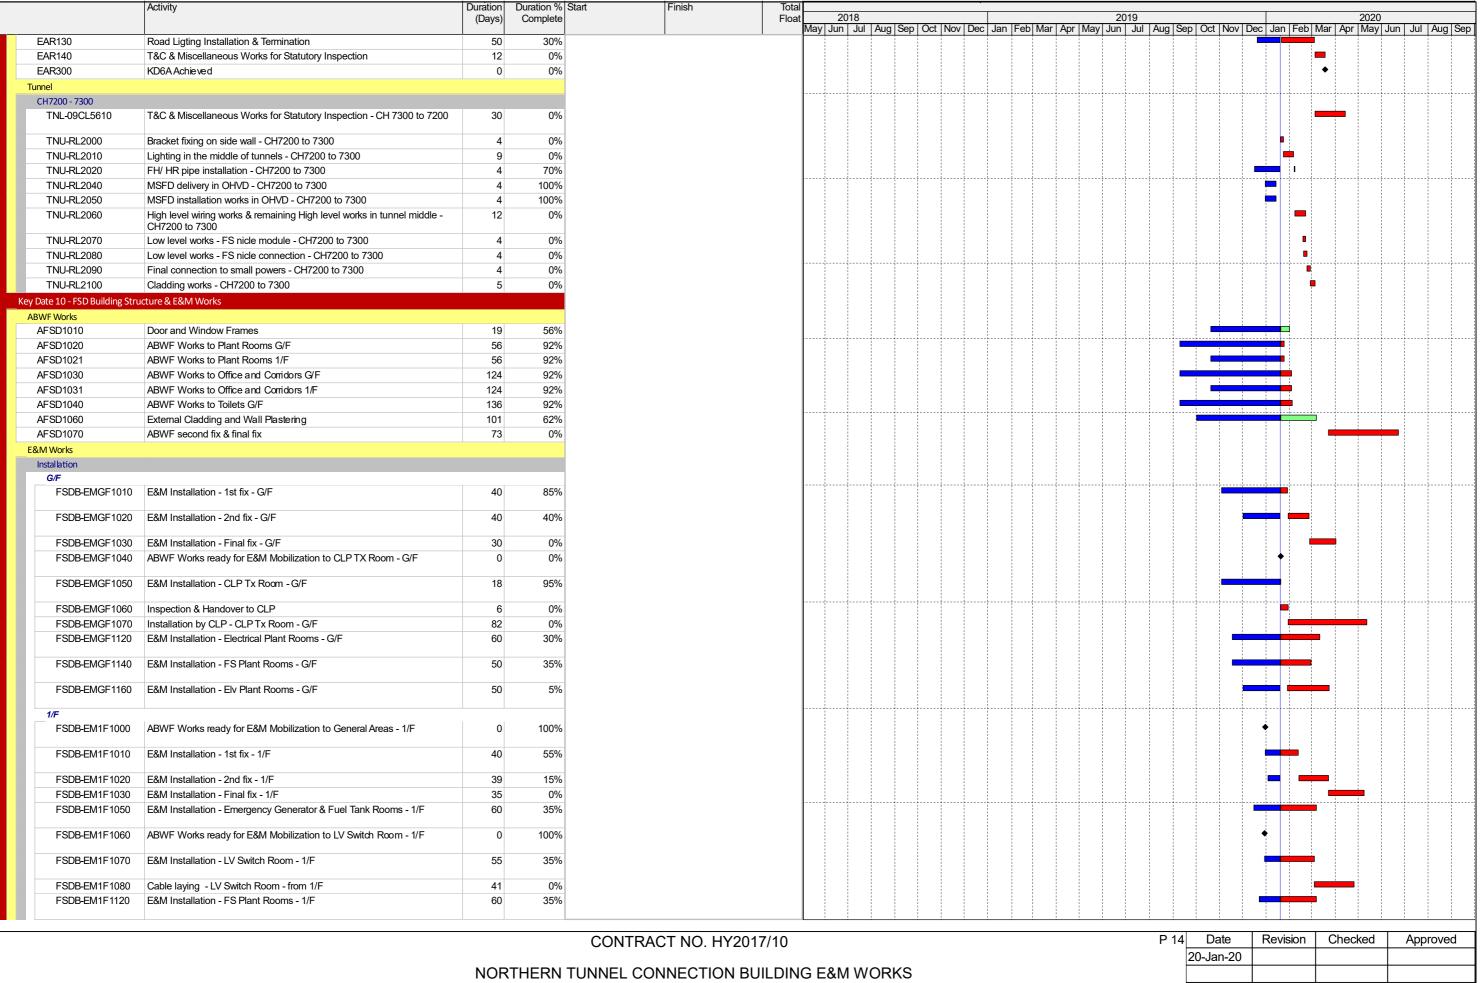

14	Date	Revision	Checked	Approved
	20-Jan-20			

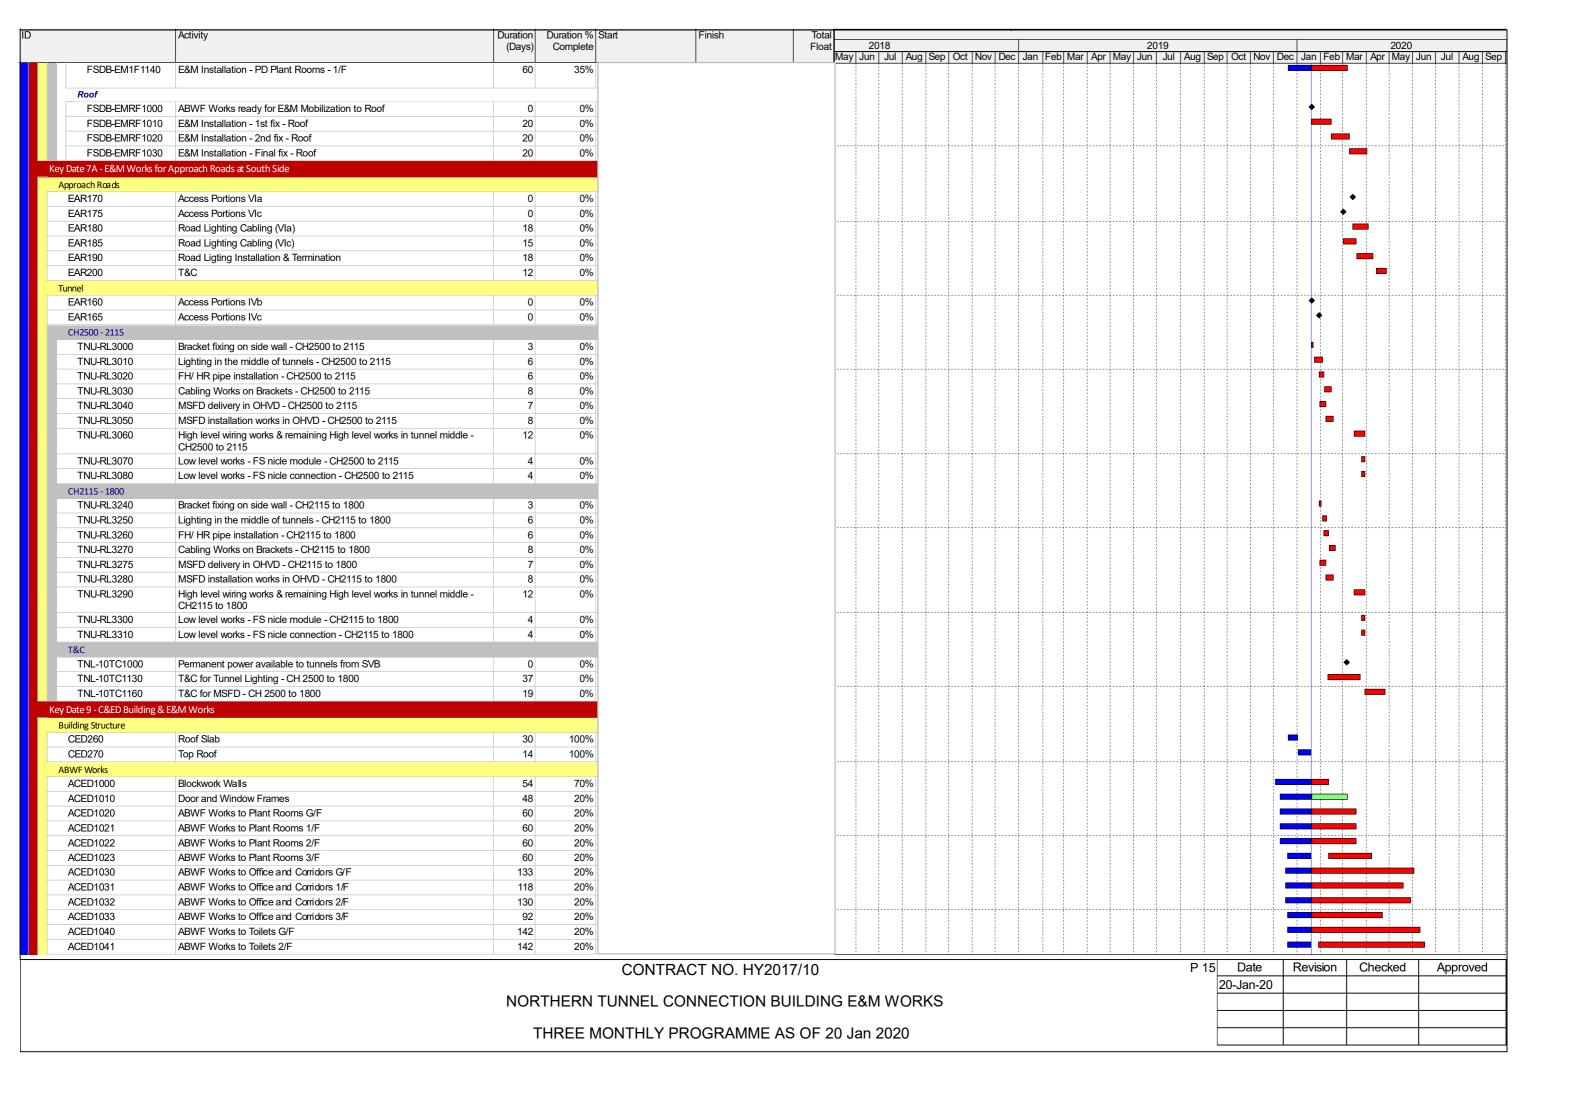

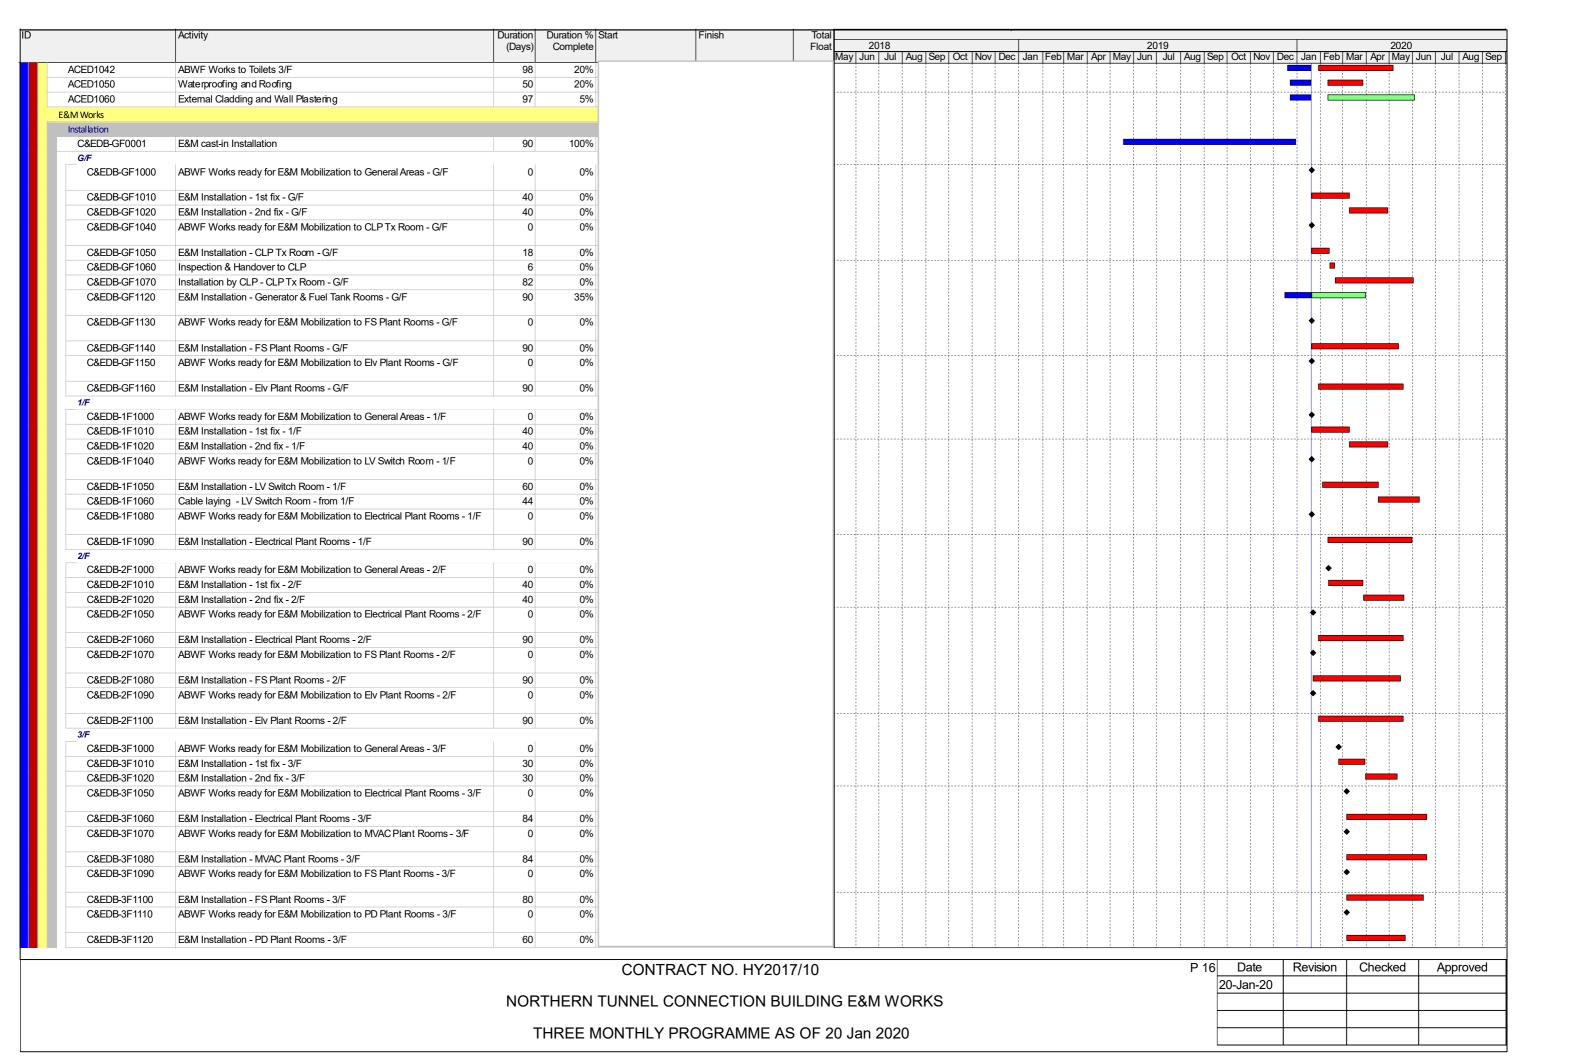

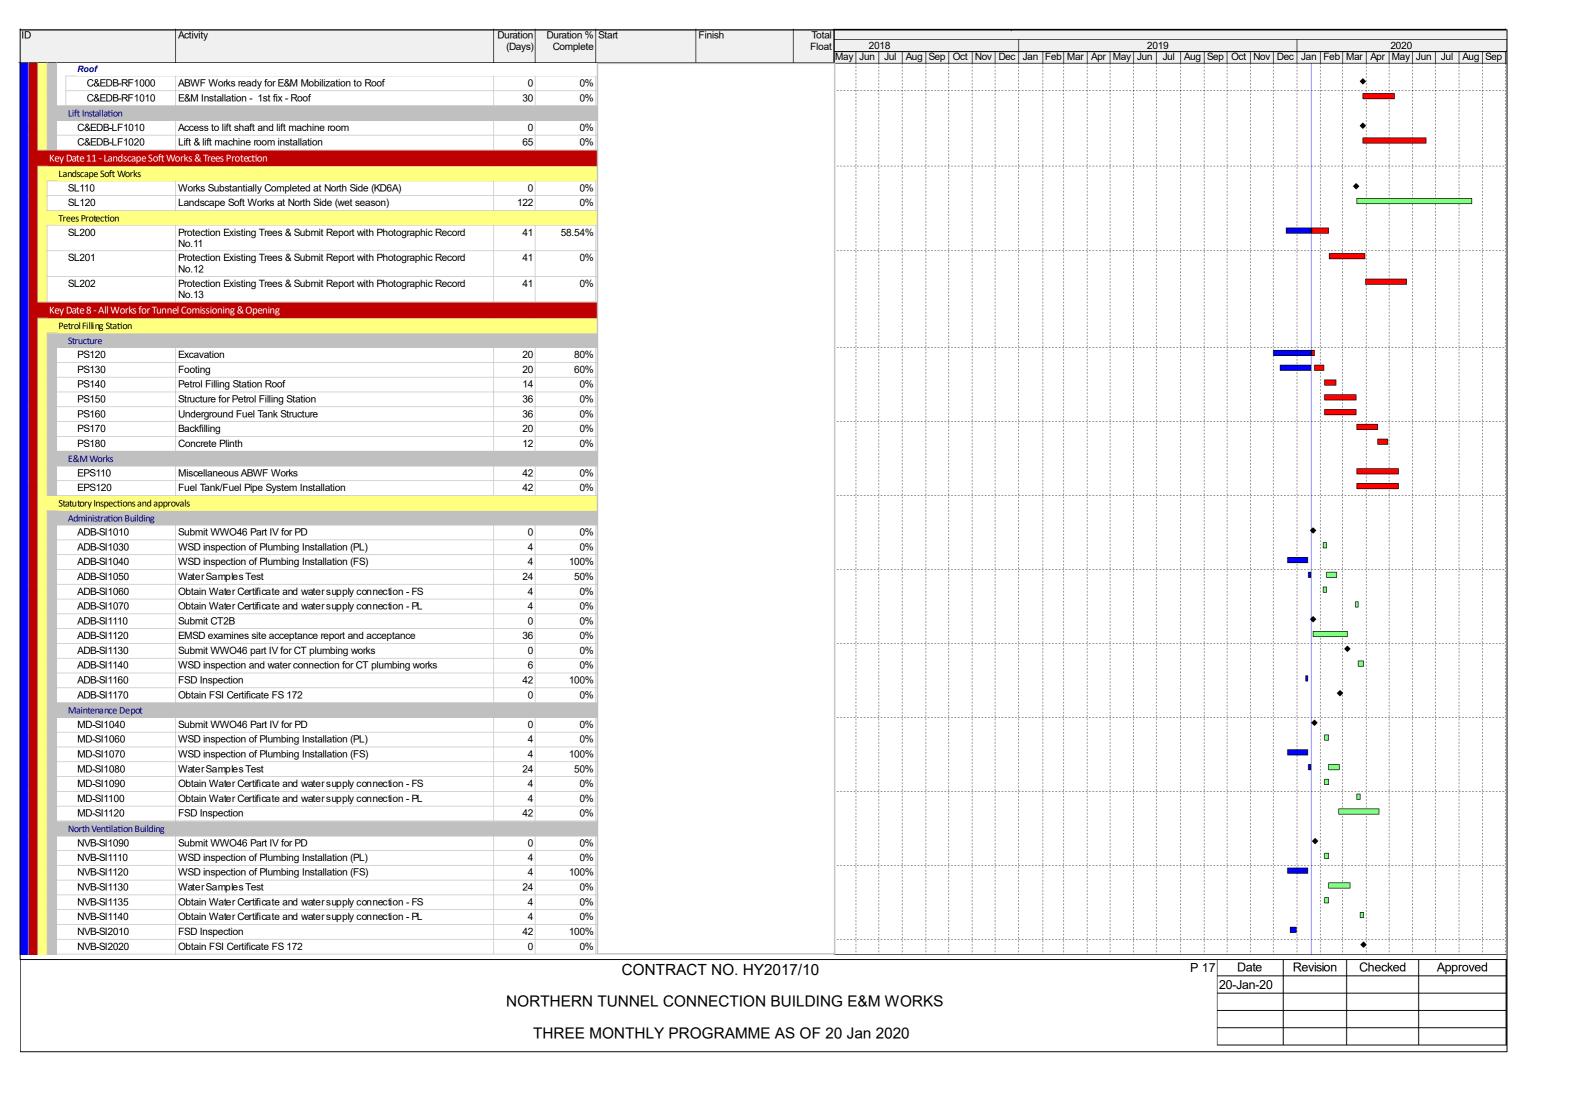

	Activity	Duration	Duration %	Tota	2018 2019 2020																			
		(Days)	Complete	Floa		2018	I Aug I	Son Oct	Nov	Doo I	n Eob	MorlA	nr Mo			Aug So	n l Oo	t Nov D	100	on Eol	h Mar			Jul Aug Se
Underpass & Plant Roo	m				Iviay Ju	JII Jul	Aug	Sep Oct	INOV	Dec J	il len	IVIAI F	pi jivia	Juii	Jui	aug Se	p Oc	LINOVID	ec J	ali Fei	D IVIAI	Api livi	ay Jun	Jui Aug Se
VUP-SI1060	Submit WWO46 Part IV for FS	0	0%																		•			
VUP-SI1080	WSD inspection of Plumbing Installation (FS)	4	0%																		0			
VUP-SI1095	Obtain Water Certificate and water supply connection - FS	4	0%																		•			
Toll Control Building &							-11		1			1		1 1				1		1	1			
TCB-SI1020	DG Inspection by FSD	36	100%																	•				
TCB-SI1030	Obtain DG Licence	0	0%																	•				
TCB-SI2000	Submit WWO46 Part IV for PD	0	0%																		•			
TCB-SI2010	Submit WWO46 Part IV for FS	0	0%				1 1				:										•			
TCB-SI2020	WSD inspection of Plumbing Installation (PL)	4	0%				-11					11		1						1	0			
TCB-SI2030	WSD inspection of Plumbing Installation (FS)	4	0%																					
TCB-SI2040	Water Samples Test	24	0%																		_			
TCB-SI2045	Obtain Water Certificate and water supply connection - FS	4	0%																			•		
TCB-SI3000	Submit CT2B	0	0%											<u>.ii</u>						•				
TCB-SI3010	EMSD examines site acceptance report and acceptance	36	0%																					
TCB-SI3020	Submit WWO46 part IV for CT plumbing works	0	0%																		•			
TCB-SI3030	WSD inspection and water connection for CT plumbing works	4	0%																					
TCB-SI4000	Final Submission of Form FSI 314 / 501 to FSD	0	0%																		•			
TCB-SI4010	FSD Inspection	42	0%									<u> </u>											=	
South Ventilation Buildi	ng																							
SVB-SI1010	DG Submission & Vent/425 to FSD	0	0%																		•			
SVB-SI1020	DG Inspection by FSD	24	0%																					
SVB-SI1030	Obtain DG Licence	0	0%										-						-	-	-	•		
SVB-SI1090	Submit WWO46 Part IV for PD	0	0%									<u> </u>		<u> </u>							•			
SVB-SI1100	Submit WWO46 Part IV for FS	0	0%																	•	•			
SVB-SI1110	WSD inspection of Plumbing Installation (PL)	4	0%																		0			
SVB-SI1120	WSD inspection of Plumbing Installation (FS)	4	0%																					
SVB-SI1130	WaterSamples Test	24	0%																					
SVB-SI1135	Obtain Water Certificate and water supply connection - FS	4	0%																		0			
SVB-SI2000	Final Submission of Form FSI 314 / 501 to FSD	0	0%				1 1					1 1		1 1								•		

CONTRACT NO. HY2017/10

NORTHERN TUNNEL CONNECTION BUILDING E&M WORKS

THREE MONTHLY PROGRAMME AS OF 20 Jan 2020

18	Date	Revision	Checked	Approved
	20-Jan-20			
