## Landfill Gas Monitoring Results on Methane Level


Project	Works	Date(yyyy-mm-dd)	Monitoring Location	Time (hh:mm, 24hour)	Results (%)	Action Level (%)	Limit Level (%)
TMCLKL	HY/2017/10	2019/01/03	Toll Control Building	8:15	0		
TMCLKL	HY/2017/10	2019/01/03	Toll Control Building	13:15	0		
TMCLKL	HY/2017/10	2019/01/04	Toll Control Building	8:15	0		20.0
TMCLKL	HY/2017/10	2019/01/04	Toll Control Building	13:15	0		
TMCLKL	HY/2017/10	2019/01/05	Toll Control Building	8:15	0		
TMCLKL	HY/2017/10	2019/01/05	Toll Control Building	13:15	0	10.0	
TMCLKL	HY/2017/10	2019/01/07	Toll Control Building	8:15	0	10.0	
TMCLKL	HY/2017/10	2019/01/07	Toll Control Building	13:15	0		
TMCLKL	HY/2017/10	2019/01/08	Toll Control Building	8:15	0		
TMCLKL	HY/2017/10	2019/01/08	Toll Control Building	13:15	0		
TMCLKL	HY/2017/10	2019/01/09	Toll Control Building	8:15	0		
TMCLKL	HY/2017/10	2019/01/09	Toll Control Building	13:15	0		
•	-			Average	0		
				Min.	0		
				Max.	0		


## Landfill Gas Monitoring Results on Oxygen Level

Project	Works	Date(yyyy-mm-dd)	Station	Time (hh:mm, 24hour)	Results (%)	Action Level (%)	Limit Level (%)
TMCLKL	HY/2017/10	2019/01/03	Toll Control Building	8:15	20.8	19.0	18.0
TMCLKL	HY/2017/10	2019/01/03	Toll Control Building	13:15	20.7		
TMCLKL	HY/2017/10	2019/01/04	Toll Control Building	8:15	20.8		
TMCLKL	HY/2017/10	2019/01/04	Toll Control Building	13:15	20.8		
TMCLKL	HY/2017/10	2019/01/05	Toll Control Building	8:15	20.8		
TMCLKL	HY/2017/10	2019/01/05	Toll Control Building	13:15	20.8		
TMCLKL	HY/2017/10	2019/01/07	Toll Control Building	8:15	20.7		
TMCLKL	HY/2017/10	2019/01/07	Toll Control Building	13:15	20.8		
TMCLKL	HY/2017/10	2019/01/08	Toll Control Building	8:15	20.8		
TMCLKL	HY/2017/10	2019/01/08	Toll Control Building	13:15	20.8		
TMCLKL	HY/2017/10	2019/01/09	Toll Control Building	8:15	20.8		
TMCLKL	HY/2017/10	2019/01/09	Toll Control Building	13:15	20.8		
				Average	20.8		•
				Min.	20.8		
				Max.	20.8		

## Landfill Gas Monitoring Results on Carbon Dioxide Level


Project	Works	Date(yyyy-mm-dd)	Station	Time (hh:mm, 24hour)	Results (%)	Action Level (%)	Limit Level (%)
TMCLKL	HY/2017/10	2019/01/03	Toll Control Building	8:15	mon TMCLKL North T		
TMCLKL	HY/2017/10	2019/01/03	Toll Control Building	13:15	0		
TMCLKL	HY/2017/10	2019/01/04	Toll Control Building	8:15	0		
TMCLKL	HY/2017/10	2019/01/04	Toll Control Building	13:15	0		1.5
TMCLKL	HY/2017/10	2019/01/05	Toll Control Building	8:15	0		
TMCLKL	HY/2017/10	2019/01/05	Toll Control Building	13:15	0	0.5	
TMCLKL	HY/2017/10	2019/01/07	Toll Control Building	8:15	0	0.5	
TMCLKL	HY/2017/10	2019/01/07	Toll Control Building	13:15	0		
TMCLKL	HY/2017/10	2019/01/08	Toll Control Building	8:15	0		
TMCLKL	HY/2017/10	2019/01/08	Toll Control Building	13:15	0		
TMCLKL	HY/2017/10	2019/01/09	Toll Control Building	8:15	0		
TMCLKL	HY/2017/10	2019/01/09	Toll Control Building	13:15	0		
				Average	0		
				Min.	0		
				Max.	0		

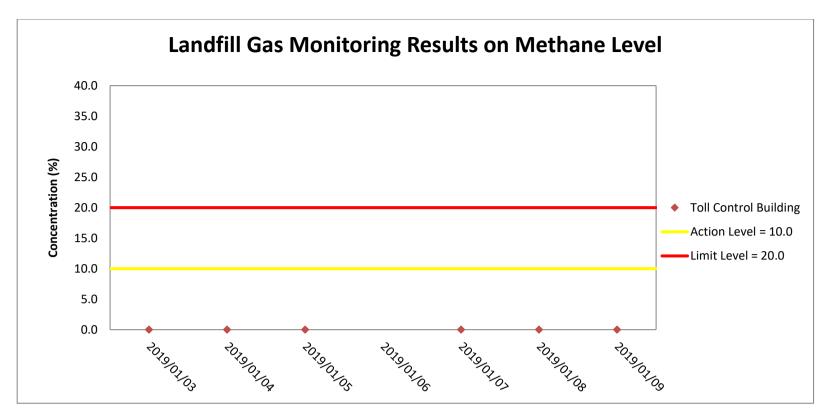

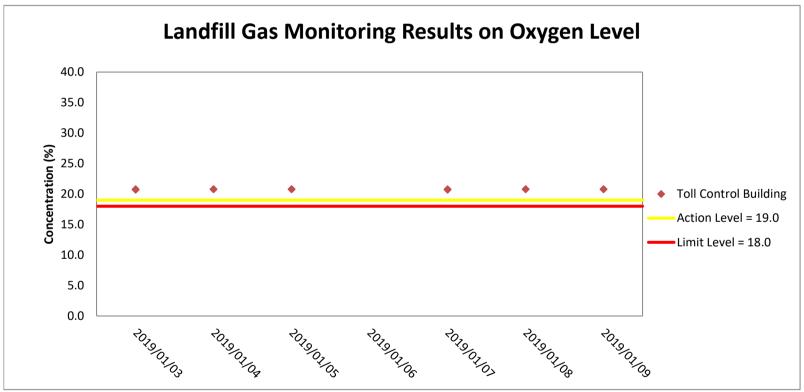

Weather condition within the reporting period was cloudy.

Major construction works undertaken within the reporting period include bar bending, timber formwork and concreting and Architectural Builder's Work and Finishes at Toll Control Building; electrical and Mechanical works at Ventilation Plant Room and North Ventilation Building, Building Structure at Administration Building and Maintenance Depot; Socket H-piling at Fire Services Department Building and Customs and Excise Department Building and Electrical and Mechanical Works and Architectural Builder's Work and Finishes at Kiosk N2.

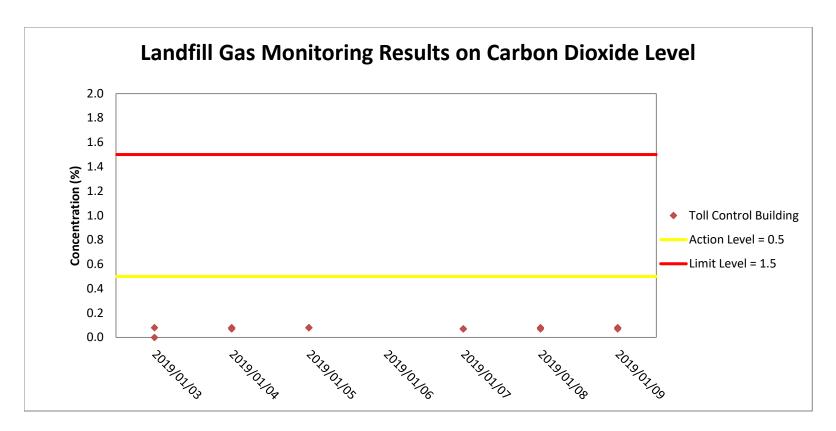

Weather condition within the reporting period was cloudy.

Major construction works undertaken within the reporting period include bar bending, timber formwork and concreting and Architectural Builder's Work and Finishes at Toll Control Building; electrical and Mechanical works at Ventilation Plant Room and North Ventilation Building, Building Structure at Administration Building and Maintenance Depot; Socket H-piling at Fire Services Department Building and Customs and Excise Department Building and Electrical and Mechanical Works and Architectural Builder's Work and Finishes at Kiosk N2.
