


Air Quality Monitoring Data

Project	Works	Date (yyyy-mm-dd)	Station	Time	Parameter	Results	Unit
HKLR	HY/2011/03	2020-03-04	AMS5	13:03	1-hr TSP	31	µg/m ³
HKLR	HY/2011/03	2020-03-04	AMS5	14:03	1-hr TSP	40	µg/m ³
HKLR	HY/2011/03	2020-03-04	AMS5	15:03	1-hr TSP	67	µg/m ³
HKLR	HY/2011/03	2020-03-10	AMS5	09:01	1-hr TSP	8	µg/m ³
HKLR	HY/2011/03	2020-03-10	AMS5	10:01	1-hr TSP	8	µg/m ³
HKLR	HY/2011/03	2020-03-10	AMS5	11:01	1-hr TSP	14	µg/m ³
HKLR	HY/2011/03	2020-03-16	AMS5	09:00	1-hr TSP	68	µg/m ³
HKLR	HY/2011/03	2020-03-16	AMS5	10:00	1-hr TSP	57	µg/m ³
HKLR	HY/2011/03	2020-03-16	AMS5	11:00	1-hr TSP	52	µg/m ³
HKLR	HY/2011/03	2020-03-20	AMS5	09:07	1-hr TSP	83	µg/m ³
HKLR	HY/2011/03	2020-03-20	AMS5	10:07	1-hr TSP	76	µg/m ³
HKLR	HY/2011/03	2020-03-20	AMS5	11:07	1-hr TSP	89	µg/m ³
HKLR	HY/2011/03	2020-03-26	AMS5	10:05	1-hr TSP	57	µg/m ³
HKLR	HY/2011/03	2020-03-26	AMS5	11:05	1-hr TSP	71	µg/m ³
HKLR	HY/2011/03	2020-03-26	AMS5	13:05	1-hr TSP	42	µg/m ³
HKLR	HY/2011/03	2020-03-31	AMS5	10:00	1-hr TSP	194	µg/m ³
HKLR	HY/2011/03	2020-03-31	AMS5	11:00	1-hr TSP	192	µg/m ³
HKLR	HY/2011/03	2020-03-31	AMS5	13:00	1-hr TSP	160	µg/m ³
HKLR	HY/2011/03	2020-03-03	AMS5	08:00	24-hr TSP	38	µg/m ³
HKLR	HY/2011/03	2020-03-09	AMS5	08:00	24-hr TSP	35	µg/m ³
HKLR	HY/2011/03	2020-03-13	AMS5	08:00	24-hr TSP	21	µg/m ³
HKLR	HY/2011/03	2020-03-19	AMS5	08:00	24-hr TSP	44	µg/m ³
HKLR	HY/2011/03	2020-03-25	AMS5	08:00	24-hr TSP	54	µg/m ³
HKLR	HY/2011/03	2020-03-30	AMS5	08:00	24-hr TSP	78	µg/m ³
HKLR	HY/2011/03	2020-03-04	AMS6	08:05	1-hr TSP	19	µg/m ³
HKLR	HY/2011/03	2020-03-04	AMS6	09:05	1-hr TSP	10	µg/m ³
HKLR	HY/2011/03	2020-03-04	AMS6	10:05	1-hr TSP	19	µg/m ³
HKLR	HY/2011/03	2020-03-10	AMS6	13:03	1-hr TSP	24	µg/m ³
HKLR	HY/2011/03	2020-03-10	AMS6	14:03	1-hr TSP	27	µg/m ³
HKLR	HY/2011/03	2020-03-10	AMS6	15:03	1-hr TSP	37	µg/m ³
HKLR	HY/2011/03	2020-03-16	AMS6	13:00	1-hr TSP	58	µg/m ³
HKLR	HY/2011/03	2020-03-16	AMS6	14:00	1-hr TSP	54	µg/m ³
HKLR	HY/2011/03	2020-03-16	AMS6	15:00	1-hr TSP	53	µg/m ³
HKLR	HY/2011/03	2020-03-20	AMS6	10:03	1-hr TSP	70	µg/m ³
HKLR	HY/2011/03	2020-03-20	AMS6	11:03	1-hr TSP	65	µg/m ³
HKLR	HY/2011/03	2020-03-20	AMS6	13:03	1-hr TSP	76	µg/m ³
HKLR	HY/2011/03	2020-03-26	AMS6	09:04	1-hr TSP	87	µg/m ³
HKLR	HY/2011/03	2020-03-26	AMS6	10:04	1-hr TSP	75	µg/m ³
HKLR	HY/2011/03	2020-03-26	AMS6	11:04	1-hr TSP	80	µg/m ³
HKLR	HY/2011/03	2020-03-31	AMS6	09:08	1-hr TSP	41	µg/m ³
HKLR	HY/2011/03	2020-03-31	AMS6	10:08	1-hr TSP	15	µg/m ³
HKLR	HY/2011/03	2020-03-31	AMS6	11:08	1-hr TSP	66	µg/m ³
HKLR	HY/2011/03	2020-03-03	AMS6	08:00	24-hr TSP	40	µg/m ³
HKLR	HY/2011/03	2020-03-09	AMS6	08:00	24-hr TSP	30	µg/m ³
HKLR	HY/2011/03	2020-03-13	AMS6	08:00	24-hr TSP	40	µg/m ³
HKLR	HY/2011/03	2020-03-19	AMS6	08:00	24-hr TSP	See Remark 1	µg/m ³
HKLR	HY/2011/03	2020-03-25	AMS6	09:33	24-hr TSP	46	µg/m ³
HKLR	HY/2011/03	2020-03-30	AMS6	08:00	24-hr TSP	81	µg/m ³

Remark:

1) Due to power failure and malfunction of High Volume Sampler (HVS) at AMS6 - Dragonair / CNAC (Group) Building (HKIA), 24-hr TSP monitoring on 19 March 2020 at AMS6 was cancelled. The HVS was repaired on 25 March 2020. The 24-hr TSP monitoring at AMS6 was resumed on 25 March 2020.


Graphical Plot of 1-hour TSP at AMS5 and AMS6

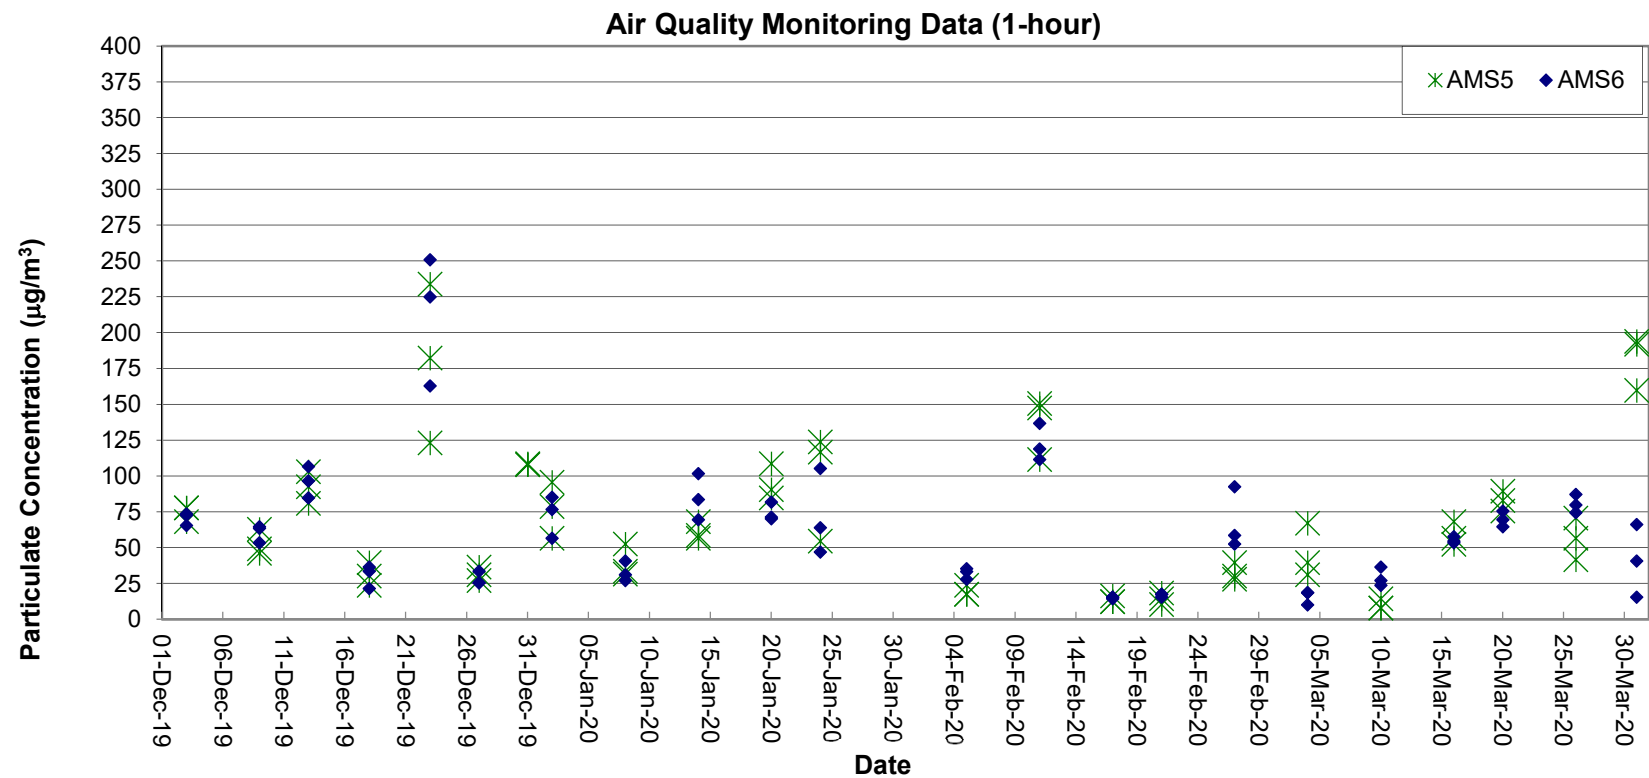

Remark:
1) There were no works for Contract No. HY/2011/03 between 25 January 2020 and 2 February 2020. As such, 1-hr TSP monitoring (which was scheduled on 30 January 2020) for stations AMS 5 and AMS 6 were suspended.

Graphical Plot of 24-hour TSP at AMS5 and AMS6

Air Quality Monitoring Data (24-hour)

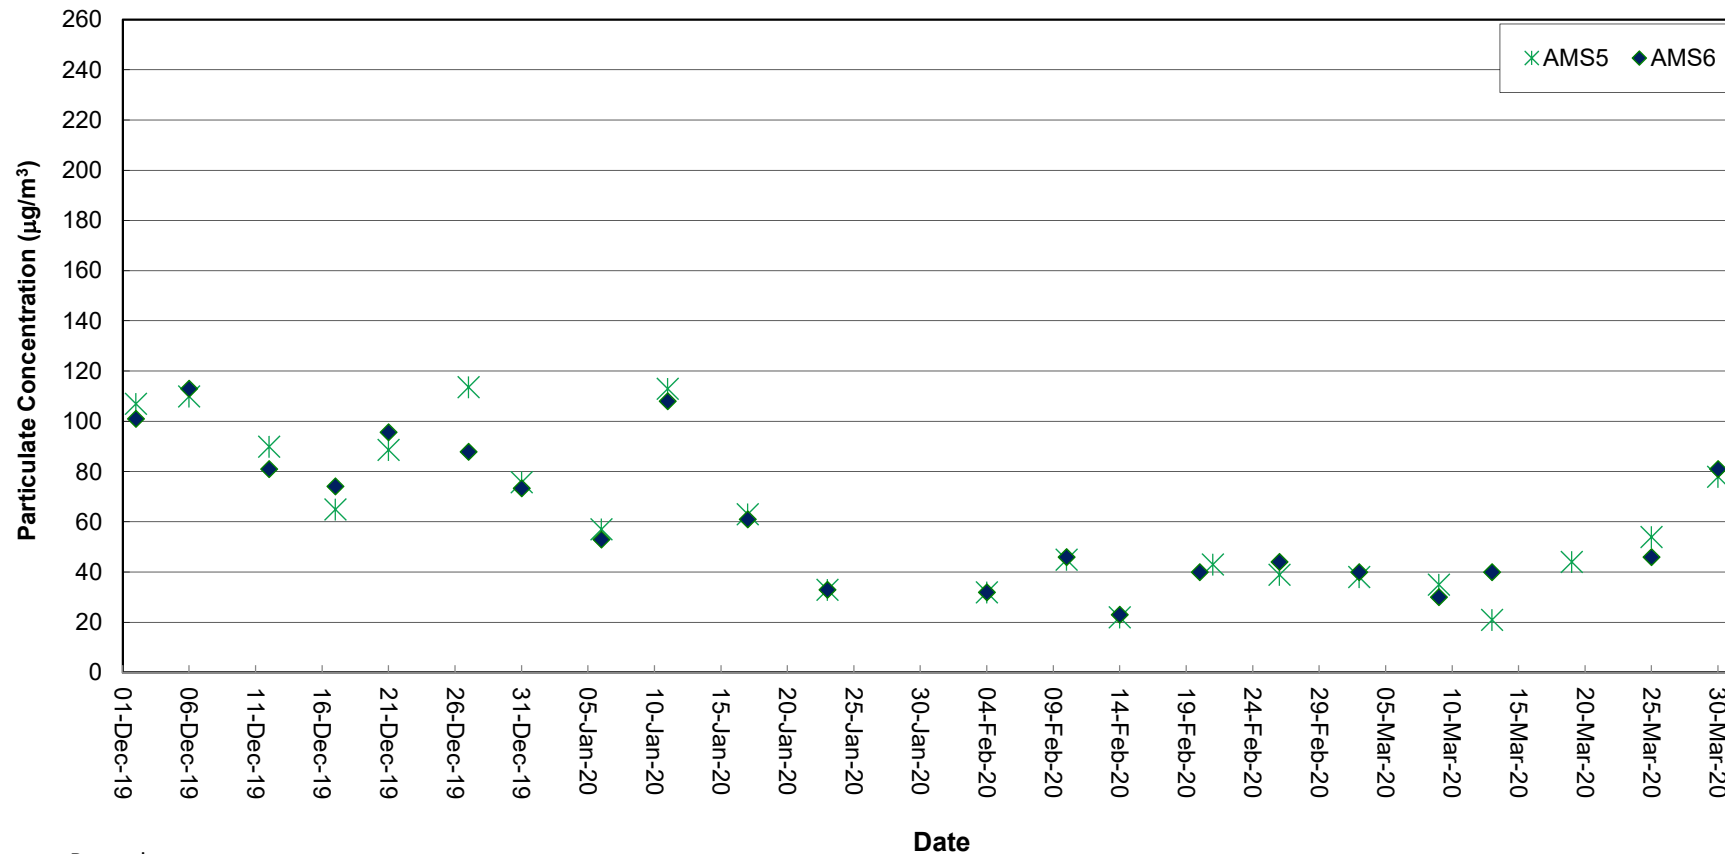

Remarks:


- 1) There were no works for Contract No. HY/2011/03 between 25 January 2020 and 2 February 2020. As such, 24-hr TSP monitoring (which was scheduled on 29 January 2020) for stations AMS 5 and AMS 6 were suspended.
- 2) Due to power failure, 24-hr TSP monitoring on 20 February 2020 at AMS5 (Ma Wan Chung Village) was rescheduled to 21 Feb 2020.
- 3) Due to power failure and malfunction of High Volume Sampler (HVS) at AMS6 - Dragonair / CNAC (Group) Building (HKIA), 24-hr TSP monitoring on 19 March 2020 at AMS6 was cancelled. The HVS was repaired on 25 March 2020. The 24-hr TSP monitoring at AMS6 was resumed on 25 March 2020.

Noise Monitoring Data

Project	Works	Date (yyyy-mm-dd)	Station	Start Time	Wind Speed, m/s	1st set 5mins		2nd set 5mins		3rd set 5mins		4th set 5mins		5th set 5mins		6th set 5mins		Overall (30mins)*		Unit
HKLR	HY/2011/03	2020-03-04	NMS5	14:03	<5	Leq:	52.3	Leq:	50.7	Leq:	50.4	Leq:	50.4	Leq:	55.3	Leq:	54.4	Leq:	56	dB(A)
						L10:	54.5	L10:	52.0	L10:	51.5	L10:	51.5	L10:	58.5	L10:	57.0	L10:	58	
						L90:	48.5	L90:	48.0	L90:	42.0	L90:	49.0	L90:	49.5	L90:	49.5	L90:	51	
HKLR	HY/2011/03	2020-03-10	NMS5	09:25	<5	Leq:	53.1	Leq:	54.6	Leq:	52.4	Leq:	54.1	Leq:	53.3	Leq:	53.0	Leq:	56	dB(A)
						L10:	54.0	L10:	56.5	L10:	53.0	L10:	54.5	L10:	54.5	L10:	54.0	L10:	58	
						L90:	52.0	L90:	51.5	L90:	50.5	L90:	51.5	L90:	51.0	L90:	51.0	L90:	54	
HKLR	HY/2011/03	2020-03-16	NMS5	09:10	<5	Leq:	52.9	Leq:	50.8	Leq:	51.5	Leq:	52.1	Leq:	52.1	Leq:	55.2	Leq:	56	dB(A)
						L10:	55.5	L10:	52.5	L10:	53.0	L10:	53.5	L10:	54.0	L10:	58.0	L10:	58	
						L90:	48.0	L90:	48.5	L90:	49.5	L90:	49.5	L90:	48.5	L90:	50.0	L90:	52	
HKLR	HY/2011/03	2020-03-26	NMS5	11:23	<5	Leq:	57.5	Leq:	57.4	Leq:	53.9	Leq:	53.5	Leq:	56.7	Leq:	56.9	Leq:	59	dB(A)
						L10:	60.0	L10:	59.0	L10:	55.0	L10:	55.5	L10:	57.0	L10:	60.5	L10:	61	
						L90:	49.5	L90:	50.5	L90:	51.0	L90:	50.5	L90:	49.0	L90:	48.5	L90:	53	
HKLR	HY/2011/03	2020-03-31	NMS5	10:14	<5	Leq:	51.2	Leq:	51.9	Leq:	53.8	Leq:	55.0	Leq:	53.4	Leq:	54.0	Leq:	56	dB(A)
						L10:	52.0	L10:	52.0	L10:	56.5	L10:	57.0	L10:	55.0	L10:	56.0	L10:	58	
						L90:	49.0	L90:	49.0	L90:	50.0	L90:	52.0	L90:	51.5	L90:	51.0	L90:	54	

(1)* A facade correction of +3 dB(A) was applied to the measured noise level.

Graphical Plot of Noise Levels at NMS5

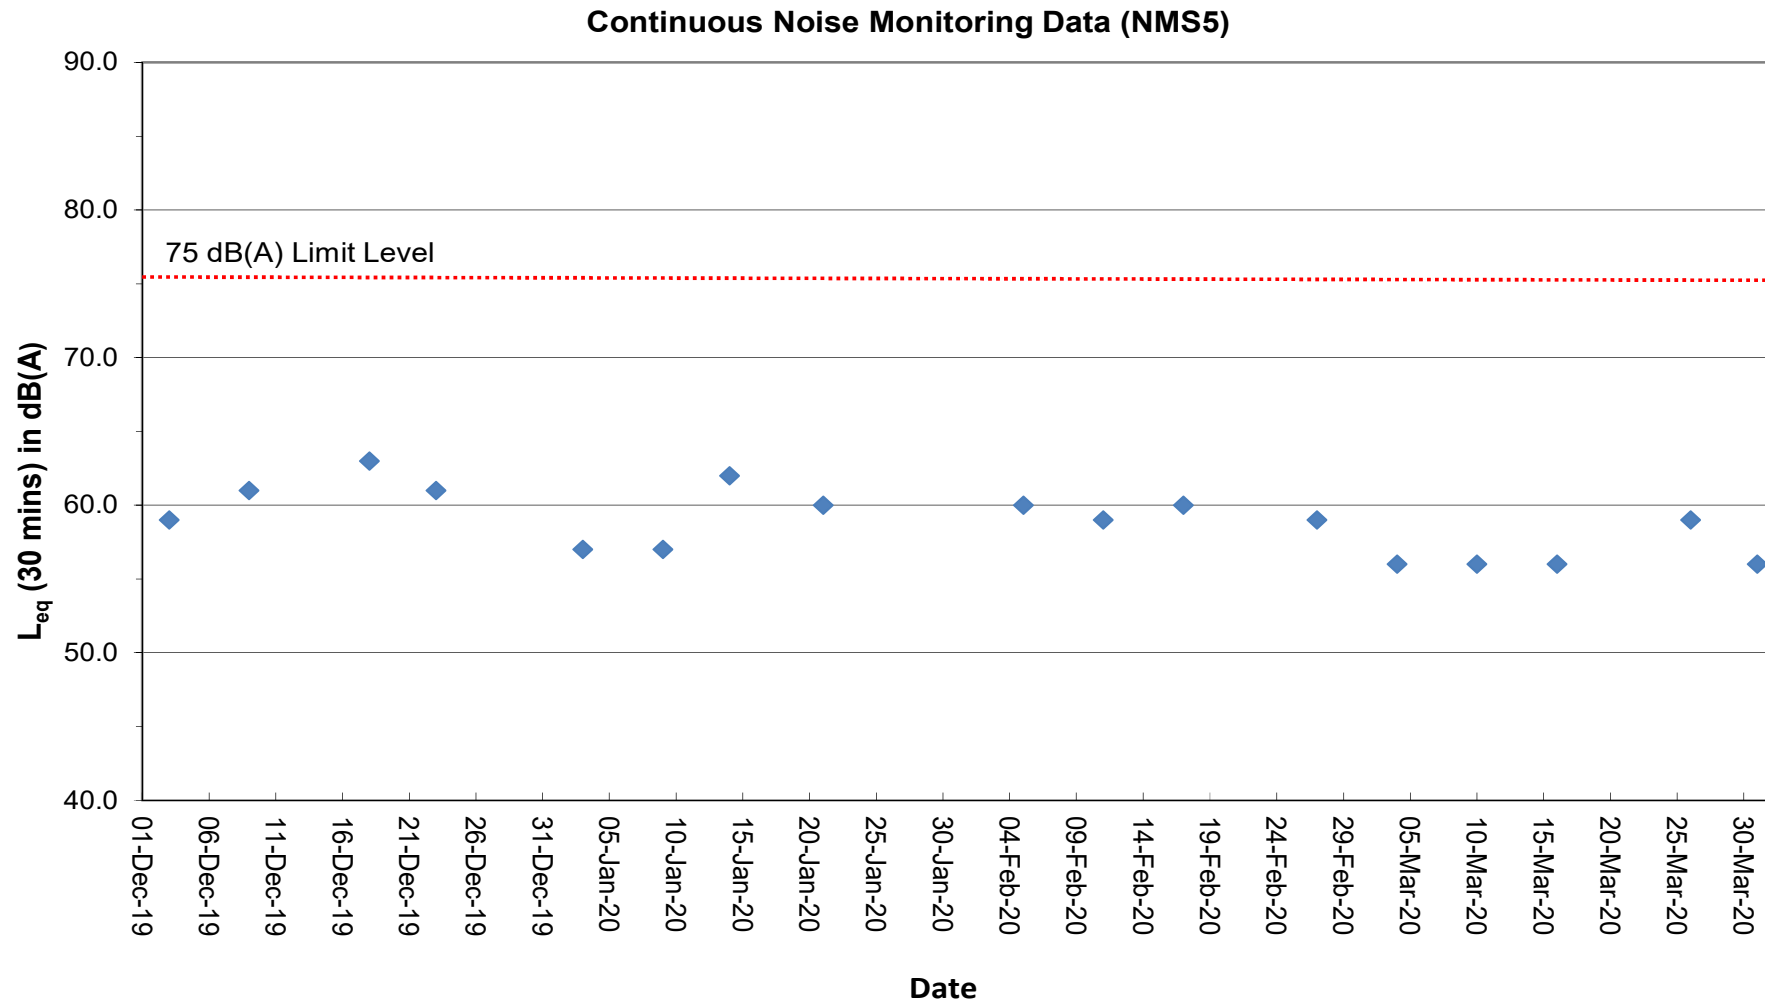

Remarks:

- (1) A facade correction of +3 dB(A) was applied to the measured noise level.
- (2) Due to resources arrangement, the noise monitoring at NMS5 was rescheduled from 2 January 2020 to 3 January 2020; from 8 January 2020 to 9 January 2020; and from 20 January 2020 to 21 January 2020.
- (3) There were no works for Contract No. HY/2011/03 between 25 January 2020 and 31 January 2020. As such, noise monitoring (which was scheduled on 30 January 2020) for station NMS5 were suspended.
