HKZMB HK Boundary Crossing Facilities - Phase 2 and Other Works

04-Mar-21

Activity Name	Start	Finish	% Completion
Revised Works Programme for HKZMB Phase 2 and Other Works (HY/2019/01)	20-Nov-19 A	31-Mar-23	37.59%
CONTRACT DATES	20-Nov-19 A	31-Mar-23	49.92%
SUBMISSIONS	04-Dec-19 A	03-Nov-21	0%
CONTRACTOR'S DESIGN	04-Dec-19 A	31-May-21	81.85%
BUILDING INFORMATION MODELING	02-Jan-20 A	30-Nov-21	62.45%
REFINEMENT WORKS AT HKP (4A)	04-Dec-19 A	30-Nov-21	60.64%
Installation of Vehicle Barrier Gate at Existing Vehicle Kiosks (4A.B)	03-Feb-20 A	30-Nov-21	56.92%
Provision of Security Measures at Existing Gate at South-west of PCB (4A.C) (KD2)	04-Dec-19 A	19-Jun-20 A	100%
Replacement of Recess Type Cover for Manhole/Drawpit/Catchpit (4A.E) (KD1)	04-Dec-19 A	21-Jun-20 A	100%
Installation of New Security Fence (4A.D)(KD3)	10-Dec-19 A	21-Jun-20 A	100%
Construction of Additional Drains at Vehicle Inspection Pit Near Building No. 023 (4A.K)	03-Jun-20 A	03-Aug-20 A	100%
Installation of Sliding Gate at Building No. 041 (4A.J)	04-Dec-19 A	28-Aug-21	70.16%
Painting for Volleyball Court	30-Apr-21	30-Jun-21	0%
SECTION 1: WORKS OF VERTICAL ACCESS TO THE ROOF OF PCB WITHIN PORTION A (4)	04-Dec-19 A	08-Feb-21 A	100%
SECTION 1A: IMPROVEMENT WORKS FOR THE EXISTING WATER FEATURES AT PCB WITHIN PORTION A (4.D-W)	04-Dec-19 A	20-Jun-20 A	100%
SECTION 1B: INSTALLATION OF WATERPROOF MEMBRANE FOR THE EXISTING WATER FEATURES (Omission PMI 10)	04-Dec-19 A	31-Jan-20 A	100%
SECTION 1C: INSTALLATION OF WATER SKIMMERS, SOLAR REFLECTIVE FILMS AND GLAZED DOORS	31-Jan-20 A	20-Jun-20 A	100%
SECTION 1D: INSTALLATION OF MINOR REMAINING WORKS AT PCB WITHIN PORTION A (4B)	04-Dec-19 A	30-Jun-20 A	100%
SECTION 2: IRRIGATION SYSTEM AT SLOPES OF NPTI WITHIN PORTION B (3)	04-Dec-19 A	31-Dec-21	58.04%
Design and Design Acceptance	04-Dec-19 A	31-May-21	66.67%
EMSD Comments on Automatic Irrigation System at SIMAR Slope of NPTI - NEC No. 120	18-Nov-20 A	03-Aug-21	49.51%
Irrigation System at Slopes of NPTI within Portion B	04-Aug-21	31-Dec-21	0%
SECTION 2A: BUILDING NO. 062 - GENERATOR AND UPS ROOM WITHIN PORTION C (4A.L)	04-Dec-19 A	16-Dec-20 A	100%
SECTION 3: NPTI - PUBLIC TOILET, COVERED WALKWAY & PAVEMENT (6)	04-Dec-19 A	30-Jul-21	73.74%
Erection of Hoarding	04-Dec-19 A	30-May-20 A	100%
Additional and Modification to Existing Covered Walkway, Area 1 - 6 (6.E)	04-Dec-19 A	03-Jul-21	77.41%
Additional & Modification of Covered Walkway adjacent to Building 003, Area 7 (6.C)	04-Dec-19 A	14-Jul-21	75.89%
Public Toilet Type 1, Building 003 (6.B)	20-May-20 A	29-Jul-21	73.87%
Additional Railing adjacent to Building 003 (6.D)	09-Jun-21	30-Jun-21	0%
Drainage, Pavement, Kerbing, Lighting, Marking and Signs (6.F)	03-Sep-20 A	30-Jul-21	50%
Completion of Section 3	30-Jul-21	30-Jul-21	0%
SECTION 4: REMOVAL OF WATERMAIN AT THE SKYCITY INTERCHANGE WITHIN PORTION C AND D	04-Dec-19 A	22-Nov-21	61.35%
SECTION 5: REMAINING WORKS	04-Dec-19 A	01-Dec-22	39.68%
Erection of Hoarding	13-Feb-20 A	31-Mar-20 A	100%
External Works at Plaza	23-Mar-20 A	03-Dec-21	52.31%
Design, Design Acceptance & Procurement for Kiosks	03-Apr-20 A	16-Dec-20 A	100%
Inbound: 11 No. of Private Car Kiosks between 027/028	23-Mar-20 A	01-Dec-22	34.05%
Builder Works (5.A)	23-Mar-20 A	01-Mar-22	47.61%
E&M Works	03-Oct-20 A	01-Dec-22	29.97%
Outbound: 11 No. of Private Car Kiosks between 029/030	03-Apr-20 A	29-Nov-22	34.14%
Builder's Works (5.A)	03-Apr-20 A	26-Feb-22	47.78%
E&M Works	03-Oct-20 A	29-Nov-22	27.72%
Drainage & Pavement Works at Kiosks (Inbound & Outbound)	16-May-20 A	30-Jun-21	61.2%
Observation Guard Booths, Building 002	04-Dec-19 A	13-Jul-21	76%
Observation Guard Booths, Building 002-2 (Deleted by PMI-13)	18-Feb-20 A	18-Feb-20 A	100%
SPTI Stage 1A & 1D	29-Feb-20 A	12-Nov-20 A	100%
SPTI Stage 2	13-Nov-20 A	18-Nov-20 A	100%
SPTI Stage 2A	02-Oct-20 A	16-Feb-21 A	100%
SPTI Stage 3	23-Feb-21 A	25-Jun-21	0%
SPTI Stage 3A	26-Jun-21	02-Nov-21	0%
SPTI Stage 3B	03-Nov-21	05-Mar-22	0%
SPTI Stage 3C	07-Mar-22	31-Mar-22	0%
Pump House for Landscape (2)	04-Dec-19 A	15-Nov-21	61.98%
Landscape Works (2)	04-Dec-19 A	30-Nov-21	60.64%
Irrigation System (Southern Portion)	04-Dec-19 A	30-Nov-21	60.64%
Design and Design Acceptance	04-Dec-19 A	29-Apr-21	88.31%
Irrigation System at Southern Portion	02-Jan-21 A	30-Nov-21	17.34%
Irrigation System (Water Point)	04-Dec-19 A	30-Nov-21	60.64%
Completion of Section 5	31-Mar-22	31-Mar-22	0%
SECTION 6: ESTABLISHMENT WORKS	01-Apr-22	31-Mar-23	0%

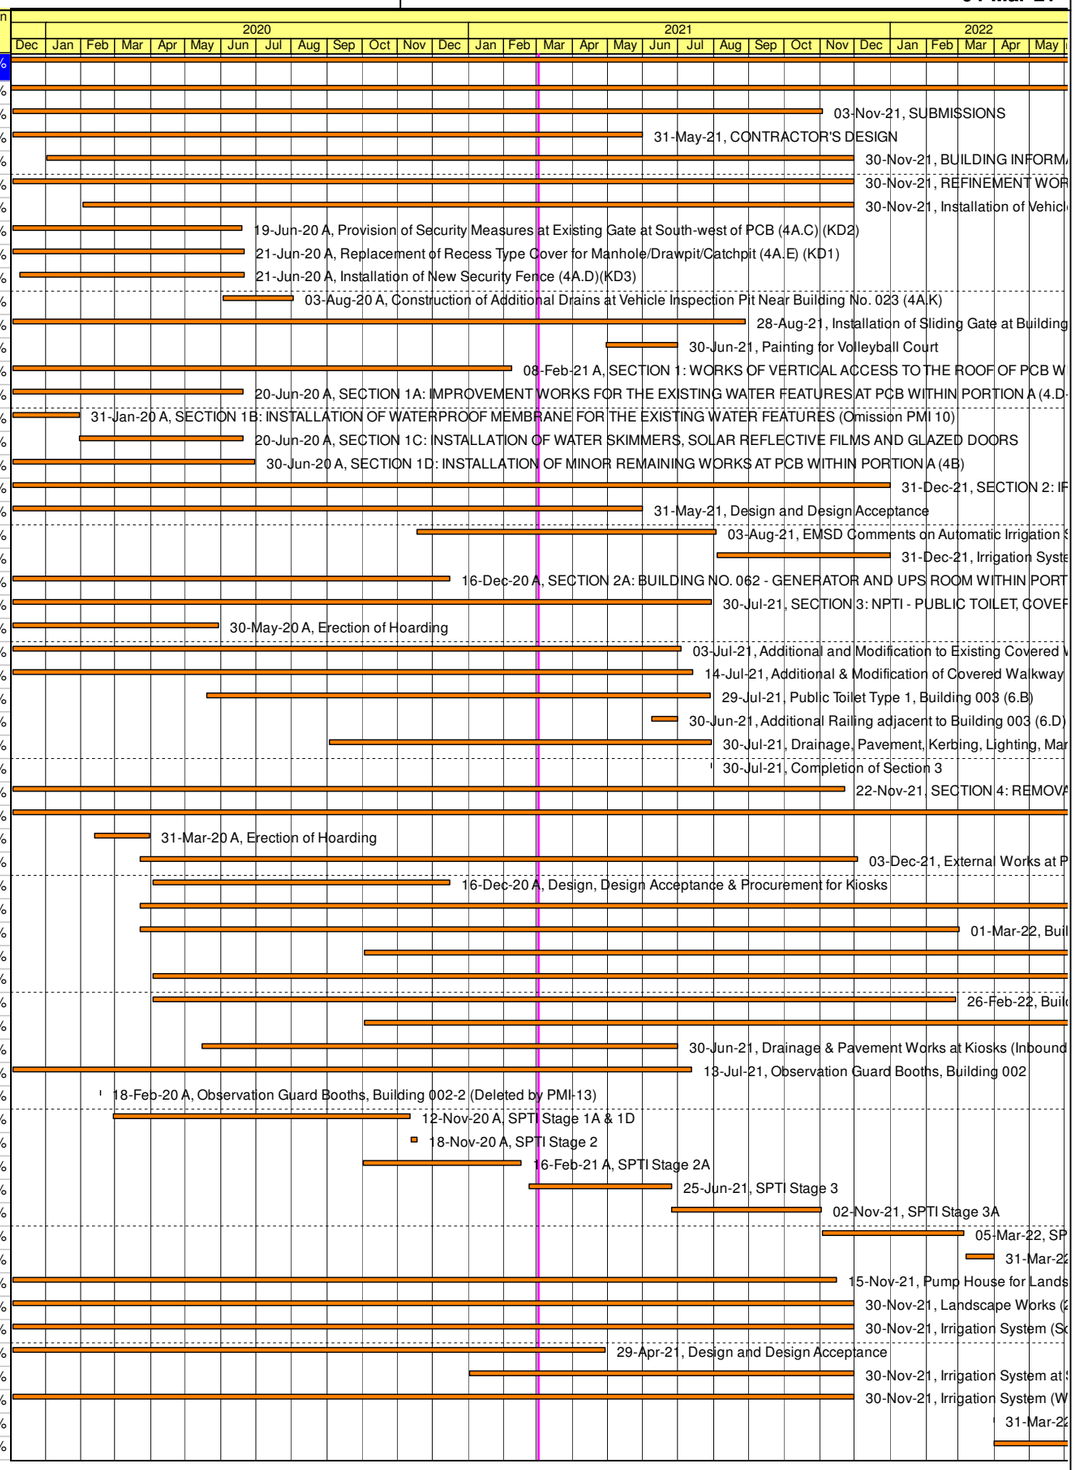

◆ Milestone

Summary

EXECUTIVE SUMMARY PROGRAMME FOR PHASE 2 AND OTHER WORKS
HKZMB - HONG KONG BOUNDARY CROSSING FACILITIES

Date	Revision	Checked	Approved
04-Mar-21	Works Programme for Phase 2	ZJ	
