路政署
HIGHWAYS DEPARTMENT
港珠澳大橋香港工程管理處
Hong Kong - Zhuhai - Macao Bridge
Hong Kong Project Management Office

Contract No. HY/2011/03

Hong Kong-Zhuhai-Macao Bridge Hong Kong Link Road Section between Scenic Hill and Hong Kong Boundary Crossing Facilities

Quarterly EM&A Report No. 51 (March 2025 to May 2025)

22 July 2025

Revision 0

Main Contractor

中國建築工程(香港)有限公司
CHINA STATE CONSTRUCTION ENGINEERING (HONG KONG) LTD.

Designer

ATKINS
Member of the SNC-Lavalin Group

Contents

Executive Summary

1 Introduction 1

1.1 Basic Project Information 1
1.2 Project Organisation 1
1.3 Construction Programme 2
1.4 Construction Works Undertaken During the Reporting Period 2

2 EM&A Requirement 3

2.1 Summary of EM&A Requirements 3
2.2 Action and Limit Levels 4
2.3 Event Action Plans 5
2.4 Mitigation Measures 5

3 Environmental Monitoring and Audit 6

3.1 Implementation of Environmental Measures 6
3.2 Air Quality Monitoring Results 6
3.3 Noise Monitoring Results 7
3.4 Water Quality Monitoring Results 7
3.5 Dolphin Monitoring Results 8
3.6 Mudflat Monitoring Results 15
3.7 Solid and Liquid Waste Management Status 34
3.8 Environmental Licenses and Permits 34

4 Environmental Complaint and Non-compliance 35

4.1 Environmental Exceedances 35
4.2 Summary of Environmental Complaint, Notification of Summons and Successful Prosecution 36

5 Comments, Recommendations and Conclusion 36

5.1 Comments 36
5.2 Recommendations 36
5.3 Conclusions 36

Figures

Figure 1.1 Location of the Site
Figure 2.1 Environmental Monitoring Stations
Figure 2.2 Transect Line Layout in Northwest and Northeast Lantau Survey Areas

Appendices

Appendix A Environmental Management Structure
Appendix B Construction Programme
Appendix C Location of Works Areas
Appendix D Event and Action Plan
Appendix E Implementation Schedule of Environmental Mitigation Measures
Appendix F Site Audit Findings and Corrective Actions
Appendix G Air Quality Monitoring Data and Graphical Plots
Appendix H Noise Monitoring Data and Graphical Plots
Appendix O Water Quality Monitoring Data and Graphical Plots
Appendix J Dolphin Monitoring Results
Appendix K Waste Flow Table
Appendix L Summary of Environmental Licenses and Permits
Appendix M Record of "Notification of Environmental Quality Limit Exceedances" and Record of "Notification of Summons and Prosecutions"
Appendix N Cumulative Statistics on Complaints
Appendix O Mudflat Monitoring Results

Executive Summary

The Hong Kong-Zhuhai-Macao Bridge (HZMB) Hong Kong Link Road (HKLR) serves to connect the HZMB Main Bridge at the Hong Kong Special Administrative Region (HKSAR) Boundary and the HZMB Hong Kong Boundary Crossing Facilities (HKBCF) located at the north eastern waters of the Hong Kong International Airport (HKIA).

The HKLR project has been separated into two contracts. They are Contract No. HY/2011/03 Hong Kong-Zhuhai-Macao Bridge Hong Kong Link Road-Section between Scenic Hill and Hong Kong Boundary Crossing Facilities (hereafter referred to as the Contract) and Contract No. HY/2011/09 Hong Kong-Zhuhai-Macao Bridge Hong Kong Link Road-Section between HKSAR Boundary and Scenic Hill.

China State Construction Engineering (Hong Kong) Ltd. was awarded by Highways Department as the Contractor to undertake the construction works of Contract No. HY/2011/03. The main works of the Contract include land tunnel at Scenic Hill, tunnel underneath Airport Road and Airport Express Line, reclamation and tunnel to the east coast of the Airport Island, at-grade road connecting to the HKBCF and highway works of the HKBCF within the Airport Island and in the vicinity of the HKLR reclamation. The Contract is part of the HKLR Project and HKBCF Project, these projects are considered to be "Designated Projects", under Schedule 2 of the Environmental Impact Assessment (EIA) Ordinance (Cap 499) and EIA Reports (Register No. AEIAR-144/2009 and AEIAR-145/2009) were prepared for the Project. The current Environmental Permit (EP) EP-352/2009/D for HKLR and EP-353/2009/K for HKBCF were issued on 22 December 2014 and 11 April 2016, respectively. These documents are available through the EIA Ordinance Register. The construction phase of Contract was commenced on 17 October 2012.

BMT Hong Kong Limited was appointed by the Contractor to implement the Environmental Monitoring & Audit (EM&A) programme for the Contract in accordance with the Updated EM&A Manual for HKLR (Version 1.0) and provided environmental team services to the Contract until 31 July 2020.

Meinhardt Infrastructure and Environment Limited has been appointed by the Contractor to implement the Environmental Monitoring & Audit (EM&A) programme for the Contract in accordance with the Updated EM&A Manual for HKLR (Version 1.0) and provide environmental team services to the Contract with effective from 1 August 2020.

Ramboll Hong Kong Limited was employed by HyD as the Independent Environmental Checker (IEC) and Environmental Project Office (ENPO) for the Project until 30 September 2022.

ANewR Consulting Limited has been employed by HyD as the Independent Environmental Checker (IEC) and Environmental Project Office (ENPO) for the Project with effective from 1 October 2022.

This is the fifty-first Quarterly EM&A report for the Contract which summarizes the monitoring results and audit findings of the EM&A programme during the reporting period from 1 March 2025 to 31 May 2025.

Environmental Monitoring and Audit Progress

The EM&A programme were undertaken in accordance with the Updated EM&A Manual for HKLR (Version 1.0). A summary of the monitoring activities during this reporting period is presented as below:

Monitoring Activity		Monitoring Date		
		March 2025	**April 2025**	**May 2025**
Air Quality	1-hr TSP at AMS5	3, 7, 13, 19, 25 and 31	3, 9, 14, 17, 23 and 28	2, 8, 14, 20, 26 and 30
	1-hr TSP at AMS6	3, 7, 13, 19, 25 and 31	3, 9, 14, 17, 23 and 28	2, 8, 14, 20, 26 and 30
	24-hr TSP at AMS5	6, 12, 18, 24 and 28	2, 8, 11, 16, 22 and 28	1, 7, 13, 19, 23 and 29
	24-hr TSP at AMS6	6, 12, 18, 24 and 28	10, 11, 16, 22 and 28	1, 7, 13, 19, 23 and 29

Monitoring Activity	Monitoring Date		
	March 2025	April 2025	May 2025
Noise	3, 13, 19, 25 and 31	9, 14, 23 and 29	7, 14, 20 and 26
Water Quality	3, 5, 7, 10, 12, 14, 17, 19, 21, 24, 26, 28 and 31	2, 4, 7, 9, 11, 14, 16, 18, 21, 23, 25, 28 and 30	2, 5, 7, 9, 12, 14, 16, 19, 21, 23, 26, 28 and 30
Chinese White Dolphin	11, 12, 14, and 18	23, 24, 25 and 26 May	28, 29, 30 and 31
Mudflat Monitoring (Ecology)	3, 4	-	-
Mudflat Monitoring (Sedimentation rate)	28	-	-
Site Inspection	5, 12, 19 and 28	2, 9, 17, 25 and 30	7, 14, 21 and 30

Remarks:

1) The existing air quality monitoring location AMS6 – Dragonair / CNAC (Group)Building (HKIA) was handed over to Airport Authority Hong Kong on 31 March 2021. 1-hr and 24-hr TSP monitoring at AMS6 was temporarily suspended starting from 1 April 2021 and resumed on 7 August 2024.
2) With the unexpected departure of the original dolphin specialist in late-March 2025, a new replacement was appointed in May 2025. The dolphin monitoring for April 2025 was re-scheduled to 23, 24, 25 and 26 May 2025.

The access to the WQM station SR4(N2) (Coordinate: E814688, N817996) is being blocked by the silt curtains of the Tung Chung New Town Extension (TCNTE) project. Water quality monitoring has been temporarily conducted at alternative stations, namely SR4(N3) (Coordinate: E814779, N818032) until 1 March 2023. Proposal for permanently relocating the SR4(N2) was approved by EPD on 3 March 2023. The water quality monitoring has been conducted at stations SR4(N3) since 3 March 2023.

Breaches of Action and Limit Levels

A summary of environmental exceedances for this reporting period is as follows:

Environmental Monitoring	Parameters	Action Level (AL)	Limit Level (LL)
Air Quality	1-hr TSP	0	0
	24-hr TSP	1	0
Noise	$L_{eq\ (30\ min)}$	0	0
Water Quality	Suspended solids level (SS)	0	0
	Turbidity level	0	0
	Dissolved oxygen level (DO)	0	0
Dolphin Monitoring	Quarterly Analysis (March 2025 to May 2025)	0	1

The Environmental Team investigated all exceedance and found that they were not project related.

All investigation report for exceedance of the Contract has been submitted to ENPO/IEC for comments and/or follow up to identify whether the exceedances occurred related to other HZMB contracts.

Implementation of Mitigation Measures

Site inspections were carried out to monitor the implementation of proper environmental pollution control and mitigation measures for the Project. Potential environmental impacts due to the construction activities were monitored and reviewed.

Complaint Log

There was no complaints received in relation to the environmental impacts during this reporting period.

Notifications of Summons and Prosecutions

There were no notifications of summons or prosecutions received during this reporting period.

Reporting Changes

This report has been developed in compliance with the reporting requirements for the subsequent EM&A reports as required by the Updated EM&A Manual for HKLR (Version 1.0).

The proposal for the change of Action Level and Limit Level for suspended solid and turbidity was approved by EPD on 25 March 2013.

The revised Event and Action Plan for dolphin monitoring was approved by EPD on 6 May 2013.

The original monitoring station at IS(Mf)9 (Coordinate: 813273E, 818850N) was observed inside the perimeter silt curtain of Contract HY/2010/02 on 1 July 2013, as such the original impact water quality monitoring location at IS(Mf)9 was temporarily shifted outside the silt curtain. As advised by the Contractor of HY/2010/02 in August 2013, the perimeter silt curtain was shifted to facilitate safe anchorage zone of construction barges/vessels until end of 2013 subject to construction progress. Therefore, water quality monitoring station IS(Mf)9 was shifted to 813226E and 818708N since 1 July 2013. According to the water quality monitoring team's observation on 24 March 2014, the original monitoring location of IS(Mf)9 was no longer enclosed by the perimeter silt curtain of Contract HY/2010/02. Thus, the impact water quality monitoring works at the original monitoring location of IS(Mf)9 has been resumed since 24 March 2014.

Transect lines 1, 2, 7, 8, 9 and 11 for dolphin monitoring have been revised due to the obstruction of the permanent structures associated with the construction works of HKLR and the southern viaduct of TM-CLKL, as well as provision of adequate buffer distance from the Airport Restricted Areas. The EPD issued a memo and confirmed that they had no objection on the revised transect lines on 19 August 2015.

The water quality monitoring stations at IS10 (Coordinate: 812577E, 820670N) and SR5 (811489E, 820455N) are located inside Hong Kong International Airport (HKIA) Approach Restricted Areas. The previously granted Vessel's Entry Permit for accessing stations IS10 and SR5 were expired on 31 December 2016. During the permit renewing process, the water quality monitoring location was shifted to IS10(N) (Coordinate: 813060E, 820540N) and SR5(N) (Coordinate: 811430E, 820978N) on 2, 4 and 6 January 2017 temporarily. The permit has been granted by Marine Department on 6 January 2017. Thus, the impact water quality monitoring works at original monitoring location of IS10 and SR5 has been resumed since 9 January 2017.

Transect lines 2, 3, 4, 5, 6 and 7 for dolphin monitoring have been revised and transect line 24 has been added due to the presence of a work zone to the north of the airport platform with intense construction activities in association with the construction of the third runway expansion for the Hong Kong International Airport. The EPD issued a memo and confirmed that they had no objection on the revised transect lines on 28 July 2017. The alternative dolphin transect lines are adopted starting from August's dolphin monitoring.

A new water quality monitoring team has been employed for carrying out water quality monitoring work for the Contract starting from 23 August 2017. Due to marine work of the Expansion of Hong Kong International Airport into a Three-Runway System (3RS Project), original locations of water quality monitoring stations CS2, SR5 and IS10 are enclosed by works boundary of 3RS Project. Alternative impact water quality monitoring stations, naming as CS2(A), SR5(N) and IS10(N) was approved on 28 July 2017 and were adopted starting from 23 August 2017 to replace the original locations of water quality monitoring for the Contract.

The role and responsibilities as the ET Leader of the Contract was temporarily taken up by Mr Willie Wong instead of Ms Claudine Lee from 25 September 2017 to 31 December 2017.

The topographical condition of the water monitoring stations SR3 (Coordinate: 810525E, 816456N), SR4 (Coordinate: 814760E, 817867N), SR10A (Coordinate: 823741E, 823495N) and SR10B (Coordinate: 823686E, 823213N) cannot be accessed safely for undertaking water quality monitoring. The water quality monitoring has been temporarily conducted at alternative stations, namely SR3(N) (Coordinate 810689E, 816591N), SR4(N) (Coordinate: 814705E, 817859N) and SR10A(N) (Coordinate: 823644E, 823484N) since 1 September 2017. The water quality monitoring at station SR10B was temporarily conducted at Coordinate: 823683E, 823187N on 1, 4, 6, 8 September 2017 and has been temporarily fine-tuned to alternative station SR10B(N2) (Coordinate: 823689E, 823159N) since 11 September 2017. Proposal for permanently relocating the aforementioned stations was approved by EPD on 8 January 2018.

The works area WA5 was handed over to other party on 22 June 2013.

According to latest information received in July 2018, the works area WA7 was handed over to other party on 28 February 2018 instead of 31 January 2018.

Original WQM stations IS8 and SR4(N) are located within the active work area of TCNTE project and the access to the WQM stations IS8 (Coordinate: E814251, N818412) and SR4(N) (Coordinate: E814705, N817859) are blocked by the silt curtains of the Tung Chung New Town Extension (TCNTE) project. Alternative monitoring stations IS8(N) (Coordinate: E814413, N818570) and SR4(N2) (Coordinate: E814688, N817996) are proposed to replace the original monitoring stations IS8 and SR4(N). Proposal for permanently relocating the aforementioned stations was approved by EPD on 20 August 2019. The water quality monitoring has been conducted at stations IS8(N) and SR4(N2) on 21 August 2019.

There were no marine works conducted by Contract No. HY/2011/03 since July 2019. A proposal for temporary suspension of marine related environmental monitoring (water quality monitoring and dolphin monitoring for the Contract No. HY/2011/03) was justified by the ET leader and verified by IEC in mid of September 2019 and it was approved by EPD on 24 September 2019. Water quality monitoring and dolphin monitoring for the Contract will not be conducted starting from 1 October 2019 until marine works (i.e. toe loading removal works) be resumed. As discussed with Contract No. HY/2012/08, they will take up the responsibility from Contract No. HY/2011/03 for the dolphin monitoring works starting from 1 October 2019.

According to information received in January 2020, the works area WA3 and WA4 were handed over to Highways Department on 23 December 2019 and 14 March 2019 respectively.

The role and responsibilities as the IEC of the Contract has been taken up by Mr. Manson Yeung instead of Mr. Ray Yan since 18 May 2020.

Mr. Leslie Leung was Environmental Team Leader of the Contract for July 2020. The role and responsibilities as the Environmental Team Leader of the Contract has been taken up by Ms. Claudine Lee with effective from 1 August 2020.

The existing air quality monitoring location AMS6 – Dragonair / CNAC (Group) Building (HKIA) was handed over to Airport Authority Hong Kong on 31 March 2021. 1-hr and 24-hr air quality monitoring at AMS6 was temporarily suspended starting from 1 April 2021 and resumed on 7 August 2024. Average flow rate is used for calculation of 24-hr air quality results of AMS6 in August 2024 due to unstable electricity supply on site.

The role and responsibilities as the IEC of the Contract has been taken up by Mr Brian Tam instead of Mr Manson Yeung since 12 April 2021. The role and responsibilities as the IEC of the Contract has been taken up by Mr Adi Lee instead of Mr Brian Tam since 3 May 2022. The role and responsibilities as the IEC of the Contract has been taken up by Mr Brian Tam instead of Mr Adi Lee since 25 July 2022.

The role and responsibilities as the ENPO Leader of the Contract has been taken up by Mr Louis Kwan from ANewR Consulting Limited instead of Mr H.Y. Hui from Ramboll Hong Kong Limited Since 1 October 2022. The role and responsibilities as the IEC of the Contract has been taken up by Mr James Choi from ANewR Consulting Limited instead of Mr Brian Tam from Ramboll Hong Kong Limited since 1 October 2022.

1 Introduction

1.1 Basic Project Information

1.1.1 The Hong Kong-Zhuhai-Macao Bridge (HZMB) Hong Kong Link Road (HKLR) serves to connect the HZMB Main Bridge at the Hong Kong Special Administrative Region (HKSAR) Boundary and the HZMB Hong Kong Boundary Crossing Facilities (HKBCF) located at the north eastern waters of the Hong Kong International Airport (HKIA).

1.1.2 The HKLR project has been separated into two contracts. They are Contract No. HY/2011/03 Hong Kong-Zhuhai-Macao Bridge Hong Kong Link Road-Section between Scenic Hill and Hong Kong Boundary Crossing Facilities (hereafter referred to as the Contract) and Contract No. HY/2011/09 Hong Kong-Zhuhai-Macao Bridge Hong Kong Link Road-Section between HKSAR Boundary and Scenic Hill.

1.1.3 China State Construction Engineering (Hong Kong) Ltd. was awarded by Highways Department (HyD) as the Contractor to undertake the construction works of Contract No. HY/2011/03. The Contract is part of the HKLR Project and HKBCF Project, these projects are considered to be "Designated Projects", under Schedule 2 of the Environmental Impact Assessment (EIA) Ordinance (Cap 499) and EIA Reports (Register No. AEIAR-144/2009 and AEIAR-145/2009) were prepared for the Project. The current Environmental Permit (EP) EP-352/2009/D for HKLR and EP-353/2009/K for HKBCF were issued on 22 December 2014 and 11 April 2016, respectively. These documents are available through the EIA Ordinance Register. The construction phase of Contract was commenced on 17 October 2012. The works area WA5 and WA7 were handed over to other party on 22 June 2013 and 28 February 2018 respectively. The works area WA3 and WA4 were handed over to Highways Department on 23 December 2019 and 14 March 2019 respectively. **Figure 1.1** shows the project site boundary. The works areas are shown in **Appendix C**.

1.1.4 BMT Hong Kong Limited was appointed by the Contractor to implement the EM&A programme for the Contract in accordance with the Updated EM&A Manual for HKLR (Version 1.0) and provided environmental team services to the Contract until 31 July 2020.

1.1.5 Meinhardt Infrastructure and Environment Limited has been appointed by the Contractor to implement the Environmental Monitoring & Audit (EM&A) programme for the Contract in accordance with the Updated EM&A Manual for HKLR (Version 1.0) and provide environmental team services to the Contract with effective from 1 August 2020. Ramboll Hong Kong Limited was employed by HyD as the Independent Environmental Checker (IEC) and Environmental Project Office (ENPO) for the Project until 30 September 2022. ANewR Consulting Limited has been appointed by HyD as the Independent Environmental Checker (IEC) and Environmental Project Office (ENPO) for the Project since 1 October 2022. The project organization with regard to the environmental works is provided in **Appendix A**.

1.1.6 This is the fifty-first Quarterly Environmental Monitoring and Audit (EM&A) report for the Contract which summarizes the monitoring results and audit findings of the EM&A programme during the reporting period from 1 March 2025 to 31 May 2025.

1.2 Project Organisation

1.2.1 The project organization structure and lines of communication with respect to the on-site environmental management structure with the key personnel contact names and numbers are shown in **Appendix A**.

1.3 Construction Programme

1.3.1 A copy of the Contractor's construction programme is provided in **Appendix B**.

1.4 Construction Works Undertaken During the Reporting Period

1.4.1 A summary of the construction activities undertaken during this reporting period is shown in **Table 1.1.** The works areas of the Contract are showed in **Appendix C**.

Table 1.1 Construction Activities during Reporting Period

Description of Activities	Site Area
Reinstatement Works	Portion X

2 EM&A Requirement

2.1 Summary of EM&A Requirements

2.1.1 The EM&A programme requires environmental monitoring of air quality, noise, water quality, dolphin monitoring and mudflat monitoring as specified in the approved EM&A Manual.

2.1.2 A summary of Impact EM&A requirements is presented in **Table 2.1**. The locations of air quality, noise and water quality monitoring stations are shown as in **Figure 2.1**. The transect line layout in Northwest and Northeast Lantau Survey Areas is presented in **Figure 2.2**.

Table 2.1 Summary of Impact EM&A Requirements

Environmental Monitoring	Description	Monitoring Station	Frequencies	Remarks
Air Quality	1-hr TSP	AMS 5 & AMS 6	At least 3 times every 6 days	While the highest dust impact was expected.
	24-hr TSP		At least once every 6 days	--
Noise	$L_{eq\ (30mins)}$, $L_{10\ (30mins)}$ and $L_{90\ (30mins)}$	NMS 5	At least once per week	Daytime on normal weekdays (0700-1900 hrs).
Water Quality	• Depth • Temperature • Salinity • Dissolved Oxygen (DO) • Suspended Solids (SS) • DO Saturation • Turbidity • pH	• Impact Stations: IS5, IS(Mf)6, IS7, IS8/IS8(N), IS(Mf)9 & IS10(N), • Control/Far Field Stations: CS2(A) & CS(Mf)5, • Sensitive Receiver Stations: SR3(N), SR4(N)/ SR4(N2), SR5(N), SR10A(N) & SR10B(N2)	Three times per week during mid-ebb and mid-flood tides (within ± 1.75 hour of the predicted time)	3 (1 m below water surface, mid-depth and 1 m above sea bed, except where the water depth is less than 6 m, in which case the mid-depth station may be omitted. Should the water depth be less than 3 m, only the mid-depth station will be monitored).
Dolphin	Line-transect Methods	Northeast Lantau survey area and Northwest Lantau survey area	Twice per month	--
Mudflat	Horseshoe crabs, seagrass beds, intertidal soft shore communities, sedimentation rates and water quality	San Tau and Tung Chung Bay	Once every 3 months	--

Remarks:
1) Original WQM stations IS8 and SR4(N) are located within the active work area of TCNTE project and the access to the WQM stations IS8 (Coordinate: E814251, N818412) and SR4(N) (Coordinate: E814705, N817859) are blocked by the silt curtains of the Tung Chung New Town Extension (TCNTE) project. Alternative monitoring stations IS8(N) (Coordinate: E814413, N818570) and SR4(N2) (Coordinate: E814688, N817996) are proposed to replace the original monitoring stations IS8 and SR4(N).

Proposal for permanently relocating the aforementioned stations was approved by EPD on 20 August 2019. The water quality monitoring has been conducted at stations IS8(N) and SR4(N2) on 21 August 2019.
2) The access to the WQM station SR4(N2) (Coordinate: E814688, N817996) is being blocked by the silt curtains of the Tung Chung New Town Extension (TCNTE) project. Water quality monitoring has been temporarily conducted at alternative stations, namely SR4(N3) (Coordinate: E814779, N818032) until 1 March 2023. Proposal for permanently relocating the SR4(N2) was approved by EPD on 3 March 2023. The water quality monitoring has been conducted at stations SR4(N3) since 3 March 2023.

2.2 Action and Limit Levels

2.2.1 **Table 2.2** presents the Action and Limit Levels for the 1-hour TSP, 24-hour TSP and noise level.

Table 2.2 Action and Limit Levels for 1-hour TSP, 24-hour TSP and Noise

Environmental Monitoring	Parameters	Monitoring Station	Action Level	Limit Level
Air Quality	1-hr TSP	AMS 5	352 μg/m^3	500 μg/m^3
		AMS 6	360 μg/m^3	
	24-hr TSP	AMS 5	164 μg/m^3	260 μg/m^3
		AMS 6	173 μg/m^3	
Noise	$L_{eq\ (30\ min)}$	NMS 5	When one documented complaint is received	75 dB(A)

2.2.2 The Action and Limit Levels for water quality monitoring are given as in **Table 2.3**.

Table 2.3 Action and Limit Levels for Water Quality

Parameter (unit)	Water Depth	Action Level	Limit Level
Dissolved Oxygen (mg/L)	Surface and Middle	5.0	4.2 except 5 for Fish Culture Zone
	Bottom	4.7	3.6
Turbidity (NTU)	Depth average	27.5 or 120% of upstream control station's turbidity at the same tide of the same day; The action level has been amended to "27.5 ***and*** 120% of upstream control station's turbidity at the same tide of the same day" since 25 March 2013.	47.0 or 130% of turbidity at the upstream control station at the same tide of same day; The limit level has been amended to "47.0 ***and*** 130% of turbidity at the upstream control station at the same tide of same day" since 25 March 2013.
Suspended Solid (SS) (mg/L)	Depth average	23.5 or 120% of upstream control station's SS at the same tide of the same day; The action level has been amended to "23.5 ***and*** 120% of upstream control station's SS at the same tide of the same day" since 25 March 2013.	34.4 or 130% of SS at the upstream control station at the same tide of same day and 10mg/L for Water Services Department Seawater Intakes; The limit level has been amended to "34.4 ***and*** 130% of SS at the upstream control station at the same tide of same day and 10mg/L for Water Services Department Seawater Intakes" since 25 March 2013

Notes:

(1) Depth-averaged is calculated by taking the arithmetic means of reading of all three depths.
(2) For DO, non-compliance of the water quality limit occurs when monitoring result is lower that the limit.
(3) For SS & turbidity non-compliance of the water quality limits occur when monitoring result is higher than the limits.
(4) The change to the Action and limit Levels for Water Quality Monitoring for the EM&A works was approved by EPD on 25 March 2013. Therefore, the amended Action and Limit Levels are applied for the water monitoring results obtained on and after 25 March 2013.

2.2.3 The Action and Limit Levels for dolphin monitoring are shown in **Tables 2.4 and 2.5**.

Table 2.4 Action and Limit Level for Dolphin Impact Monitoring

	North Lantau Social Cluster	
	NEL	**NWL**
Action Level	STG < 70% of baseline & ANI < 70% of baseline	STG < 70% of baseline & ANI < 70% of baseline
Limit Level	STG < 40% of baseline & ANI < 40% of baseline	

Remarks:
(1) STG means quarterly average encounter rate of number of dolphin sightings.
(2) ANI means quarterly average encounter rate of total number of dolphins.
(3) For North Lantau Social Cluster, AL will be triggered if either NEL or NWL fall below the criteria; LL will be triggered if both NEL and NWL fall below the criteria.

Table 2.5 Derived Value of Action Level (AL) and Limit Level (LL)

	North Lantau Social Cluster	
	NEL	**NWL**
Action Level	STG < 4.2 & ANI < 15.5	STG < 6.9 & ANI < 31.3
Limit Level	(STG < 2.4 & ANI < 8.9) and (STG < 3.9 & ANI < 17.9)	

Remarks:
(1) STG means quarterly average encounter rate of number of dolphin sightings.
(2) ANI means quarterly average encounter rate of total number of dolphins.
(3) For North Lantau Social Cluster, AL will be triggered if either NEL or NWL fall below the criteria; LL will be triggered if both NEL and NWL fall below the criteria.

2.3 Event Action Plans

2.3.1 The Event Actions Plans for air quality, noise, water quality, dolphin monitoring and mudflat monitoring and Action Plan for Landscape Works are annexed in **Appendix D.**

2.4 Mitigation Measures

2.4.1 Environmental mitigation measures for the contract were recommended in the approved EIA Report. **Appendix E** lists the recommended mitigation measures and the implementation status.

3 Environmental Monitoring and Audit

3.1 Implementation of Environmental Measures

3.1.1 Details of site audit findings and the corrective actions during the reporting period are presented in **Appendix F**.

3.1.2 A summary of the Implementation Schedule of Environmental Mitigation Measures (EMIS) is presented in **Appendix E**. Most of the necessary mitigation measures were implemented properly.

3.1.3 Regular marine travel route for marine vessels were implemented properly in accordance to the submitted plan and relevant records were kept properly.

3.1.4 Dolphin Watching Plan was implemented during the reporting period. No dolphins inside the silt curtain were observed. The relevant records were kept properly.

3.2 Air Quality Monitoring Results

3.2.1 The monitoring results for 1-hour TSP and 24-hour TSP are summarized in **Tables 3.1** and **3.2** respectively. Detailed impact air quality monitoring results and relevant graphical plots are presented in **Appendix G**. The existing air quality monitoring location AMS6 – Dragonair / CNAC (Group) Building (HKIA) was handed over to Airport Authority Hong Kong on 31 March 2021. 1-hr and 24-hr TSP monitoring at AMS6 was temporarily suspended starting from 1 April 2021 and resumed on 7 August 2024. Average flow rate is used for calculation of 24-hr air quality results of AMS6 during August 2024 due to unstable electricity supply on site.

Table 3.1 Summary of 1-hour TSP Monitoring Results Obtained During the Reporting Period

Reporting Period	Monitoring Station	Average (μg/m³)	Range (μg/m³)	Action Level (μg/m³)	Limit Level (μg/m³)
Mar 2025	AMS5	100	67-122	352	500
	AMS6	79	49-110	360	
Apr 2025	AMS5	100	61-130	352	
	AMS6	100	73-122	360	
May 2025	AMS5	109	85-125	352	
	AMS6	91	74-105	360	

Table 3.2 Summary of 24-hour TSP Monitoring Results Obtained During the Reporting Period

Reporting Period	Monitoring Station	Average (μg/m³)	Range (μg/m³)	Action Level (μg/m³)	Limit Level (μg/m³)
Mar 2025	AMS5	33	18-53	164	260
	AMS6	40	25-71	173	
Apr 2025	AMS5	42	22-97	164	
	AMS6	88	27-245	173	
May 2025	AMS5	32	20-40	164	
	AMS6	33	25-49	173	

3.2.2 No Action and Limit Level exceedances of 1-hr TSP were recorded at AMS5 and AMS6. No Action and Limit Level exceedances of 24-hr TSP were recorded at AMS5. No Action level exceedances of 24-hr TSP was recorded at AMS6 whereas One Action Level exceedance of 24-hr TSP was recorded at AMS6.

3.3 Noise Monitoring Results

3.3.1 The monitoring results for construction noise are summarized in **Table 3.3** and the monitoring results and relevant graphical plots for this reporting period are provided in **Appendix H.**

Table 3.3 Summary of Construction Noise Monitoring Results Obtained During the Reporting Period

Reporting period	Monitoring Station	Average $L_{eq\ (30\ mins)}$, dB(A)*	Range of L_{eq} (30 mins), dB(A)*	Action Level	Limit Level $L_{eq\ (30\ mins)}$, dB(A)
Mar 2025	NMS5	66	62-69	When one documented complaint is received	75
Apr 2025		61	57-67		
May 2025		60	59-62		

*A correction factor of +3dB(A) from free field to facade measurement was included.

3.3.2 No Action/Limit Level exceedances for noise were recorded during daytime on normal weekdays of the reporting period.

3.3.3 Other noise sources during the noise monitoring included aircraft/helicopter noise, construction activities by other parties and human activities nearby.

3.4 Water Quality Monitoring Results

3.4.1 Impact water quality monitoring was conducted at all designated monitoring stations during the reporting period. Impact water quality monitoring results and relevant graphical plots are provided in **Appendix O**.

3.4.2 Water quality impact sources during water quality monitoring were nearby construction activities by other parties and nearby operating vessels by other parties.

3.4.3 For marine water quality monitoring, no Action Level and Limit Level exceedances of dissolved oxygen level, turbidity level and suspended solid level were recorded during the reporting month.

3.5 Dolphin Monitoring Results

Data Analysis

3.5.1 Distribution Analysis: line-transect survey sightings data were integrated with a Geographic Information System (GIS), QGIS (3.42.3), to visualise and interpret spatial and temporal distribution patterns within the two survey areas (NEL and NWL). As no dolphins were sighted, no distribution analysis was conducted.

3.5.2 Encounter rate analysis: monthly encounter rates of Chinese White dolphins, i.e., the number of sightings per 100 km of survey effort on the transect lines (STG) and the total number of dolphins sighted per 100 km of survey effort on the transect lines (ANI) were calculated for both NEL and NWL survey areas, to compare to baseline and other monitoring conducted for this project. Dolphin encounter rates were also calculated using total survey effort (on transect lines plus the effort transiting between lines) for comparison to the AFCD long-term marine mammal monitoring data.

3.5.3 To compare this quarterly period with the HZMB baseline monitoring period, encounter rates were calculated using effort conducted during Beaufort Sea State 3 or better. The average encounter rate of sightings (STG) and average encounter rate of dolphins (ANI) were calculated from all six line-transect surveys conducted in NEL and NWL areas and compared to the six surveys conducted in the same area for the baseline period.

3.5.4 To compare this quarterly period with AFCD long-term marine mammal monitoring data, encounter rates were calculated using effort conducted during Beaufort 3 or better. The average encounter rate of sightings (STG) and average encounter rate of dolphins (ANI) were calculated from all six line-transect surveys plus the transit length between lines, conducted in NEL and NWL areas.

3.5.5 Quantitative grid analysis of habitat use was conducted by plotting sightings of Chinese White dolphins recorded during this quarterly period onto 1km^2 grids superimposed across both NWL and NEL survey areas. Sighting densities (number of sightings per km^2) and dolphin densities (total number of dolphins per km^2) were then calculated for each 1 km by 1 km grid using an inbuilt function of the GIS software. As no dolphins were sighted, there were no data to plot.

3.5.6 Sighting density grids and dolphin density were assessed to account for the amount of survey effort conducted within each grid. The total amount of survey effort spent in each grid was calculated by examining how many times each grid was surveyed during the survey period, e.g., 50 passages across a specific grid resulted in 50 units of effort being assigned to that grid. Once effort was calculated for each grid, sighting and dolphin densities were calculated accordingly. As no dolphins were sighted, no density analysis was conducted.

3.5.7 Sighting density (SPSE) and dolphin density (DPSE) thus represent the number of sightings and dolphins, respectively, per 100 units of survey effort. If a 1km^2 grid also contained land, the percentage of the sea area was calculated using GIS tools, and SPSE and DPSE values adjusted accordingly. The following formulae were used to estimate SPSE and DPSE in each 1km^2 grid within the study area:

$$SPSE = ((S / E) \times 100 / SA\%$$

$$DPSE = ((D / E) \times 100 / SA\%$$

S = total number of on-effort sightings
D = total number of dolphins from on-effort sightings
E = total number of units of survey effort
SA% = percentage of sea area

As no dolphins were sighted, no density analysis was conducted.

3.5.8 Behavioural analysis: the behaviour of dolphins sighted during vessel surveys were assigned to a category, e.g., feeding, milling/resting, traveling, socialising, and recorded in the sighting database. These data were mapped in the GIS system to visualise which activities and behaviours occurred within the study area, so that important areas for different dolphin activities could be identified. As no sightings were recorded, no behavioural analysis was conducted for this quarter.

3.5.9 Ranging pattern analysis; the location of individually identified dolphins that were recorded during the 3-month baseline monitoring period were obtained from the dolphin sighting database. The home range for individual dolphins was calculated using a fixed kernel method, using the Animove plug-in in QGIS and the R statistical package. As no sightings were recorded, no home range analysis was conducted for this quarterly period.

Summary of Survey Effort and Dolphin Sightings

3.5.10 During the period of March to May 2025, six line-transect vessel surveys were conducted in NWL and NEL areas. All transect lines in each area were surveyed twice per month.

3.5.11 From these surveys, a total of 808.9 km of survey effort was collected, with 770.27 km (95.22%) of the total survey effort being conducted under favourable weather conditions (i.e., Beaufort Sea State 3 or better with visibility of more than 5km). Total survey effort conducted in NEL and NWL was 312.57 km and 496.33 km, respectively.

3.5.12 Of the 808.9km of total survey effort, 602.62 km was conducted on the transect line and 206.28 km of effort was conducted while transiting between transect lines. Observers continuously monitored the area in front of the survey vessel both while travelling the transect lines and when in transit between transects. A summary table of the survey effort is shown in **Annex I** of **Appendix J**.

3.5.13 No dolphins were recorded during the monitoring surveys conducted between March to May 2025. Since monitoring for this project began (2012), this is the second March-May quarterly period during which no sightings were recorded (the previous quarterly period that recorded no sightings was March-May 2022). Two other quarterly periods during this project's impact monitoring, also did not record any sightings (June-August 2021 and September-November 2022).

Encounter Rate

3.5.14 During this quarterly period, no dolphins were recorded while surveying the transect lines under favourable conditions (Beaufort 3 or better) (**Table 3.4**). The encounter rates averaged across all surveys were compared to the baseline monitoring period (September-November 2011) (**Table 3.5**).

Table 3.4 Dolphin Encounter Rates (Sightings Per 100 km of Survey Effort) During Reporting Period (March 2025 to May 2025)

SURVEY AREA	DOLPHIN MONITORING DATES	Encounter rate (STG) (no. of on-effort dolphin sightings per 100 km of survey effort)	Encounter rate (ANI) (no. of dolphins from all on-effort sightings per 100 km of survey effort)
		Primary Lines Only	Primary Lines Only
Northeast Lantau	Set 1: March 11th / 12th	0.00	0.00
	Set 2: March 14th / 18th	0.00	0.00
	Set 3: April (23rd/24th May)	0.00	0.00
	Set 4: April (25th/26th May)	0.00	0.00
	Set 5: May 27th / 28th	0.00	0.00
	Set 6: May 29th / 30th	0.00	0.00
Northwest Lantau	Set 1: March 11th / 12th	0.00	0.00
	Set 2: March 14th / 18th	0.00	0.00
	Set 3: April (23rd/24th May)	0.00	0.00
	Set 4: April (25th/26th May)	0.00	0.00
	Set 5: May 27th / 28th	0.00	0.00
	Set 6: May 29th / 30th	0.00	0.00

Table 3.5 Comparison of average dolphin encounter rates from impact monitoring period (March 2025 to May 2025) and baseline monitoring period (September – November 2011)

	Encounter rate (STG) (no. of on-effort dolphin sightings per 100 km of survey effort)		Encounter rate (ANI) (no. of dolphins from all on-effort sightings per 100 km of survey effort)	
	March - May 2025	**September - November 2011**	**March - May 2025**	**September - November 2011**
Northeast Lantau	0.00	6.00 ± 5.05	0.00	22.19 ± 26.81
Northwest Lantau	0.00	9.85 ± 5.85	0.00	44.66 ± 29.85

Notes:
1) The encounter rates deduced from the baseline monitoring period have been recalculated based only on survey effort and on-effort sighting data made along the primary transect lines under favourable conditions.
2) ± denotes the standard deviation of the average encounter rates.

3.5.15 To facilitate comparison with the AFCD long-term monitoring results, encounter rates were also calculated for this quarterly period using both sightings recorded on the transect lines and while transiting between them. No sightings were recorded therefore, the sightings encounter rate (STG) and total number of dolphins encounter rate (ANI) in NWL and NEL were both 0.

3.5.16 In NEL, the dolphin encounter rates (both STG and ANI) in the present three-month impact monitoring period were both 0. Dolphin sightings within NEL have been rarely recorded during this quarterly period throughout this project's monitoring period; dolphin sightings have only been recorded in March-May 2013 and March-May 2024 (**Table 3.6**). Since this project's monitoring began, dolphins have been largely absent from the NEL area, which is consistent with AFCD long-term monitoring which records only two sightings in NEL since 2015 (all months of the year).

Table 3.6 Comparison of average dolphin encounter rates in the Northeast Lantau (NEL) survey area from all spring quarters (March-May) from the impact monitoring period and baseline monitoring period (September-November 2011).

	Encounter rate (STG) (no. of on-effort dolphin sightings per 100 km of survey effort)	**Encounter rate (ANI)** (no. of dolphins from all on-effort sightings per 100 km of survey effort)
September - November 2011 (Baseline)	6.00 ± 5.05	22.19 ± 26.81
March - May 2013 (HKLR03 Impact)	0.42 ± 1.03	0.42 ± 1.03

	Encounter rate (STG) (no. of on-effort dolphin sightings per 100 km of survey effort)	**Encounter rate (ANI)** (no. of dolphins from all on-effort sightings per 100 km of survey effort)
March - May 2014 (HKLR03 Impact)	0.00	0.00
March - May 2015 (HKLR03 Impact)	0.00	0.00
March - May 2016 (HKLR03 Impact)	0.00	0.00
March - May 2017 (HKLR03 Impact)	0.00	0.00
March - May 2018 (HKLR03 Impact)	0.00	0.00
March - May 2019 (HKLR03 Impact)	0.00	0.00
March - May 2020 (HKLR03 Impact)	0.00	0.00
March - May 2021 (TMCLKL Post-Construction)	0.00	0.00
March - May 2022 (TMCLKL Post-Construction)	0.00	0.00
March - May 2023 (HKLR03 Impact)	0.00	0.00
March - May 2024 (HKLR03 Impact)	0.48 ± 1.17	0.48 ± 1.17
March - May 2025 (HKLR03 Impact)	0.00	0.00

Notes:
1) The encounter rates deduced from the baseline monitoring period have been recalculated based only on survey effort and on-effort sighting data made along the primary transect lines under favourable conditions.
2) ± denotes the standard deviation of the average encounter rates.

3.5.17 In NWL, the dolphin encounter rates (both STG and ANI) in this quarterly period in 2025 were both 0. A complete absence of dolphins in the NWL area during this quarterly period is unusual. Since this project's monitoring began, only one other quarterly period did not record any dolphins; March-May 2022 (**Table 3.7**).

Table 3.7 Comparison of average dolphin encounter rates in the Northwest Lantau (NWL) survey area from all spring quarters (March-May) from the impact monitoring period and baseline monitoring period (September-November 2011).

	Encounter rate (STG) (no. of on-effort dolphin sightings per 100 km of survey effort)	**Encounter rate (ANI)** (no. of dolphins from all on-effort sightings per 100 km of survey effort)
September - November 2011 (Baseline)	9.85 ± 5.85	44.66 ± 29.85
March - May 2013 (HKLR03 Impact)	7.75 ± 3.96	24.23 ± 18.05
March - May 2014 (HKLR03 Impact)	6.51 ± 3.34	19.14 ± 7.19
March - May 2015 (HKLR03 Impact)	0.47 ± 0.73	2.36 ± 4.07
March - May 2016 (HKLR03 Impact)	0.98 ± 1.10	4.78 ± 6.85
March - May 2017 (HKLR03 Impact)	0.93 ± 1.03	5.25 ± 9.53
March - May 2018 (HKLR03 Impact)	2.88 ± 4.81	11.12 ± 22.46
March - May 2019 (HKLR03 Impact)	1.13 ± 1.39	2.54 ± 3.00
March - May 2020 (HKLR03 Impact)	0.56 ± 0.86	0.56 ± 0.86
March - May 2021 (TMCLKL Post-Construction)	1.13 ± 1.37	3.44 ± 4.26
March - May 2022 (TMCLKL Post-Construction)	0.00	0.00
March - May 2023 (HKLR03 Impact)	0.55 ± 0.86	1.35 ± 2.56
March - May 2024 (HKLR03 Impact)	0.57 ± 0.89	1.14 ± 1.77
March - May 2025 (HKLR03 Impact)	0.00	0.00

3.5.18 On review of the past 12 years' March-May quarterly periods (2013-2024), both STG and ANI have markedly decreased since 2015 (**Table 3.7**). As yet, there is no evidence that dolphins are returning to NWL, noting that HKLR03 marine works are still ongoing but will soon be completed. This quarter's findings are consistent with the data presented in the AFCD long-term monitoring report which records only two sightings in the past year April 2023-March 2024 (in September 2023 and January 2024) in the NWL area.

3.5.19 A two-way ANOVA with repeated measures and unequal sample sizes was conducted to examine whether there was a significant difference in average encounter rates between

baseline and impact monitoring periods. The two variables that were examined included the two periods (baseline and impact phases) and two locations (NEL and NWL).

3.5.20 To compare the baseline period and the present quarter (40th quarter of the impact phase), the p-values for the differences in average dolphin encounter rates of STG and ANI were both 0.000000. If the alpha value is set at 0.000001, significant differences were still detected between the baseline and present quarter, in both the average dolphin encounter rates of STG and ANI.

3.5.21 To compare the baseline monitoring and all quarterly impact phase monitoring periods (i.e., 50 quarterly periods of the HKLR03/TMCLKL project), the p-values for the differences in average dolphin encounter rates of STG and ANI were 0.000000 and 0.000000, respectively. If the alpha value is set at 0.000001, significant differences were still detected between the baseline and present quarter, in both the average dolphin encounter rates of STG and ANI

3.5.22 As evidenced from encounter rate calculations, dolphin usage was markedly reduced in both NEL and NWL survey areas during the present quarterly period, when compared to the baseline period. A reduced occurrence of dolphins has been documented throughout the overall HZMB construction period.

3.5.23 The decline in the dolphin's use of both NEL and NWL is ongoing as are construction works for HZMB-related projects and other developments (Hung 2018). There is no indication that dolphins are returning to northern Lantau waters, however, HKLR03 construction works are still ongoing. It is noted that the Brothers Marine Park was established in 2016 to compensate for the permanent habitat loss that occurred during HZMB-related reclamation works.

Conclusion

3.5.24 During the present quarter of dolphin monitoring, no adverse impact from the activities of this construction project on Chinese White dolphins was noticeable from general observations.

3.5.25 Dolphins occurred infrequently in the NEL area immediately prior to the commencement of this project, including during the baseline monitoring period. There has been a declining use of the NEL area by dolphins since at least the late 1990's and many known individuals from the Brothers Islands habitat have re-located to other areas of Lantau Island or have not been recorded in Hong Kong waters.

3.5.26 As the EIA predicted that dolphins will return to northern Lantau waters following the completion of construction work, it is critical to keep monitoring both the NEL and NWL areas to continuously document how the dolphin’s habitat use is impacted by changes in construction activities, related to HZMB and other projects, and to assess if further mitigation measures can be applied.

3.6 Mudflat Monitoring Results

Sedimentation Rate Monitoring

3.6.1 The baseline sedimentation rate monitoring was in September 2012 and impact sedimentation rate monitoring was undertaken on 28 March 2025. The mudflat surface levels at the four established monitoring stations and the corresponding XYZ HK1980 GRID coordinates are presented in **Table 3.8 and Table 3.9**.

Table 3.8 Measured Mudflat Surface Level Results

	Baseline Monitoring (September 2012)			Impact Monitoring (March 2025)		
Monitoring Station	Easting (m)	Northing (m)	Surface Level (mPD)	Easting (m)	Northing (m)	Surface Level (mPD)
S1	810291.160	816678.727	0.950	810291.150	816678.678	1.082
S2	810958.272	815831.531	0.864	810958.288	815831.534	0.959
S3	810716.585	815953.308	1.341	810716.575	815953.306	1.456
S4	811221.433	816151.381	0.931	811221.450	816151.390	1.121

Table 3.9 Comparison of Measurement

	Comparison of Measurement			Remarks and Recommendation
Monitoring Station	Easting (m)	Northing (m)	Surface Level (mPD)	
S1	-0.010	-0.049	0.132	Level continuously increased, need attention
S2	0.016	0.003	0.095	Level continuously increased, need attention
S3	-0.010	-0.002	0.115	Level continuously increased, need attention
S4	0.017	0.009	0.190	Level continuously increased, need attention

3.6.2 This measurement result was generally and relatively higher than the baseline measurement at S1, S2, S3 and S4. The mudflat level is continuously increased.

Water Quality Monitoring

3.6.3 The mudflat monitoring covered water quality monitoring data. Reference was made to the water quality monitoring data of the representative water quality monitoring station (i.e. SR3(N)) as in the EM&A Manual. The water quality monitoring location (SR3(N)) is shown in **Figure 2.1**)

3.6.4 Water quality monitoring in San Tau (monitoring station SR3(N)) was conducted in March 2025 as part of mudflat monitoring. The monitoring parameters included dissolved oxygen (DO), turbidity and suspended solids (SS).

3.6.5 The water monitoring result for SR3(N) were extracted and summarised in **Table 3.10**:

Table 3.10 Impact Water Quality Monitoring Results (Depth Average) at Station SR3(N)

	Mid Ebb Tide			Mid Flood Tide		
	DO (mg/L)	Turbidity (NTU)	SS (mg/L)	DO (mg/L)	Turbidity (NTU)	SS (mg/L)
3 Mar 2025	6.7	2.8	12.1	6.3	2.8	16.9
5 Mar 2025	6.6	2.8	4.0	6.2	2.6	4.2
7 Mar 2025	5.8	3.4	3.3	5.9	3.5	3.3
10 Mar 2025	6.2	2.3	3.1	6.6	2.4	5.2
12 Mar 2025	6.8	2.7	2.9	6.6	2.3	2.7
14 Mar 2025	6.6	2.7	3.7	6.2	2.4	3.3
17 Mar 2025	6.9	3.1	5.2	6.5	2.7	4.9
19 Mar 2025	6.3	3.2	2.8	6.1	2.9	2.7
21 Mar 2025	6.6	3.1	5.1	6.3	2.8	5.2
24 Mar 2025	6.5	3.1	2.2	6.1	2.9	1.9
26 Mar 2025	6.1	3.3	3.8	6.0	3.3	3.1
28 Mar 2025	6.0	3.4	3.3	6.2	3.3	3.3
31 Mar 2025	6.1	3.3	2.4	6.0	3.2	2.6
Average	6.4	3.0	4.1	6.2	2.8	4.5

Mudflat Ecology Monitoring

Sampling Zone

3.6.6 To collect baseline information of mudflats in the study site, the study site was divided into three sampling zones (labeled as TC1, TC2, TC3) in Tung Chung Bay and one zone in San Tau (labeled as ST) (**Figure 2.1 of Appendix O**). The horizontal shoreline of sampling zones TC1, TC2, TC3 and ST were about 250 m, 300 m, 300 m and 250 m, respectively **(Figure 2.2 of Appendix O)**. Survey of horseshoe crabs, seagrass beds and intertidal communities were conducted in every sampling zone. The present survey was conducted in March 2025 (totally 3 sampling days 1st (for ST), 2nd (for TC3), 3rd (for TC2 and TC1).

3.6.7 Since the field survey of June 2016, increasing number of trashes and even big trashes (**Figure 2.3 of Appendix O**) were found in every sampling zone. It raised a concern about the solid waste dumping and current-driven waste issues in Tung Chung Wan. Respective measures (e.g., manual clean-up) should be implemented by responsible governmental agency units.

Horseshoe Crabs

3.6.8 Active search method was adopted for horseshoe crab monitoring by two experienced surveyors in every sampling zone. During the search period, any accessible and potential area would be investigated for any horseshoe crab individuals within 2-3 hour of low tide period (tidal level below 1.2 m above Chart Datum (C.D.)). Once a horseshoe crab individual was found, the species was identified referencing to Li (2008). The prosomal width, inhabiting substratum and respective GPS coordinate were recorded. A photographic record was taken for future investigation. Any grouping behavior of individuals, if found, was recorded.

3.6.9 In June 2017, a big horseshoe crab was tangled by a trash gill net in ST mudflat (**Figure 2.3 of Appendix O**). It was released to sea once after photo recording. The horseshoe crab of such size should be inhabiting sub-tidal environment while it forages on intertidal shore occasionally during high tide period. If it is tangled by the trash net for few days, it may die due to starvation or overheat during low tide period. These trash gill nets are definitely 'fatal trap' for the horseshoe crabs and other marine life. Manual clean-up should be implemented as soon as possible by responsible governmental agency units.

Seagrass Beds

3.6.10 Active search method was adopted for seagrass bed monitoring by two experienced surveyors in every sampling zone. During the search period, any accessible and potential area would be investigated for any seagrass beds within 2-3 hours of low tide period. Once seagrass bed was found, the species, estimated area, estimated coverage percentage and respective GPS coordinates were recorded.

Intertidal Soft Shore Communities

3.6.11 The intertidal soft shore community surveys were conducted in low tide period. In every sampling zone, three 100m horizontal transect lines were laid at high tidal level (H: 2.0m above C.D.), mid tidal level (M: 1.5m above C.D.) and low tidal level (L: 1.0m above C.D.). Along every horizontal transect line, ten random quadrats (0.5 m x 0.5m) were placed.

3.6.12 Inside a quadrat, any visible epifauna was collected and was in-situ identified to the lowest practical taxonomical resolution. Whenever possible a hand core sample (10 cm internal diameter $\times$ 20 cm depth) of sediments was collected in the quadrat. The core sample was gently washed through a sieve of mesh size 2.0 mm in-situ. Any visible infauna was collected and identified. Finally, the top 5 cm surface sediment was dug for visible infauna in the quadrat regardless of hand core sample was taken.

3.6.13 All collected fauna were released after recording except some tiny individuals that were too small to be identified on site. These tiny individuals were taken to laboratory for identification under dissecting microscope.

3.6.14 The taxonomic classification was conducted in accordance to the following references: Polychaetes: Fauchald (1977), Yang and Sun (1988); Arthropods: Dai and Yang (1991), Dong (1991); Mollusks: Chan and Caley (2003), Qi (2004), AFCD (2018).

Data Analysis

3.6.15 Data collected from direct counting and core sampling was pooled in every quadrat for data analysis. Shannon-Weaver Diversity Index (H') and Pielou's Species Evenness (J) were calculated for every quadrat using the formulae below,

$$H' = -\Sigma (Ni / N) \ln (Ni / N) \text{ (Shannon and Weaver, 1963)}$$

$$J = H' / \ln S \text{ (Pielou, 1966)}$$

where S is the total number of species in the sample, N is the total number of individuals, and Ni is the number of individuals of the i^{th} species.

Mudflat Ecology Monitoring Results and Conclusion

Horseshoe Crabs

3.6.16 Four juvenile horseshoe crabs and no adult were recorded in present surveys. Photo records of previously and currently observed horseshoe crabs are shown in **Figure 3.1 of Appendix O** and **Figure 3.4 of Appendix O**. The present survey results regarding horseshoe crabs are presented in **Table 3.1 of Appendix O**. The complete survey records are presented in **Annex II of Appendix O**.

3.6.17 In the survey of March 2015, there was one important finding that a mating pair of *Carcinoscorpius rotundicauda* was found in ST (prosomal width: male 155.1mm, female 138.2mm). It indicated the importance of ST as a breeding ground of horseshoe crab. In June 2017, mating pairs of *Carcinoscorpius rotundicauda* were found in TC2 (male 175.27 mm, female 143.51 mm) and TC3 (male 182.08 mm, female 145.63 mm) **(Figure 3.2 of Appendix O)**. In December 2017 and June 2018, one mating pair was of *Carcinoscorpius rotundicauda* was found in TC3 (December 2017: male 127.80 mm, female 144.61 mm; June 2018: male 139 mm, female 149 mm). In June 2019, two mating pairs of *Tachypleus tridentatus* with large body sizes (male 150mm and Female 200mm; Male 180mm and Female 220mm) were found in TC3. Another mating pair of *Tachypleus tridentatus* was found in ST (male 140mm and Female 180mm). In March 2020, a pair of *Tachypleus tridentatus* with large body sizes (male 123mm and Female 137mm was recorded in TC1. **Figure 3.2 of Appendix O** shows the photographic records of the mating pair found. The recorded mating pairs were found nearly burrowing in soft mud at low tidal level (0.5-1.0 m above C.D.). The smaller male was holding the opisthosoma (abdomen carapace) of larger female from behind. A mating pair was found in TC1 in March 2020, it indicated that breeding of horseshoe crab could be possible along the coast of Tung Chung Wan rather than ST only, as long as suitable substratum was available. Based on the frequency of encounter, the shoreline between TC3 and ST should be more suitable mating ground. Moreover, suitable breeding period was believed in wet season (March – September) because tiny individuals (i.e. newly hatched) were usually recorded in June and September every year **(Figure 3.3 of Appendix O)**. One mating pair was found in June 2022. 3 adult individuals (prosomal width >100mm) of *Carcinoscorpius rotundicauda* were recorded in September 2022 survey, with one alive, one dead in TC3 and one dead in TC2. June 2022, 7 large individuals (prosomal width >100mm) of *Carcinoscorpius rotundicauda* was recorded (prosomal width ranged 131.4mm - 140.3mm) in TC3. In December 2018, one large individual of *Carcinoscorpius rotundicauda* was found in TC3 (prosomal width 148.9 mm). In March 2019, 3 large individuals (prosomal width ranged 220 – 310mm) of *Carcinoscorpius rotundicauda* were observed in TC2. In June 2019, there were 3 and 7 large individuals of *Tachypleus tridentatus* recorded in ST (prosomal width ranged 140 – 180mm) and TC3 (prosomal width ranged 150 – 220mm), respectively. In March 2020, a mating pair of *Tachypleus tridentatus* was recorded in TC1 with prosomal width 123 mm and 137mm. Base on their sizes, it indicated that individuals of prosomal width larger than 100 mm would progress its nursery stage from

intertidal habitat to sub-tidal habitat of Tung Chung Wan. The photo records of the large horseshoe crab are shown in **Figure 3.4 of Appendix O**. A dead specimen of adult horseshoe crab was seen at TC3 in March 2025 (**Figure 3.4 (Cont'd) of Appendix O**). These large individuals might move onto the intertidal shore occasionally during high tide for foraging and breeding. Because they should be inhabiting sub-tidal habitat most of the time. Their records were excluded from the data analysis to avoid mixing up with juvenile population living on intertidal habitat.

3.6.18 Some marked individuals were found in the previous surveys of September 2013, March 2014, and September 2014. All of them were released through a conservation programme in charged by Prof. Paul Shin (Department of Biology and Chemistry, The City University of Hong Kong (CityU)). It was a re-introduction trial of artificial bred horseshoe crab juvenile at selected sites. So that the horseshoe crab's population might be restored in the natural habitat. Through a personal conversation with Prof. Shin, about 100 individuals were released in the sampling zone ST on 20 June 2013. All of them were marked with color tape and internal chip detected by specific chip sensor. There should be second round of release between June and September 2014 since new marked individuals were found in the survey of September 2014.

3.6.19 The artificial bred individuals, if found, would be excluded from the results of present monitoring programme in order to reflect the changes of natural population. However, the mark on their prosoma might have been detached during moulting after a certain period of release. The artificially released individuals were no longer distinguishable from the natural population without the specific chip sensor. The survey data collected would possibly cover both natural population and artificially bred individuals.

Population difference among the sampling zones

3.6.20 **Figure 3.5 and 3.6 of Appendix O** show the changes of number of individuals, meaning prosomal width and search record of horseshoe crabs *Carcinoscorpius rotundicauda* and *Tachypleus tridentatus* in respectively in each sampling zone throughout the monitoring period.

3.6.21 To consider the entire monitoring period for TC3 and ST, medium to high search records (i.e. number of individuals) of both species (*Carcinoscorpius rotundicauda* and *Tachypleus tridentatus*) were usually found in wet season (June and September). The search record of ST was higher from September 2012 to June 2014 while it was replaced by TC3 from September 2014 to June 2015. The search records were similar between two sampling zones from September 2015 to June 2016. In September 2016, the search record of *Carcinoscorpius rotundicauda* in ST was much higher than TC3. From March to June 2017, the search records of both species were similar again between two sampling zones. It showed a natural variation of horseshoe crab population in these two zones due to weather condition and tidal effect. No obvious difference of horseshoe crab population was noted between TC3 and ST. In September 2017, the search records of both horseshoe crab species decreased except the *Carcinoscorpius rotundicauda* in TC3. The survey results were different from previous findings that there were usually higher search records in September. One possible reason was that the serial cyclone hit decreased horseshoe crab activity (totally 4 cyclone records between June and September 2017, to be discussed in 'Seagrass survey' section). From December 2017 to September 2018, the search records of both species increased again to low-moderate level in ST and TC3. From December 2018 to September 2019, the search records of *Carcinoscorpius rotundicauda* change from very low to low while the change of *Tachypleus tridentatus* was similar during this period. Relatively higher population fluctuation of *Carcinoscorpius rotundicauda* was observed in TC3. From March 2020 to September 2020, the search records of both species, *Carcinoscorpius rotundicauda* and *Tachypleus tridentatus,* were increased to moderate level in ST. However, the search records of both species, *Carcinoscorpius*

rotundicauda and *Tachypleus tridentatus,* were decreased from very low to none in TC3 in this period. From March 2021 to September 2021, the search records of both species, *Carcinoscorpius rotundicauda* and *Tachypleus tridentatus,* were kept at low-moderate level in both ST and TC3. It is like the previous findings of June. It shows another growing phenomenon of horseshoe crabs, and it may be due to the weather variation of the start of wet season. The survey results were different from previous findings that there were usually higher search records in September. One possible reason was that September of 2021 was one of the hottest months in Hong Kong in record. As such, hot and shiny weather decreased horseshoe crab activity. In December 2021, no juvenile was recorded like previous in December due to the season. In March 2022, only juveniles recorded in both ST and TC3, no adult specimen was observed. In June 2022, total of 13 individuals of *Carcinoscorpius rotundicauda* and *Tachypleus tridentatus* were found, with 6 juveniles, 6 adults and 1 died recorded. In September 2022, total of 7 individuals of were found, with 4 juveniles, 3 adults (1 alive and 2 died) recorded. In March 2023, a total of 12 individuals of juveniles *Carcinoscorpius rotundicauda* and *Tachypleus tridentatus* were found and recorded. In June 2023, a total of 27 individuals of juveniles *Tachypleus tridentatus* were found and recorded. In September 2023, a total of 2 individuals of juveniles *Tachypleus tridentatus* were found and recorded. In December 2023, no horseshoe crab was found. In March and September 2024, *Tachypleus tridentatus* were found for each month. In December 2024, 2 individuals of juveniles *Carcinoscorpius rotundicauda* were found. Four individuals of juveniles *Tachypleus tridentatus* were recorded in March 2025.

3.6.22 For TC1, the search record was at a low to moderate level throughout the monitoring period. The change of *Carcinoscorpius rotundicauda* was relatively more variable than that of *Tachypleus tridentatus*. Relatively, the search record was very low in TC2. There were occasional records of 1 to 4 individuals between March and September throughout the monitoring period. The maximum record was 6 individuals only in June 2016.

3.6.23 About the body size, larger individuals of *Carcinoscorpius rotundicauda* were usually found in ST and TC1 relative to that in TC3 from September 2012 to June 2017. But the body size was higher in TC3 and ST followed by TC1 from September 2017 to March 2020. From June 2020 to December 2020, there was no individuals of *Carcinoscorpius rotundicauda* recorded in TC3 but in ST. The body size of *Carcinoscorpius rotundicauda* in ST was recorded gradually increased (from mean prosomal width 23.6mm to 49.6mm) since March 2020 to September 2020. From December 2020 to March 2021, the body size of *Carcinoscorpius rotundicauda* in ST was recorded decreased (from mean prosomal width 49.6mm to 43.3mm). In March 2021, the body size of *Carcinoscorpius rotundicauda* in TC3 (mean prosomal width 46.2mm) was recorded larger than that in ST (mean prosomal width 43.3mm). From September 2021 to June 2022, the body size of *Carcinoscorpius rotundicauda* in ST was recorded increased (from mean prosomal width 39.8mm to 54.42mm). For *Tachypleus tridentatus*, larger individuals were usually found in ST and TC3 followed by TC1 throughout the monitoring period. In June 2019, all found horseshoe crabs were large individuals and mating pairs. It is believed that the sizes of horseshoe crabs would decrease and gradually rise afterward due to the stable growth of juveniles after the spawning season. From March 2019 to September 2021, *Tachypleus tridentatus* were only recorded in TC3 and ST. The body size in TC3 increased from September 2019 to December 2019 then decreased in March 2020 and no recorded species in TC3 for three consecutive quarters from June 2020 to December 2020. From March 2020 to Sep 2021, the body size of *Tachypleus tridentatus* in TC3 increased (from mean prosomal width 34.00mm to 38.8mm). It showed a natural variation of horseshoe crab population in TC3. Apart from natural mortality, migration from nursery soft shore to subtidal habitat was another possible cause. The body size in ST was gradually growth since December 2019 to September 2020 then slightly dropped in December 2020. In June 2022, *T. tridentatus* were only recorded in ST, the body size in ST decreased from mean prosomal width 77.59mm to 54.02mm in March 2022.

In September 2022 *T. tridentatus* were only recorded in TC3. The mean prosomal was 61.09mm. In March 2023, 7 *T. tridentatus* were recorded in ST and TC3. The mean prosomal was 62.68mm. In March 2024, 2 *T. tridentatus* were recorded in ST with a mean prosomal width 70.55mm. No horseshoe crab was recorded in all sites in June 2024, and 2 *T. tridentatus* were recorded in ST with a mean prosomal width 40.00mm. In December 2024 2 *Carcinoscorpius rotundicauda* recorded with a mean prosomal width 43.00mm. In March 2025, 3 *T. tridentatus* were recorded in ST and 1 recorded at TC3.

3.6.24 In general, it was obvious that the shoreline along TC3 and ST (western shore of Tung Chung Wan) was an important nursery ground for horseshoe crab especially newly hatched individuals due to larger area of suitable substratum (fine sand or soft mud) and less human disturbance (far from urban district). Relatively, other sampling zones were not a suitable nursery ground, especially TC2. Possible factors were less area of suitable substratum (especially TC1) and higher human disturbance (TC1 and TC2: close to urban district and easily accessible). In TC2, large daily salinity fluctuation was a possible factor since it was flushed by two rivers under tidal inundation. The individuals inhabiting TC1 and TC2 were confined in small foraging area due to limited area of suitable substratum. Although there were mating pairs seldomly found in TC1 and TC2, the hatching rate and survival rate of newly hatched individuals were believed to be very low.

Seasonal variation of horseshoe crab population

3.6.25 Throughout the monitoring period, the search records of horseshoe crabs were fluctuated and at moderate – very low level in June (**Figure 3.5 and 3.6 of Appendix O**). Low – Very low search record was found in June 2013, totally 82 individuals of *Tachypleus tridentatus* and 0 ind. of *Carcinoscorpius rotundicauda* were found in TC1, TC3 and ST. Compare with the search record of June 2013, the numbers of *Tachypleus tridentatus* were gradually decreased in June 2014 and 2015 (55 ind. in 2014 and 18 ind. in 2015); the number of *Carcinoscorpius rotundicauda* raise to 88 and 66 ind. in June 2014 and 2015 respectively. In June 2016, the search record increased about 3 times compare with June 2015. In total, 182 individuals of *Carcinoscorpius rotundicauda* and 47 individuals of *Tachypleus tridentatus* were noted, respectively. Then, the search record was similar to June 2016. The number of recorded *Carcinoscorpius rotundicauda* (133 ind.) slightly dropped in June 2017. However, that of *Tachypleus tridentatus* rapidly increased (125 ind.). In June 2018, the search record was low to moderate while the numbers of *Tachypleus tridentatus* dropped sharply (39 ind.). In June 2019, 10 individuals of *Tachypleus tridentatus* were observed in TC3 and ST. All of them, however, were large individuals (prosomal width >100mm), their records are excluded from the data analysis to avoid mixing up with the juvenile population living on intertidal habitat. Until September 2020, the number of *Carcinoscorpius rotundicauda* and *Tachypleus tridentatus* gradually increased to 39 ind. and 28 ind., respectively. In December 2020, the number of *Carcinoscorpius rotundicauda* and *Tachypleus tridentatus* greatly decreased to 3 ind. and 7 ind., respectively. In March 2022, the number of *Carcinoscorpius rotundicauda* and *Tachypleus tridentatus* gradually decreased to 7 ind. and 2 ind., respectively in comparing with the March of previous record. The drop of abundance may be related to the unusual cold weather in the beginning of March 2022. Throughout the monitoring period, similar distribution of horseshoe crab population was found.

3.6.26 The search record of horseshoe crab declined obviously in all sampling zones during dry season especially December (**Figure 3.5 and 3.6 of Appendix O**) throughout the monitoring period. Very low – low search record was found in December from 2012 to 2015 (0-4 ind. of *Carcinoscorpius rotundicauda* and 0 – 12 ind. of *Tachypleus tridentatus*). The horseshoe crabs were inactive and burrowed in the sediments during cold weather (<15 ºC). Similar results of low search record in dry season were reported in a previous territory-wide survey of horseshoe

crab. For example, the search records in Tung Chung Wan were 0.17 ind. hr^{-1} $person^{-1}$ and 0.00 ind. hr^{-1} $person^{-1}$ in wet season and dry season respectively (details see Li, 2008). Compare with the search record of December from 2012 to 2015, which of December 2016 were much higher relatively. There were totally 70 individuals of *Carcinoscorpius rotundicauda* and 24 individuals of *Tachypleus tridentatus* in TC3 and ST. Since the survey was carried in earlier December with warm and sunny weather (~22 ºC during dawn according to Hong Kong Observatory database, Chek Lap Kok station on 5 December 2016), the horseshoe crab was more active (i.e. move onto intertidal shore during high tide for foraging and breeding) and easier to be found. In contrast, there was no search record in TC1 and TC2 because the survey was conducted in mid December with colder and cloudy weather (~20°C during dawn on 19 December). The horseshoe crab activity would decrease gradually with the colder climate. In December of 2017, 2018 and 2019, very low search records were found again as mentioned above. No record of houseshoe crab was recorded in December 2022 and 2023.

3.6.27 From September 2012 to December 2013, *Carcinoscorpius rotundicauda* was less common species relative to *Tachypleus tridentatus*. Only 4 individuals were ever recorded in ST in December 2012. This species had ever been believed of very low density in ST hence the encounter rate was very low. In March 2014, it was found in all sampling zones with higher abundance in ST. Based on its average size (mean prosomal width 39.28 – 49.81 mm), it indicated that breeding and spawning of this species had occurred about 3 years ago along the coastline of Tung Chun Wan. However, these individuals were still small while their walking trails were inconspicuous. Hence there was no search record in previous sampling months. Since March 2014, more individuals were recorded due to larger size and higher activity (i.e. more conspicuous walking trail).

3.6.28 For *Tachypleus tridentatus,* sharp increase of number of individuals was recorded in ST during the wet season of 2013 (from March to September). According to a personal conversation with Prof. Shin (CityU), his monitoring team had recorded similar increase of horseshoe crab population during wet season. It was believed that the suitable ambient temperature increased its conspicuousness. However similar pattern was not recorded in the following wet seasons. The number of individuals increased in March and June 2014 and followed by a rapid decline in September 2014. Then the number of individuals fluctuated slightly in TC3 and ST until March 2017. Apart from natural mortality, migration from nursery soft shore to subtidal habitat was another possible cause. Since the mean prosomal width of *Tachypleus tridentatus* continued to grow and reached about 50 mm since March 2014. Then it varied slightly between 35-65 mm from September 2014 to March 2017.Most of the individuals might have reached a suitable size (e.g. prosomal width 50 – 60 mm) strong enough to forage in sub-tidal habitat. In June 2017, the number of individuals increased sharply again in TC3 and ST. Although mating pair of *Tachypleus tridentatus* was not found in previous surveys, there should be new round of spawning in the wet season of 2016. The individuals might have grown to a more conspicuous size in 2017 accounting for higher search record. In September 2017, moderate numbers of individual were found in TC3 and ST indicating a stable population size. From September 2018 to March 2020, the population size was low while natural mortality was the possible cause. From June 2020 to September 2020, the population size of *Tachypleus tridentatus* increased to moderate level in ST while the mean proposal width of them conitued to grow and reach about 55mm. The population size of *Tachypleus tridentatus* slightly decreased in ST from March 2021 to March 2022 and the mean proposal width of them increased to about 77.59mm.

3.6.29 In recent year, the *Carcinoscorpius rotundicauda* was a more common horseshoe crab species in Tung Chung Wan. It was recorded in the four sampling zones while the majority of population located in TC3 and ST. Due to potential breeding last year, the number of *Tachypleus tridentatus* increased in ST. Since TC3 and ST were regarded as important nursery ground for

both horseshoe crab species, box plots of prosomal width of two horseshoe crab species were constructed to investigate the changes of population in details.

Box plot of horseshoe crab populations in TC3

3.6.30 **Figure 3.7 of Appendix O** shows the changes of prosomal width of *Carcinoscorpius rotundicauda* and *Tachypleus tridentatus* in ST. As mentioned above, *Carcinoscorpius rotundicauda* was rarely found between September 2012 and December 2013 hence the data were lacking. From March 2014 to September 2018, the size of major population decreased, and more small individuals (i.e. lower whisker) were recorded after June of every year. It indicated a new round of spawning. Also, there were similar increasing trends of body size from September to June of next year between 2014 and 2017. It indicated a stable growth of individuals. The larger juveniles (i.e. upper whisker usually ranged 60 – 80 mm in prosomal width except one individual (prosomal width 107.04 mm) found in March 2017. It reflected that juveniles reaching this size would gradually migrate to sub-tidal habitats.

3.6.31 For *Tachypleus tridentatus,* the major size ranged 20-50 mm while the number of individuals fluctuated from September 2012 to June 2014. Then a slight but consistent growing trend was observed from September 2014 to June 2015. The prosomal width increased from 25 – 35 mm to 35 – 65 mm. As mentioned, the large individuals might have reached a suitable size for migrating from the nursery soft shore to subtidal habitat. It accounted for the declined population in TC3. From March to September 2016, slight increasing trend of major size was noticed again. From December 2016 to June 2017, similar increasing trend of major size was noted with much higher number of individuals. It reflected new round of spawning. In September 2017, the major size decreased while the trend was different from previous two years. Such decline might be the cause of serial cyclone hit between June and September 2017 (to be discussed in the 'Seagrass survey' section). From December 2017 to September 2018, increasing trend was noted again. It indicated a stable growth of individuals. From September 2018 to that of next year, the average prosomal widths were decreased from 60mm to 36mm. It indicated new rounds of spawning occurred during September to November 2018. In December 2019, an individual with larger body size (prosomal width 65mm) was found in TC3 which reflected the stable growth of individuals. In March 2020, the average prosomal width (middle line of the whole box) of *Tachypleus tridentatus* in TC3 was 33.97mm which is smaller than that in December 2019. It was in normal fluctuation. From June 2020 to December 2020, no horseshoe crab was recorded in TC3. In Sep 2021, only one *Tachypleus tridentatus* with body size (prosomal width 38.78mm) was found in TC3. The decrease in the species population was considered to be related to hot weather in September, which may affect their activity. Across the whole monitoring period, the larger juveniles (upper whisker) usually reached 60 – 80 mm in prosomal width, even 90 mm occasionally. The juveniles reaching this size might gradually migrate to sub-tidal habitats.

Box plot of horseshoe crab populations in ST

3.6.32 **Figure 3.8 of Appendix O** shows the changes of prosomal width of *Carcinoscorpius rotundicauda* and *Tachypleus tridentatus* in ST. As mentioned above, *Carcinoscorpius rotundicauda* was rarely found between September 2012 and December 2013 hence the data were lacking. From March 2014 to September 2018, the size of major population decreased and more small individuals (i.e. lower whisker) were recorded after June of every year. It indicated new round of spawning. Also there were similar increasing trends of body size from September to June of next year between 2014 and 2017. It indicated a stable growth of individuals. The larger juveniles (i.e. upper whisker usually ranged 60 – 80 mm in prosomal

width except one individual (prosomal width 107.04 mm) found in March 2017. It reflected juveniles reaching this size would gradually migrate to sub-tidal habitats.

3.6.33 For *Tachypleus tridentatus,* a consistent growing trend was observed for the major population from December 2012 to December 2014 regardless of change of search record. The prosomal width increased from 15 – 30 mm to 60 – 70 mm. As mentioned, the large juveniles might have reached a suitable size for migrating from the nursery soft shore to subtidal habitat. From March to September 2015, the size of major population decreased slightly to a prosomal width 40 – 60 mm. At the same time, the number of individuals decreased gradually. It further indicated some of large juveniles might have migrated to sub-tidal habitat, leaving the smaller individuals on shore. There was an overall growth trend. In December 2015, two big individuals (prosomal width 89.27 mm and 98.89 mm) were recorded only while it could not represent the major population. In March 2016, the number of individual was very few in ST that no box plot could be produced. In June 2016, the prosomal width of major population ranged 50 – 70 mm. But it dropped clearly to 30 – 40 mm in September 2016 followed by an increase to 40 – 50 mm in December 2016, 40 – 70 mm in March 2017 and 50 – 60mm in June 2017. Based on overall higher number of small individuals from June 2016 to September 2017, it indicated another round of spawning. From September 2017 to June 2018, the major size range increased slightly from 40 – 50 mm to 45 – 60 mm indicating a continuous growth. In September 2018, decrease of major size was noted again that might reflect new round of spawning. Throughout the monitoring period, the larger juveniles ranged 60-80 mm in prosomal width. Juveniles reaching this size would gradually migrate to sub-tidal habitats.

3.6.34 As a summary for horseshoe crab populations in TC3 and ST, there were spawning ground of *Carcinoscorpius rotundicauda* from 2014 to 2018 while the spawning time should be in spring. The population size was consistent in these two sampling zones. For *Tachypleus tridentatus*, small individuals were rarely found in both zones from 2014 to 2015. It was believed no occurrence of successful spawning. The existing individuals (that recorded since 2012) grew to a mature size and migrated to sub-tidal habitat. Hence the number of individuals decreased gradually. From 2016 to 2018, new rounds of spawning were recorded in ST while the population size increased to a moderate level.

3.6.35 In March 2019 to June 2019 and Dec 2021, no horseshoe crab juveniles (prosomal width <100mm) were recorded in TC3 and ST. All recorded horseshoe crabs were large individuals (prosomal width >100mm) or mating pairs which were all excluded from the data analysis. From September 2019 to September 2020, the population size of both horseshoe crab species in ST gradually increased to moderate level while their body sizes were mostly in small to medium range (~23 – 55mm). It indicated the natural stable growth of the horseshoe crab juveniles. In December 2020, the population size of both horseshoe crab species in ST dropped to low level while their body sizes were mostly in small to medium range (~28 – 56mm). It showed the natural mortality and seasonal variation of horseshoe crab. In June 2022, the population size of both horseshoe crab species in ST was kept as low-moderate level while their body sizes were mostly in small to medium range (~51–78mm). In September 2022, the population size of both horseshoe crab species in TC3 and ST was kept as low-moderate level while their body sizes were mostly in small to medium range (~56–62mm). In September 2023, the population size of both horseshoe crab species in TC3 and ST was kept as low-moderate level while their body sizes were mostly in small to medium range (~44-79mm).

Impact of the HKLR project

3.6.36 It was the 51st survey of the EM&A programme during the construction period. Based on the monitoring results, no detectable impact on horseshoe crab was revealed due to HKLR project. The population change was mainly determined by seasonal variation, no abnormal

phenomenon of horseshoe crab individual, such as large number of dead individuals on the shore had been reported.

Discussion

3.6.37 There are 4 juvenile horseshoe crabs recorded in March 2025. The population of horseshoe crabs recorded in recent years has been in a decreasing trend since 2021, referring to Figure **3.5 of Appendix O**. It is noted that the inter-tidal habitat for the juvenile horseshoe crabs within the monitoring sites is become smaller in area due to increased seagrass colonization as indicated by seagrass monitoring results, i.e. seagrasses cover area increased in recent years (refer to **Figure 3.11 of Appendix O**). The juvenile horseshoe crabs prefer open soft mud/sand habitat as they can easily burrow in the mud/sand to hide themselves when the habitat exposed during low tide. When the mud/sand habitat was colonized by seagrasses, the roots of seagrasses made it difficult for horseshoe crab to burrow and hide. In this situation, horseshoe crabs may avoid habitat or being easily predated by predators such as birds. All seagrasses disappeared as observed during monitoring in December 2024, and one of the two seagrasses is observed in March 2025 re-generated at a small area along mangal edge. Attention will be given to subsequent monitoring, if it will affect the breeding activities of the horseshoe crabs

Seagrass Beds

3.6.38 All seagrasses were observed disappeared within monitoring areas of Tung Chung and San Tau during the last quarterly ecological monitoring in December 2024. However, one of the two seagrass species, i.e., Zostera japonica is re-generated during the survey in March 2025. It is likely that the underground roots of this seagrass maintained alive when the above ground plant part died during last season, i.e., December 2024. Zostera japonica was found only in ST. At close vicinity to mangrove, one small sized 25 square meter) of Zostera japonica beds were observed at tidal zone 2.0m above C.D in ST. The widely distributed seagrass, Halophila ovalis in recent years totally disappeared in December 2024 and did not observe re-generation in March 2025. **Table 3.2 of Appendix O** summarizes the results of the present seagrass beds survey, and the photograph records of the seagrass bed are shown in **Figure 3.9 of Appendix O**. The complete record throughout the monitoring period is presented in **Annex III of Appendix O**.

3.6.39 Since the commencement of the EM&A monitoring programme, two species of seagrass *Halophila ovalis* and *Zostera japonica* were recorded in TC3 and ST (**Figure 3.10 of Appendix O**). In general, *Halophila ovalis* was occasionally found in TC3 in few small to medium patches. But it was commonly found in ST in medium to large seagrass bed. Moreover, it had sometimes grown extensively and had covered significant mudflat area at 0.5 – 2.0 m above C.D. between TC3 and ST. Another seagrass species *Zostera japonica* was found in ST only. It has restricted distribution in a few locations with small vegetation coverage, and it partially co-existed with *Halophila ovalis* near the edge of the mangrove strand at 2.0 m above C.D.

3.6.40 According to the previous results, majority of seagrass bed was confined in ST, while it increasingly established at TC3 in recent years, and the temporal change of both seagrass species was investigated in detail:

Temporal variation of seagrass beds in ST

3.6.41 **Figure 3.11 of Appendix O** shows the changes of estimated total area of seagrass beds in ST along the sampling months. For *Zostera japonica*, it was not recorded in the 1st and 2nd surveys of monitoring programme. Seasonal recruitment of few, small patches (total seagrass area: 10 m^2) was found in March 2013 that grew within the large patch of seagrass *Halophila ovalis*. Then, the patch size increased and merged gradually with the warmer climate from March to June 2013 (15 m^2). However, the patch size decreased and remained similar from September 2013 (4 m^2) to March 2014 (3 m^2). In June 2014, the patch size increased obviously again (41 m^2) with warmer climate followed by a decrease between September 2014 (2 m^2) and December 2014 (5 m^2). From March to June 2015, the patch size increased sharply again (90 m^2). It might be due to the disappearance of the originally dominant seagrass *Halophila ovalis* resulting in less competition for substratum and nutrients. From September 2015 to June 2016, it was found coexisting with seagrass *Halophila ovalis* with steady increasing patch size (from 44 m^2 to 115 m^2) and variable coverage. In September 2016, the patch size decreased again to (38 m^2) followed by an increase to a horizontal strand (105.4 m^2) in June 2017. And it did no longer co-existed with *Halophila ovalis*. Between September 2014 and June 2017, an increasing trend was noticed from September to June of next year followed by a rapid decline in September of next year. It was possibly the cause of heat stress, typhoon and stronger grazing pressure during the wet season. However, such increasing trend was not found from September 2017 to March 2021, while no patch of *Zostera japonica* was found. From June 2021, the species was recorded again with a coverage of 45m^2 in area. The recorded area of the seagrass bed in September 2021 survey was slightly decreased to 15m^2. The *Z. japonica* was consistently present at the monitoring site still September 2024, and it disappeared in December 2024.

3.6.42 For *Halophila ovalis*, it was recorded as 3 – 4 media to large patches (area 18.9- 251.7 m^2; vegetation coverage 50 – 80%) beside the mangrove vegetation at tidal level 2 m above C.D. in September 2012. The total seagrass bed area grew steadily from 332.3 m^2 in September 2012 to 727.4 m^2 in December 2013. Flowers were observed in the largest patch during its flowering period. In March 2014, 31 small to medium patches were newly recorded (variable area 1 – 72 m^2 per patch, vegetation coverage 40-80% per patch) in lower tidal zone between 1.0 and 1.5 m above C.D. The total seagrass area increased further to 1350 m^2. In June 2014, these small and medium patches grew and extended to each other. These patches were no longer distinguishable and were covering a significant mudflat area of ST. It was generally grouped into 4 large patches (1116 – 2443 m^2) of seagrass beds characterized of patchy distribution, variable vegetable coverage (40-80%) and smaller leaves. The total seagrass bed area increased sharply to 7629 m^2. In September 2014, the total seagrass area declined sharply to 1111m^2. There were only 3-4 small to large patches (6 – 253 m^2) at high tidal level and 1 large patch at low tidal level (786 m^2). Typhoons or strong water current was a possible cause (Fong, 1998). In September 2014, there were two tropical cyclone records in Hong Kong (7th – 8thSeptember: no cyclone name, maximum signal number 1; 14th – 17th September: Kalmaegi, maximum signal number 8SE) before the seagrass survey dated 21st September 2014. The strong water current caused by the cyclone Kalmaegi especially might have damaged the seagrass beds. In addition, natural heat stress and grazing force were other possible causes reducing seagrass beds area. Besides, very small patches of *Halophila ovalis* could be found in other mud flat areas in addition to the recorded patches. But it was hardly distinguished due to very low coverage (10 – 20%) and small leaves.

3.6.43 In December 2014, all the seagrass patches of *Halophila ovalis* disappeared in ST. **Figure 3.12 of Appendix O** shows the difference of the original seagrass beds area nearby the mangrove vegetation at high tidal level between June 2014 and December 2014. Such rapid loss would not be seasonal phenomenon because the seagrass beds at higher tidal level (2.0 m above C.D.) were present and normal in December 2012 and 2013. According to Fong (1998), similar incident had occurred in ST in the past. The original seagrass area had declined significantly during the commencement of the construction and reclamation works for the international airport at Chek Lap Kok in 1992. The seagrass almost disappeared in 1995 and recovered gradually after the completion of reclamation works. Moreover, incident of rapid loss of seagrass area was also recorded in another intertidal mudflat in Lai Chi Wo in 1998 with unknown reason. Hence, *Halophila ovalis* was regarded as a short- lived and *r*- strategy seagrass that could colonize areas in short period but disappears quickly under unfavourable conditions (Fong, 1998).

Unfavourable conditions to seagrass *Halophila ovalis*

3.6.44 Typhoon or strong water current was suggested as one unfavorable condition to *Halophila ovalis* (Fong, 1998). As mentioned above, there were two tropical cyclone records in Hong Kong in September 2014. The strong water current caused by the cyclones might have given damage to the seagrass beds.

3.6.45 Prolonged light deprivation due to turbid water would be another unfavorable condition. Previous studies reported that *Halophila ovalis* had little tolerance to light deprivation. During experimental darkness, seagrass biomass declined rapidly after 3-6 days and seagrass died completely after 30 days. The rapid death might be due to shortage of available carbohydrate under limited photosynthesis or accumulation of phytotoxic end products of anaerobic respiration (details see Longstaff *et al*., 1999). Hence the seagrass bed of this species was susceptible to temporary light deprivation events such as flooding river runoff (Longstaff and Dennison, 1999).

3.6.46 In order to investigate any deterioration of water quality (e.g. more turbid) in ST, the water quality measurement results at two closest monitoring stations SR3 and IS5 of the EM&A programme were obtained from the water quality monitoring team. Based on the results from June to December 2014, the overall water quality was in normal fluctuation except there was one exceedance of suspended solids (SS) at both stations in September. On 10th September 2014, the SS concentrations measured during mid-ebb tide at stations SR3 (27.5 mg/L) and IS5 (34.5 mg/L) exceeded the Action Level (≤ 23.5 mg/L and 120% of upstream control station's reading) and Limit Level (≤ 34.4 mg/L and 130% of upstream control station's reading) respectively. The turbidity readings at SR3 and IS5 reached 24.8 – 25.3 NTU and 22.3 – 22.5 NTU, respectively. The temporary turbid water should not be caused by the runoff from upstream rivers. Because there was no rain or slight rain from 1st to 10th September 2014 (daily total rainfall at the Hong Kong International Airport: 0 – 2.1 mm; extracted from the climatological data of Hong Kong Observatory). The effect of upstream runoff on water quality should be neglectable in that period. Moreover the exceedance of water quality was considered unlikely to be related to the contract works of HKLR according to the 'Notifications of Environmental Quality Limits Exceedances' provided by the respective environmental team. The respective construction of seawall and stone column works, which possibly caused turbid water, was carried out within silt curtain as recommended in the EIA report. Moreover there was no leakage of turbid water, abnormity or malpractice recorded during water sampling. In general, the exceedance of suspended solids concentration was considered to be attributed to other external factors, rather than the contract works.

3.6.47 Based on the weather condition and water quality results in ST, the co-occurrence of cyclone hit and turbid waters in September 2014 might have combined the adverse effects on *Halophila ovalis* that leaded to disappearance of this short-lived and *r*-strategy seagrass species. Fortunately *Halophila ovalis* was a fast-growing species (Vermaat *et al*., 1995). Previous studies showed that the seagrass bed could be recovered to the original sizes in 2 months through vegetative propagation after experimental clearance (Supanwanid, 1996). Moreover it was reported to recover rapidly in less than 20 days after dugong herbivory (Nakaoka and Aioi, 1999). As mentioned, the disappeared seagrass in ST in 1995 could recover gradually after the completion of reclamation works for international airport (Fong, 1998). The seagrass beds of *Halophila ovalis* might recolonize in the mudflat of ST through seed reproduction as long as there was no unfavourable condition in the coming months.

Recolonization of seagrass beds

3.6.48 **Figure 3.12 of Appendix O** shows the recolonization of seagrass bed in ST from December 2014 to September 2024. From March to June 2015, 2 – 3 small patches of *Halophila ovalis* were newly found co-inhabiting with another seagrass species *Zostera japonica*. But the total patch area of *Halophila ovalis* was still very low compared with previous records. The recolonization rate was low while cold weather and insufficient sunlight were possible factors between December 2014 and March 2015. Moreover, it would need to compete with seagrass Zostera japonica for substratum and nutrient, because Zostera japonica had extended and covered the original seagrass bed of *Halophila ovalis* at certain degree. From June 2015 to March 2016, the total seagrass area of *Halophila ovalis* had increased rapidly from 6.8 m^2 to 230.63 m^2. It had recolonized its original patch locations and covered its competitor *Zostera japonica*. In June 2016, the total seagrass area increased sharply to 4707.3m^2. Like the previous records of March to June 2014, the original patch area of *Halophila ovalis* increased further to a horizontally long strand. Another large seagrass beds colonized the lower tidal zone (1.0 – 1.5 m above C.D.). In September 2016, this patch extended much and covered significant soft mud area of ST, resulting in sharp increase of total area (24245 m^2). It indicated the second extensive colonization of this *r*-selected seagrass. In December 2016, this extensive seagrass

patch decreased in size and had been separated into few, undistinguishable patches. Moreover, the horizontal strand nearby the mangrove vegetation decreased in size. The total seagrass bed decreased to 12550 m^2. From March to June 2017, the seagrass bed area remained generally stable (12438- 17046.5 m^2) but the vegetation coverage fluctuated (20 – 50% in March 2017 to 80 – 100% in June 2017). The whole recolonization process took about 2.5 years.

Second disappearance of seagrass bed

3.6.49 In September 2017, the whole seagrass bed of *Halophila ovalis* disappeared again along the shore of TC3 and ST (**Figure 3.12 of Appendix O**). Like the first disappearance of seagrass bed occurred between September and December 2014, strong water current (e.g. cyclone) or deteriorated water qualities (e.g. high turbidity) was the possible cause.

3.6.50 Between the survey periods of June and September 2017, there were four tropical cyclone records in Hong Kong (Merbok in 12- 13th, June; Roke in 23rd, Jul.; Hato in22 – 23rd, Aug.; Pakhar in 26 – 27th, Aug.) (Online database of Hong Kong Observatory) All of them reached signal 8 or above, especially Hato with highest signal 10.

3.6.51 According to the water quality monitoring results (July to August 2017) of the two closest monitoring stations SR3 and IS5 of the respective EM&A programme, the overall water quality was in normal fluctuation. There was an exceedance of suspended solids (SS) at SR3 on 12 July 2017. The SS concentration reached 24.7 mg/L during mid-ebb tide, which exceeded the Action Level (≤ 23.5 mg/L). But it was far below the Limit Level (≤ 34.4 mg/L). Since such exceedance was slight and temporary, its effect to seagrass bed should be minimal.

3.6.52 Overall, the disappearance of seagrass beds in ST has believed the cause of serial cyclone hit in July and August 2017. Based on previous findings, the seagrass beds of both species were expected to recolonize in the mudflat if the vicinal water quality was normal. The whole recolonization process (from few, small patches to extensive strand) would gradually lasting at least 2 years. From December 2017 to March 2018, there was still no recolonization of few, small patches of seagrass at the usual location (**Figure 3.12 of Appendix O**). It was different from the previous round (March 2015 – June 2017). Until June 2018, the new seagrass patches with small-medium size were found at the usual location (seaward side of mangrove plantation at 2.0 m C.D.) again, indicating the recolonization. However, the seagrass bed area decreased sharply to 22.5 m^2 in September 2018. Again it was believed that the decrease was due to the hit of the super cyclone in September 2018 (Mangkhuton 16th September, highest signal 10). From December 2018 to June 2019, the seagrass bed area increased from 404 m^2 to 1229 m^2 while the vegetation coverage is also increased (December 2018: 5– 85%; March 2019: 50 – 100% and June 2019: 60 – 100%). Relatively, the whole recolonization process would occur slower than the previous round (more than 2 years). From September 2019 to March 2021, the seagrass bed area in ST slightly decreased from 1200 m^2 to 942.05 m^2, which were in normal fluctuation. From March 2021 to December 2021, the seagrass bed area in ST decreased from 942.05 m^2 to 680m^2, which were in normal fluctuation. In March 2022, the seagrass bed area in ST increased significantly to approximately 2040 m^2, which believed to be related to more rain in current dry season. It was observed that the brown filamental algae bloom occurred at ST site in March 2022. Distribution of the algae was overlapped with seagrass beds, mainly the species *Halophila ovalis* and the algae was grown over the top of the seagrass. In some areas, the brown filamental algae fully covered the seagrass bed, referring to Figure 3.9. The seagrass was still alive when checked during the field survey. Whether the algae bloom will kill seagrass in longer period time is unknown. The seagrass distribution and health condition should be checked in the coming June monitoring. The algae bloom of the brown filamental algae at the seagrass bed disappeared as observed in June 2022, referring to Figure 3.9. Seagrass in December 2022 and September 2022 have decreased compared to June 2022 due to normal

seasonal change. Seagrass in March 2023 have increased compare to previous quarter due to normal seasonal change. Seagrass in June 2023 have further increased around 20% compared to the previous period. Seagrass in September and December 2023 have decreased compared to previous quarter due to normal seasonal change. In March 2024, seagrass increased compared to the previous quarter. In September 2024, seagrass coverage increased compare to the previous quarter.

Third disappearance of seagrass bed

3.6.53 All seagrass beds were observed disappeared at the monitoring sites during the December monitoring event in 2024. There were two typhoon/cyclone events that occurred during November 2024 which was an unusual local weather condition, and it may cause the disappearance of the seagrasses.

Impact of the HKLR project

3.6.54 It was the 51st survey of the EM&A Programme during the construction period. Throughout the monitoring period, the disappearance of seagrass beds in three occasions was believed to be the cause of cyclone hits rather than impact of HKLR project. The seagrass bed was recolonized since there had been a gradual increase in size and number from December 2018 to September 2024 after the hit of the super cyclone in September 2018. The seagrass bed area decreased from March 2021 to December 2021, which was in normal fluctuation. It is observed that the seagrass *Halophila ovalis* covered a larger area than before. Total seagrass bed area significantly increased from March 2022 to June 2022 and slightly reduced in September 2022. Seagrass in September and December 2023 have decreased compared to previous quarter and increased in March, June, and September 2024. The third time seagrass bed disappearance was observed during quarterly monitoring in December 2024 and one of the two seagrass species regenerated in March 2025 in ST.

Intertidal Soft Shore Communities

Substratum

3.6.55 **Table 3.3 of Appendix O** and **Figure 3.13 of Appendix O** show the substratum types along the horizontal transect at every tidal level in all sampling zones. The relative distribution of substratum types was estimated by categorizing the substratum types (Gravels & Boulders / Sands / Soft mud) of the ten random quadrats along the horizontal transect. The distribution of substratum types varied among tidal levels and sampling zones:

- In TC1, high percentages of ‘Gravels and Boulders’ (80%) were recorded at a high tidal level. At mid tidal level, Gravels and Boulders ’ was the main substratum type (80%), following by ‘Sands’ (15%) and ‘Soft mud’ (5%). At low tidal level, ‘Soft mud’ was the main substratum type (90%), followed by ‘Sands’ (10%).
- In TC2, the high percentages of ‘Gravels and Boulders’ (90%) was recorded at high tidal level, following by ‘Sands’ (10%). At mid tidal levels, Gravels and Boulders’ was the main substratum type (80%), following by ‘Sands’ (10%) and ‘Soft mud’ (10%). At low tidal level, ‘Soft mud’ covered 95%, ‘Gravels and Boulders’ and ‘Sands ’ covered the remaining 5% of the transect.
- In TC3, the higher percentage of ‘Gravels and Boulders’ was recorded at high tidal level (90%), following by ‘Sands’ and Soft mud covered remaining 10%. At mid tidal level,

'Gravels and Boulders' was the main substratum type (70%), following by 'Sands' (15%) and 'Soft mud' 15%). At low tidal level, 'Soft mud' covered 90% of the transect, and 'Sands ' covered 5% and 'Gravels and Boulders' covered 5% of the transect.

- In ST, 'Gravels and Boulders' was the main substratum type (90%) at high tidal level, followed by 'Sands' (510). At mid tidal levels, Gravels and Boulders' was the main substratum type (70%), following by 'Sands' (15%) and 'Soft mud' (15%). At low tidal level, 'Soft mud' was the main substratum type (85%), 'Sands' covered 10% of the transect, 'Gravels and Boulders' covered 5% of the transect.

3.6.56 There was neither consistent vertical nor horizontal zonation pattern of substratum type in all sampling zones. Such heterogeneous variation should be caused by different hydrology (e.g. wave in different direction and intensity) received by the four sampling zones.

Soft shore communities

3.6.57 **Table 3.4 of Appendix O** lists the total abundance, density and number of taxon of every phylum in this survey. A total of 7,580 individuals were recorded. Mollusca was the most abundant phylum (total abundance 6,633 ind., density 221 ind. m^{-2}, relative abundance 87.5%). The second and third were Arthropoda 559 ind., 19 ind. m^{-2}, 7.4%) which followed by Sipuncula (172 ind., 6 ind. m^{-2}, 2.3%) and Annelida (102 ind., 3 ind. m^{-2}, 1.3%), respectively. The fifth was Cnidania with total abundance 60 ind., density 2 ind.m^{-2} and relative abundance 0.8%. The sixth was Nemertea with total abundance 39 ind., density 1 ind.m^{-2} and relative abundance 0.5%. Platyhelminthes was very low in abundances (density 1 ind. m^{-2}, relative abundance 0.2%). Moreover, the most diverse phylum was Mollusca (32 taxa) followed by Arthropoda (6 taxa). Annelida (3 taxa) and Sipuncula (2 taxa). There was 1 taxon for Nemertea, Cnidaria and Platyhelminthes.

3.6.58 The taxonomic resolution and complete list of recorded fauna are shown in Appendix OV and V respectively. As reported in June 2018, taxonomic revision of three potamidid snail species was conducted according to the latest identification key published by Agriculture, Fisheries and Conservation Department (details see AFCD, 2018), the species names of following gastropod species were revised:

- *Cerithidea cingulata* was revised as *Pirenella* asiatica
- *Cerithidea djadjariensis* was revised as *Pirenella* incisa
- *Cerithidea rhizophorarum* was revised as *Cerithidea moerchii*

Moreover, taxonomic revision was conducted on another snail species while the specie name was revised:

- *Batillaria bornii* was revised as *Clypeomorus bifasciata*

3.6.59 In March 2021, an increased number of sea slugs and their eggs were observed in all sampling zones. It may due to the breeding season of sea slug and the increased of algae on the intertidal.

3.6.60 **Table 3.5 of Appendix O** shows the number of individuals, relative abundance and density of each phylum in every sampling zone. The total abundance (1,787 – 2,009 ind.) varied among the four sampling zones while the phyla distributions were similar. In general, Mollusca was the most dominant phylum (no. of individuals: 1,548 – 1,793 ind.; relative abundance 83.6% - 89.2%; density 206 - 239 ind. m^{-2}). Other phyla were much lower in number of individuals. Arthropoda

(109 - 225 ind.; 5.4% – 12.1%; 15 - 30 ind. m^{-2}) was common phyla relatively. Other phyla were very low in abundance in all sampling zones.

Dominant species in every sampling zone

3.6.61 **Table 3.6 of Appendix O** lists the abundant species in every sampling zone. In the present survey, most of the listed abundant species were of low to moderate densities (42 – 95 ind. m^{-2}). Few of the listed species were of high or very high density (>100 ind. m^{-2}), which were regarded as dominant species. Other listed species of lower density (<42 ind. m^{-2}) were regarded as common species.

3.6.62 In TC1, the substratum was mainly 'Gravels and Boulders' at high and mid tidal levels. At high tidal level, the rock oyster *Saccostrea cucullata (*mean density 109 ind. m^{-2}; relative abundance 39%) was the dominant species found at high density and the gastropod *Monodonta labio* (65 ind. m^{-2}; relative abundance 23%) was of low to moderate density. At mid tidal level, the rock oyster *Saccostrea cucullata* (80 ind. m^{-2}, 33%) was at dominant species with low to moderate density. The gastropod *Monodonta labio* (51 ind. m^{-2}, 21%) was at low to moderate densities, followed by *Batillaria zonalis* (36ind. M^{-2}, 15%) at low to moderate densities. At low tidal level (main substratum type 'Soft mud'), the *Batillaria multiformis* (44 ind. m^{-2}, 22%), the *Nodilittorina radiata* (39 ind. m^{-2}, 20%) and *Barbatia virescens* (32 ind. m^{-2}, 16%) were of lower density, regarded as common species.

3.6.63 In TC2, the substratum types were mainly ' Gravels and Boulders' at a high tidal level. The rock oyster *Saccostrea cucullata* (113 ind. m^{-2}, 38%) was the dominant species found at high density. The gastropod *Monodonta labio* (60 ind. m^{-2}, 20%) was dominant at low to moderate density and the *Batillaria multiformis* (38 ind. m^{-2}, 13%) was at lower density. At mid tidal level (main substratum types 'Soft mud' and 'Gravels and Boulders'), rock oyster *Saccostrea cucullata* (79 ind. m^{-2}, 34%), gastropods *Monodonta zonalis* (32 ind. m^{-2}, 14%) and *Batillaria labio* (38 ind. m^{-2}, 16%) were dominant at low density. Substratum types 'Soft Mud' were mainly distributed at low tidal level, the *Barbatia virescens* (54 ind. m^{-2}, 26%) was dominant at low densities, the *Batillaria multiformis* (40 ind. m^{-2}, 19%) were of lower densities, regarded as common species.

3.6.64 In TC3, the substratum type was mainly 'Gravels and Boulders' at high tidal level. The rock oyster *Saccostrea cucullata* (117 ind. m^{-2}, 40%) was of dominant species at high density and the gastropod *Monodonta labio* (66 ind. m^{-2}, 22%) was of low to moderate density. At mid tidal level (main substratum types 'Gravels and Boulders'), the rock oyster *Saccostrea cucullata* (86 ind. m^{-2}, 35%) was of the dominant species at low to moderate density. The gastropod *Monodonta labio* (40 ind. m^{-2}, 17%) was at low density level. At low tidal level, the major substratum type was 'Soft mud'. The *Barbatia virescens* (51 ind. m^{-2}, 22%) at low to moderate density. The *Lunella granulate* (37 ind. m^{-2}, 16%), *Batillaria multiformis* (35 ind. m^{-2}, 15%) were dominant at low densities.

3.6.65 In ST, the major substratum type was 'Gravels and Boulders' at high tidal level. At high tidal level, the rock oyster *Saccostrea cucullata* (110 ind. m^{-2}, 38%) was abundant at high density. The gastropods *Monodonta labio*(48 ind. m^{-2}, 16%) were at low to moderate densities. At mid tidal level (main substratum types 'Gravels and Boulders'), the gastropod *Monodonta labio* (100 ind. m^{-2}, 33%) was abundant at high density. The rock oyster *Saccostrea cucullata* (82 ind. m^{-2}, 27%) was the dominant species at low to moderate densities. At low tidal level (major substratum: 'Soft mud'), the *Batillaria zonalis* (61 ind. m^{-2}, 29%) was at low to moderate densities and *Lunella granulata* (39 ind. m^{-2}, 18%) was at low density.

3.6.66 In general, there was no consistent zonation pattern of species distribution across all sampling zones and tidal levels. The species distribution was determined by the type of substratum

primarily. In general, rock oyster *Saccostrea cucullata* (776 ind.), gastropods *Monodonta labio* (468 ind.) and *Batillaria multiformis* (188 ind.) were the most common species on gravel and boulders substratum. *Batillaria zonalis* (130 ind.) was the most common species on sands and soft mud substrata.

Biodiversity and abundance of soft shore communities

3.6.67 **Table 3.7 of Appendix O** shows the mean values of species number, density, and biodiversity index *H'* and species evenness *J* of soft shore communities at every tidal level and in every sampling zone. As mentioned above, the differences among sampling zones and tidal levels were determined by the major type of substratum primarily.

3.6.68 Among the sampling zones, the mean species number was varied from 15 - 18 spp. 0.25 m^{-2} among the four sampling zones. The mean densities of ST (269 ind. m^{-2}) and TC3 (257 ind. m^{-2}) is higher than TC2 (247 ind. m^{-2} TC1 (238 ind. m^{-2}). The higher densities of ST and TC3 are due to the relatively high number of individuals in each quadrat. The mean H' for TC3 was 2.23, ST was 2.2, TC2 was 2.13 and TC1 was 2.07, followed by while the mean J of ST and TC3 was 0.8, slightly higher than TC1 and TC2 (0.77). This can be due to the relatively non-even taxa distribution.

3.6.69 In the present survey, no clear trend of mean species number, mean density, *H'* and *J* observed among the tidal level.

3.6.70 **Figures 3.14-3.17 of Appendix O** show the temporal changes of mean species number, mean density, *H'* and *J* at every tidal level and in every sampling zone along the sampling months. In general, all the biological parameters fluctuated seasonally throughout the monitoring period. Lower mean species number and density were recorded in dry season (December) but the mean *H'* and *J* fluctuated within a limited range.

3.6.71 From June to December 2017, there were steady decreasing trends of mean species number and density in TC2, TC3 and ST regardless of tidal levels. It might be an unfavorable change reflecting environmental stress. The heat stress and serial cyclone hit were believed to be the causes during the wet season of 2017. From March 2018 to December 2024 (present survey), generally increases of mean species number and density were observed in all sampling zones. It indicated the recovery of intertidal community.

Impact of the HKLR project

3.6.72 It was the 51st survey of the EM&A programme during the construction period. Based on the results, impacts of the HKLR project were not detected on intertidal soft shore community. Abnormal phenomena (e.g. rapid, consistent or non-seasonal decline of fauna densities and species number) were not recorded.

3.7 Solid and Liquid Waste Management Status

3.7.1 The Contractor registered with EPD as a Chemical Waste Producer on 12 July 2012 for the Contract. Sufficient numbers of receptacles were available for general refuse collection and sorting.

3.7.2 The summary of waste flow table is detailed in **Appendix K**.

3.7.3 The Contractor was reminded that chemical waste containers should be properly treated and stored temporarily in designated chemical waste storage area on site in accordance with the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes.

3.8 Environmental Licenses and Permits

3.8.1 The valid environmental licenses and permits during the reporting period are summarized in **Appendix L.**

4 Environmental Complaint and Non-compliance

4.1 Environmental Exceedances

4.1.1 The detailed air quality, noise, water quality and dolphin exceedances are provided in **Appendix M**. Also, the summaries of the environmental exceedances are presented as follows:

Air Quality

4.1.2 No Action and Limit Level exceedances of 1-hr TSP were recorded at AMS5 and AMS6. No Action and Limit Level exceedances of 24-hr TSP were recorded at AMS5. No Action level exceedances of 24-hr TSP was recorded at AMS6 whereas One Action Level exceedance of 24-hr TSP was recorded at AMS6.

Noise

4.1.3 No Action/Limit Level exceedances for noise were recorded during daytime on normal weekdays of the reporting period.

Water Quality

4.1.4 For marine water quality monitoring, no Action Level and Limit Level exceedances of dissolved oxygen level, turbidity level and suspended solid level were recorded.

Dolphin

4.1.5 There was a Limit Level exceedance of dolphin monitoring for the quarterly monitoring data (between March 2025 and May 2025). According to the contractor's information, toe loading removal works and reinstatement works were undertaken for HKLR03 during the quarter of March 2025 and May 2025.

4.1.6 There is no evidence showing the current LL non-compliance directly related to the construction works of HKLR03 (where the amounts of working vessels for HKLR03 have been decreasing), although the generally increased amount of vessel traffic in NEL during the impact phase has been partly contributed by HKLR03 works since October 2012. It should also be noted that work area under HKLR03 (adjoining the Airport Island) situates in waters which has rarely been used by dolphins in the past, and the working vessels under HKLR03 have been travelling from source to destination in accordance with the Marine Travel Route to minimize impacts on Chinese White Dolphin (CWD). In addition, the contractor will implement proactive mitigation measures such as avoiding anchoring at Marine Department's designated anchorage site – Sham Shui Kok Anchorage (near Brothers Island) as far as practicable.

4.1.7 All dolphin protective measures are fully and properly implemented in accordance with the EM&A Manual, EIA report and EP. According to the Regular Marine Travel Route Plan, the travelling speed of vessels must not exceed 5 knots when crossing the edge of the Brothers Marine Park. The Contractor will continue to provide training for skippers to ensure that their working vessels travel from source to destination to minimize impacts on Chinese White Dolphin and avoid anchoring at Marine Department's designated anchorage site - Sham Shui Kok Anchorage (near Brothers Island) as far as practicable. Also, it is recommended to complete the marine works of the Contract as soon as possible so as to reduce the overall duration of impacts and allow the dolphins population to recover as early as possible.

4.2 Summary of Environmental Complaint, Notification of Summons and Successful Prosecution

4.2.1 There was no complaint received in relation to the environmental impacts during this reporting period. The details of cumulative statistics of Environmental Complaints are provided in **Appendix N**.

4.2.2 No notification of summons and prosecution was received during the reporting period. Statistics on notifications of summons and successful prosecutions are summarized in **Appendix M**.

5 Comments, Recommendations and Conclusion

5.1 Comments

5.1.1 According to the environmental site inspections undertaken during the reporting period, no comments were issued.

5.2 Recommendations

5.2.1 The impact monitoring programme ensured that any deterioration in environmental condition was readily detected and timely actions taken to rectify any non-compliance. Assessment and analysis of monitoring results collected demonstrated the environmental impacts of the contract. With implementation of the recommended environmental mitigation measures, the contract's environmental impacts were considered environmentally acceptable. The weekly environmental site inspections ensured that all the environmental mitigation measures recommended were effectively implemented.

5.2.2 The recommended environmental mitigation measures, as included in the EM&A programme, effectively minimize the potential environmental impacts from the contract. Also, the EM&A programme effectively monitored the environmental impacts from the construction activities and ensure the proper implementation of mitigation measures. No particular recommendation was advised for the improvement of the programme.

5.3 Conclusions

5.3.1 The construction phase and EM&A programme of the Contract commenced on 17 October 2012. This is the fifty-first Quarterly EM&A Report which summarizes the monitoring results and audit findings of the EM&A programme during the reporting period from 1 March 2025 to 31 May 2025.

Air Quality

5.3.2 No Action and Limit Level exceedances of 1-hr TSP were recorded at AMS5 and AMS6. No Action and Limit Level exceedances of 24-hr TSP were recorded at AMS5. No Action level exceedances of 24-hr TSP was recorded at AMS6 whereas One Action Level exceedance of 24-hr TSP was recorded at AMS6. The existing air quality monitoring location AMS6 - Dragonair / CNAC (Group) Building (HKIA) was handed over to Airport Authority Hong Kong on 31 March 2021. 1-hr and 24-hr TSP monitoring at AMS6 was temporarily suspended starting from 1 April 2021 and resumed on 7 August 2024.

Noise

5.3.3 No Action/Limit Level exceedances for noise were recorded during daytime on normal weekdays of the reporting period.

Water Quality

5.3.4 For marine water quality monitoring, no Action Level and Limit Level exceedances of dissolved oxygen level, turbidity level and suspended solid level were recorded during the reporting month.

Dolphin

5.3.5 During the present quarter of dolphin monitoring, no adverse impact from the activities of this construction project on Chinese White Dolphins was noticeable from general observations.

5.3.6 Although dolphins rarely occurred in the area of HKLR03 construction in the past and during the baseline monitoring period, it is apparent that dolphin usage has been significantly reduced in NEL since 2012, and many individuals have shifted away from the important habitat around the Brothers Islands.

5.3.7 It is critical to continuously monitor the dolphin usage in North Lantau region to determine whether the dolphins are continuously affected by the construction activities in relation to the HZMB-related works, and whether suitable mitigation measure can be applied to revert the situation.

Mudflat - Sedimentation Rate

5.3.8 This measurement result was generally and relatively higher than the baseline measurement at S1, S2, S3 and S4. The mudflat level is continuously increased.

Mudflat - Ecology

5.3.9 The March 2025 survey results indicate that impacts of the HKLR project were not detected on intertidal soft shore community. Abnormal phenomena (e.g. rapid, consistent or non-seasonal decline of fauna densities and species number) were not recorded. Based on the monitoring results, no detectable impact on horseshoe crab was revealed due to HKLR project. The population change was mainly determined by seasonal variation, no abnormal phenomenon of horseshoe crab individual, such as large number of dead individuals on the shore had been reported. Throughout the monitoring period, the disappearance of seagrass beds in three occasions was believed to be the cause of cyclone hits rather than impact of HKLR project. The seagrass bed was recolonized since there had been a gradual increase in size and number from December 2018 to September 2024 after the hit of the super cyclone in September 2018. The seagrass bed area decreased from March 2021 to December 2021, which was in normal fluctuation. It is observed that the seagrass *Halophila ovalis* covered a larger area than before. Total seagrass bed area significantly increased from March 2022 to June 2022 and slightly reduced in September 2022. Seagrass in September and December 2023 have decreased compared to previous quarter and increased in March, June, and September 2024. The third time seagrass bed disappearance was observed during quarterly monitoring in December 2024 and one of the two seagrass species regenerated in March 2025 in ST. Based on the results, impacts of the HKLR project were not detected on intertidal soft shore community.

Environmental Site Inspection and Audit

5.3.10 Environmental site inspection was carried out on 5,12, 19 and 28 March 2025; 2, 9, 17, 25 and 30 April 2025; 7, 14, 21 and 30 May 2025.

5.3.11 There was no complaint received in relation to the environmental impact during the reporting period.

5.3.12 No notification of summons and prosecution was received during the reporting period.

FIGURES

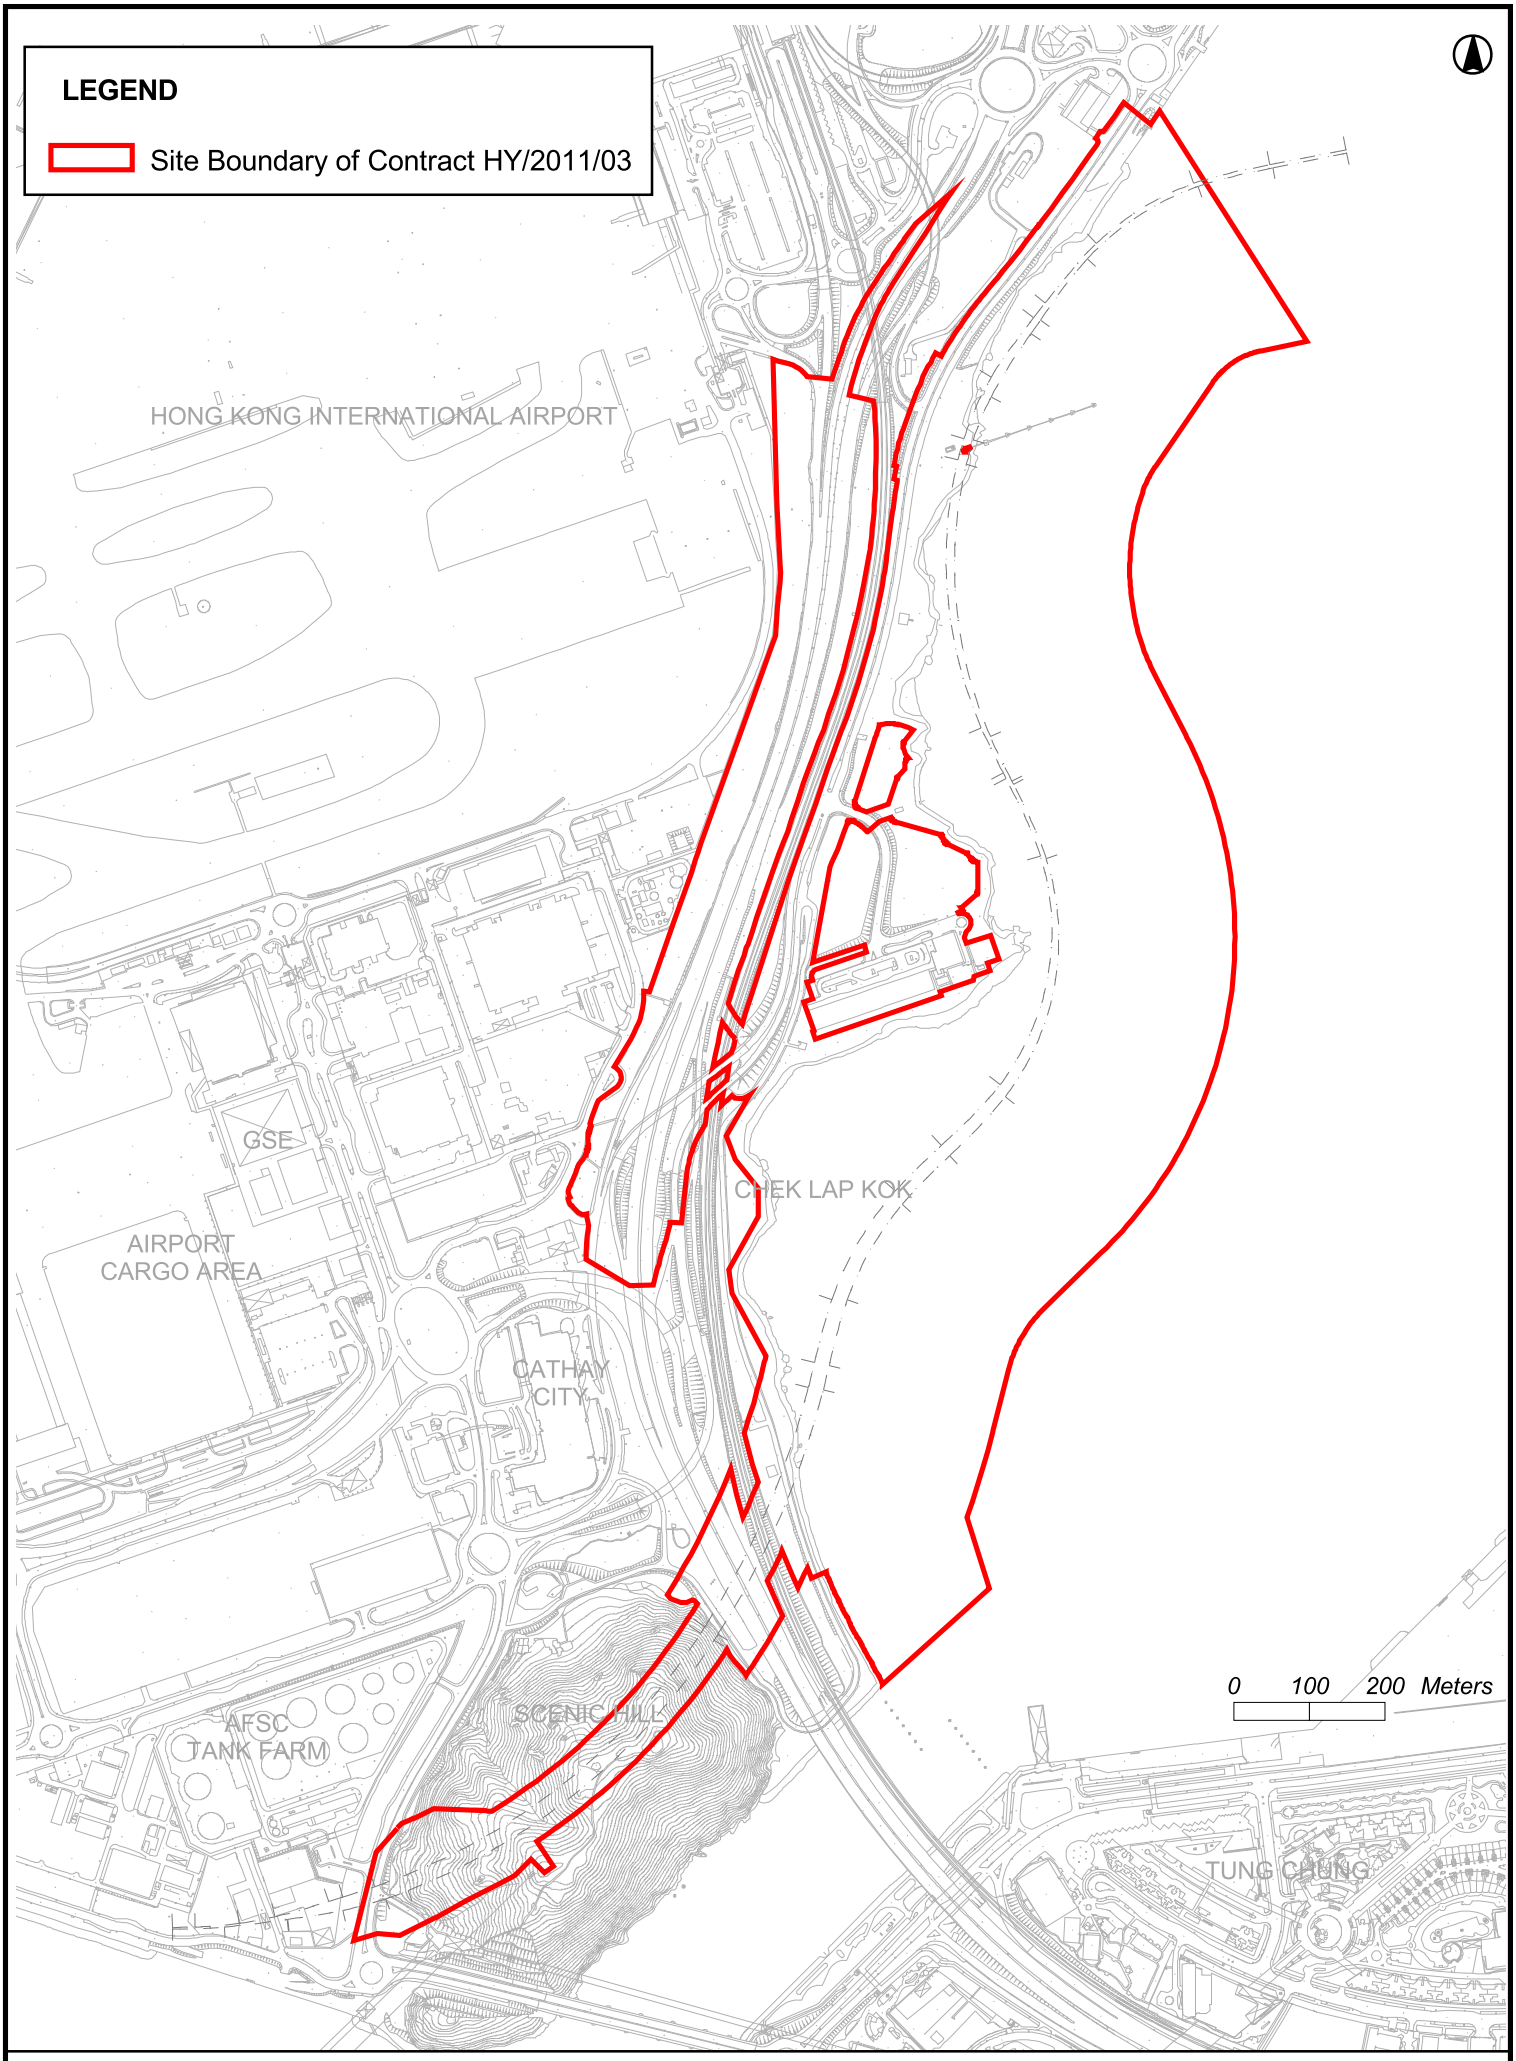

Figure 1.1 Location of the Site

DO NOT SCALE DRAWING. CHECK ALL DIMENSIONS ON SITE.
ALL RIGHTS RESERVED.
© OVE ARUP & PARTNERS HONG KONG LIMITED.

INSET A

824500 N
822000 N
822500 E
825000 E
827500 E
805000 E
810000 E
815000 E
820000 N
815000 N

SR10A(N)
SR10A
SR10B
SR10B(N2)
TSING MA BRIDGE
TSING YI
MA WAN
LANTAU ISLAND

Indicative 3RS Project Site Boundary

SR5(N)
IS10(N)
IS10
Proposed Hong Kong Boundary Crossing Facilities (HKBCF) (By others)
SR5
PROPOSED TUEN MUN-CHEK LAP KOK LINK (BY OTHERS)
CS(Mf)5

HONG KONG INTERNATIONAL AIRPORT (HKIA)
CS2
CS2(A)
IS7
IS(Mf)9
AMS6
IS(Mf)6
IS8(N)
IS8
SR4(N3)
SR4(N2)
SR4(N)
SR4
IS5
AIRPORT CHANNEL
SR3(N)
SR3
AMS5
NMS5
TUNG CHUNG
SAN SHEK WAN
SHA LO WAN
MUDFLAT SURVEY (SAN TAU)
MUDFLAT SURVEY (TUNG CHUNG BAY)
LANTAU ISLAND

HKSAR BOUNDARY
HZMB MAIN BRIDGE (BY OTHERS)
PROPOSED HKLR
PROPOSED HONG KONG LINK ROAD (HKLR)

Monitoring Stations	Coordinates	
	Easting	Northing
IS5	811579	817106
IS(Mf)6	812101	817873
IS7	812244	818777
IS8	814251	818412
IS8(N)	814413	818570
IS(Mf)9	813273	818850
IS10(N)	812942	820881
SR3(N)	810689	816591
SR4(N2)	814688	817996
SR4(N3)	814779	818032
SR5(N)	812569	821475
SR10A(N)	823644	823484
SR10B(N2)	823689	823159
CS2(A)	805232	818606
CS(Mf)5	817990	821129

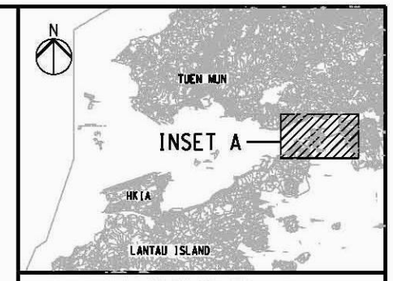

KEY PLAN

NOTES

1. EXACT LOCATIONS OF MONITORING STATIONS ARE TO BE DETERMINED ON SITE. THE CONTRACTOR AND ENVIRONMENTAL TEAM (ET) SHALL AGREE WITH THE INDEPENDENT ENVIRONMENTAL CHECKER (IEC) AND ENVIRONMENTAL PROJECT OFFICE (ENPO) AND APPROVED BY THE SUPERVISING OFFICER FOR THE PROPOSED LOCATION OF THE MONITORING STATIONS.
2. THE LOCATION AND EXTENT OF MUDFLAT SURVEY SHOWN ON THIS DRAWING ARE APPROXIMATE ONLY. THE CONTRACTOR AND ET SHALL DETERMINE AND AGREE WITH THE IEC, ENPO AND SUPERVISING OFFICER THE DETAILS OF THE MUDFLAT SURVEY IN ACCORDANCE WITH THE REQUIREMENTS STIPULATED IN THE EIA REPORTS AND EM&A MANUALS.
3. THE CONTRACTOR SHALL COMPLY WITH THE REQUIREMENTS STIPULATED IN THE EM&A MANUALS TO CONDUCT THE ENVIRONMENTAL MONITORING AND AUDIT WORKS.

LEGEND

- WORKS BOUNDARY OF CONTRACT HY/2011/03
- IS — IMPACT STATIONS (WATER QUALITY)
- CS — CONTROL/FAR FIELD STATIONS (WATER QUALITY)
- SR — SENSITIVE RECEIVERS STATIONS (WATER QUALITY)
- ST — STATION FOR SENS(T)IVITY TEST RESULT (WATER QUALITY)
- AMS — MONITORING STATIONS (AIR QUALITY)
- NMS — MONITORING STATIONS (NOISE)
- MUDFLAT ECOLOGICAL SAMPLING LOCATION

Rev	Description	By	Date
A	TENDER ADDENDUM ISSUE	AW	11/11

Consultant
ARUP 奧雅納工程顧問 Ove Arup & Partners Hong Kong Limited

Contract No. and Title:
Contract No. HY/2011/03
Hong Kong-Zhuhai-Macao Bridge
Hong Kong Link Road -
Section Between Scenic Hill and
Hong Kong Boundary Crossing Facilities

Drawing title
ENVIRONMENTAL MONITORING STATIONS

Drawing: Figure 2.1 | Rev. A
Drawn: RY | Date: 11/11 | Checked: AW | Approved: SK
Scale: 1:25000 @A1 | Status:

COPYRIGHT RESERVED

路政署 HIGHWAYS DEPARTMENT
港珠澳大橋香港工程管理處 Hong Kong - Zhuhai - Macao Bridge Hong Kong Project Management Office

Printed by : 10/11/2011
Filename : J:\21448?\Record\HY_2011_03\Tender Addendum (2011-11-11)\DGN\E-HY_2011_03-DRG_310-A-00.dgn

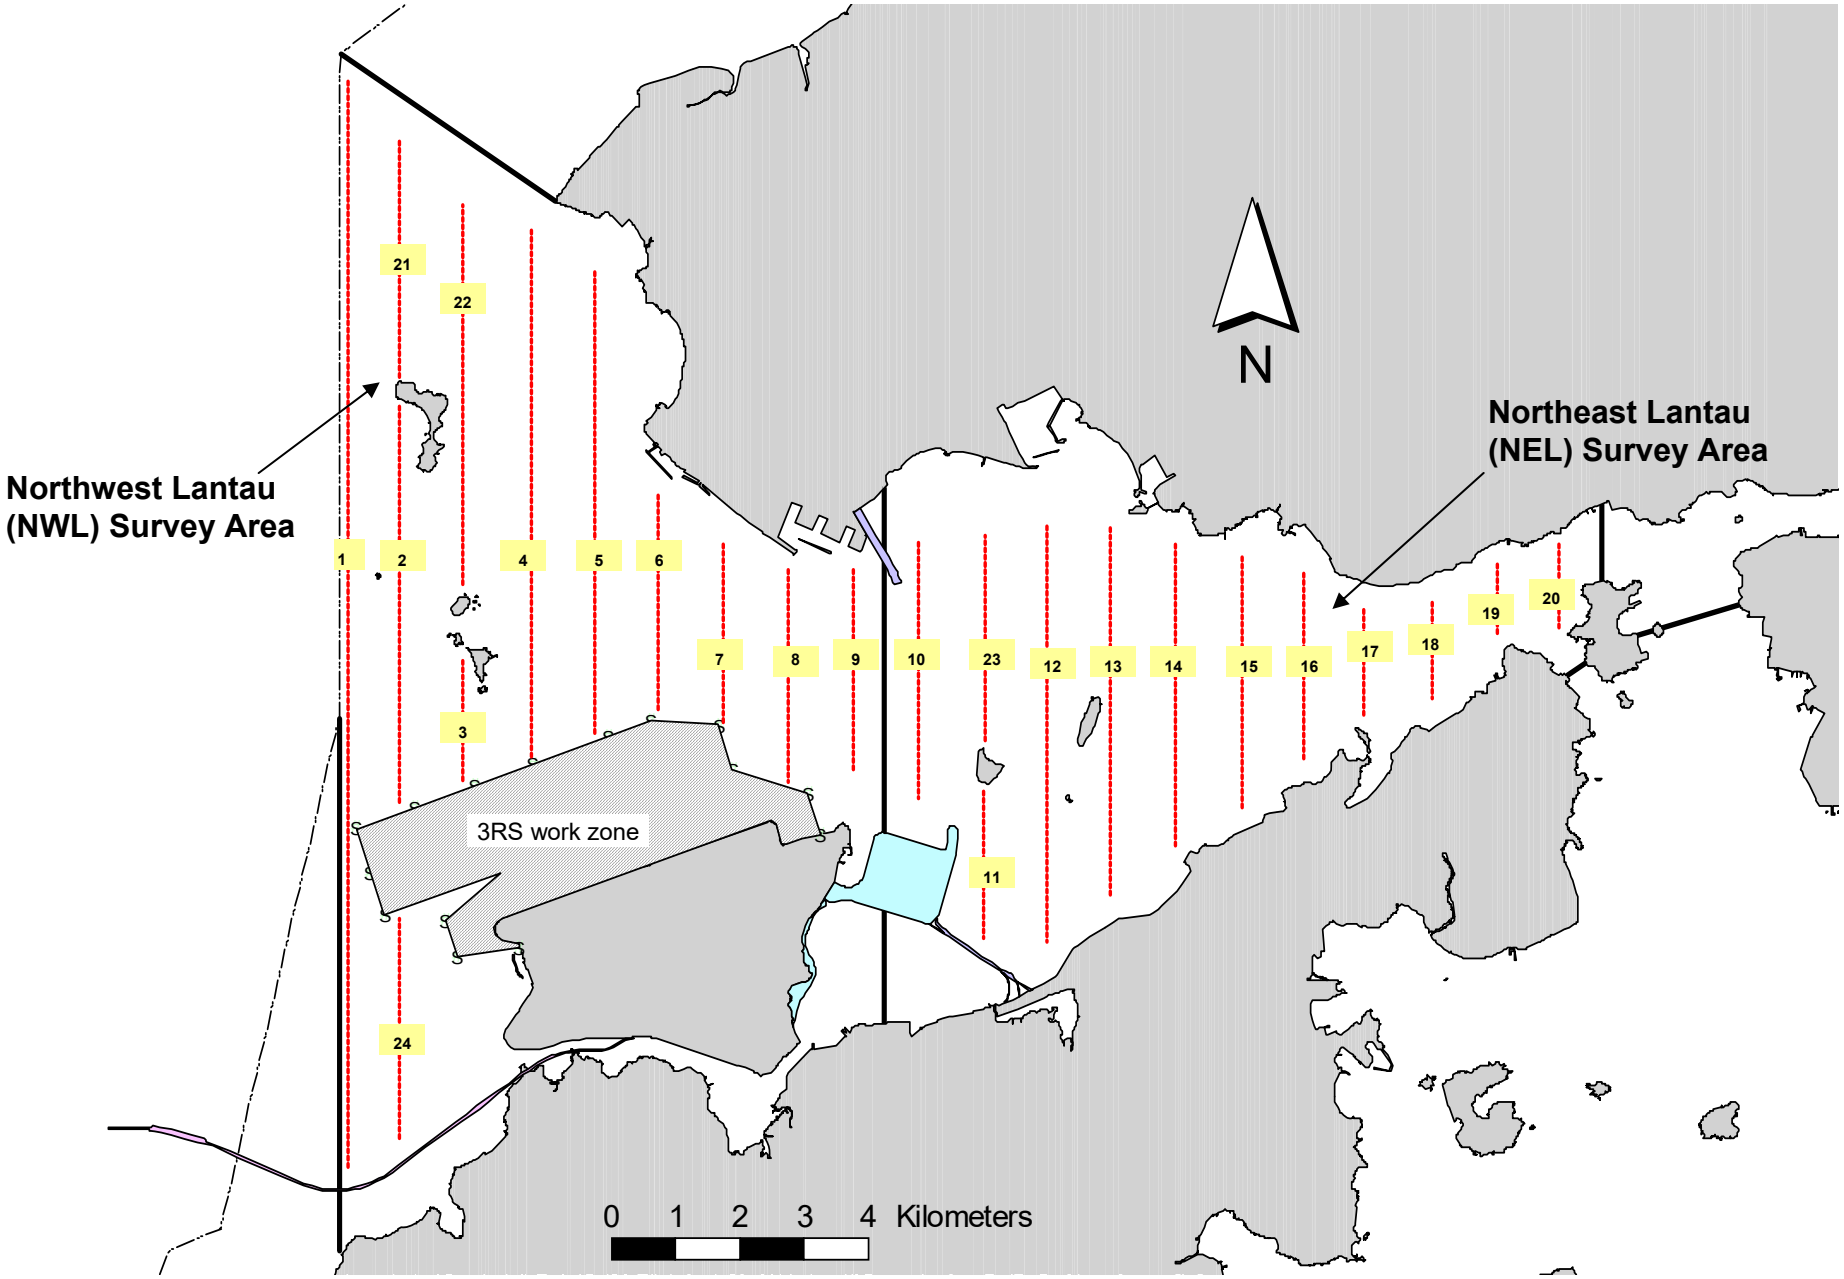

Figure 2.2. Transect Line Layout in Northwest and Northeast Lantau Survey Areas

APPENDIX A

Environmental Management Structure

Contact Information of Key Personnel

Party	Position	Name	Telephone	Fax
Supervising Officer's Representative (Ove Arup & Partners Hong Kong Limited)	(Senior Resident Engineer, SRE)	Eddie Tsang	3968 4802	2109 1882
Environmental Project Office / Independent Environmental Checker (ANewR Consulting Limited) [1]	Environmental Project Office Leader	Louis Kwan	9275 0975	3007 8648
	Independent Environmental Checker	James Choi	6122 5213	3007 8648
Contractor (China State Construction Engineering (Hong Kong) Ltd.)	Project Manager	S. Y. Tse	3968 7002	2109 2588
	Environmental Officer	Federick Wong	3968 7117	2109 2588
Environmental Team (Meinhardt Infrastructure and Environment Limited)	Environmental Team Leader	Claudine Lee	2859 5409	2559 0738
24 hours complaint hotline	---	---	5699 5730	---

Remark 1: ANewR Consulting Limited has been employed by HyD as the Independent Environmental Checker (IEC) and Environmental Project Office (ENPO) for the Project with effective from 1 October 2022.

APPENDIX B

Construction Programme

中國建築工程(香港)有限公司
CHINA STATE CONSTRUCTION ENGRG. (HONG KONG) LTD.

Hong Kong-Zhuhai-Macao Bridge Hong Kong Link Road - Section Between Scenic Hill and Hong Kong Boundary Crossing Facilities

Construction Programme Mar - Jun 2025

Description	Mar-25				Apr-25				May-25				Jun-25			
	W1	W2	W3	W4	W1	W2	W3	W4	W1	W2	W3	W4	W1	W2	W3	W4
Reinstatement Works																

APPENDIX C

Location of Works Areas

DO NOT SCALE DRAWING. CHECK ALL DIMENSIONS ON SITE.
ALL RIGHTS RESERVED.
© OVE ARUP & PARTNERS HONG KONG LIMITED.

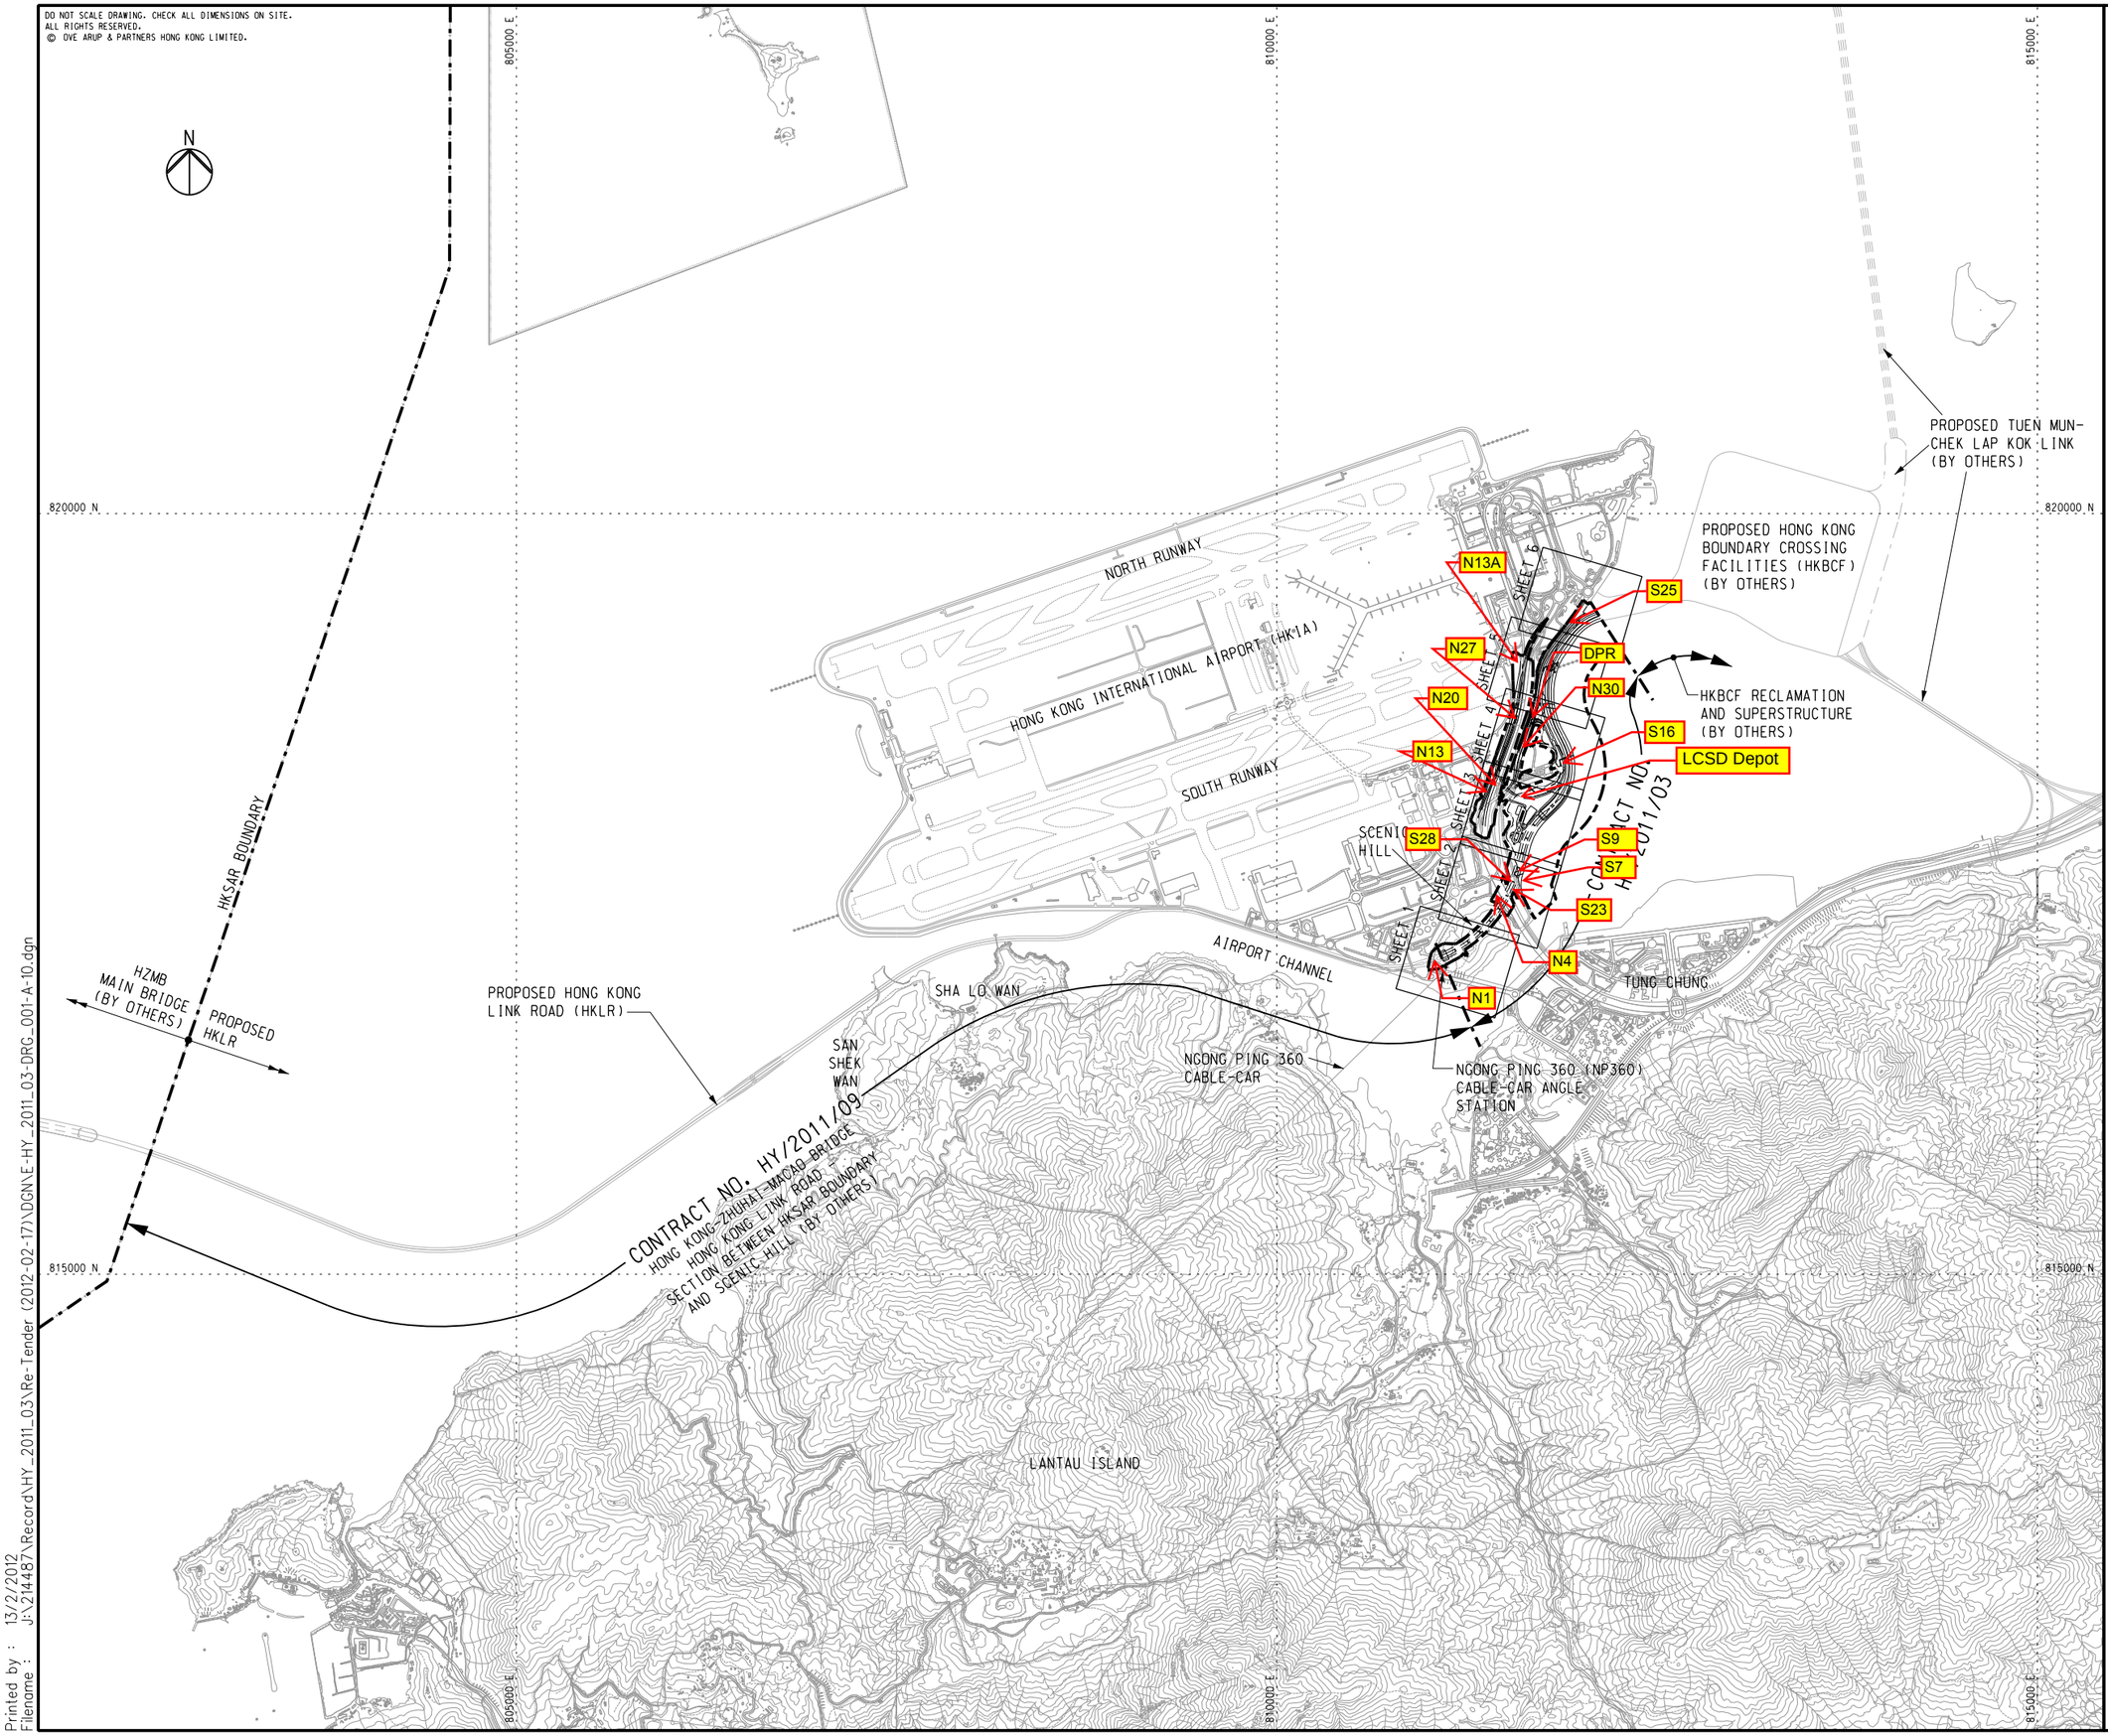

NOTES

1. THIS DRAWING SHALL BE READ IN CONJUNCTION WITH DRG. NOS. 214487/2/T/002 - 007.

LEGEND

SITE BOUNDARY

Rev	Description	By	Date
A	TENDER ISSUE	IL	02/12

Consultant

ARUP 奧雅納工程顧問 Ove Arup & Partners Hong Kong Limited

Contract No. and Title:

Contract No. HY/2011/03

Hong Kong-Zhuhai-Macao Bridge
Hong Kong Link Road -
Section Between Scenic Hill and
Hong Kong Boundary Crossing Facilities

Drawing title

GENERAL LAYOUT
KEY PLAN

Drawing no.		Rev.
214487/2/T/001		A
Drawn: RY	Date: 02/12	Checked: IL	Approved: SK
Scale: 1:20000 @A1		Status: TENDER	

COPYRIGHT RESERVED

路政署 HIGHWAYS DEPARTMENT
港珠澳大橋香港工程管理處
Hong Kong - Zhuhai - Macao Bridge
Hong Kong Project Management Office

Printed by : 13/2/2012
Filename : J:\214487\Record\HY_2011_03\Re-Tender (2012-02-17)\DGN\E-HY_2011_03-DRG_001-A-10.dgn

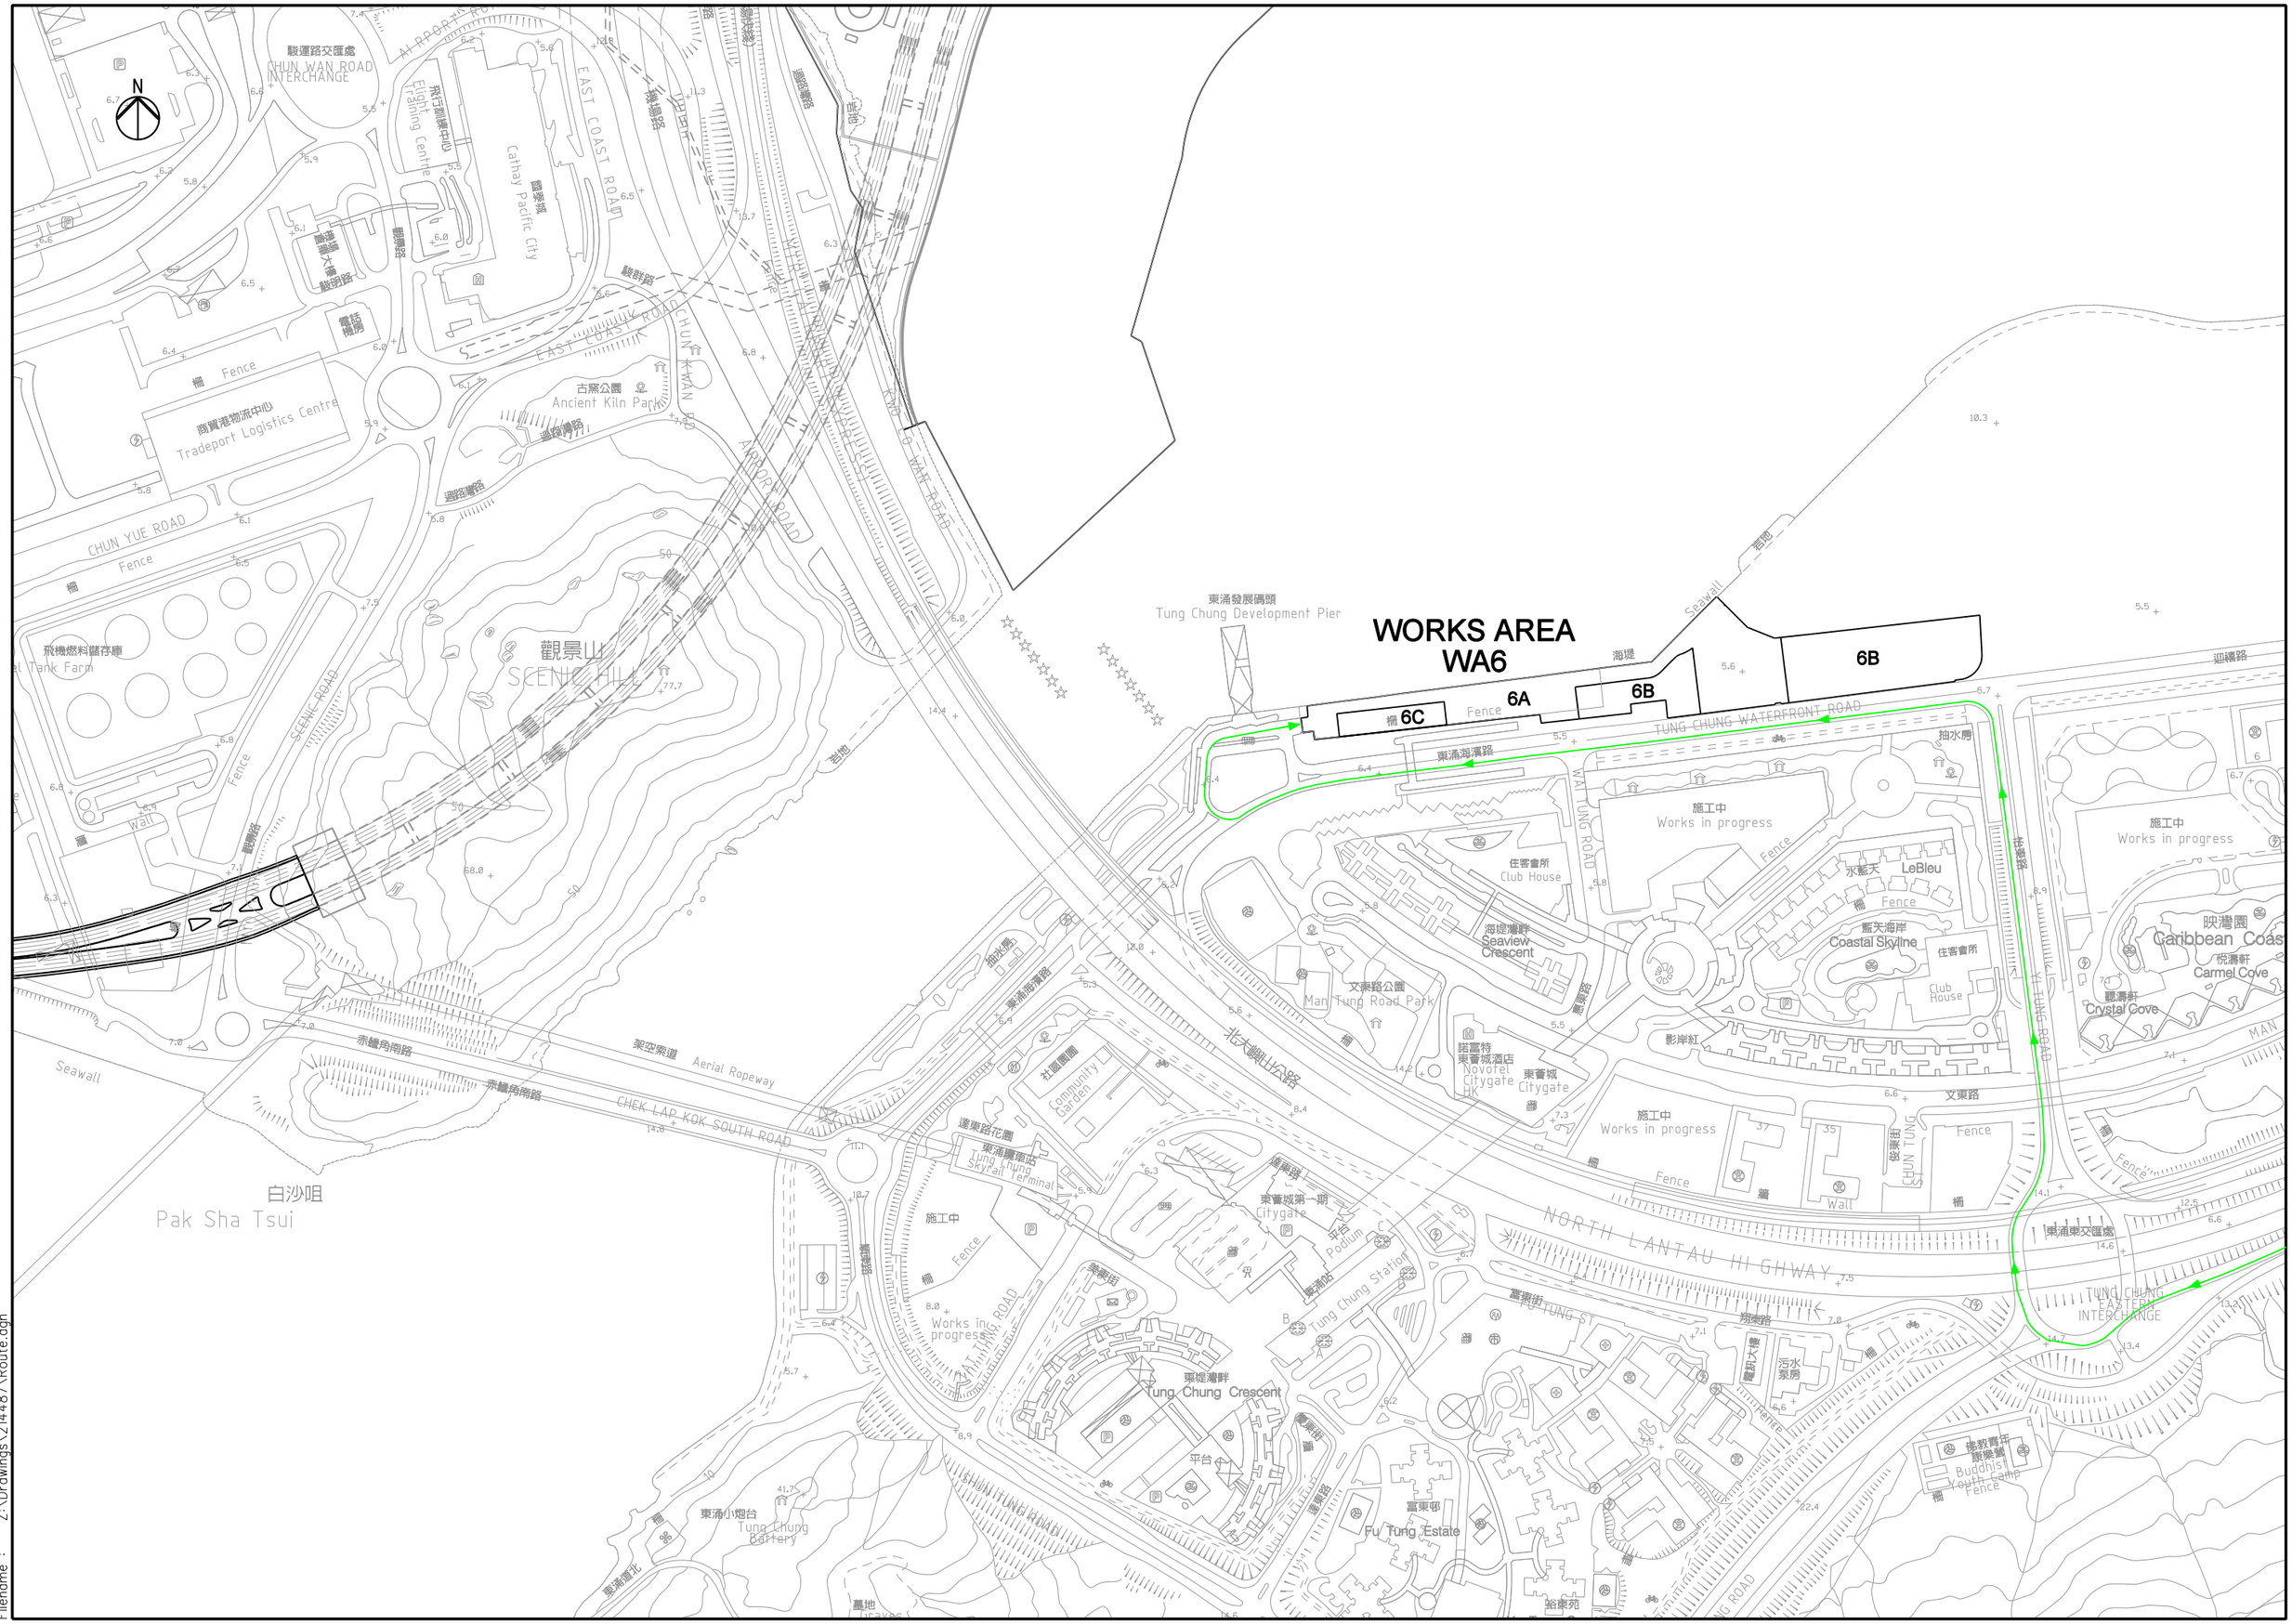

Printed by : 30/5/2012
Filename : Z:\Drawings\214487\Route.dgn

DO NOT SCALE DRAWING. CHECK ALL DIMENSIONS ON SITE.
ALL RIGHTS RESERVED.
© OVE ARUP & PARTNERS HONG KONG LIMITED.

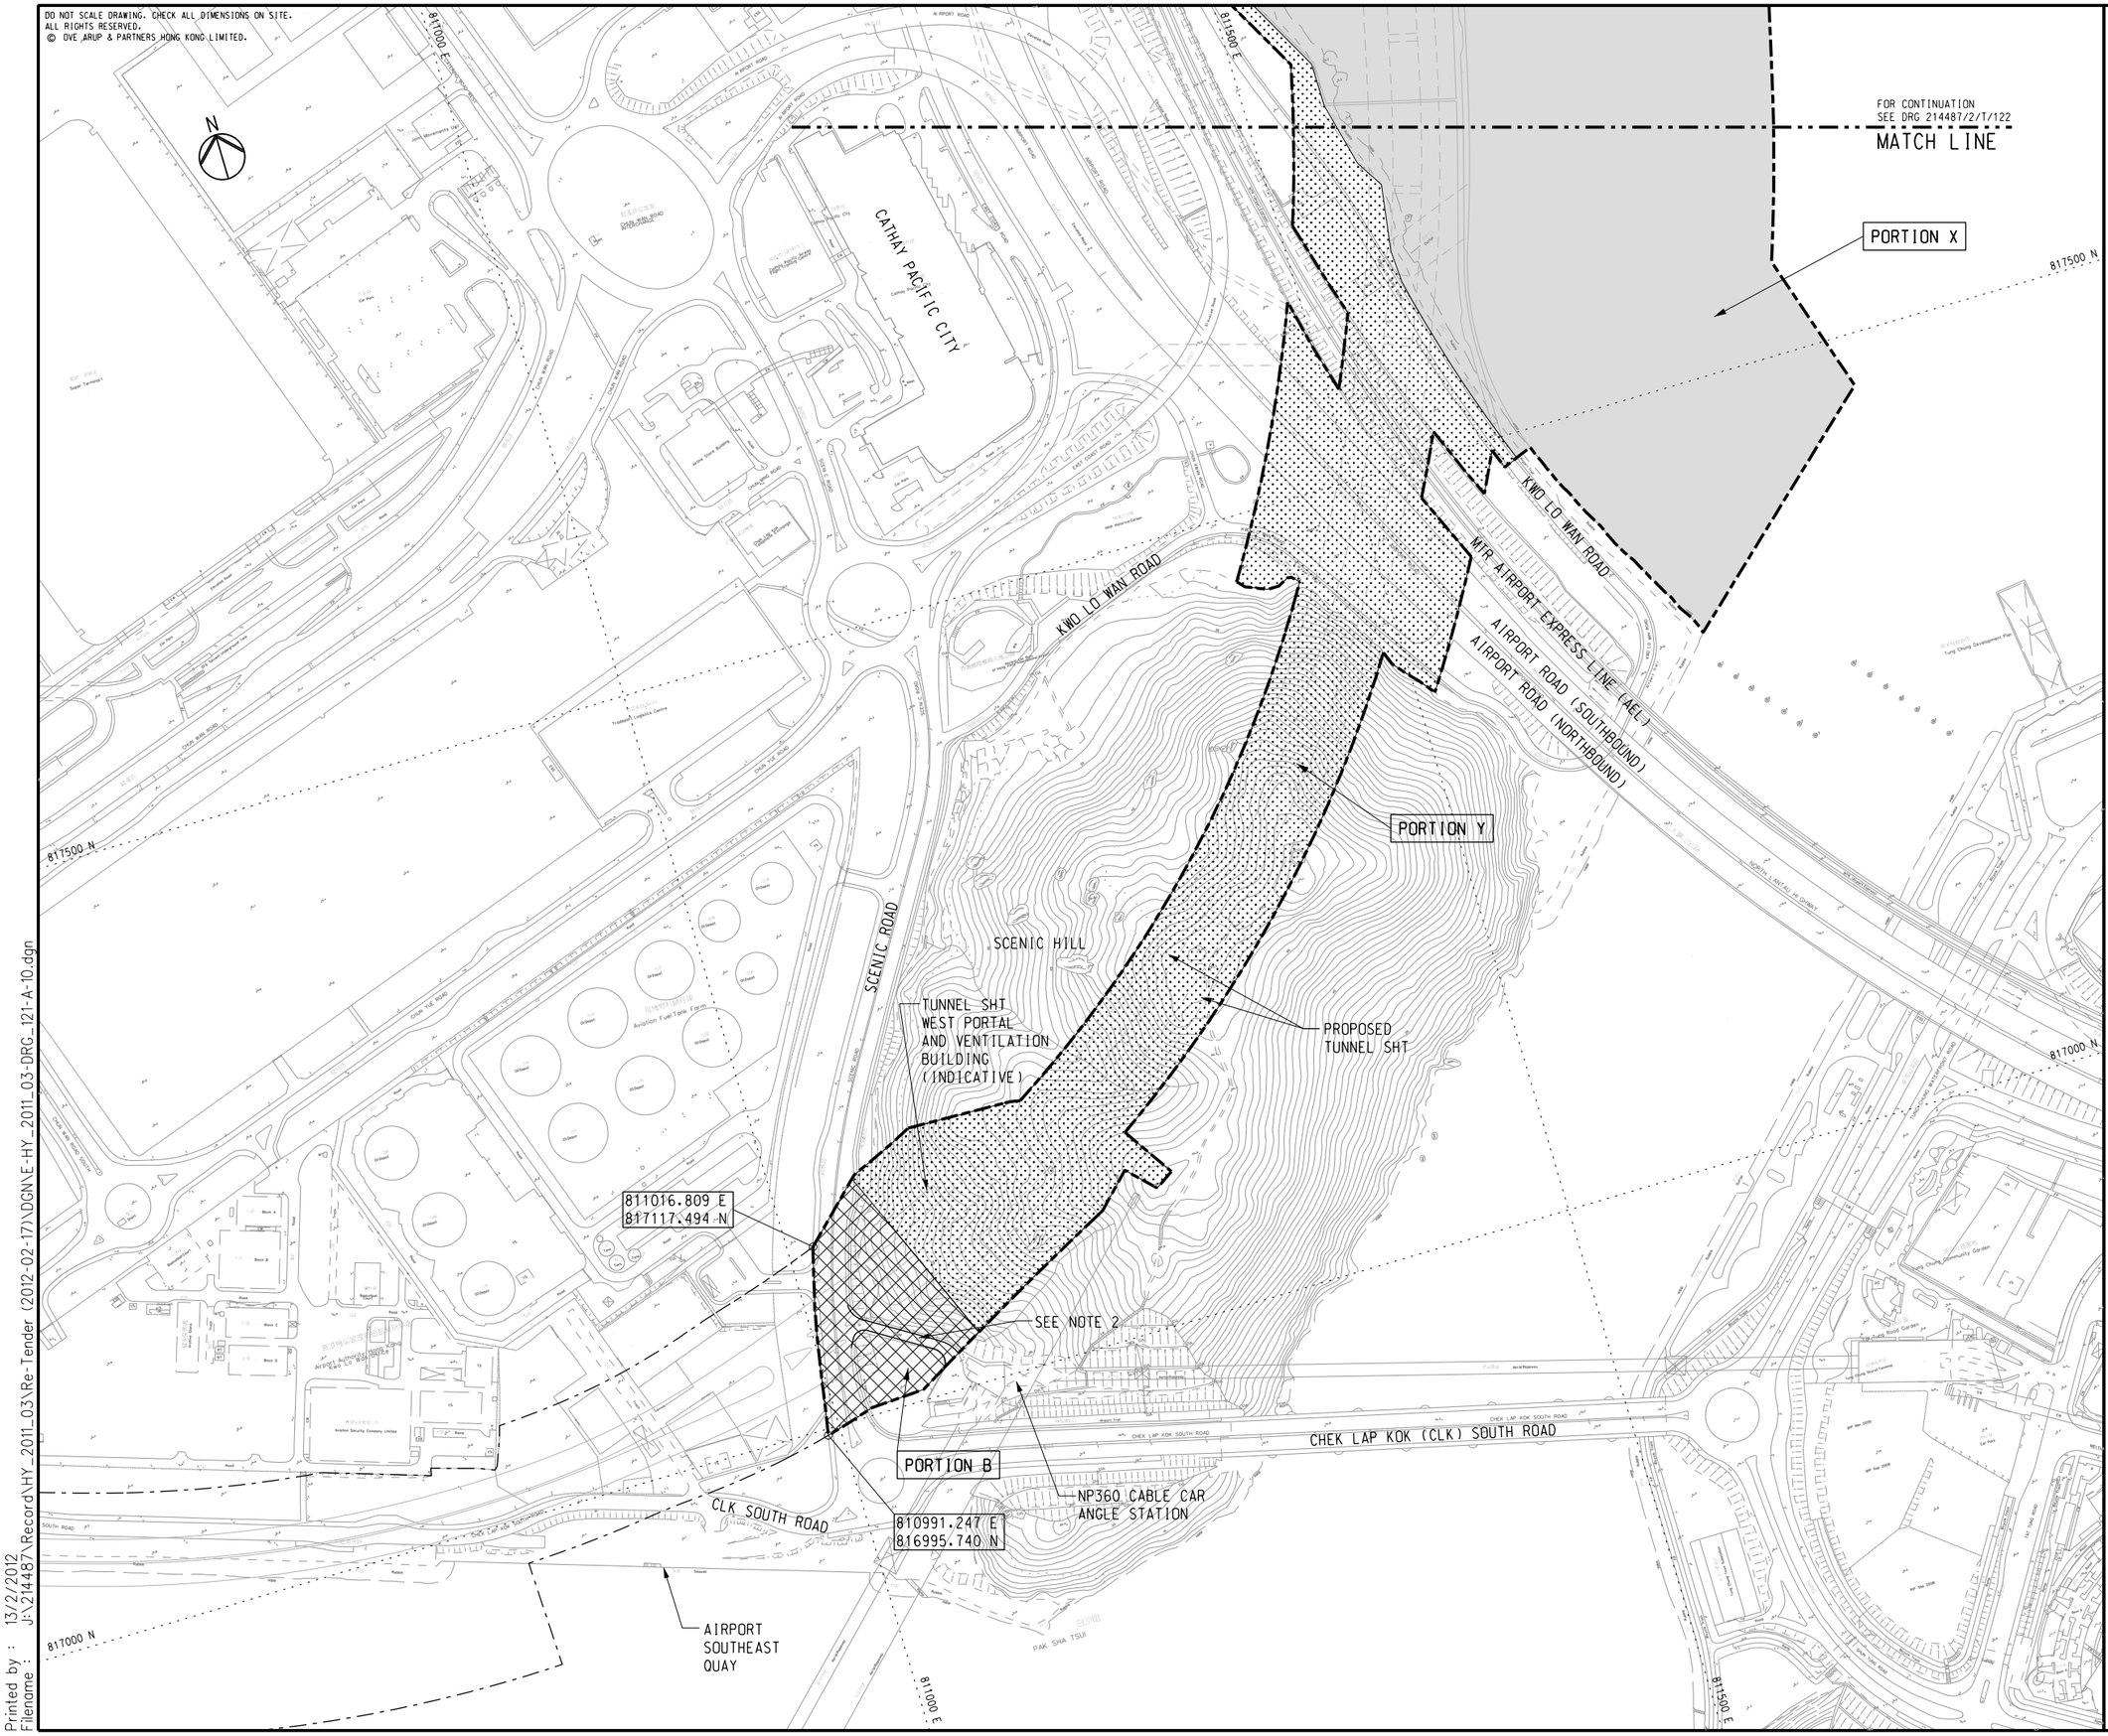

NOTES

1. FOR DETAILED DESCRIPTION OF PORTION OF SITE, REFER TO ER PART 2 GENERAL SITE DATA.
2. ACCESS ROAD TO NP360 CABLE CAR ANGLE STATION SHALL BE MAINTAINED AT ALL TIMES.

LEGEND

- SITE BOUNDARY
- PORTION X
- PORTION Y
- PORTION B
- PORTION C
- PORTION D1

Rev	Description	By	Date
A	TENDER ISSUE	IL	02/12

Consultant

ARUP 奧雅納工程顧問 Ove Arup & Partners Hong Kong Limited

Contract No. and Title:

Contract No. HY/2011/03

Hong Kong-Zhuhai-Macao Bridge
Hong Kong Link Road -
Section Between Scenic Hill and
Hong Kong Boundary Crossing Facilities

Drawing title

PORTION OF SITE
(SHEET 1 OF 3)

Drawing no.		Rev.
214487/2/T/121		A
Drawn: RY	Date: 02/12	Checked: IL	Approved: SK
Scale: 1:2000 @A1		Status: TENDER	

COPYRIGHT RESERVED

路政署 HIGHWAYS DEPARTMENT
港珠澳大橋香港工程管理處
Hong Kong - Zhuhai - Macao Bridge
Hong Kong Project Management Office

Printed by : 13/2/2012
Filename : J:\214487\Record\HY_2011_03\Re-Tender (2012-02-17)\DGN\E-HY_2011_03-DRG_121-A-10.dgn

DO NOT SCALE DRAWING. CHECK ALL DIMENSIONS ON SITE.
ALL RIGHTS RESERVED.
© OVE ARUP & PARTNERS HONG KONG LIMITED.

NOTES

1. FOR GENERAL NOTES AND LEGEND, REFER TO DRG. NO. 214487/2/T/121.

Rev	Description	By	Date
A	TENDER ISSUE	IL	02/12

Consultant

ARUP 奧雅納工程顧問 Ove Arup & Partners Hong Kong Limited

Contract No. and Title:

Contract No. HY/2011/03

Hong Kong-Zhuhai-Macao Bridge
Hong Kong Link Road -
Section Between Scenic Hill and
Hong Kong Boundary Crossing Facilities

Drawing title

PORTION OF SITE
(SHEET 2 OF 3)

Drawing no.			Rev.
214487/2/T/122			A
Drawn	Date	Checked	Approved
RY	02/12	IL	SK
Scale		Status	
1:2000 @A1		TENDER	

COPYRIGHT RESERVED

路政署 HIGHWAYS DEPARTMENT
港珠澳大橋香港工程管理處
Hong Kong - Zhuhai - Macao Bridge
Hong Kong Project Management Office

Printed by : 13/2/2012
Filename : J:\214487\Record\HY_2011_03\Re-Tender (2012-02-17)\DGN\E-HY_2011_03-DRG_122-A-10.dgn

DO NOT SCALE DRAWING. CHECK ALL DIMENSIONS ON SITE.
ALL RIGHTS RESERVED.
© OVE ARUP & PARTNERS HONG KONG LIMITED.

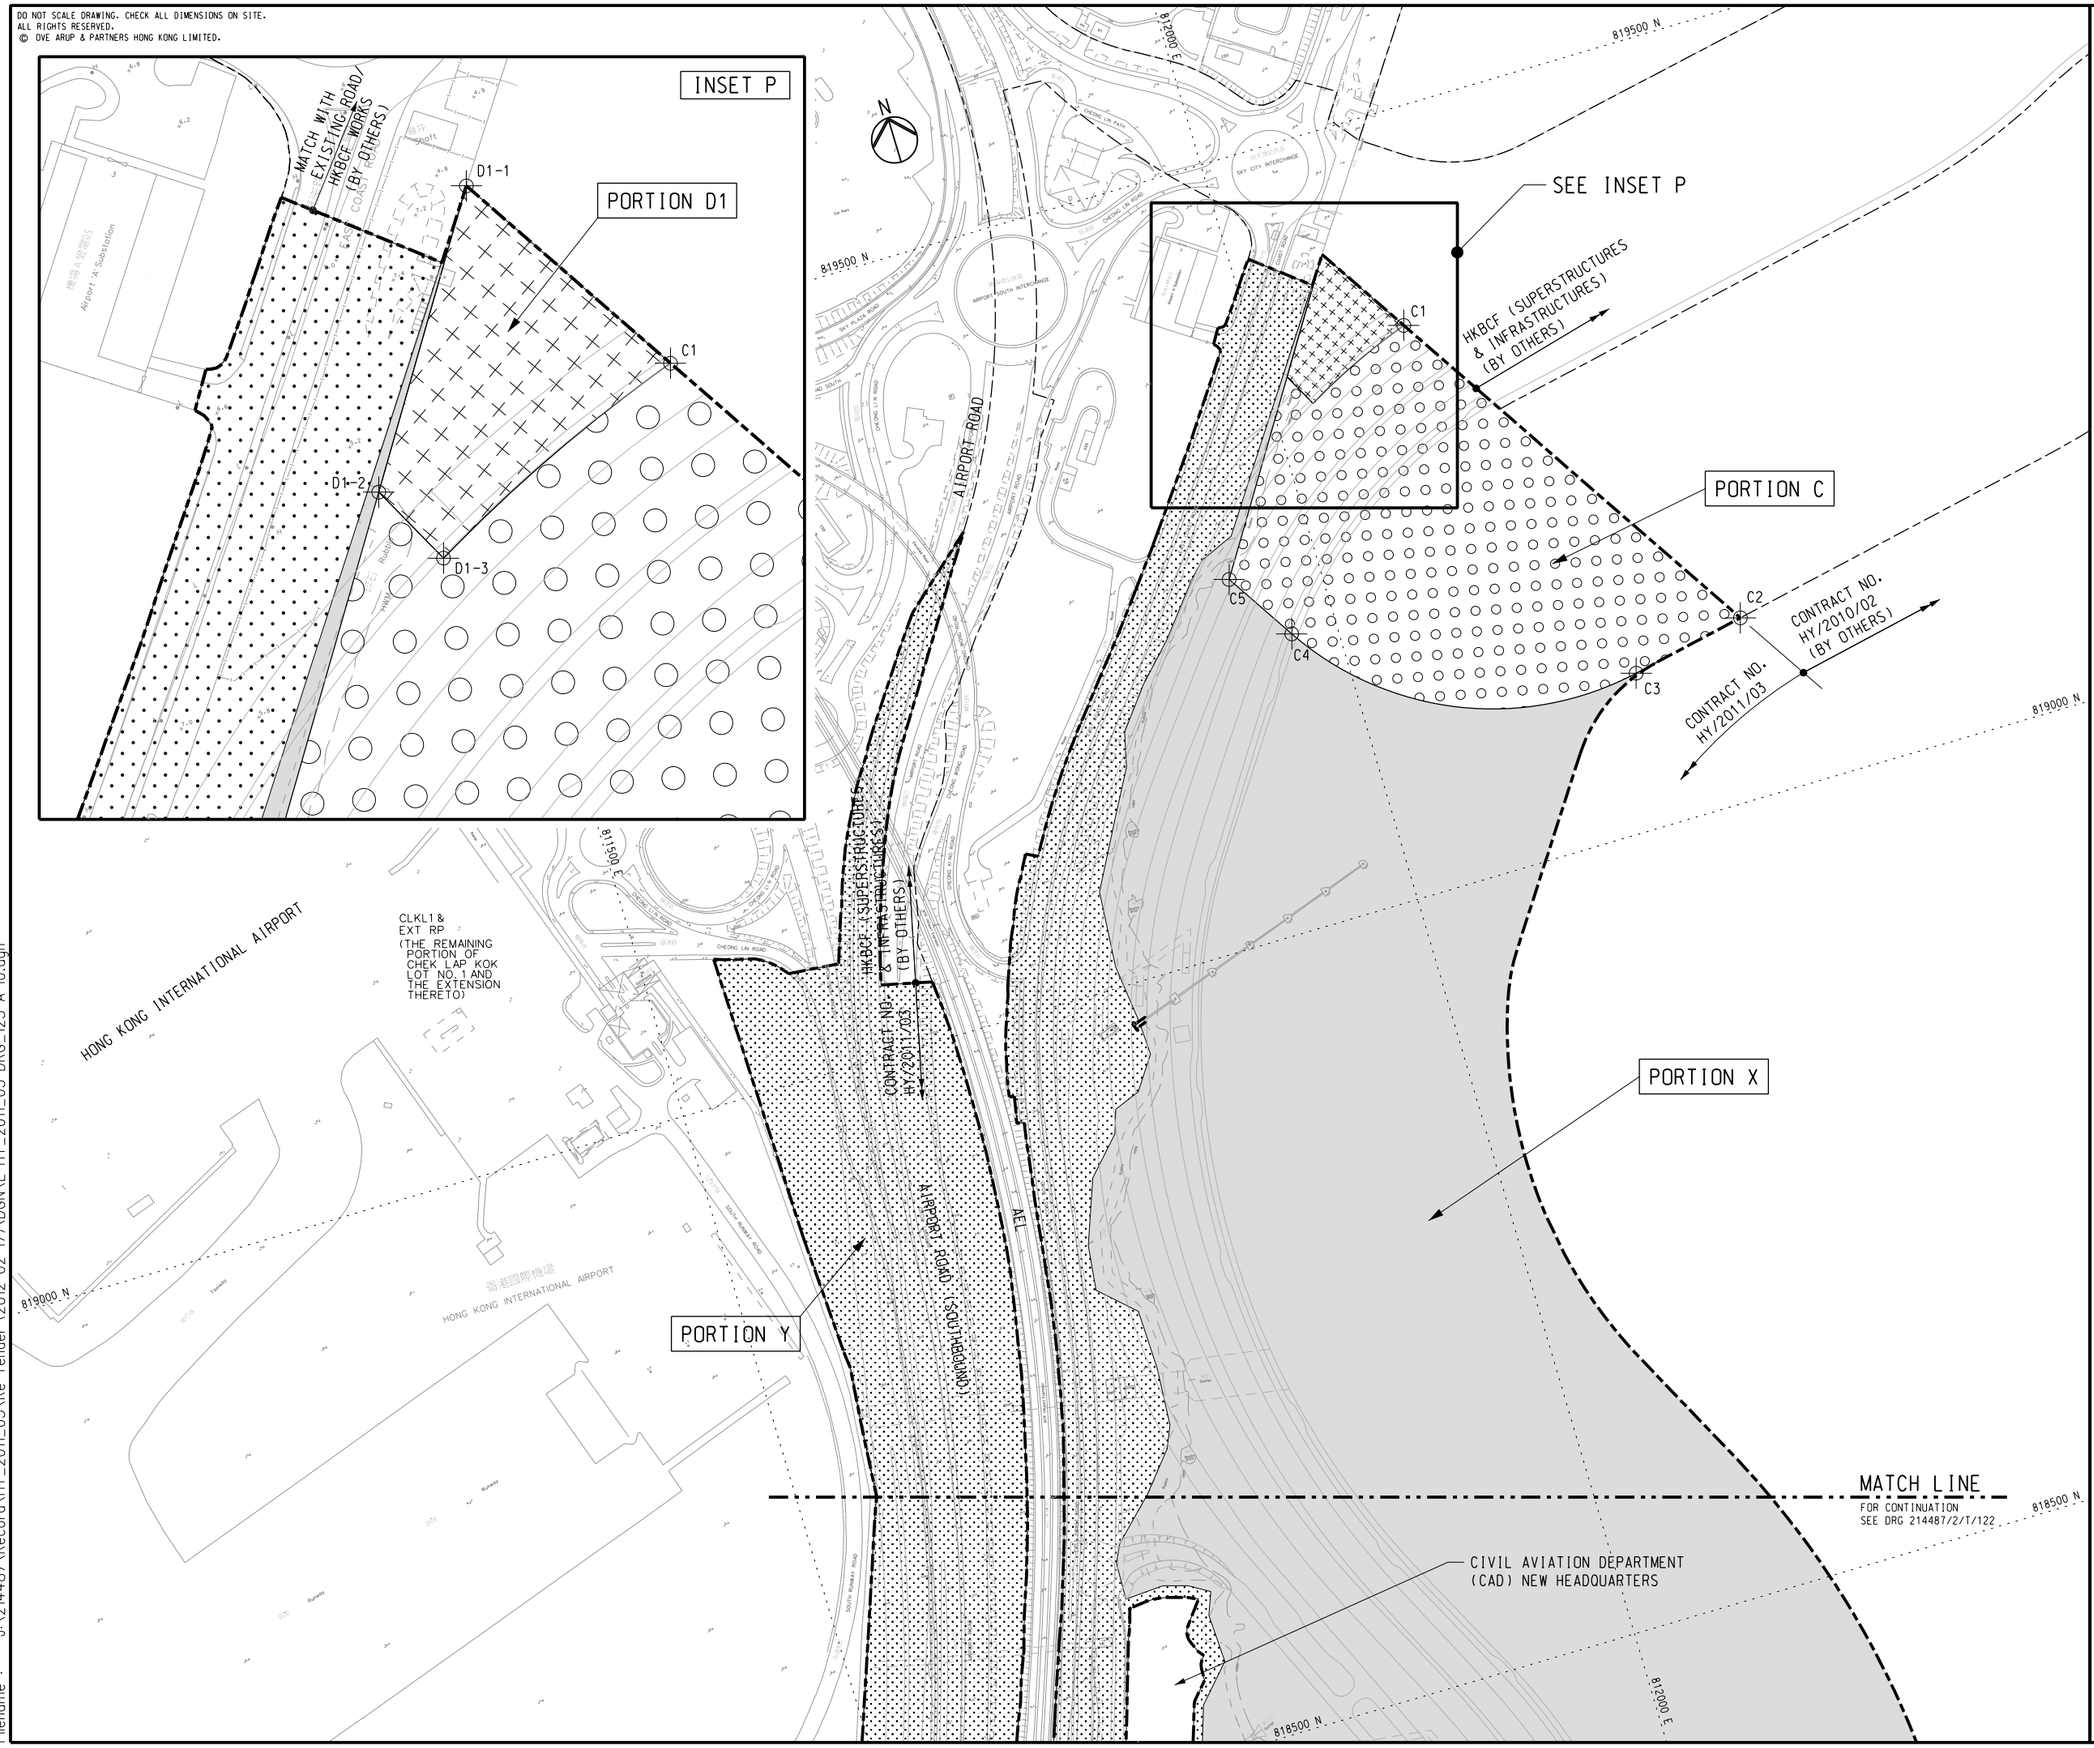

NOTES

1. FOR GENERAL NOTES AND LEGEND, REFER TO DRG. NO. 214487/2/T/121.

SETTING OUT CO-ORDINATES OF SITE PORTION C

POINT	CO-ORDINATES	
	EASTING	NORTHING
C1	812097.481	819361.966
C2	812254.199	819116.562
C3	812178.695	819101.208
C4	811970.282	819189.551
C5	811941.125	819235.206

SETTING OUT CO-ORDINATES OF SITE PORTION D1

POINT	CO-ORDINATES	
	EASTING	NORTHING
D1-1	812059.460	819421.497
D1-2	812014.853	819351.273
D1-3	812026.200	819329.938

Rev	Description	By	Date
A	TENDER ISSUE	IL	02/12

Consultant

ARUP 奧雅納工程顧問 Ove Arup & Partners Hong Kong Limited

Contract No. and Title:

Contract No. HY/2011/03

Hong Kong-Zhuhai-Macao Bridge
Hong Kong Link Road -
Section Between Scenic Hill and
Hong Kong Boundary Crossing Facilities

Drawing title

PORTION OF SITE
(SHEET 3 OF 3)

Drawing no.		Rev.
214487/2/T/123		A
Drawn: RY	Date: 02/12	Checked: IL / Approved: SK
Scale: 1:2000 @A1	Status: TENDER	

COPYRIGHT RESERVED

路政署 HIGHWAYS DEPARTMENT
港珠澳大橋香港工程管理處
Hong Kong - Zhuhai - Macao Bridge
Hong Kong Project Management Office

Printed by : 13/2/2012
Filename : J:\214487\Record\HY_2011_03\Re-Tender (2012-02-17)\DGN\E-HY_2011_03-DRG_123-A-10.dgn

APPENDIX D

Event and Action Plan

Event and Action Plan for Air Quality

Event	Action			
	ET	IEC	SO	Contractor
Exceedance of Action Level for one sample	1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform IEC and SO; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily.	1. Check monitoring data submitted by ET; 2. Check Contractor's working method.	1. Notify Contractor.	1. Rectify any unacceptable practice; 2. Amend working methods if appropriate.
Exceedance of Action Level for two or more consecutive samples	1. Identify source; 2. Inform IEC and SO; 3. Advise the SO on the effectiveness of the proposed remedial measures; 4. Repeat measurements to confirm findings; 5. Increase monitoring frequency to daily; 6. Discuss with IEC and Contractor on remedial actions required; 7. If exceedance continues, arrange meeting with IEC and SO; 8. If exceedance stops, cease additional monitoring.	1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the ET on the effectiveness of the proposed remedial measures; 5. Supervise Implementation of remedial measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor;	1. Submit proposals for remedial to SO within 3 working days of notification; 2. Implement the agreed proposals; 3. Amend proposal if appropriate.

Event	Action			
	ET	**IEC**	**SO**	**Contractor**
Exceedance of Limit Level for one sample	1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Inform SO, Contractor and EPD; 3. Repeat measurement to confirm finding; 4. Increase monitoring frequency to daily; 5. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and SO informed of the results.	1. Check monitoring data submitted by ET; 2. Check Contractor's working method; 3. Discuss with ET and Contractor on possible remedial measures; 4. Advise the SO on the effectiveness of the proposed remedial measures; 5. Supervise implementation of remedial measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Ensure remedial measures properly implemented.	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Amend proposal if appropriate.
Exceedance of Limit Level for two or more consecutive samples	1. Notify IEC, SO, Contractor and EPD; 2. Identify source; 3. Repeat measurement to confirm findings; 4. Increase monitoring frequency to daily; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Arrange meeting with IEC and SO to discuss the remedial actions to be taken; 7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and SO informed of the results; 8. If exceedance stops, cease additional monitoring.	1. Discuss amongst SO, ET, and Contractor on the potential remedial actions; 2. Review Contractor's remedial actions whenever necessary to assure their effectiveness and advise the SO accordingly; 3. Supervise the implementation of remedial measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. In consultation with the IEC, agree with the Contractor on the remedial measures to be implemented; 4. Ensure remedial measures properly implemented; 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not under control; 5. Stop the relevant portion of works as determined by the SO until the exceedance is abated.

Event and Action Plan for Noise

Event	Action			
	ET	IEC	SO	Contractor
Exceedance of Action Level	1. Identify source, investigate the causes of exceedance and propose remedial measures; 2. Notify IEC and Contractor; 3. Report the results of investigation to the IEC, SO and Contractor; 4. Discuss with the Contractor and formulate remedial measures; 5. Increase monitoring frequency to check mitigation effectiveness.	1. Review the analysed results submitted by the ET; 2. Review the proposed remedial measures by the Contractor and advise the SO accordingly; 3. Supervise the implementation of remedial measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Require Contractor to propose remedial measures for the analysed noise problem; 4. Ensure remedial measures are properly implemented	1. Submit noise mitigation proposals to IEC; 2. Implement noise mitigation proposals.
Exceedance of Limit Level	1. Identify source; 2. Inform IEC, SO, EPD and Contractor; 3. Repeat measurements to confirm findings; 4. Increase monitoring frequency; 5. Carry out analysis of Contractor's working procedures to determine possible mitigation to be implemented; 6. Inform IEC, SO and EPD the causes and actions taken for the exceedances; 7. Assess effectiveness of Contractor's remedial actions and keep IEC, EPD and SO informed of the results; 8. If exceedance stops, cease additional monitoring.	1. Discuss amongst SO, ET, and Contractor on the potential remedial actions; 2. Review Contractors remedial actions whenever necessary to assure their effectiveness and advise the SO accordingly; 3. Supervise the implementation of remedial measures.	1. Confirm receipt of notification of failure in writing; 2. Notify Contractor; 3. Require Contractor to propose remedial measures for the analysed noise problem; 4. Ensure remedial measures properly implemented; 5. If exceedance continues, consider what portion of the work is responsible and instruct the Contractor to stop that portion of work until the exceedance is abated.	1. Take immediate action to avoid further exceedance; 2. Submit proposals for remedial actions to IEC within 3 working days of notification; 3. Implement the agreed proposals; 4. Resubmit proposals if problem still not under control; 5. Stop the relevant portion of works as determined by the SO until the exceedance is abated.

Event and Action Plan for Water Quality

Event	Action			
	ET Leader	IEC	SO	Contractor
Action level being exceeded by one sampling day	1. Repeat in situ measurement on next day of exceedance to confirm findings; 2. Identify source(s) of impact; 3. Inform IEC, contractor and SO; 4. Check monitoring data, all plant, equipment and Contractor's working methods.	1. Check monitoring data submitted by ET and Contractor's working methods.	1. Confirm receipt of notification of non-compliance in writing; 2. Notify Contractor.	1. Inform the SO and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Amend working methods if appropriate.
Action level being exceeded by two or more consecutive sampling days	1. Repeat measurement on next day of exceedance to confirm findings; 2. Identify source(s) of impact; 3. Inform IEC, contractor, SO and EPD; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5; Ensure mitigation measures are implemented; 6. Increase the monitoring frequency to daily until no exceedance of Action level.	1. Check monitoring data submitted by ET and Contractor's working method; 2. Discuss with ET and Contractor on possible remedial actions; 3. Review the proposed mitigation measures submitted by Contractor and advise the SO accordingly; 4. Supervise the implementation of mitigation measures.	1. Discuss with IEC on the proposed mitigation measures; 2. Ensure mitigation measures are properly implemented; 3. Assess the effectiveness of the implemented mitigation measures.	1. Inform the Engineer and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment and consider changes of working methods; 4. Submit proposal of additional mitigation measures to SO within 3 working days of notification and discuss with ET, IEC and SO; 5. Implement the agreed mitigation measures.
Limit level being exceeded by one sampling day	1. Repeat measurement on next day of exceedance to confirm findings; 2. Identify source(s) of impact; 3. Inform IEC, contractor, SO and EPD; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IEC, SO and Contractor;	1. Check monitoring data submitted by ET and Contractor's working method; 2. Discuss with ET and Contractor on possible remedial actions; 3. Review the proposed mitigation measures submitted by Contractor and advise the SO accordingly.	1. Confirm receipt of notification of failure in writing; 2. Discuss with IEC, ET and Contractor on the proposed mitigation measures; 3. Request Contractor to review the working methods.	1. Inform the SO and confirm notification of the non-compliance in writing; 2. Rectify unacceptable practice; 3. Check all plant and equipment and consider changes of working methods; 4. Submit proposal of mitigation measures to SO within 3 working days of notification and discuss with ET, IEC and SO.

Event	Action			
	ET Leader	IEC	SO	Contractor
Limit level being exceeded by two or more consecutive sampling days	1. Repeat measurement on next day of exceedance to confirm findings; 2. Identify source(s) of impact; 3. Inform IEC, contractor, SO and EPD; 4. Check monitoring data, all plant, equipment and Contractor's working methods; 5. Discuss mitigation measures with IEC, SO and Contractor; 6. Ensure mitigation measures are implemented;	1. Check monitoring data submitted by ET and Contractor's working method; 2. Discuss with ET and Contractor on possible remedial actions; 3. Review the Contractor's mitigation measures whenever necessary to assure their effectiveness and advise the SO accordingly; 4. Supervise the implementation of mitigation measures.	1. Discuss with IEC, ET and Contractor on the proposed mitigation measures; 2. Request Contractor to critically review the working methods; 3. Make agreement on the mitigation measures to be implemented; 4. Ensure mitigation measures are properly implemented; 5. Consider and instruct, if necessary, the Contractor to slow down or to stop all or part of the construction activities until no exceedance of Limit level.	1. Take immediate action to avoid further exceedance; 2. Submit proposal of mitigation measures to SO within 3 working days of notification and discuss with ET, IEC and SO; 3. Implement the agreed mitigation measures; 4. Resubmit proposals of mitigation measures if problem still not under control; 5. As directed by the Engineer, to slow down or to stop all or part of the construction activities until no exceedance of Limit level.

Event and Action Plan for Dolphin Monitoring

Event	ET Leader	IEC	ER / SOR	Contractor
Action Level	1. Repeat statistical data analysis to confirm findings; 2. Review all available and relevant data, including raw data and statistical analysis results of other parameters covered in the EM&A, to ascertain if differences are as a result of natural variation or previously observed seasonal differences; 3. Identify source(s) of impact; 4. Inform the IEC, ER/SOR and Contractor; 5. Check monitoring data. 6. Review to ensure all the dolphin protective measures are fully and properly implemented and advise on additional measures if necessary.	1. Check monitoring data submitted by ET and Contractor; 2. Discuss monitoring results and findings with the ET and the Contractor.	1. Discuss monitoring with the IEC and any other measures proposed by the ET; 2. If ER/SOR is satisfied with the proposal of any other measures, ER/SOR to signify the agreement in writing on the measures to be implemented.	1. Inform the ER/SOR and confirm notification of the non-compliance in writing; 2. Discuss with the ET and the IEC and propose measures to the IEC and the ER/SOR; 3. Implement the agreed measures.
Limit Level	1. Repeat statistical data analysis to confirm findings; 2. Review all available and relevant data, including raw data and statistical analysis results of other parameters covered in the EM&A, to ascertain if differences are as a result of natural variation or previously observed seasonal differences; 3. Identify source(s) of impact; 4. Inform the IEC, ER/SOR and Contractor of findings; 5. Check monitoring data; 6. Repeat review to ensure all the dolphin protective measures are fully and properly implemented and advise on additional measures if necessary;	1. Check monitoring data submitted by ET and Contractor; 2. Discuss monitoring results and findings with the ET and the Contractor; 3. Attend the meeting to discuss with ET, ER/SOR and Contractor the necessity of additional dolphin monitoring and any other potential mitigation measures; 4. Review proposals for additional monitoring and any other mitigation measures submitted by ET and Contractor and advise ER/SOR of the results and findings accordingly; 5. Supervise / Audit the	1. Attend the meeting to discuss with ET, IEC and Contractor the necessity of additional dolphin monitoring and any other potential mitigation measures; 2. If ER/SOR is satisfied with the proposals for additional dolphin monitoring and/or any other mitigation measures submitted by ET and Contractor and verified by IEC, ER/SOR to signify the agreement in writing on such proposals and any other mitigation measures; 3. Supervise the implementation of additional monitoring	1. Inform the ER/SOR and confirm notification of the non-compliance in writing; 2. Attend the meeting to discuss with ET, IEC and ER/SOR the necessity of additional dolphin monitoring and any other potential mitigation measures; 3. Jointly submit with ET to IEC a proposal of additional dolphin monitoring and/or any other mitigation measures when necessary; 4. Implement the agreed additional dolphin monitoring and/or any other mitigation measures.

Event	ET Leader	IEC	ER / SOR	Contractor
	7. If ET proves that the source of impact is caused by any of the construction activity by the works contract, ET to arrange a meeting to discuss with IEC, ER/SOR and Contractor the necessity of additional dolphin monitoring and/or any other potential mitigation measures (e.g., consider to modify the perimeter silt curtain or consider to control/temporarily stop relevant construction activity etc.) and submit to IEC a proposal of additional dolphin monitoring and/or mitigation measures where necessary.	implementation of additional monitoring and/or any other mitigation measures and advise ER/SOR the results and findings accordingly.	and/or any other mitigation measures.	

Event and Action Plan for Mudflat Monitoring

Event	ET Leader	IEC	SO	Contractor
Density or the distribution pattern of horseshoe crab, seagrass or intertidal soft shore communities recorded in the impact or post-construction monitoring are significantly lower than or different from those recorded in the baseline monitoring.	Review historical data to ensure differences are as a result of natural variation or previously observed seasonal differences; Identify source(s) of impact; Inform the IEC, SO and Contractor; Check monitoring data; Discuss additional monitoring and any other measures, with the IEC and Contractor.	Discuss monitoring with the ET and the Contractor; Review proposals for additional monitoring and any other measures submitted by the Contractor and advise the SO accordingly.	Discuss with the IEC additional monitoring requirements and any other measures proposed by the ET; Make agreement on the measures to be implemented.	Inform the SO and in writing; Discuss with the ET and the IEC and propose measures to the IEC and the ER; Implement the agreed measures.

Action Plan for Landscape Works

Event	ACTION			
	ET Leader	IEC	SO	Contractor
Conflicts occur	● Check Contractor's proposed remedial design conforms to the requirements of EP and prepare checking report(s)	● Check and endorse ET's report(s). ● Check and certify Contractor's proposed remedial design	● Supervise the Contractor to carry out the proposed remediation work	● Propose remedial design and carry out the proposed work

APPENDIX E

Implementation Schedule of Environmental Mitigation Measures

Implementation Schedule of Environmental Mitigation Measures

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the Measures	When to implement the measures?	Implementation Status
Air Quality							
S5.5.6.1	A1	1) The contractor shall follow the procedures and requirements given in the Air Pollution Control (Construction Dust) Regulation	Good construction site practices to control the dust impact at the nearby sensitive receivers to within the relevant criteria.	Contractor	All construction sites	Construction stage	√
S5.5.6.2	A2	2) Proper watering of exposed spoil should be undertaken throughout the construction phase: • Any excavated or stockpile of dusty material should be covered entirely by impervious sheeting or sprayed with water to maintain the entire surface wet and then removed or backfilled or reinstated where practicable within 24 hours of the excavation or unloading; • Any dusty materials remaining after a stockpile is removed should be wetted with water and cleared from the surface of roads; • A stockpile of dusty material should not be extended beyond the pedestrian barriers, fencing or traffic cones. • The load of dusty materials on a vehicle leaving a construction site should be covered entirely by impervious sheeting to ensure that the dusty materials do not leak from the vehicle; • Where practicable, vehicle washing facilities with high pressure water jet should be provided at every discernible or designated vehicle exit point. The area where vehicle washing takes place and the road section between the washing facilities and the exit point should be paved with concrete, bituminous materials or hardcores;	Good construction site practices to control the dust impact at the nearby sensitive receivers to within the relevant criteria.	Contractor	All construction sites	Construction stage	√
S5.5.6.2	A2	• When there are open excavation and reinstatement works, hoarding of not less than 2.4m high should be provided as far as practicable along the site boundary with provision for public crossing. Good site practice shall also be adopted by the Contractor to ensure the conditions of the hoardings are properly maintained throughout the construction period; • Any skip hoist for material transport should be totally enclosed by impervious sheeting;	Good construction site practices to control the dust impact at the nearby sensitive receivers to within the relevant criteria.	Contractor	All construction sites	Construction stage	√

Implementation Schedule of Environmental Mitigation Measures

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the Measures	When to implement the measures?	Implementation Status
S5.5.6.2	A2	• The portion of any road leading only to construction site that is within 30m of a vehicle entrance or exit should be kept clear of dusty materials; • Surfaces where any pneumatic or power-driven drilling, cutting, polishing or other mechanical breaking operation takes place should be sprayed with water or a dust suppression chemical continuously; • Any area that involves demolition activities should be sprayed with water or a dust suppression chemical immediately prior to, during and immediately after the activities so as to maintain the entire surface wet; • Where a scaffolding is erected around the perimeter of a building under construction, effective dust screens, sheeting or netting should be provided to enclose the scaffolding from the ground floor level of the building, or a canopy should be provided from the first floor level up to the highest level of the scaffolding; • Every stock of more than 20 bags of cement or dry pulverized fuel ash (PFA) should be covered entirely by impervious sheeting or placed in an area sheltered on the top and the 3 sides;	Good construction site practices to control the dust impact at the nearby sensitive receivers to within the relevant criteria.	Contractor	All construction sites	Construction stage	√
S5.5.6.2	A2	• Cement or dry PFA delivered in bulk should be stored in a closed silo fitted with an audible high level alarm which is interlocked with the material filling line and no overfilling is allowed; • Loading, unloading, transfer, handling or storage of bulk cement or dry PFA should be carried out in a totally enclosed system or facility, and any vent or exhaust should be fitted with an effective fabric filter or equivalent air pollution control system; and • Exposed earth should be properly treated by compaction, turfing, hydroseeding, vegetation planting or sealing with latex, vinyl, bitumen, shotcrete or other suitable surface stabiliser within six months after the last construction activity on the construction site or part of the construction site where the exposed earth lies.	Good construction site practices to control the dust impact at the nearby sensitive receivers to within the relevant criteria.	Contractor	All construction sites	Construction stage	√

Implementation Schedule of Environmental Mitigation Measures

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
S5.5.6.3	A3	3) The Contractor should undertake proper watering on all exposed spoil (with at least 8 times per day) throughout the construction phase.	Control construction dust	Contractor	All construction sites	Construction stage	√
S5.5.6	A5	5) Implement regular dust monitoring under EM&A programme during the construction stage.	Monitor the 24 hr and 1hr TSP levels at the representative dust monitoring stations to ensure compliance with relevant criteria Throughout the construction period	Contractor	Selected representative dust monitoring station	Construction stage	√
S5.5.71	A6	The following mitigation measures should be adopted to prevent fugitive dust emissions for concrete batching plant: • Loading, unloading, handling, transfer or storage of any dusty materials should be carried out in totally enclosed system; • All dust-laden air or waste gas generated by the process operations should be properly extracted and vented to fabric filtering system to meet the emission limits for TSP; • Vents for all silos and cement/ pulverised fuel ash (PFA) weighing scale should be fitted with fabric filtering system; • The materials which may generate airborne dusty emissions should be wetted by water spray system; • All receiving hoppers should be enclosed on three sides up to 3m above unloading point; • All conveyor transfer points should be totally enclosed; • All access and route roads within the premises should be paved and wetted; and • Vehicle cleaning facilities should be provided and used by all concrete trucks before leaving the premises to wash off any dust on the wheels and/or body.	Monitor the 24 hr and 1hr TSP levels at the representative dust monitoring stations to ensure compliance with relevant criteria Throughout the construction period	Contractor	Selected representative dust monitoring station	Construction stage	√

Implementation Schedule of Environmental Mitigation Measures

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the Measures	When to implement the measures?	Implementation Status
S5.5.2.7	A7	The following mitigation measures should be adopted to prevent fugitive dust emissions at barging point: • All road surface within the barging facilities will be paved; • Dust enclosures will be provided for the loading ramp; • Vehicles will be required to pass through designated wheels wash facilities; and • Continuous water spray at the loading points.	Control construction dust	Contractor	All construction sites	Construction stage	√
Noise							
S6.4.10	N1	1) Use of good site practices to limit noise emissions by considering the following: • only well-maintained plant should be operated on-site and plant should be serviced regularly during the construction programme; • machines and plant (such as trucks, cranes) that may be in intermittent use should be shut down between work periods or should be throttled down to a minimum; • plant known to emit noise strongly in one direction, where possible, be orientated so that the noise is directed away from nearby NSRs; • silencers or mufflers on construction equipment should be properly fitted and maintained during the construction works • mobile plant should be sited as far away from NSRs as possible and practicable; • material stockpiles, mobile container site officer and other structures should be effectively utilised, where practicable, to screen noise from on-site construction activities.	Control construction airborne noise by means of good site practices	Contractor	All construction sites	Construction stage	√

Implementation Schedule of Environmental Mitigation Measures

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
S6.4.11	N2	2) Install temporary hoarding located on the site boundaries between noisy construction activities and NSRs. The conditions of the hoardings shall be properly maintained throughout the construction period.	Reduce the construction noise levels at low-level zone of NSRs through partial screening.	Contractor	All construction sites	Construction stage	√
S6.4.12	N3	3) Install movable noise barriers (typically density @ 14kg/m^2), acoustic mat or full enclosure close to noisy plants including air compressor, generators, saw.	Screen the noisy plant items to be used at all construction sites	Contractor	For plant items listed in Appendix 6D of the EIA report at all construction sites	Construction stage	√
S6.4.13	N4	4) Select "Quiet plants" which comply with the BS 5228 Part 1 or TM standards.	Reduce the noise levels of plant items	Contractor	For plant items listed in Appendix 6D of the EIA report at all construction sites	Construction stage	√
S6.4.14	N5	5) Sequencing operation of construction plants where practicable.	Operate sequentially within the same work site to reduce the construction airborne noise	Contractor	All construction sites where practicable	Construction stage	√
	N6	6) Implement a noise monitoring under EM&A programme.	Monitor the construction noise levels at the selected representative locations	Contractor	Selected representative noise monitoring station	Construction stage	√
Waste Management (Construction waste)							
S8.3.8	WM1	<u>Construction and Demolition Material</u> The following mitigation measures should be implemented in handling the waste: • Maintain temporary stockpiles and reuse excavated fill material for backfilling and reinstatement; • Carry out on-site sorting; • Make provisions in the Contract documents to allow and promote the use of recycled aggregates where appropriate; • Adopt 'Selective Demolition' technique to demolish the existing structures and facilities with a view to recovering broken concrete effectively for recycling purpose, where possible;	Good site practice to minimize the waste generation and recycle the C&D materials as far as practicable so as to reduce the amount for final disposal	Contractor	All construction sites	Construction stage	√

Implementation Schedule of Environmental Mitigation Measures

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
		• Implement a trip-ticket system for each works contract to ensure that the disposal of C&D materials are properly documented and verified; and • Implement an enhanced Waste Management Plan similar to ETWBTC (Works) No. 19/2005. Environmental Management on Construction Sites. to encourage on-site sorting of C&D materials and to minimize their generation during the course of construction. • In addition, disposal of the C&D materials onto any sensitive locations such as agricultural lands, etc. should be avoided. The Contractor shall propose the final disposal sites to the Project Proponent and get its approval before implementation.					
S8.3.9 - S8.3.11	WM2	C&D Waste • Standard formwork or pre-fabrication should be used as far as practicable in order to minimise the arising of C&D materials. The use of more durable formwork or plastic facing for the construction works should be considered. Use of wooden hoardings should not be used, as in other projects. Metal hoarding should be used to enhance the possibility of recycling. The purchasing of construction materials will be carefully planned in order to avoid over ordering and wastage. • The Contractor should recycle as much of the C&D materials as possible on-site. Public fill and C&D waste should be segregated and stored in different containers or skips to enhance reuse or recycling of materials and their proper disposal. Where practicable, concrete and masonry can be crushed and used as fill. Steel reinforcement bar can be used by scrap steel mills. Different areas of the sites should be considered for such segregation and storage.	Good site practice to minimize the waste generation and recycle the C&D materials as far as practicable so as to reduce the amount for final disposal	Contractor	All construction sites	Construction stage	√

Implementation Schedule of Environmental Mitigation Measures

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
S8.2.12-S8.3.15	WM3	Chemical Waste • Chemical waste that is produced, as defined by Schedule 1 of the Waste Disposal (Chemical Waste) (General) Regulation, should be handled in accordance with the Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes. • Containers used for the storage of chemical wastes should be suitable for the substance they are holding, resistant to corrosion, maintained in a good condition, and securely closed; have a capacity of less than 450 liters unless the specification has been approved by the EPD; and display a label in English and Chinese in accordance with instructions prescribed in Schedule 2 of the regulation. • The storage area for chemical wastes should be clearly labeled and used solely for the storage of chemical waste; enclosed on at least 3 sides; have an impermeable floor and bunding of sufficient capacity to accommodate 110% of the volume of the largest container or 20 % of the total volume of waste stored in that area, whichever is the greatest; have adequate ventilation; covered to prevent rainfall entering; and arranged so that incompatible materials are adequately separated. • Disposal of chemical waste should be via a licensed waste collector; be to a facility licensed to receive chemical waste, such as the Chemical Waste Treatment Centre which also offers a chemical waste collection service and can supply the necessary storage containers; or be to a reuser of the waste, under approval from the EPD.	Control the chemical waste and ensure proper storage, handling and disposal.	Contractor	All construction sites	Construction stage	√

Implementation Schedule of Environmental Mitigation Measures

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
S8.3.16	WM4	*Sewage* • Adequate numbers of portable toilets should be provided for the workers. The portable toilets should be maintained in a state, which will not deter the workers from utilizing these portable toilets. Night soil should be collected by licensed collectors regularly.	Proper handling of sewage from worker to avoid odour, pest and litter impacts	Contractor	All construction sites	Construction stage	√
S8.3.17	WM5	*General Refuse* • General refuse generated on-site should be stored in enclosed bins or compaction units separately from construction and chemical wastes. • A reputable waste collector should be employed by the Contractor to remove general refuse from the site, separately from construction and chemical wastes, on a daily basis to minimize odour, pest and litter impacts. Burning of refuse on construction sites is prohibited by law. • Aluminium cans are often recovered from the waste stream by individual collectors if they are segregated and made easily accessible. Separate labelled bins for their deposit should be provided if feasible. • Office wastes can be reduced through the recycling of paper if volumes are large enough to warrant collection. Participation in a local collection scheme should be considered by the Contractor. In addition, waste separation facilities for paper, aluminum cans, plastic bottles etc., should be provided. • Training should be provided to workers about the concepts of site cleanliness and appropriate waste management procedure, including reduction, reuse and recycling of wastes.	Minimize production of the general refuse and avoid odour, pest and litter impacts	Contractor	All construction sites	Construction stage	√

Implementation Schedule of Environmental Mitigation Measures

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
Water quality (Construction Phase)							
S9.11.1-S9.11.1. 2	W1	• Mitigation during the marine works to reduce impacts to within acceptable levels have been recommended and will comprise a series of measures that restrict the method and sequencing of filling work, as well as protection measures. Details of the measures are provided below and summarised in the Environmental Mitigation Implementation Schedule in EM&A Manual. • Construction of seawalls to be advanced by at least 100-200m before the filling can commence. It should be noted that the protection by advanced seawall is a dynamic process depending on the progress of the construction activities. The part of the works where such measures can be undertaken for the majority of the time includes the following locations: - TMCLKL northern reclamation; -TMCLKL southern reclamation (after formation of the nips); - Reclamation filling for Portion 1 of HKLR.	To control construction water quality	Contractor	During seawall filling	Construction stage	√
S9.11.1-S9.11.1. 2	W1	• Single layer silt curtains will be applied around all works; • Silt curtain shall be fully maintained throughout the works.	To control construction water quality	Contractor	During seawall filling	Construction stage	P

Implementation Schedule of Environmental Mitigation Measures

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
S9.11.1-S9.11.1. 2	W1	• Mechanical grabs shall be designed and maintained to avoid spillage and should seal tightly while being lifted; • barges shall have tight fitting seals to their bottom openings to prevent leakage of material; • any pipe leakages shall be repaired quickly. Plant should not be operated with leaking pipes; • loading of barges shall be controlled to prevent splashing of filling materials to the surrounding water. • barges shall not be filled to a level which will cause overflow of materials or pollution of water during loading or transportation; • adequate freeboard shall be maintained on barges to reduce the likelihood of decks being washed by wave action; • all vessels shall be sized such that adequate clearance is maintained between vessels and the sea bed at all states of the tide to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash; and • the works shall not cause foam, oil, grease, litter or other objectionable matter to be present in the water within and adjacent to the works site.	To control construction water quality	Contractor	During seawall filling	Construction stage	√
S9.11.1.3	W2	<u>Land Works</u> General construction activities on land should also be governed by standard good working practice. Specific measures to be written into the works contracts should include: • wastewater from temporary site facilities should be controlled to prevent direct discharge to surface or marine waters;	To control construction water quality	Contractor	During seawall filling	Construction stage	√

Implementation Schedule of Environmental Mitigation Measures

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
S9.11.1.3	W2	• sewage effluent and discharges from on-site kitchen facilities shall be directed to Government sewer in accordance with the requirements of the WPCO or collected for disposal offsite. The use of soakaways shall be avoided; • storm drainage shall be directed to storm drainage shall be directed to storm drains via adequately designed sand/silt removal facilities such as sand traps, silt traps and sediment basins. Channels, earth bunds or sand bag barriers should be provided on site to properly direct stormwater to such silt removal facilities. Catchpits and perimeter channels should be constructed in advance of site formation works and earthworks; • silt removal facilities, channels and manholes shall be maintained and any deposited silt and grit shall be removed regularly, including specifically at the onset of and after each rainstorm; • temporary access roads should be surfaced with crushed stone or gravel; • rainwater pumped out from trenches or foundation excavations should be discharged into storm drains via silt removal facilities; • measures should be taken to prevent the washout of construction materials, soil, silt or debris into any drainage system; • open stockpiles of construction materials (e.g. aggregates and sand) on site should be covered with tarpaulin or similar fabric during rainstorms; • manholes (including any newly constructed ones) should always be adequately covered and temporarily sealed so as to prevent silt, construction materials or debris from getting into the drainage system, and to prevent storm run-off from getting into foul sewers; • discharges of surface run-off into foul sewers must always be prevented in order not to unduly overload the foul sewerage system;	To control construction water quality	Contractor	During seawall filling	Construction stage	√

Implementation Schedule of Environmental Mitigation Measures

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
S9.11.1.3	W2	• all vehicles and plant should be cleaned before they leave the construction site to ensure that no earth, mud or debris is deposited by them on roads. A wheel washing bay should be provided at every site exit; • wheel wash overflow shall be directed to silt removal facilities before being discharged to the storm drain; • the section of construction road between the wheel washing bay and the public road should be surfaced with crushed stone or coarse gravel; • wastewater generated from concreting, plastering, internal decoration, cleaning work and other similar activities, shall be screened to remove large objects; • vehicle and plant servicing areas, vehicle wash bays and lubrication facilities shall be located under roofed areas. The drainage in these covered areas shall be connected to foul sewers via a petrol interceptor in accordance with the requirements of the WPCO or collected for off site disposal; • the contractors shall prepare an oil / chemical cleanup plan and ensure that leakages or spillages are contained and cleaned up immediately; • waste oil should be collected and stored for recycling or disposal, in accordance with the Waste Disposal Ordinance; • all fuel tanks and chemical storage areas should be provided with locks and be sited on sealed areas. The storage areas should be surrounded by bunds with a capacity equal to 110% of the storage capacity of the largest tank; and • surface run-off from bunded areas should pass through oil/ grease traps prior to discharge to the stormwater system.	To control construction water quality	Contractor	During seawall filling	Construction stage	√
S9.14	W3	• Implement a water quality monitoring programme	Control water quality	Contractor	At identified monitoring location	During construction	√

Implementation Schedule of Environmental Mitigation Measures

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
Ecology (Construction Phase)							
S10.7	E1	• Good site practices to avoid runoff entering woodland habitats in Scenic Hill; • Reinstate works areas in Scenic Hill; • Avoid stream modification in Scenic Hill.	Avoid potential disturbance on habitat of Romer.s Tree Frog in Scenic Hill	Designer; Contractor	Scenic Hill	During construction	√
S10.7	E2	• Install silt curtain during the construction; • Construct seawall prior to reclamation filling where practicable; • Good site practices; • Site runoff control; • Spill response plan.	Minimise marine water quality impacts	Contractor	Seawall, reclamation area	During construction	P
S10.7	E4	• Watering to reduce dust generation; prevention of siltation of freshwater habitats; Site runoff should be desilted, to reduce the potential for suspended sediments, organics and other contaminants to enter streams and standing freshwater.	Prevent Sedimentation from Land-based works areas	Contractor	Land-based works areas	During construction	√
S10.7	E5	• Good site practices, including strictly following the permitted works hours, using quieter machines where practicable, and avoiding excessive lightings during night time.	Prevent disturbance to terrestrial fauna and habitats	Contractor	Land-based works areas	During construction	√
S10.7	E6	• Dolphin Exclusion Zone; • Dolphin watching plan.	Minimize temporary marine habitat loss impact to dolphins	Contractor	Marine works	During marine works	√
S10.7	E7	• Decouple compressors and other equipment on working vessels; • Avoidance of percussive piling; • Marine underwater noise monitoring; • Temporal suspension of drilling bored pile casing in rock during peak dolphin calving season in May and June; • Handling with care for the installation of sheet piling for reclamation site.	Minimize temporary marine habitat loss impact to dolphins	Contractor	Marine works	During marine works	√

Implementation Schedule of Environmental Mitigation Measures

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
S10.7	E8	• Control vessel speed; • Skipper training; • Predefined and regular routes for working vessels; avoid Brothers Islands.	Minimise marine traffic disturbance on dolphins	Contractor	Marine traffic	During marine works	√
S10.10	E9	• Dolphin vessel monitoring; • Mudflat ecological monitoring.	Minimise marine traffic disturbance on dolphins	Contractor	North Lantau and West Lantau	Prior to construction, during construction, and 1 year after operation	√ See Note 1
Ecology (Operation Phase)							
S10.7	E10	• Preconstruction dive survey for corals	Minimise impacts on marine ecology	Contractor	The marine pier sites nearest to intertidal zone and along the shore of the HKLR reclamation site	Prior to marine construction works in these locations	√
Fisheries							
S11.7	F2	• Reduce re-suspension of sediments • Good site practices • Spill response plan	Minimise marine water quality impacts	Contractor	Seawall, reclamation area	During construction	√
S11.7	F3	• Install silt-grease trap in the drainage system collecting surface runoff	Minimise impacts on marine water quality impacts	Designer	Reclamation area	During construction	√
S11.7	F4	• Maritime Oil Spill Response Plan (MOSRP); • Contingency plan.	Minimise impacts on marine water quality impacts	Management	HKLR	During operation stage	√

Note:
1) The mudflat ecological monitoring will be conducted quarterly during the construction period. The mudflat ecological monitoring was not conducted during the reporting month.

Implementation Schedule of Environmental Mitigation Measures

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
Landscape & Visual (Detailed Design Phase)							
S14.3.3. 1	LV1	General design measures include: • Roadside planting and planting along the edge of the reclamation is proposed; • Transplanting of mature trees in good health and amenity value where appropriate and reinstatement of areas disturbed during construction by compensatory hydro-seeding and planting; • Protection measures for the trees to be retained during construction activities; • Optimizing the sizes and spacing of the bridge columns; • Fine-tuning the location of the bridge columns to avoid visually sensitive locations; • Aesthetic design of the bridge form and its structural elements for HKLR, e.g. parapet, soffit, columns, lightings and so on; • Considering the decorative urban design elements for HKLR, e.g. decorative road lightings; • Maximizing new tree, shrub and other vegetation planting to compensate tree felled and vegetation removed; • Providing planting area around peripheral of HKLR for tree planting screening effect. • Providing salt-tolerant native trees along the planter strip at affected seawall and newly reclaimed coastline. • For HKLR, providing aesthetic design on the viaduct, tunnel portals, at-grade roads and reclamation (e.g. subtle colour tone and slim form for viaduct to minimize the bulkiness of the structure and to blend the viaduct better with the background environment, featured form of tunnel portals, roadside planting along at-grade roads and landscape berm on & planting along edge of reclamation area) to beautify the HKLR alignment (refer to Figure 14.4.3).	Minimise visual & landscape impact	Detailed designer	HKLR	Design stage	N/A

Implementation Schedule of Environmental Mitigation Measures

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
Landscape & Visual (Construction Phase)							
S14.3.3.3	LV2	Mitigate both Landscape and Visual Impacts G1. Grass-hydroseed bare soil surface and stock pile areas. G2. Add planting strip and automatic irrigation system if appropriate at some portions of bridge or footbridge to screen bridge and traffic. G3. For HKLR, providing aesthetic design on the viaduct, tunnel portals, at-grade roads and reclamation (e.g. subtle colour tone and slim form for viaduct, featured form of tunnel portals, roadside planting along at-grade roads and landscape berm on & planting along edge of reclamation area) to beautify the HKLR alignment. G4. Not Applicable. G5 Vegetation reinstatement and upgrading to disturbed areas. G6. Maximize new tree, shrub and other vegetation planting to compensate tree felled and vegetation removed. G7. Provide planting area around peripheral of and within HKLR for tree screening buffer effect. G8. Plant salt tolerant native tree and shrubs etc along the planter strip at affected seawall. G9. Reserve of loose natural granite rocks for re-use. Provide new coastline to adopt .natural- look. by means of using armour rocks in the form of natural rock materials and planting strip area accommodating screen buffer to enhance .natural-look. of the new coastline (see Figure 14.4.2 for example).	Minimise visual & landscape impact	Contractor	HKLR	Construction stage	√
S14.3.3.3	LV3	Mitigate Visual Impacts V1.Minimize time for construction activities during construction period. V2.Provide screen hoarding at the portion of the project site / works areas / storage areas near VSRs who have close low-level views to the Project during HKLR construction.					

Implementation Schedule of Environmental Mitigation Measures

EIA Ref.	EM&A Log Ref.	Recommended Mitigation Measures	Objectives of the Recommended Measures & Main Concerns to address	Who to implement the measures?	Location of the measures	When to implement the measures?	Implementation Status
EM&A							
S15.5 - S15.6	EM2	1) An Environmental Team needs to be employed as per the EM&A Manual. 2) Prepare a systematic Environmental Management Plan to ensure effective implementation of the mitigation measures. 3) An environmental impact monitoring needs to be implementing by the Environmental Team to ensure all the requirements given in the EM&A Manual are fully complied with.	Perform environmental monitoring & auditing	Contractor	All construction sites	Construction stage	√

Legends:
√ Implemented
X Not Implemented
P Partially Implemented
N/A Not Applicable

APPENDIX F

Site Audit Findings and Corrective Actions

Appendix F – Site Audit Findings and Corrective Actions

Environmental site inspections were carried out on a weekly basis to monitor the implementation of proper environmental pollution control and mitigation measures for the Project. During the reporting period, site inspections were carried out on 5,12, 19 and 28 March 2025; 2, 9, 17, 25 and 30 April 2025; 7, 14, 21 and 30 May 2025. A summary of observations found during the site inspections and the follow up actions taken by the Contractor are described below:

Summary of Environmental Site Inspections

Date of Audit	Observations	Actions Taken by Contractor / Recommendation	Date of Observations Closed
5 March 2025	No particular environmental issue was recorded during the site inspection.	N.A.	N.A.
12 March 2025	No particular environmental issue was recorded during the site inspection.	N.A.	N.A.
19 March 2025	No particular environmental issue was recorded during the site inspection.	N.A.	N.A.
28 March 2025	No particular environmental issue was recorded during the site inspection.	N.A.	N.A.
2 April 2025	No particular environmental issue was recorded during the site inspection.	N.A.	N.A.
9 April 2025	No particular environmental issue was recorded during the site inspection.	N.A.	N.A.
17 April 2025	No particular environmental issue was recorded during the site inspection.	N.A.	N.A.

Date of Audit	Observations	Actions Taken by Contractor / Recommendation	Date of Observations Closed
25 April 2025	No particular environmental issue was recorded during the site inspection.	N.A.	N.A.
30 April 2025	No particular environmental issue was recorded during the site inspection.	N.A.	N.A.
7 May 2025	No particular environmental issue was recorded during the site inspection.	N.A.	N.A.
14 May 2025	No particular environmental issue was recorded during the site inspection.	N.A.	N.A.
21 May 2025	No particular environmental issue was recorded during the site inspection.	N.A.	N.A.
30 May 2025	No particular environmental issue was recorded during the site inspection.	N.A.	N.A.

APPENDIX G

Air Quality Monitoring Data and Graphical Plots

Air Quality Monitoring Data

Project	Works	Date (yyyy-mm-dd)	Station	Time	Parameter	Results	Unit
HKLR	HY/2011/03	2025-03-03	AMS5	08:50	1-hr TSP	90	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-03	AMS5	09:50	1-hr TSP	107	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-03	AMS5	10:50	1-hr TSP	107	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-07	AMS5	08:15	1-hr TSP	67	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-07	AMS5	09:15	1-hr TSP	77	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-07	AMS5	10:15	1-hr TSP	77	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-13	AMS5	09:00	1-hr TSP	82	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-13	AMS5	10:00	1-hr TSP	80	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-13	AMS5	11:00	1-hr TSP	80	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-19	AMS5	13:00	1-hr TSP	122	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-19	AMS5	14:00	1-hr TSP	120	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-19	AMS5	15:00	1-hr TSP	120	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-25	AMS5	08:50	1-hr TSP	99	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-25	AMS5	09:50	1-hr TSP	120	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-25	AMS5	10:50	1-hr TSP	120	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-31	AMS5	13:20	1-hr TSP	95	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-31	AMS5	14:20	1-hr TSP	120	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-31	AMS5	15:20	1-hr TSP	120	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-03	AMS6	13:05	1-hr TSP	74	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-03	AMS6	14:05	1-hr TSP	83	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-03	AMS6	15:05	1-hr TSP	83	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-07	AMS6	13:35	1-hr TSP	83	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-07	AMS6	14:35	1-hr TSP	62	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-07	AMS6	15:35	1-hr TSP	62	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-13	AMS6	08:45	1-hr TSP	61	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-13	AMS6	09:45	1-hr TSP	70	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-13	AMS6	10:45	1-hr TSP	70	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-19	AMS6	08:45	1-hr TSP	109	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-19	AMS6	09:45	1-hr TSP	102	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-19	AMS6	10:45	1-hr TSP	102	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-25	AMS6	13:25	1-hr TSP	110	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-25	AMS6	14:25	1-hr TSP	97	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-25	AMS6	15:25	1-hr TSP	97	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-31	AMS6	08:15	1-hr TSP	49	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-31	AMS6	09:15	1-hr TSP	57	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-31	AMS6	10:15	1-hr TSP	57	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-06	AMS5	08:00	24-hr TSP	18	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-12	AMS5	08:00	24-hr TSP	32	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-18	AMS5	08:00	24-hr TSP	40	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-24	AMS5	08:00	24-hr TSP	53	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-28	AMS5	08:00	24-hr TSP	24	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-06	AMS6	08:00	24-hr TSP	25	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-12	AMS6	08:00	24-hr TSP	37	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-18	AMS6	08:00	24-hr TSP	38	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-24	AMS6	08:00	24-hr TSP	71	$\mu g/m^3$
HKLR	HY/2011/03	2025-03-28	AMS6	08:00	24-hr TSP	30	$\mu g/m^3$

Remarks:

1) The existing air quality monitoring location AMS6 - Dragonair / CNAC (Group) Building (HKIA) was handed over to Airport Authority Hong Kong on 31 March 2021. 1hr and 24 hr air quality monitoring at AMS6 was temporarily suspended starting from 1 April 2021.

Air Quality Monitoring Data

Project	Works	Date (yyyy-mm-dd)	Station	Time	Parameter	Results	Unit
HKLR	HY/2011/03	2025-04-03	AMS5	13:00	1-hr TSP	117	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-03	AMS5	14:00	1-hr TSP	118	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-03	AMS5	15:00	1-hr TSP	118	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-09	AMS5	08:50	1-hr TSP	97	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-09	AMS5	09:50	1-hr TSP	102	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-09	AMS5	10:50	1-hr TSP	102	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-14	AMS5	13:10	1-hr TSP	130	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-14	AMS5	14:10	1-hr TSP	115	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-14	AMS5	15:10	1-hr TSP	115	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-17	AMS5	09:00	1-hr TSP	61	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-17	AMS5	10:00	1-hr TSP	66	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-17	AMS5	11:00	1-hr TSP	66	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-23	AMS5	13:25	1-hr TSP	77	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-23	AMS5	14:25	1-hr TSP	89	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-23	AMS5	15:25	1-hr TSP	89	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-28	AMS5	13:27	1-hr TSP	128	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-28	AMS5	14:27	1-hr TSP	123	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-28	AMS5	15:27	1-hr TSP	123	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-03	AMS6	08:30	1-hr TSP	122	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-03	AMS6	09:30	1-hr TSP	118	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-03	AMS6	10:30	1-hr TSP	118	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-09	AMS6	13:25	1-hr TSP	84	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-09	AMS6	14:25	1-hr TSP	95	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-09	AMS6	15:25	1-hr TSP	95	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-14	AMS6	08:25	1-hr TSP	100	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-14	AMS6	09:25	1-hr TSP	119	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-14	AMS6	10:25	1-hr TSP	119	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-17	AMS6	09:00	1-hr TSP	73	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-17	AMS6	10:00	1-hr TSP	76	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-17	AMS6	11:00	1-hr TSP	76	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-23	AMS5	08:10	1-hr TSP	74	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-23	AMS5	09:10	1-hr TSP	83	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-23	AMS5	10:10	1-hr TSP	83	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-28	AMS5	08:45	1-hr TSP	110	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-28	AMS5	09:45	1-hr TSP	110	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-28	AMS5	10:45	1-hr TSP	110	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-02	AMS5	08:00	24-hr TSP	46	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-08	AMS5	08:00	24-hr TSP	40	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-11	AMS5	08:00	24-hr TSP	24	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-16	AMS5	08:00	24-hr TSP	97	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-22	AMS5	08:00	24-hr TSP	25	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-28	AMS5	08:00	24-hr TSP	22	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-10	AMS6	08:00	24-hr TSP	52	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-11	AMS6	08:00	24-hr TSP	40	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-16	AMS6	08:00	24-hr TSP	245	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-22	AMS6	08:00	24-hr TSP	76	$\mu g/m^3$
HKLR	HY/2011/03	2025-04-28	AMS6	08:00	24-hr TSP	27	$\mu g/m^3$

Remarks:

1) The existing air quality monitoring location AMS6 - Dragonair / CNAC (Group) Building (HKIA) was handed over to Airport Authority Hong Kong on 31 March 2021. 1hr and 24 hr air quality monitoring at AMS6 was temporarily suspended starting from 1 April 2021.

2) Due to power supply issue, the 24-hr TSP monitoring at AMS6 on 2 April 2025 has been cancelled.

3) Due to power supply issue, the 24-hs TSP monitoring at AMS6 on 8 April 2025 has been rescheduled to 10 April 2025.

Air Quality Monitoring Data

Project	Works	Date (yyyy-mm-dd)	Station	Time	Parameter	Results	Unit
HKLR	HY/2011/03	2025-05-02	AMS5	13:00	1-hr TSP	94	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-02	AMS5	14:00	1-hr TSP	113	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-02	AMS5	15:00	1-hr TSP	113	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-08	AMS5	08:50	1-hr TSP	100	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-08	AMS5	09:50	1-hr TSP	120	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-08	AMS5	10:50	1-hr TSP	120	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-14	AMS5	13:10	1-hr TSP	125	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-14	AMS5	14:10	1-hr TSP	115	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-14	AMS5	15:10	1-hr TSP	115	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-20	AMS5	09:00	1-hr TSP	105	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-20	AMS5	10:00	1-hr TSP	113	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-20	AMS5	11:00	1-hr TSP	113	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-26	AMS5	13:25	1-hr TSP	85	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-26	AMS5	14:25	1-hr TSP	96	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-26	AMS5	15:25	1-hr TSP	96	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-30	AMS5	13:27	1-hr TSP	118	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-30	AMS5	14:27	1-hr TSP	111	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-30	AMS5	15:27	1-hr TSP	111	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-02	AMS6	08:30	1-hr TSP	87	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-02	AMS6	09:30	1-hr TSP	102	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-02	AMS6	10:30	1-hr TSP	102	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-08	AMS6	13:25	1-hr TSP	85	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-08	AMS6	14:25	1-hr TSP	91	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-08	AMS6	15:25	1-hr TSP	91	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-14	AMS6	08:25	1-hr TSP	74	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-14	AMS6	09:25	1-hr TSP	90	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-14	AMS6	10:25	1-hr TSP	90	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-20	AMS6	09:00	1-hr TSP	102	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-20	AMS6	10:00	1-hr TSP	92	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-20	AMS6	11:00	1-hr TSP	92	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-26	AMS6	08:10	1-hr TSP	77	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-26	AMS6	09:10	1-hr TSP	82	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-26	AMS6	10:10	1-hr TSP	82	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-30	AMS6	08:45	1-hr TSP	95	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-30	AMS6	09:45	1-hr TSP	105	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-30	AMS6	10:45	1-hr TSP	105	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-01	AMS5	08:00	24-hr TSP	35	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-07	AMS5	08:00	24-hr TSP	40	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-13	AMS5	08:00	24-hr TSP	37	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-19	AMS5	08:00	24-hr TSP	23	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-23	AMS5	08:00	24-hr TSP	37	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-29	AMS5	08:00	24-hr TSP	20	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-01	AMS6	08:00	24-hr TSP	49	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-07	AMS6	08:00	24-hr TSP	25	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-13	AMS6	08:00	24-hr TSP	40	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-19	AMS6	08:00	24-hr TSP	26	$\mu g/m^3$
HKLR	HY/2011/03	2025-05-23	AMS6	08:00	24-hr TSP	32	$\mu g/m^3$
HKLR	HY/2011/04	2025-05-29	AMS6	09:00	24-hr TSP	25	$\mu g/m^4$

Remarks:

1) The existing air quality monitoring location AMS6 - Dragonair / CNAC (Group) Building (HKIA) was handed over to Airport Authority Hong Kong on 31 March 2021. 1hr and 24 hr air quality monitoring at AMS6 was temporarily suspended starting from 1 April 2021.

Graphical Plot of 1-hour TSP at AMS5 and AMS6

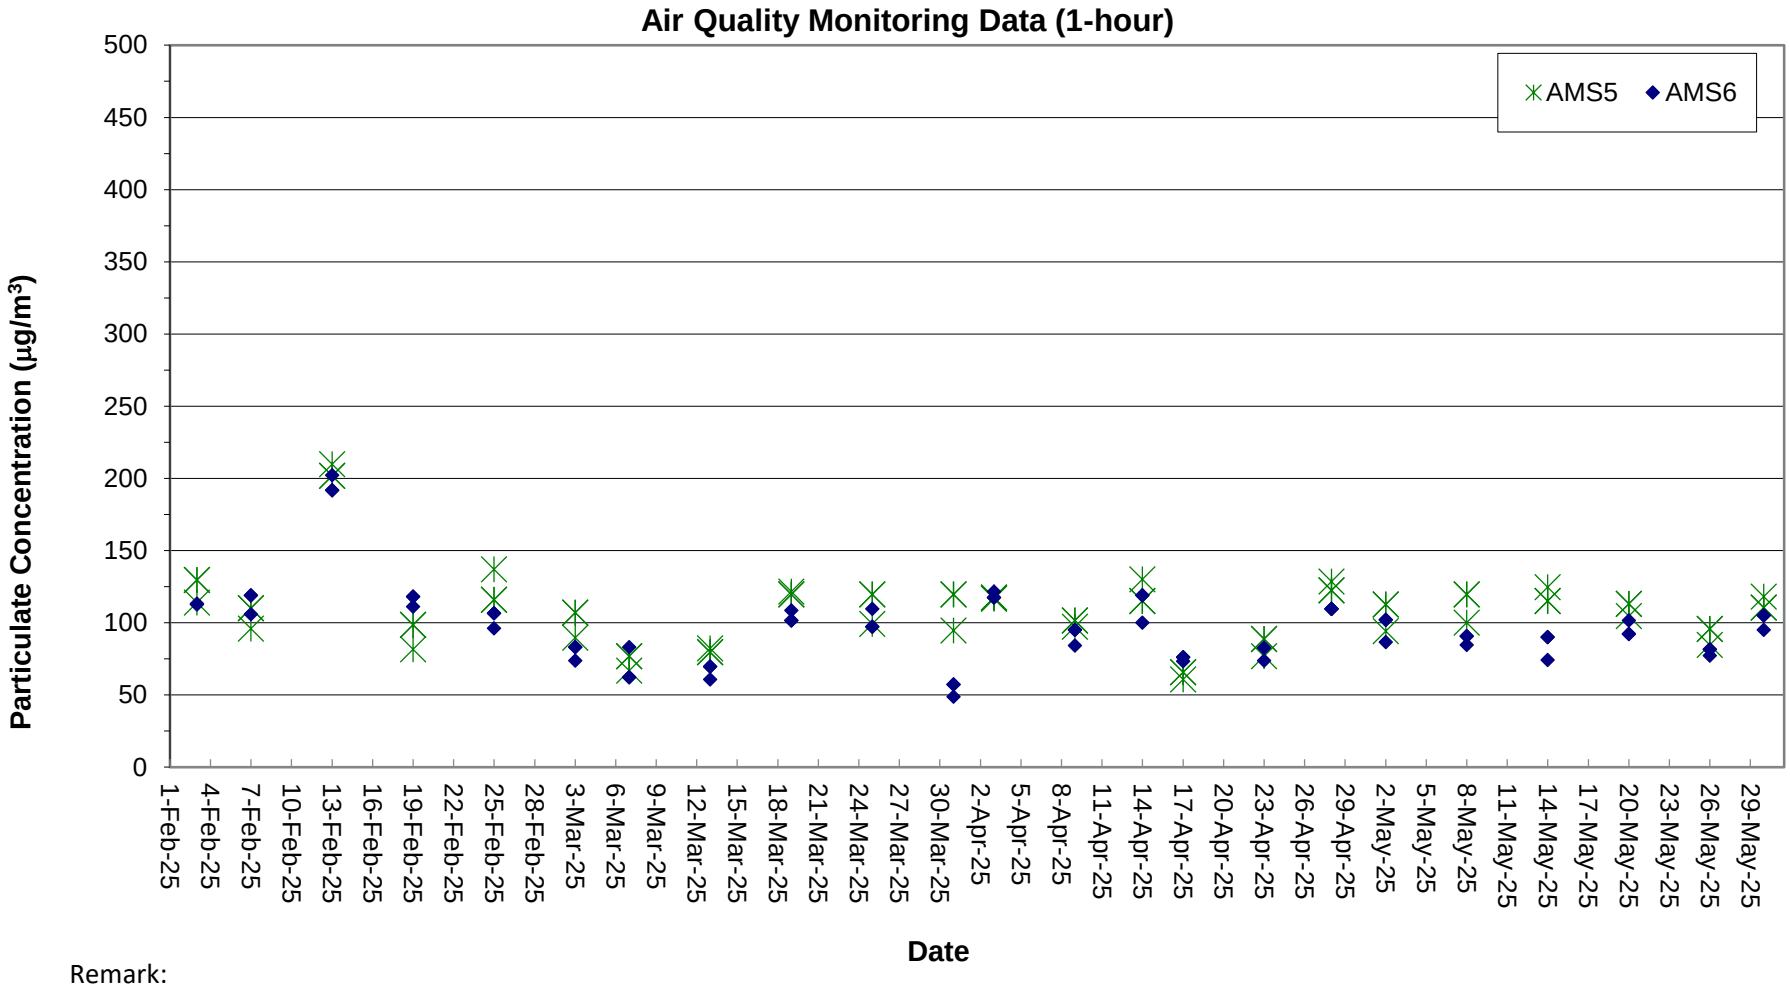

Remark:

1) The existing air quality monitoring location AMS6 - Dragonair / CNAC (Group) Building (HKIA) was handed over to Airport Authority Hong Kong on 31 March 2021. 1-hr TSP monitoring at AMS6 was temporarily suspended from 1 April 2021 to 31 July 2024 and restarted from 7 August 2024.

Graphical Plot of 24-hour TSP at AMS5 and AMS6

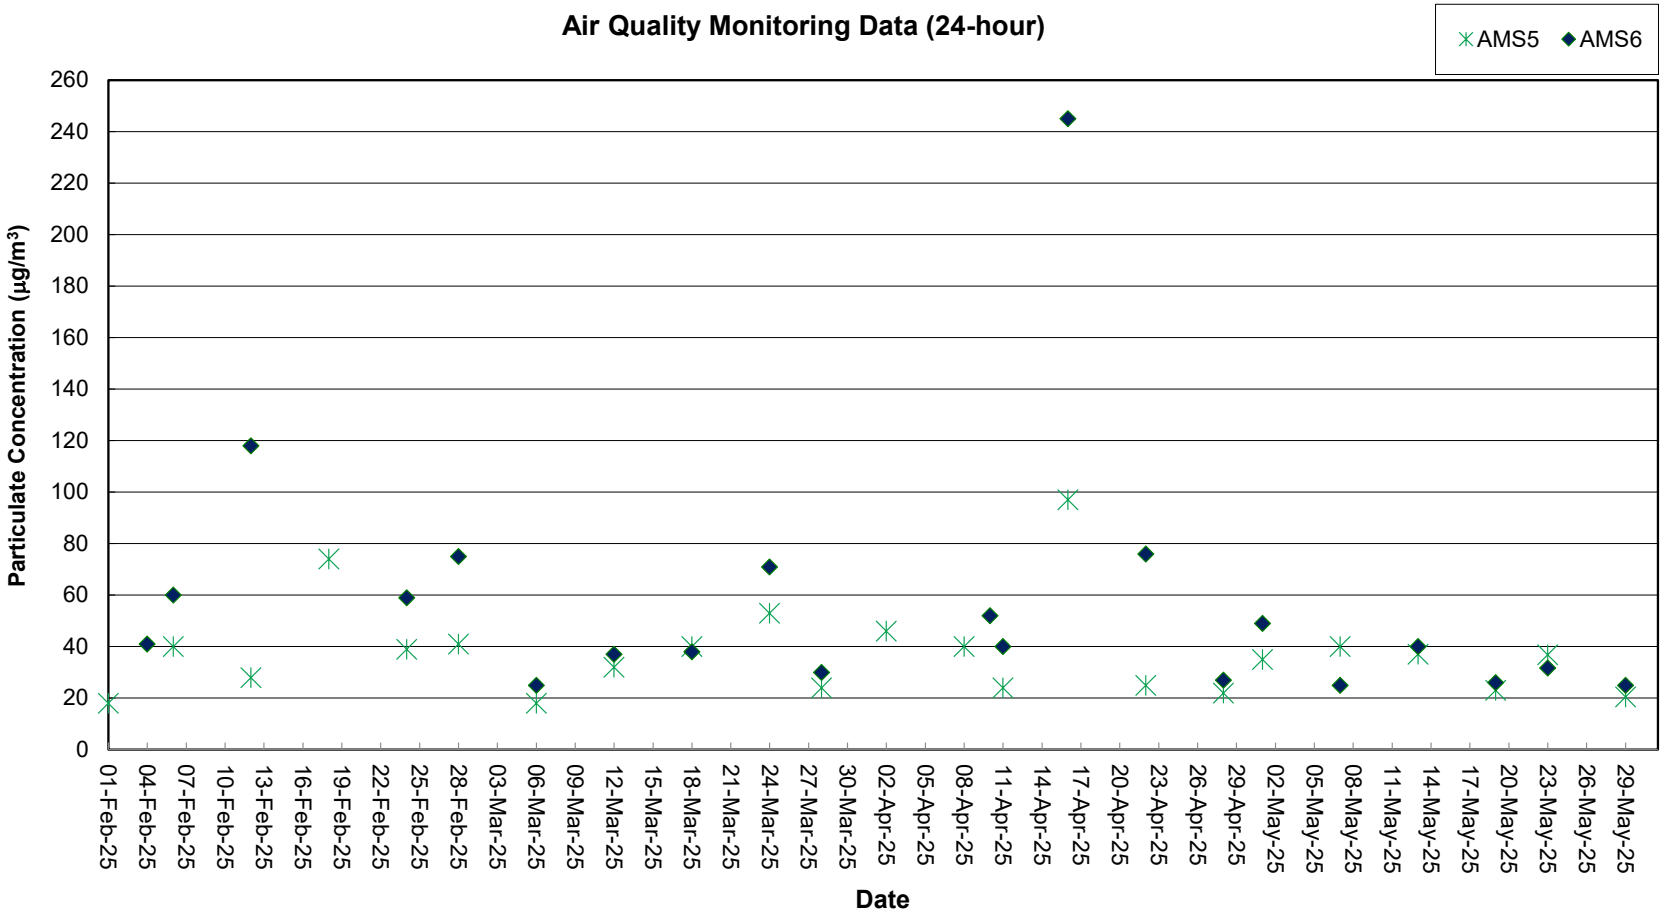

Remarks:

1) The existing air quality monitoring location AMS6 - Dragonair / CNAC (Group) Building (HKIA) was handed over to Airport Authority Hong Kong on 31 March 2021. 24-hr TSP monitoring at AMS6 was temporarily suspended starting from 1 April 2021 to 31 July 2024 and restarted from 7 August 2024.

APPENDIX H

Noise Monitoring Data and Graphical Plots

Noise Monitoring Data

Project	Works	Date (yyyy-mm-dd)	Station	Start Time	Wind Speed, m/s	1st set 5mins		2nd set 5mins		3rd set 5mins		4th set 5mins		5th set 5mins		6th set 5mins		Overall (30mins)*		Unit
HKLR	HY/2011/03	2025-03-03	NMS5	09:15	<5	Leq:	58.0	Leq:	56.9	Leq:	58.0	Leq:	56.6	Leq:	63.4	Leq:	65.9	Leq:	64	dB(A)
						L10:	60.0	L10:	59.0	L10:	60.2	L10:	58.7	L10:	63.7	L10:	67.8	L10:	66	
						L90:	54.8	L90:	53.9	L90:	54.9	L90:	53.9	L90:	55.1	L90:	59.5	L90:	59	
HKLR	HY/2011/03	2025-03-13	NMS5	09:00	<5	Leq:	59.4	Leq:	57.7	Leq:	57.0	Leq:	59.2	Leq:	58.2	Leq:	59.5	Leq:	62	dB(A)
						L10:	61.6	L10:	59.8	L10:	58.8	L10:	61.6	L10:	60.0	L10:	61.6	L10:	64	
						L90:	55.1	L90:	54.4	L90:	52.9	L90:	55.9	L90:	55.5	L90:	56.1	L90:	58	
HKLR	HY/2011/03	2025-03-19	NMS5	13:10	<5	Leq:	59.4	Leq:	62.4	Leq:	63.3	Leq:	67.3	Leq:	61.6	Leq:	63.9	Leq:	67	dB(A)
						L10:	62.8	L10:	64.4	L10:	65.7	L10:	67.5	L10:	62.4	L10:	66.5	L10:	68	
						L90:	55.8	L90:	55.4	L90:	60.1	L90:	61.3	L90:	61.3	L90:	61.3	L90:	63	
HKLR	HY/2011/03	2025-03-25	NMS5	09:05	<5	Leq:	65.0	Leq:	64.5	Leq:	63.2	Leq:	61.8	Leq:	61.7	Leq:	61.8	Leq:	66	dB(A)
						L10:	64.3	L10:	68.0	L10:	65.7	L10:	63.6	L10:	63.4	L10:	62.6	L10:	68	
						L90:	60.1	L90:	60.3	L90:	60.0	L90:	60.0	L90:	60.2	L90:	60.2	L90:	63	
HKLR	HY/2011/03	2025-03-31	NMS5	13:25	<5	Leq:	69.6	Leq:	62.7	Leq:	68.5	Leq:	64.7	Leq:	64.2	Leq:	64.4	Leq:	69	dB(A)
						L10:	72.9	L10:	65.1	L10:	71.7	L10:	68.4	L10:	68.1	L10:	69.2	L10:	73	
						L90:	57.3	L90:	56.7	L90:	57.0	L90:	57.1	L90:	56.5	L90:	55.9	L90:	60	

Remark:
(1)* A free field correction of +3 dB(A) was applied to the measured noise level.

Noise Monitoring Data

Project	Works	Date (yyyy-mm-dd)	Station	Start Time	Wind Speed, m/s	1st set 5mins		2nd set 5mins		3rd set 5mins		4th set 5mins		5th set 5mins		6th set 5mins		Overall (30mins)*		Unit
HKLR	HY/2011/03	2025-04-09	NMS5	09:20	<5	Leq:	58.5	Leq:	58.8	Leq:	56.4	Leq:	52.2	Leq:	52.3	Leq:	56.8	Leq:	60	dB(A)
						L10:	60.0	L10:	60.5	L10:	58.9	L10:	54.0	L10:	54.3	L10:	59.0	L10:	61	
						L90:	56.5	L90:	56.7	L90:	53.1	L90:	49.4	L90:	49.5	L90:	52.3	L90:	57	
HKLR	HY/2011/03	2025-04-14	NMS5	13:05	<5	Leq:	54.7	Leq:	54.5	Leq:	53.2	Leq:	53.6	Leq:	54.9	Leq:	53.9	Leq:	57	dB(A)
						L10:	55.1	L10:	55.8	L10:	54.6	L10:	54.9	L10:	56.0	L10:	55.4	L10:	58	
						L90:	51.0	L90:	52.2	L90:	51.5	L90:	51.7	L90:	52.3	L90:	51.8	L90:	55	
HKLR	HY/2011/03	2025-04-23	NMS5	13:20	<5	Leq:	55.1	Leq:	54.9	Leq:	56.9	Leq:	56.6	Leq:	56.2	Leq:	56.0	Leq:	59	dB(A)
						L10:	57.2	L10:	57.2	L10:	59.4	L10:	58.9	L10:	58.2	L10:	57.7	L10:	61	
						L90:	52.6	L90:	52.1	L90:	53.5	L90:	53.6	L90:	53.4	L90:	53.6	L90:	56	
HKLR	HY/2011/03	2025-04-29	NMS5	13:30	<5	Leq:	63.2	Leq:	60.2	Leq:	62.4	Leq:	63.6	Leq:	65.9	Leq:	65.3	Leq:	67	dB(A)
						L10:	65.4	L10:	63.4	L10:	65.4	L10:	65.8	L10:	69.1	L10:	68.3	L10:	70	
						L90:	56.8	L90:	57.4	L90:	58.7	L90:	58.8	L90:	60.5	L90:	60.8	L90:	62	

Remark:
(1)* A free field correction of +3 dB(A) was applied to the measured noise level.

Noise Monitoring Data

Project	Works	Date (yyyy-mm-dd)	Station	Start Time	Wind Speed, m/s	1st set 5mins		2nd set 5mins		3rd set 5mins		4th set 5mins		5th set 5mins		6th set 5mins		Overall (30mins)*		Unit
HKLR	HY/2011/03	2025-05-07	NMS5	13:40	<5	Leq:	58.6	Leq:	59.0	Leq:	59.1	Leq:	58.2	Leq:	58.4	Leq:	58.5	Leq:	62	dB(A)
						L10:	60.4	L10:	60.9	L10:	60.8	L10:	59.7	L10:	59.9	L10:	60.2	L10:	63	
						L90:	56.2	L90:	55.8	L90:	57.1	L90:	56.3	L90:	56.3	L90:	56.6	L90:	59	
HKLR	HY/2011/03	2025-05-14	NMS5	08:40	<5	Leq:	56.3	Leq:	54.1	Leq:	59.2	Leq:	54.0	Leq:	54.8	Leq:	54.0	Leq:	59	dB(A)
						L10:	57.3	L10:	55.5	L10:	62.8	L10:	55.9	L10:	56.8	L10:	55.3	L10:	61	
						L90:	53.5	L90:	52.4	L90:	53.4	L90:	52.0	L90:	51.9	L90:	52.0	L90:	56	
HKLR	HY/2011/03	2025-05-20	NMS5	08:50	<5	Leq:	58.5	Leq:	56.3	Leq:	56.8	Leq:	56.1	Leq:	58.9	Leq:	57.2	Leq:	60	dB(A)
						L10:	60.8	L10:	58.1	L10:	58.8	L10:	58.2	L10:	62.0	L10:	58.7	L10:	63	
						L90:	54.8	L90:	53.8	L90:	53.0	L90:	53.3	L90:	54.3	L90:	55.0	L90:	57	
HKLR	HY/2011/03	2025-05-26	NMS5	13:35	<5	Leq:	58.5	Leq:	56.3	Leq:	56.8	Leq:	56.1	Leq:	58.9	Leq:	57.2	Leq:	60	dB(A)
						L10:	60.8	L10:	58.1	L10:	58.8	L10:	58.2	L10:	62.0	L10:	58.7	L10:	63	
						L90:	54.8	L90:	53.8	L90:	53.0	L90:	53.3	L90:	54.3	L90:	55.0	L90:	57	

Remark:

(1)* A free field correction of +3 dB(A) was applied to the measured noise level.

Graphical Plot of Noise Levels at NMS5

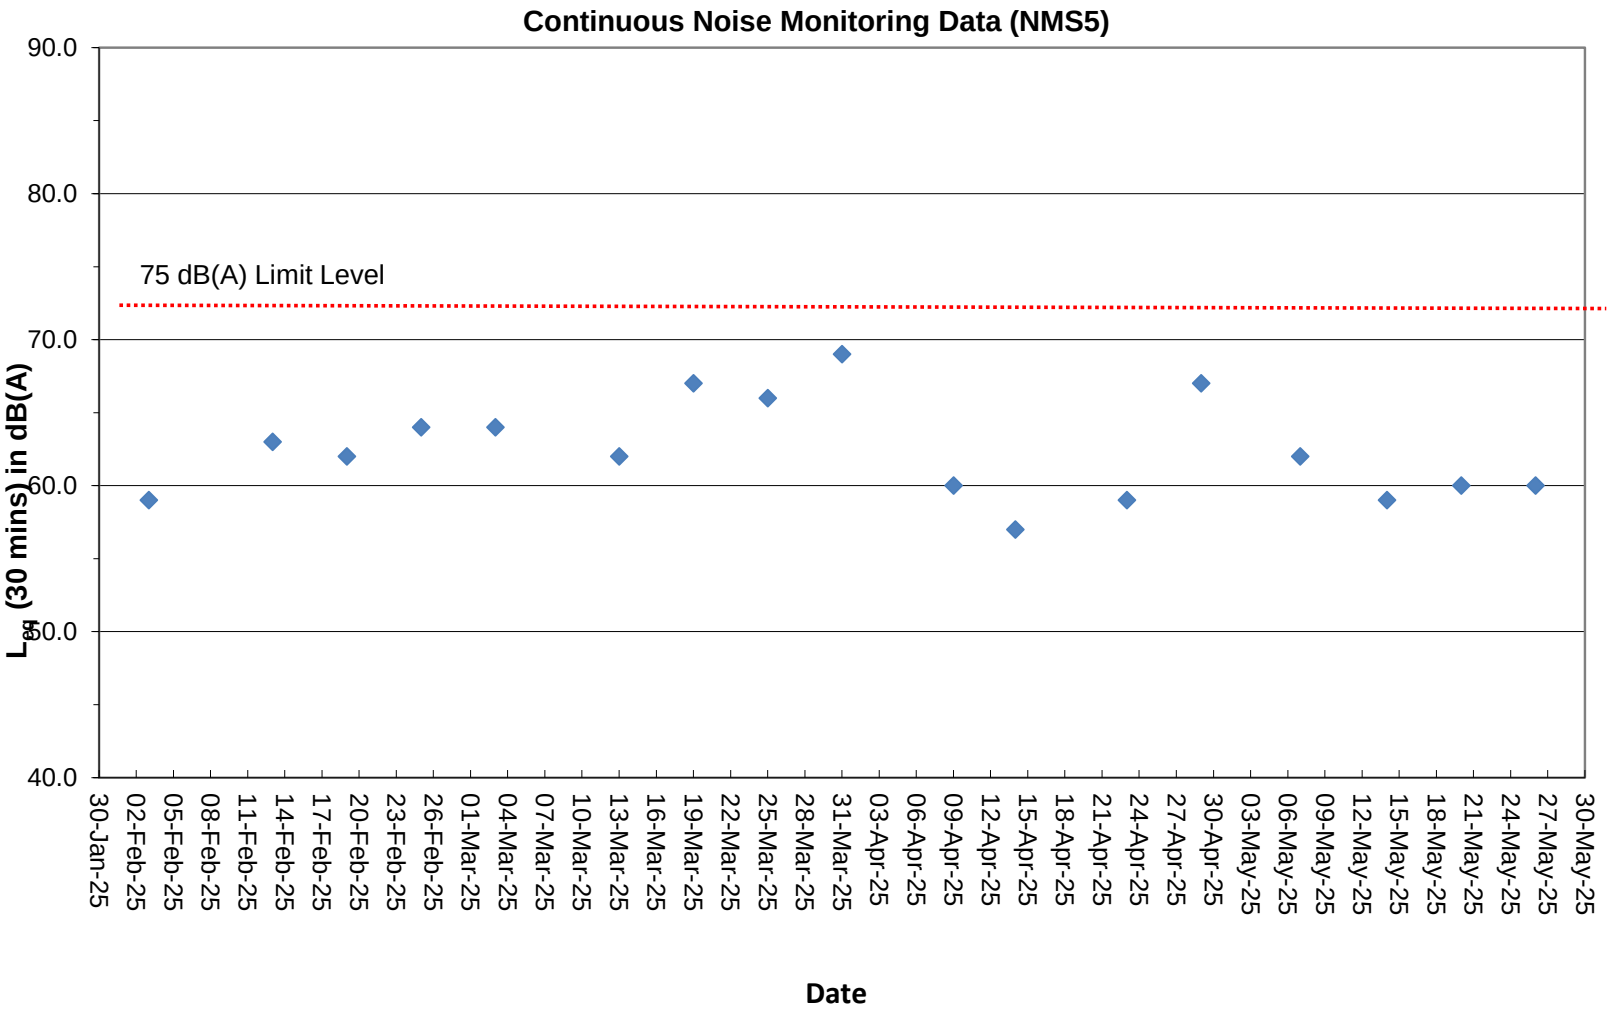

Remarks:

(1) A free field correction of +3 dB(A) was applied to the measured noise level.

APPENDIX I

Water Quality Monitoring Data and Graphical Plots

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	IS5	14:20:49	1.0	Surface	1	1	18.16	8.06	32.12	92.90	6.6	2.6	11.0
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	IS5	14:21:25	1.0	Surface	1	2	18.19	8.07	32.11	93.00	6.6	2.5	10.9
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	IS5	14:21:12	4.3	Middle	2	1	18.02	8.04	32.97	91.60	6.5	2.9	8.5
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	IS5	14:20:37	4.3	Middle	2	2	18.00	8.03	33.02	91.10	6.5	2.9	9.2
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	IS5	14:20:28	7.5	Bottom	3	1	17.99	8.03	33.18	90.30	6.5	3.0	13.9
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	IS5	14:21:02	7.5	Bottom	3	2	18.01	8.03	33.15	91.20	6.5	3.1	13.0
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	IS(Mf)6	14:29:06	1.0	Surface	1	1	18.21	8.07	32.17	95.50	6.8	2.7	11.7
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	IS(Mf)6	14:28:48	1.0	Surface	1	2	18.20	8.08	32.14	94.60	6.7	2.7	12.4
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	IS(Mf)6	14:28:57	2.2	Bottom	3	1	18.19	8.07	32.27	94.00	6.7	3.2	10.1
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	IS(Mf)6	14:28:38	2.2	Bottom	3	2	18.14	8.08	32.29	93.00	6.6	3.2	12.0
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	IS7	14:37:51	1.0	Surface	1	1	18.22	8.08	32.17	95.20	6.8	2.3	11.9
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	IS7	14:37:34	1.0	Surface	1	2	18.19	8.08	32.19	94.70	6.8	2.5	10.9
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	IS7	14:37:25	2.3	Bottom	3	1	18.16	8.08	32.31	94.10	6.7	2.7	13.3
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	IS7	14:37:41	2.3	Bottom	3	2	18.18	8.08	32.27	94.30	6.7	2.6	14.2
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	IS8(N)	15:10:41	1.0	Surface	1	1	18.19	8.06	32.15	92.50	6.6	2.7	12.7
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	IS8(N)	15:11:00	1.0	Surface	1	2	18.21	8.07	32.13	93.00	6.6	2.6	13.6
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	IS8(N)	15:10:50	2.9	Bottom	3	1	18.18	8.06	32.28	92.40	6.6	3.0	12.3
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	IS8(N)	15:10:32	2.9	Bottom	3	2	18.11	8.05	32.38	91.90	6.6	3.1	11.9
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	IS(Mf)9	14:47:38	1.0	Surface	1	1	18.22	8.08	32.18	94.80	6.8	2.5	11.8
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	IS(Mf)9	14:47:18	1.0	Surface	1	2	18.22	8.08	32.18	94.20	6.7	2.6	11.8
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	IS(Mf)9	14:47:27	2.5	Bottom	3	1	18.20	8.08	32.30	94.20	6.7	2.8	11.4
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	IS(Mf)9	14:47:10	2.5	Bottom	3	2	18.16	8.07	32.31	93.90	6.7	2.8	12.2
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	IS10(N)	15:19:08	1.0	Surface	1	1	18.09	8.08	31.77	88.20	6.1	2.0	11.6
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	IS10(N)	15:18:22	1.0	Surface	1	2	18.08	8.08	31.78	87.80	6.1	2.1	10.0
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	IS10(N)	15:18:07	5.3	Middle	2	1	17.90	8.05	32.81	86.70	6.0	2.4	11.3
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	IS10(N)	15:18:53	5.3	Middle	2	2	17.89	8.05	32.85	86.90	6.0	2.3	10.2
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	IS10(N)	15:17:57	9.6	Bottom	3	1	17.89	8.05	32.89	87.00	6.0	2.5	12.4
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	IS10(N)	15:18:43	9.6	Bottom	3	2	17.89	8.05	32.94	86.70	6.0	2.6	11.0
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	SR3(N)	14:04:44	1.0	Surface	1	1	18.21	8.07	32.07	94.20	6.7	2.7	12.4
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	SR3(N)	14:05:02	1.0	Surface	1	2	18.21	8.07	32.08	95.10	6.8	2.8	12.3
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	SR3(N)	14:04:51	2.3	Bottom	3	1	18.19	8.07	32.14	93.70	6.7	2.8	12.0
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	SR3(N)	14:04:34	2.3	Bottom	3	2	18.17	8.07	32.19	92.80	6.6	2.9	11.6
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	SR4(N3)	15:02:40	1.0	Surface	1	1	18.19	8.08	32.14	92.80	6.6	2.5	10.4
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	SR4(N3)	15:02:24	1.0	Surface	1	2	18.20	8.06	32.14	92.30	6.6	2.6	8.9
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	SR4(N3)	15:02:32	2.8	Bottom	3	1	18.17	8.06	32.28	92.00	6.6	2.8	13.6
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	SR4(N3)	15:02:15	2.8	Bottom	3	2	17.92	8.05	32.32	91.30	6.5	2.8	14.2
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	SR5(N)	15:09:38	1.0	Surface	1	1	18.09	8.08	31.72	89.00	6.2	2.0	11.6
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	SR5(N)	15:08:59	1.0	Surface	1	2	18.06	8.08	31.77	88.60	6.2	2.0	10.6
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	SR5(N)	15:09:26	4.7	Middle	2	1	17.92	8.06	32.66	87.10	6.1	2.3	13.4
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	SR5(N)	15:08:47	4.7	Middle	2	2	17.91	8.06	32.64	87.20	6.1	2.3	15.3
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	SR5(N)	15:09:13	8.3	Bottom	3	1	17.90	8.05	32.98	87.40	6.1	2.7	10.6
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	SR5(N)	15:08:35	8.3	Bottom	3	2	17.88	8.07	32.97	87.40	6.1	2.7	9.3
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	SR10A(N)	16:13:27	1.0	Surface	1	1	18.04	8.08	32.70	89.30	6.2	2.0	10.9
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	SR10A(N)	16:12:40	1.0	Surface	1	2	18.06	8.09	32.66	89.10	6.2	2.0	9.9
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	SR10A(N)	16:12:22	6.6	Middle	2	1	17.83	8.07	33.70	86.90	6.0	2.3	11.5
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	SR10A(N)	16:13:08	6.6	Middle	2	2	17.85	8.07	33.66	86.30	6.0	2.2	12.4
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	SR10A(N)	16:12:10	12.2	Bottom	3	1	17.84	8.09	33.78	87.00	6.0	2.6	11.3
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	SR10A(N)	16:12:57	12.2	Bottom	3	2	17.87	8.07	33.70	86.80	6.0	2.5	10.7
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	SR10B(N2)	16:24:34	1.0	Surface	1	1	18.05	8.08	32.74	87.90	6.1	1.8	10.2
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	SR10B(N2)	16:25:13	1.0	Surface	1	2	18.05	8.08	32.76	88.00	6.1	1.9	12.8
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	SR10B(N2)	16:24:21	3.7	Middle	2	1	17.92	8.07	33.30	86.90	6.0	2.0	11.6
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	SR10B(N2)	16:25:01	3.7	Middle	2	2	17.92	8.07	33.28	86.90	6.0	2.1	12.4
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	SR10B(N2)	16:24:11	6.3	Bottom	3	1	17.90	8.07	33.53	87.00	6.0	2.4	11.1
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	SR10B(N2)	16:24:47	6.3	Bottom	3	2	17.92	8.07	33.49	87.00	6.0	2.4	12.5
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	CS2(A)	14:16:03	1.0	Surface	1	1	18.00	8.09	31.87	92.00	6.4	1.9	13.2
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	CS2(A)	14:16:35	1.0	Surface	1	2	18.02	8.09	31.82	91.60	6.4	1.8	13.4
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	CS2(A)	14:16:23	3.4	Middle	2	1	17.89	8.07	32.68	89.30	6.2	2.2	13.4
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	CS2(A)	14:15:51	3.4	Middle	2	2	17.87	8.09	32.66	89.70	6.3	2.3	14.2
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	CS2(A)	14:15:40	5.7	Bottom	3	1	17.86	8.09	32.91	89.30	6.2	2.6	11.4
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	CS2(A)	14:16:14	5.7	Bottom	3	2	17.89	8.07	32.88	89.40	6.2	2.6	11.5
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	CS(Mf)5	15:53:49	1.0	Surface	1	1	18.18	8.10	32.32	89.30	6.4	2.3	9.2
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	CS(Mf)5	15:54:29	1.0	Surface	1	2	18.18	8.11	32.34	89.60	6.4	2.2	10.3
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	CS(Mf)5	15:54:15	6.3	Middle	2	1	17.80	8.02	33.65	86.70	6.2	2.6	7.7
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	CS(Mf)5	15:53:35	6.3	Middle	2	2	17.80	8.03	33.65	86.80	6.2	2.5	6.9
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	CS(Mf)5	15:54:04	11.6	Bottom	3	1	17.78	8.04	33.49	85.50	6.1	2.8	10.0
HKLR	HY/2011/03	2025-03-03	Mid-Ebb	Fine	CS(Mf)5	15:53:21	11.6	Bottom	3	2	17.75	8.02	33.92	85.30	6.1	2.7	13.8
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	IS5	09:40:48	1.0	Surface	1	1	18.06	8.08	32.25	89.90	6.3	2.6	10.6
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	IS5	09:40:03	1.0	Surface	1	2	18.08	8.09	32.25	90.80	6.4	2.5	8.8
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	IS5	09:39:50	4.3	Middle	2	1	17.82	8.03	33.30	87.20	6.1	2.9	11.2
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	IS5	09:40:35	4.3	Middle	2	2	17.81	8.02	33.28	87.40	6.1	2.9	10.8
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	IS5	09:40:17	7.5	Bottom	3	1	17.77	8.02	33.50	86.00	6.0	3.1	15.7
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	IS5	09:39:39	7.5	Bottom	3	2	17.80	8.02	33.51	86.00	6.0	3.1	15.0
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	IS(Mf)6	09:30:42	1.0	Surface	1	1	18.11	8.09	32.17	92.10	6.5	2.4	20.8
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	IS(Mf)6	09:30:26	1.0	Surface	1	2	18.09	8.09	32.17	91.80	6.4	2.4	18.4
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	IS(Mf)6	09:30:16	2.2	Bottom	3	1	18.05	8.07	32.39	91.60	6.4	2.7	12.3
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	IS(Mf)6	09:30:33	2.2	Bottom	3	2	18.07	8.07	32.35	91.50	6.4	2.7	10.5
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	IS7	09:20:56	1.0	Surface	1	1	18.11	8.07	32.16	91.60	6.4	2.4	9.3
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	IS7	09:20:39	1.0	Surface	1	2	18.09	8.08	32.18	91.30	6.4	2.4	14.3
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	IS7	09:20:47	2.3	Bottom	3	1	18.07	8.07	32.33	91.20	6.4	2.7	12.4
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	IS7	09:20:31	2.3	Bottom	3	2	18.05	8.06	32.36	91.20	6.4	2.7	10.4
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	IS8(N)	08:47:41	1.0	Surface	1	1	18.07	8.06	32.11	91.50	6.4	2.4	10.6
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	IS8(N)	08:46:51	1.0	Surface	1	2	18.08	8.06	32.09	91.00	6.4	2.5	10.7
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	IS8(N)	08:47:00	3.0	Bottom	3	1	18.01	8.04	32.49	90.50	6.4	2.6	13.1
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	IS8(N)	08:46:40	3.0	Bottom	3	2	17.98	8.05	32.55	90.00	6.3	2.8	16.6
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	IS(Mf)9	09:12:11	1.0	Surface	1	1	18.12	8.08	32.11	91.60	6.4	2.3	16.2
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	IS(Mf)9	09:11:55	1.0	Surface	1	2	18.11	8.08	32.12	91.20	6.4	2.4	14.6
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	IS(Mf)9	09:12:02	2.5	Bottom	3	1	18.08	8.06	32.36	90.80	6.4	2.8	15.9
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	IS(Mf)9	09:11:45	2.5	Bottom	3	2	18.03	8.06	32.39	90.40	6.3	2.7	14.3
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	IS10(N)	09:23:06	1.0	Surface	1	1	17.98	8.09	32.16	89.20	6.2	1.9	9.8
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	IS10(N)	09:23:47	1.0	Surface	1	2	18.00	8.09	32.14	89.40	6.2	2.0	10.1
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	IS10(N)	09:23:31	5.3	Middle	2	1	17.83	8.07	33.19	86.90	6.1	2.3	12.2
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	IS10(N)	09:22:50	5.3	Middle	2	2	17.83	8.07	33.18	87.00	6.1	2.3	12.5
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	IS10(N)	09:23:22	9.6	Bottom	3	1	17.84	8.06	33.25	86.90	6.0	2.7	14.5
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	IS10(N)	09:22:41	9.6	Bottom	3	2	17.82	8.07	33.28	86.80	6.0	2.6	13.0
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	SR3(N)	09:53:58	1.0	Surface	1	1	18.11	8.08	32.21	91.10	6.4	2.5	20.4
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	SR3(N)	09:53:41	1.0	Surface	1	2	18.10	8.08	32.23	90.30	6.3	2.6	13.2
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	SR3(N)	09:53:49	2.4	Bottom	3	1	18.08	8.08	32.37	90.20	6.3	2.9	16.3
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	SR3(N)	09:53:32	2.4	Bottom	3	2	18.03	8.07	32.42	89.40	6.3	3.0	17.7
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	SR4(N3)	08:57:13	1.0	Surface	1	1	18.06	8.05	32.12	90.70	6.4	2.3	17.3
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	SR4(N3)	08:57:32	1.0	Surface	1	2	18.09	8.05	32.12	90.40	6.4	2.3	18.3
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	SR4(N3)	08:57:22	2.9	Bottom	3	1	18.01	8.03	32.47	89.90	6.3	2.5	12.7
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	SR4(N3)	08:57:02	2.9	Bottom	3	2	17.98	8.03	32.51	90.40	6.4	2.5	13.2
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	SR5(N)	09:32:13	1	Surface	1	1	17.96	8.09	32.18	88.00	6.1	1.9	11.2
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	SR5(N)	09:31:28	1	Surface	1	2	17.98	8.09	32.23	88.00	6.1	1.9	10.7
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	SR5(N)	09:31:58	4.7	Middle	2	1	17.86	8.08	33.06	86.70	6.0	2.2	10.9
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	SR5(N)	09:31:15	4.7	Middle	2	2	17.86	8.07	33.07	86.70	6.0	2.3	10.7
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	SR5(N)	09:31:03	8.3	Bottom	3	1	17.82	8.06	33.27	86.90	6.0	2.5	10.4
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	SR5(N)	09:31:46	8.3	Bottom	3	2	17.84	8.06	33.25	87.00	6.0	2.6	11.5
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	SR10A(N)	08:26:43	1	Surface	1	1	18.07	8.09	32.41	87.50	6.1	1.8	10.1
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	SR10A(N)	08:26:00	1	Surface	1	2	18.09	8.08	32.41	87.50	6.1	1.9	10.7
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	SR10A(N)	08:25:44	6.6	Middle	2	1	17.86	8.05	33.53	86.00	6.0	2.1	11.2
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	SR10A(N)	08:26:26	6.6	Middle	2	2	17.86	8.05	33.53	85.60	5.9	2.1	10.5
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	SR10A(N)	08:25:32	12.2	Bottom	3	1	17.87	8.05	33.63	85.90	5.9	2.6	10.8
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	SR10A(N)	08:26:16	12.2	Bottom	3	2	17.89	8.05	33.64	85.80	5.9	2.6	11.8
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	SR10B(N2)	08:14:52	1.0	Surface	1	1	18.08	8.08	32.36	91.90	6.4	1.9	10.5
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	SR10B(N2)	08:14:11	1.0	Surface	1	2	18.09	8.06	32.35	91.90	6.4	1.9	9.8
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	SR10B(N2)	08:13:55	3.7	Middle	2	1	17.93	8.04	33.18	88.90	6.2	2.2	8.7
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	SR10B(N2)	08:14:38	3.7	Middle	2	2	17.95	8.06	33.13	88.20	6.1	2.2	12.1
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	SR10B(N2)	08:14:25	6.4	Bottom	3	1	17.93	8.05	33.45	87.20	6.0	2.5	12.0
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	SR10B(N2)	08:13:42	6.4	Bottom	3	2	17.77	8.03	33.52	87.20	6.1	2.5	10.4
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	CS2(A)	10:28:01	1	Surface	1	1	17.95	8.10	32.21	89.10	6.2	2.2	10.3
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	CS2(A)	10:27:21	1	Surface	1	2	17.95	8.11	32.16	89.10	6.2	2.1	11.7
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	CS2(A)	10:27:47	3.4	Middle	2	1	17.86	8.09	32.86	88.10	6.1	2.4	10.8
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	CS2(A)	10:27:09	3.4	Middle	2	2	17.87	8.09	32.86	88.00	6.1	2.5	11.5
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	CS2(A)	10:27:36	5.7	Bottom	3	1	17.85	8.09	33.10	87.90	6.1	2.8	12.4

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	CS2(A)	10:26:57	5.7	Bottom	3	2	17.82	8.09	33.13	87.80	6.1	2.7	12.5
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	CS(Mf)5	08:02:56	1.0	Surface	1	1	18.05	8.09	32.18	90.40	6.4	2.2	16.4
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	CS(Mf)5	08:03:43	1.0	Surface	1	2	18.07	8.09	32.17	90.90	6.4	2.1	16.4
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	CS(Mf)5	08:03:26	6.2	Middle	2	1	17.77	8.07	33.51	87.90	6.2	2.4	18.8
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	CS(Mf)5	08:02:40	6.2	Middle	2	2	17.77	8.06	33.48	88.40	6.2	2.4	14.9
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	CS(Mf)5	08:03:14	11.4	Bottom	3	1	17.76	8.06	33.73	86.20	6.0	2.8	13.1
HKLR	HY/2011/03	2025-03-03	Mid-Flood	Fine	CS(Mf)5	08:02:28	11.4	Bottom	3	2	17.77	8.05	33.71	86.60	6.1	2.6	14.3
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	IS5	15:58:29	1.0	Surface	1	1	18.23	8.08	32.11	91.80	6.5	2.5	5.5
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	IS5	15:59:06	1.0	Surface	1	2	18.26	8.09	32.11	91.90	6.5	2.5	4.0
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	IS5	15:58:52	4.4	Middle	2	1	18.08	8.07	32.84	90.50	6.4	2.8	3.1
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	IS5	15:58:16	4.4	Middle	2	2	18.05	8.06	32.88	90.10	6.4	2.8	4.4
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	IS5	15:58:07	7.7	Bottom	3	1	18.04	8.06	33.00	89.60	6.4	3.0	5.3
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	IS5	15:58:42	7.7	Bottom	3	2	18.07	8.06	32.97	90.40	6.4	3.0	4.3
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	IS(Mf)6	16:08:35	1.0	Surface	1	1	18.28	8.08	32.14	94.70	6.7	2.5	4.3
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	IS(Mf)6	16:08:15	1.0	Surface	1	2	18.27	8.08	32.12	93.80	6.7	2.5	4.8
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	IS(Mf)6	16:08:26	2.2	Bottom	3	1	18.25	8.08	32.23	93.20	6.6	2.9	5.9
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	IS(Mf)6	16:08:06	2.2	Bottom	3	2	18.21	8.08	32.25	92.20	6.5	3.0	5.1
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	IS7	16:18:10	1.0	Surface	1	1	18.30	8.09	32.12	94.30	6.7	2.2	5.0
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	IS7	16:17:53	1.0	Surface	1	2	18.27	8.09	32.13	93.80	6.7	2.4	4.5
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	IS7	16:17:44	2.3	Bottom	3	1	18.24	8.09	32.25	93.00	6.6	2.6	4.1
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	IS7	16:18:00	2.3	Bottom	3	2	18.26	8.09	32.21	93.30	6.6	2.5	5.3
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	IS8(N)	16:49:44	1.0	Surface	1	1	18.24	8.09	32.09	91.50	6.5	2.7	4.9
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	IS8(N)	16:50:03	1.0	Surface	1	2	18.27	8.10	32.07	92.10	6.6	2.6	4.8
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	IS8(N)	16:49:53	2.9	Bottom	3	1	18.23	8.09	32.20	91.40	6.5	2.9	4.6
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	IS8(N)	16:49:35	2.9	Bottom	3	2	18.16	8.08	32.30	90.80	6.5	3.0	5.6
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	IS(Mf)9	16:27:07	1.0	Surface	1	1	18.30	8.09	32.12	93.80	6.7	2.4	3.8
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	IS(Mf)9	16:26:46	1.0	Surface	1	2	18.29	8.08	32.12	93.20	6.6	2.5	4.7
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	IS(Mf)9	16:26:56	2.5	Bottom	3	1	18.27	8.08	32.24	93.20	6.6	2.7	5.1
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	IS(Mf)9	16:26:38	2.5	Bottom	3	2	18.24	8.07	32.24	92.90	6.6	2.6	3.9
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	IS10(N)	16:33:30	1.0	Surface	1	1	18.09	8.09	31.70	88.00	6.1	2.5	3.1
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	IS10(N)	16:34:14	1.0	Surface	1	2	18.12	8.10	31.69	88.60	6.1	2.4	3.4
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	IS10(N)	16:33:16	5.2	Middle	2	1	17.91	8.07	32.85	87.00	6.0	2.8	3.3
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	IS10(N)	16:34:00	5.2	Middle	2	2	17.91	8.07	32.89	87.10	6.0	2.8	3.6
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	IS10(N)	16:33:05	9.4	Bottom	3	1	17.93	8.07	32.94	87.30	6.0	2.9	3.9
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	IS10(N)	16:33:50	9.4	Bottom	3	2	17.93	8.07	32.97	87.00	6.0	3.0	3.7
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	SR3(N)	15:45:12	1.0	Surface	1	1	18.29	8.08	32.07	94.50	6.7	2.7	4.5
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	SR3(N)	15:44:54	1.0	Surface	1	2	18.29	8.08	32.08	93.80	6.7	2.7	3.3
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	SR3(N)	15:45:01	2.3	Bottom	3	1	18.27	8.08	32.13	93.20	6.6	2.8	4.4
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	SR3(N)	15:44:42	2.3	Bottom	3	2	18.24	8.08	32.19	92.20	6.4	2.9	3.6
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	SR4(N3)	16:40:45	1.0	Surface	1	1	18.26	8.11	32.08	92.10	6.5	2.5	3.8
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	SR4(N3)	16:40:28	1.0	Surface	1	2	18.26	8.10	32.09	91.70	6.5	2.6	4.4
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	SR4(N3)	16:40:36	2.8	Bottom	3	1	18.24	8.09	32.22	91.40	6.5	2.8	4.8
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	SR4(N3)	16:40:18	2.8	Bottom	3	2	18.00	8.08	32.26	90.70	6.4	2.8	4.3
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	SR5(N)	16:23:32	1.0	Surface	1	1	18.10	8.09	31.66	89.10	6.2	2.2	4.5
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	SR5(N)	16:22:54	1.0	Surface	1	2	18.08	8.10	31.69	88.80	6.1	2.2	4.8
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	SR5(N)	16:23:20	4.7	Middle	2	1	17.94	8.07	32.71	87.30	6.0	2.5	2.7
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	SR5(N)	16:22:42	4.7	Middle	2	2	17.93	8.08	32.69	87.50	6.0	2.6	4.1
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	SR5(N)	16:23:07	8.3	Bottom	3	1	17.94	8.07	32.99	87.70	6.0	3.1	4.6
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	SR5(N)	16:22:30	8.3	Bottom	3	2	17.92	8.08	33.00	87.90	6.1	3.0	3.6
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	SR10A(N)	17:29:39	1.0	Surface	1	1	18.01	8.10	32.74	89.80	6.2	2.2	4.0
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	SR10A(N)	17:28:53	1.0	Surface	1	2	18.04	8.11	32.70	89.40	6.2	2.1	3.6
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	SR10A(N)	17:29:20	6.6	Middle	2	1	17.84	8.09	33.70	86.50	5.9	2.4	4.6
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	SR10A(N)	17:28:36	6.6	Middle	2	2	17.81	8.10	33.79	87.20	6.0	2.5	3.8
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	SR10A(N)	17:28:24	12.1	Bottom	3	1	17.82	8.11	33.86	87.10	6.0	2.7	5.6
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	SR10A(N)	17:29:10	12.1	Bottom	3	2	17.86	8.09	33.75	86.90	6.0	2.6	4.6
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	SR10B(N2)	17:39:34	1.0	Surface	1	1	18.04	8.10	32.78	87.90	6.0	2.0	4.0
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	SR10B(N2)	17:40:11	1.0	Surface	1	2	18.03	8.10	32.82	88.10	6.1	2.1	3.3
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	SR10B(N2)	17:39:22	3.6	Middle	2	1	17.92	8.09	33.35	86.90	6.0	2.2	4.6
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	SR10B(N2)	17:39:59	3.6	Middle	2	2	17.92	8.09	33.31	87.00	6.0	2.3	3.6
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	SR10B(N2)	17:39:11	6.2	Bottom	3	1	17.90	8.09	33.59	87.00	6.0	2.6	4.1
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	SR10B(N2)	17:39:47	6.2	Bottom	3	2	17.93	8.09	33.53	87.10	6.0	2.6	3.8
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	CS2(A)	15:30:07	1.0	Surface	1	1	18.03	8.11	31.79	92.50	6.4	2.1	4.5
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	CS2(A)	15:30:40	1.0	Surface	1	2	18.06	8.11	31.73	91.90	6.4	2.0	3.8
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	CS2(A)	15:30:28	3.3	Middle	2	1	17.93	8.09	32.67	89.60	6.2	2.5	4.3
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	CS2(A)	15:29:57	3.3	Middle	2	2	17.91	8.10	32.66	90.20	6.3	2.6	4.2
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	CS2(A)	15:29:46	5.6	Bottom	3	1	17.91	8.11	32.90	89.80	6.2	2.9	3.6
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	CS2(A)	15:30:19	5.6	Bottom	3	2	17.94	8.09	32.87	89.80	6.2	2.9	4.9
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	CS(Mf)5	17:31:13	1.0	Surface	1	1	18.26	8.08	32.19	88.50	6.3	2.2	4.6
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	CS(Mf)5	17:31:55	1.0	Surface	1	2	18.25	8.08	32.21	88.90	6.3	2.1	3.8
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	CS(Mf)5	17:31:40	6.3	Middle	2	1	17.87	8.04	33.31	86.10	6.1	2.4	4.1
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	CS(Mf)5	17:30:59	6.3	Middle	2	2	17.86	8.05	33.31	86.20	6.1	2.4	3.8
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	CS(Mf)5	17:31:30	11.6	Bottom	3	1	17.86	8.06	33.10	85.00	6.0	2.6	4.2
HKLR	HY/2011/03	2025-03-05	Mid-Ebb	Fine	CS(Mf)5	17:30:47	11.6	Bottom	3	2	17.81	8.05	33.51	84.80	6.0	2.6	3.2
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	IS5	10:13:40	1.0	Surface	1	1	18.13	8.08	32.17	88.70	6.1	2.5	3.9
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	IS5	10:12:55	1.0	Surface	1	2	18.15	8.09	32.17	89.70	6.2	2.4	3.7
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	IS5	10:13:27	4.2	Middle	2	1	17.86	8.05	33.02	86.20	6.0	2.8	4.6
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	IS5	10:12:42	4.2	Middle	2	2	17.87	8.06	33.04	86.00	5.9	2.8	4.4
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	IS5	10:13:10	7.3	Bottom	3	1	17.83	8.05	33.20	85.00	5.9	3.0	4.8
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	IS5	10:12:32	7.3	Bottom	3	2	17.84	8.06	33.21	85.00	5.9	3.1	5.0
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	IS(Mf)6	10:03:38	1.0	Surface	1	1	18.17	8.07	32.10	91.40	6.3	2.3	4.8
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	IS(Mf)6	10:03:21	1.0	Surface	1	2	18.15	8.08	32.10	91.10	6.3	2.3	5.1
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	IS(Mf)6	10:03:28	2.2	Bottom	3	1	18.13	8.10	32.26	90.80	6.3	2.6	5.0
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	IS(Mf)6	10:03:06	2.2	Bottom	3	2	18.10	8.10	32.30	90.90	6.3	2.6	3.9
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	IS7	09:53:58	1.0	Surface	1	1	18.18	8.10	32.08	91.10	6.3	2.4	3.5
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	IS7	09:53:42	1.0	Surface	1	2	18.15	8.10	32.11	90.60	6.2	2.4	2.9
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	IS7	09:53:50	2.3	Bottom	3	1	18.13	8.10	32.25	90.40	6.2	2.7	3.4
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	IS7	09:53:33	2.3	Bottom	3	2	18.10	8.09	32.27	90.40	6.2	2.7	4.1
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	IS8(N)	09:21:28	1.0	Surface	1	1	18.13	8.10	32.02	90.70	6.3	2.7	4.2
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	IS8(N)	09:20:49	1.0	Surface	1	2	18.14	8.10	32.01	90.20	6.2	2.8	3.2
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	IS8(N)	09:20:57	3.0	Bottom	3	1	18.07	8.07	32.40	89.60	6.2	3.0	3.2
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	IS8(N)	09:20:38	3.0	Bottom	3	2	18.03	8.09	32.44	89.20	6.2	3.1	3.6
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	IS(Mf)9	09:44:32	1.0	Surface	1	1	18.18	8.08	32.04	90.80	6.3	2.5	4.6
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	IS(Mf)9	09:44:15	1.0	Surface	1	2	18.17	8.09	32.05	90.20	6.2	2.6	3.4
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	IS(Mf)9	09:44:22	2.5	Bottom	3	1	18.13	8.09	32.27	89.90	6.2	3.0	3.3
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	IS(Mf)9	09:44:05	2.5	Bottom	3	2	18.08	8.09	32.30	89.40	6.2	2.9	2.8
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	IS10(N)	09:42:28	1.0	Surface	1	1	18.00	8.10	32.13	89.20	6.2	2.2	4.8
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	IS10(N)	09:41:47	1.0	Surface	1	2	17.97	8.10	32.14	89.20	6.2	2.2	3.7
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	IS10(N)	09:42:12	5.3	Middle	2	1	17.86	8.08	33.08	87.00	6.0	2.5	5.0
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	IS10(N)	09:41:31	5.3	Middle	2	2	17.85	8.08	33.07	87.30	6.0	2.6	4.0
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	IS10(N)	09:42:03	9.6	Bottom	3	1	17.88	8.08	33.15	87.20	6.0	3.0	4.9
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	IS10(N)	09:41:22	9.6	Bottom	3	2	17.86	8.08	33.18	87.20	6.0	2.9	4.4
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	SR3(N)	10:27:04	1.0	Surface	1	1	18.17	8.08	32.14	90.50	6.2	2.4	3.3
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	SR3(N)	10:26:47	1.0	Surface	1	2	18.17	8.08	32.16	89.70	6.2	2.5	4.3
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	SR3(N)	10:26:55	2.3	Bottom	3	1	18.14	8.08	32.27	89.70	6.2	2.7	4.3
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	SR3(N)	10:26:38	2.3	Bottom	3	2	18.10	8.07	32.32	88.70	6.1	2.8	4.7
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	SR4(N3)	09:30:10	1.0	Surface	1	1	18.12	8.09	32.02	89.60	6.2	2.6	4.8
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	SR4(N3)	09:30:29	1.0	Surface	1	2	18.14	8.09	32.03	89.20	6.2	2.6	3.8
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	SR4(N3)	09:30:18	2.9	Bottom	3	1	18.06	8.06	32.41	88.70	6.1	2.9	3.7
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	SR4(N3)	09:29:59	2.9	Bottom	3	2	18.03	8.06	32.43	89.20	6.2	2.9	4.0
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	SR5(N)	09:53:27	1	Surface	1	1	17.96	8.10	32.15	88.00	6.1	2.1	4.6
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	SR5(N)	09:52:42	1	Surface	1	2	17.98	8.10	32.20	88.00	6.1	2.1	3.8
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	SR5(N)	09:53:13	4.7	Middle	2	1	17.88	8.09	32.96	86.80	6.0	2.4	3.8
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	SR5(N)	09:52:29	4.7	Middle	2	2	17.88	8.08	32.99	86.70	6.0	2.4	3.6
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	SR5(N)	09:52:17	8.4	Bottom	3	1	17.86	8.08	33.18	87.00	6.0	2.7	3.4
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	SR5(N)	09:53:01	8.4	Bottom	3	2	17.88	8.07	33.14	87.20	6.0	2.9	3.2
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	SR10A(N)	08:51:49	1	Surface	1	1	18.06	8.08	32.32	87.60	6.0	1.9	3.2
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	SR10A(N)	08:51:06	1	Surface	1	2	18.07	8.09	32.34	87.70	6.1	2.0	3.8
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	SR10A(N)	08:50:49	6.7	Middle	2	1	17.87	8.07	33.24	86.20	5.9	2.2	3.6
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	SR10A(N)	08:51:32	6.7	Middle	2	2	17.87	8.07	33.24	85.80	5.9	2.2	3.2
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	SR10A(N)	08:50:38	12.3	Bottom	3	1	17.90	8.07	33.43	86.20	5.9	2.8	3.2
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	SR10A(N)	08:51:21	12.3	Bottom	3	2	17.92	8.07	33.47	86.20	5.9	2.8	4.4
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	SR10B(N2)	08:41:51	1.0	Surface	1	1	18.07	8.09	32.29	92.50	6.4	1.9	3.9
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	SR10B(N2)	08:41:09	1.0	Surface	1	2	18.08	8.08	32.25	92.30	6.4	1.9	3.4
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	SR10B(N2)	08:40:53	3.7	Middle	2	1	17.95	8.06	33.01	89.40	6.2	2.3	2.8
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	SR10B(N2)	08:41:37	3.7	Middle	2	2	17.96	8.08	32.97	88.40	6.1	2.2	4.0

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	SR10B(N2)	08:41:24	6.4	Bottom	3	1	17.95	8.07	33.28	87.60	6.0	2.6	3.8
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	SR10B(N2)	08:40:40	6.4	Bottom	3	2	17.85	8.06	33.32	87.50	6.0	2.6	3.3
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	CS2(A)	10:51:20	1	Surface	1	1	17.96	8.11	32.14	89.00	6.2	2.5	2.9
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	CS2(A)	10:50:41	1	Surface	1	2	17.96	8.11	32.12	89.10	6.2	2.4	3.2
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	CS2(A)	10:51:06	3.4	Middle	2	1	17.89	8.10	32.78	88.10	6.1	2.7	3.0
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	CS2(A)	10:50:29	3.4	Middle	2	2	17.90	8.10	32.77	88.00	6.1	2.8	3.2
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	CS2(A)	10:50:56	5.7	Bottom	3	1	17.90	8.09	32.99	88.00	6.1	3.1	3.2
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	CS2(A)	10:50:16	5.7	Bottom	3	2	17.87	8.10	33.02	88.10	6.1	3.0	4.2
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	CS(Mf)5	08:37:06	1.0	Surface	1	1	18.13	8.06	32.11	89.10	6.2	2.2	3.0
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	CS(Mf)5	08:37:53	1.0	Surface	1	2	18.15	8.08	32.08	90.00	6.2	2.1	3.0
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	CS(Mf)5	08:37:35	6.3	Middle	2	1	17.81	8.07	33.23	86.60	6.0	2.4	2.8
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	CS(Mf)5	08:36:50	6.3	Middle	2	2	17.81	8.06	33.22	86.90	6.0	2.4	3.2
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	CS(Mf)5	08:36:38	11.5	Bottom	3	1	17.81	8.05	33.34	85.20	5.9	2.7	3.9
HKLR	HY/2011/03	2025-03-05	Mid-Flood	Fine	CS(Mf)5	08:37:23	11.5	Bottom	3	2	17.82	8.06	33.40	84.50	5.8	2.8	3.2
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Cloudy	IS5	18:22:26	1.0	Surface	1	1	18.03	7.96	30.85	89.80	5.8	3.4	2.1
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Cloudy	IS5	18:23:11	1.0	Surface	1	2	18.03	7.96	30.92	90.40	5.9	3.5	2.4
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Cloudy	IS5	18:22:16	4.1	Middle	2	1	18.00	7.98	31.36	89.10	5.8	3.5	1.6
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Cloudy	IS5	18:22:51	4.1	Middle	2	2	17.96	7.95	30.81	90.10	5.8	3.5	1.9
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Cloudy	IS5	18:21:59	7.2	Bottom	3	1	18.05	7.97	31.35	89.00	5.8	3.6	2.8
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Cloudy	IS5	18:22:40	7.2	Bottom	3	2	17.73	7.96	31.31	90.10	5.9	3.5	3.4
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Cloudy	IS(Mf)6	18:32:02	1.0	Surface	1	1	18.03	7.94	30.80	91.20	5.9	3.4	2.3
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Cloudy	IS(Mf)6	18:32:25	1.0	Surface	1	2	18.02	7.94	30.85	91.00	5.9	3.5	3.1
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Cloudy	IS(Mf)6	18:31:45	2.0	Bottom	3	1	18.00	7.93	31.33	91.00	5.9	3.4	2.2
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Cloudy	IS(Mf)6	18:32:14	2.0	Bottom	3	2	17.97	7.93	31.01	90.90	5.9	3.4	3.2
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Cloudy	IS7	18:43:41	1.0	Surface	1	1	17.95	7.93	30.80	89.80	5.8	3.4	3.9
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Cloudy	IS7	18:43:56	1.0	Surface	1	2	17.95	7.93	30.79	90.10	5.8	3.4	2.9
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Cloudy	IS7	18:43:25	2.0	Bottom	3	1	17.81	7.93	31.03	89.70	5.8	3.4	1.9
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Cloudy	IS7	18:43:49	2.0	Bottom	3	2	17.85	7.93	31.00	89.40	5.8	3.5	1.6
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Cloudy	IS8(N)	19:16:27	1.0	Surface	1	1	18.05	7.98	30.95	90.40	5.8	3.4	2.2
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Cloudy	IS8(N)	19:16:51	1.0	Surface	1	2	18.06	7.98	30.96	90.20	5.8	3.5	3.4
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Cloudy	IS8(N)	19:16:10	2.8	Bottom	3	1	17.98	7.97	31.16	90.20	5.8	3.4	3.8
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Cloudy	IS8(N)	19:16:39	2.8	Bottom	3	2	18.01	7.98	31.22	90.10	5.8	3.4	4.4
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Cloudy	IS(Mf)9	18:56:16	1.0	Surface	1	1	17.99	7.96	30.92	90.80	5.9	3.4	2.6
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Cloudy	IS(Mf)9	18:56:54	1.0	Surface	1	2	18.06	7.97	30.88	91.00	5.9	3.4	2.5
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Cloudy	IS(Mf)9	18:56:06	2.6	Bottom	3	1	17.88	7.95	31.16	91.00	5.9	3.4	3.6
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Cloudy	IS(Mf)9	18:56:24	2.6	Bottom	3	2	17.89	7.96	31.15	90.90	5.9	3.5	3.9
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Fine	IS10(N)	19:45:28	1.0	Surface	1	1	18.00	8.09	31.94	89.20	6.1	2.3	2.6
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Fine	IS10(N)	19:46:12	1.0	Surface	1	2	18.02	8.09	31.92	89.70	6.2	2.2	3.6
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Fine	IS10(N)	19:45:15	5.3	Middle	2	1	17.85	8.07	32.78	88.30	6.1	2.6	3.0
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Fine	IS10(N)	19:45:58	5.3	Middle	2	2	17.85	8.07	32.78	88.00	6.0	2.6	3.1
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Fine	IS10(N)	19:45:03	9.6	Bottom	3	1	17.85	8.07	32.89	88.00	6.0	2.8	2.4
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Fine	IS10(N)	19:45:45	9.6	Bottom	3	2	17.86	8.07	32.86	87.70	6.0	2.8	2.7
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Cloudy	SR3(N)	18:11:28	1.0	Surface	1	1	17.94	7.96	30.78	88.80	5.8	3.4	3.3
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Cloudy	SR3(N)	18:11:51	1.0	Surface	1	2	17.94	7.96	30.78	88.80	5.8	3.4	4.1
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Cloudy	SR3(N)	18:11:12	2.0	Bottom	3	1	17.87	7.95	30.95	88.40	5.7	3.4	3.4
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Cloudy	SR3(N)	18:11:35	2.0	Bottom	3	2	17.91	7.96	31.04	89.40	5.8	3.4	2.2
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Cloudy	SR4(N3)	19:07:04	1.0	Surface	1	1	17.99	7.94	30.84	91.10	5.9	3.5	3.3
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Cloudy	SR4(N3)	19:07:35	1.0	Surface	1	2	17.98	7.94	30.84	90.90	5.9	3.5	2.2
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Cloudy	SR4(N3)	19:06:43	2.8	Bottom	3	1	17.96	7.94	30.99	91.00	5.9	3.5	3.0
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Cloudy	SR4(N3)	19:07:14	2.8	Bottom	3	2	17.93	7.94	31.03	91.10	5.9	3.4	2.0
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Fine	SR5(N)	19:35:52	1.0	Surface	1	1	18.02	8.08	31.91	90.20	6.2	2.0	2.1
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Fine	SR5(N)	19:35:12	1.0	Surface	1	2	17.99	8.09	31.93	89.90	6.2	2.0	2.5
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Fine	SR5(N)	19:35:38	4.8	Middle	2	1	17.87	8.07	32.69	88.70	6.1	2.3	1.8
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Fine	SR5(N)	19:34:58	4.8	Middle	2	2	17.86	8.08	32.69	89.00	6.1	2.4	1.6
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Fine	SR5(N)	19:35:26	8.6	Bottom	3	1	17.86	8.07	32.90	88.50	6.1	2.8	2.6
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Fine	SR5(N)	19:34:46	8.6	Bottom	3	2	17.85	8.08	32.91	88.70	6.1	2.8	2.5
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Fine	SR10A(N)	20:39:15	1.0	Surface	1	1	18.05	8.09	32.70	90.40	6.2	2.2	2.7
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Fine	SR10A(N)	20:40:01	1.0	Surface	1	2	18.04	8.08	32.72	90.50	6.2	2.2	1.8
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Fine	SR10A(N)	20:38:58	6.5	Middle	2	1	17.86	8.08	33.53	88.30	6.0	2.5	2.4
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Fine	SR10A(N)	20:39:42	6.5	Middle	2	2	17.88	8.07	33.47	87.20	5.9	2.5	3.2
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Fine	SR10A(N)	20:38:45	12.0	Bottom	3	1	17.87	8.09	33.57	87.70	6.0	2.6	2.0
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Fine	SR10A(N)	20:39:31	12.0	Bottom	3	2	17.90	8.08	33.51	87.20	5.9	2.6	2.5
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Fine	SR10B(N2)	20:50:13	1.0	Surface	1	1	18.05	8.09	32.76	88.40	6.0	2.0	2.5
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Fine	SR10B(N2)	20:50:51	1.0	Surface	1	2	18.05	8.09	32.78	88.60	6.0	2.1	3.2
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Fine	SR10B(N2)	20:50:01	3.7	Middle	2	1	17.94	8.08	33.19	87.30	5.9	2.2	2.2
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Fine	SR10B(N2)	20:50:39	3.7	Middle	2	2	17.94	8.08	33.15	87.30	5.9	2.3	2.1
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Fine	SR10B(N2)	20:49:50	6.4	Bottom	3	1	17.93	8.08	33.40	87.60	6.0	2.5	1.8
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Fine	SR10B(N2)	20:50:26	6.4	Bottom	3	2	17.94	8.08	33.36	87.50	6.0	2.5	2.0
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Fine	CS2(A)	18:39:00	1.0	Surface	1	1	17.91	8.10	31.94	93.00	6.4	2.3	2.8
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Fine	CS2(A)	18:39:33	1.0	Surface	1	2	17.93	8.09	31.90	92.60	6.4	2.2	1.9
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Fine	CS2(A)	18:39:22	3.4	Middle	2	1	17.82	8.08	32.58	90.30	6.2	2.7	3.4
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Fine	CS2(A)	18:38:51	3.4	Middle	2	2	17.81	8.09	32.58	90.90	6.3	2.7	1.8
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Fine	CS2(A)	18:38:40	5.7	Bottom	3	1	17.81	8.10	32.81	90.40	6.2	2.9	2.6
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Fine	CS2(A)	18:39:12	5.7	Bottom	3	2	17.83	8.08	32.74	90.20	6.2	3.0	2.0
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Cloudy	CS(Mf)5	19:59:55	1.0	Surface	1	1	17.95	7.95	30.80	88.30	5.7	3.5	4.6
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Cloudy	CS(Mf)5	20:00:37	1.0	Surface	1	2	18.02	7.94	30.93	88.50	5.7	3.5	5.4
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Cloudy	CS(Mf)5	19:59:38	5.8	Middle	2	1	17.75	7.94	31.40	88.20	5.7	3.4	4.8
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Cloudy	CS(Mf)5	20:00:23	5.8	Middle	2	2	17.77	7.94	31.41	87.90	5.7	3.4	3.8
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Cloudy	CS(Mf)5	19:59:19	10.6	Bottom	3	1	17.73	7.94	31.34	87.90	5.7	3.4	3.7
HKLR	HY/2011/03	2025-03-07	Mid-Ebb	Cloudy	CS(Mf)5	20:00:05	10.6	Bottom	3	2	17.74	7.94	31.39	87.50	5.7	3.5	3.2
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Cloudy	IS5	06:38:59	1.0	Surface	1	1	17.87	7.96	30.65	92.50	6.0	3.4	4.2
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Cloudy	IS5	06:39:44	1.0	Surface	1	2	17.99	7.97	30.79	92.90	6.0	3.3	4.6
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Cloudy	IS5	06:38:39	4.2	Middle	2	1	18.01	7.96	31.24	91.50	6.0	3.4	3.3
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Cloudy	IS5	06:39:23	4.2	Middle	2	2	17.99	7.96	31.25	92.80	6.0	3.4	2.4
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Cloudy	IS5	06:38:21	7.4	Bottom	3	1	17.73	7.96	31.29	91.00	5.9	3.4	4.0
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Cloudy	IS5	06:39:11	7.4	Bottom	3	2	17.91	7.96	31.29	92.70	6.0	3.4	3.0
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Cloudy	IS(Mf)6	06:29:08	1.0	Surface	1	1	17.98	8.00	30.65	90.30	5.9	3.5	5.0
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Cloudy	IS(Mf)6	06:29:31	1.0	Surface	1	2	18.00	8.00	30.64	90.30	5.9	3.6	4.1
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Cloudy	IS(Mf)6	06:28:55	2.2	Bottom	3	1	17.89	7.99	30.97	89.90	5.9	3.6	4.8
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Cloudy	IS(Mf)6	06:29:21	2.2	Bottom	3	2	17.93	8.00	30.92	90.20	5.9	3.5	4.4
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Cloudy	IS7	06:19:58	1.0	Surface	1	1	18.06	7.97	30.79	90.90	5.9	3.4	2.6
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Cloudy	IS7	06:20:25	1.0	Surface	1	2	18.05	7.97	30.71	90.70	5.9	3.4	2.2
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Cloudy	IS7	06:19:34	2.0	Bottom	3	1	17.99	7.96	31.04	90.80	5.9	3.4	2.8
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Cloudy	IS7	06:20:08	2.0	Bottom	3	2	17.99	7.96	31.00	90.50	5.9	3.4	2.8
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Cloudy	IS8(N)	05:48:02	1.0	Surface	1	1	17.75	7.98	30.63	89.80	5.8	3.4	3.5
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Cloudy	IS8(N)	05:48:28	1.0	Surface	1	2	17.76	7.98	30.64	89.70	5.8	3.5	2.6
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Cloudy	IS8(N)	05:47:46	2.8	Bottom	3	1	17.77	7.97	30.83	89.70	5.8	3.4	3.2
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Cloudy	IS8(N)	05:48:12	2.8	Bottom	3	2	17.95	7.97	30.89	89.50	5.8	3.4	3.2
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Cloudy	IS(Mf)9	06:10:02	1.0	Surface	1	1	18.07	7.95	30.68	89.70	5.8	3.6	2.2
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Cloudy	IS(Mf)9	06:10:25	1.0	Surface	1	2	18.09	7.95	30.66	89.70	5.8	3.5	3.2
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Cloudy	IS(Mf)9	06:09:38	2.6	Bottom	3	1	17.96	7.94	31.00	88.90	5.8	3.6	2.4
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Cloudy	IS(Mf)9	06:10:12	2.6	Bottom	3	2	17.96	7.94	31.01	89.90	5.9	3.5	2.6
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Fine	IS10(N)	06:16:31	1.0	Surface	1	1	17.89	8.09	32.15	90.60	6.2	2.3	1.5
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Fine	IS10(N)	06:15:50	1.0	Surface	1	2	17.86	8.09	32.19	90.90	6.3	2.3	2.2
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Fine	IS10(N)	06:15:33	5.4	Middle	2	1	17.75	8.07	32.89	88.90	6.1	2.7	2.5
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Fine	IS10(N)	06:16:14	5.4	Middle	2	2	17.76	8.07	32.91	88.60	6.1	2.6	1.8
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Fine	IS10(N)	06:16:05	9.7	Bottom	3	1	17.77	8.07	32.95	88.50	6.1	3.1	1.6
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Fine	IS10(N)	06:15:24	9.7	Bottom	3	2	17.76	8.08	32.97	88.70	6.1	3.0	2.3
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Cloudy	SR3(N)	06:49:41	1.0	Surface	1	1	17.72	7.96	30.75	90.70	5.9	3.4	2.8
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Cloudy	SR3(N)	06:50:13	1.0	Surface	1	2	17.75	7.96	30.71	91.00	5.9	3.5	3.5
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Cloudy	SR3(N)	06:49:10	2.0	Bottom	3	1	17.74	7.96	31.03	90.60	5.9	3.5	3.7
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Cloudy	SR3(N)	06:49:54	2.0	Bottom	3	2	17.94	7.97	30.86	90.30	5.9	3.4	3.0
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Cloudy	SR4(N3)	05:59:02	1.0	Surface	1	1	17.89	7.99	30.73	89.90	5.8	3.4	3.2
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Cloudy	SR4(N3)	05:59:29	1.0	Surface	1	2	17.94	7.99	30.70	89.70	5.8	3.5	2.6
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Cloudy	SR4(N3)	05:58:47	2.6	Bottom	3	1	17.82	7.98	31.01	89.90	5.8	3.4	3.0
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Cloudy	SR4(N3)	05:59:12	2.6	Bottom	3	2	17.86	7.98	30.96	89.60	5.8	3.4	2.5
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Fine	SR5(N)	06:26:51	1	Surface	1	1	17.88	8.09	32.17	89.30	6.1	2.4	3.4
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Fine	SR5(N)	06:26:05	1	Surface	1	2	17.89	8.09	32.20	89.30	6.1	2.3	2.2
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Fine	SR5(N)	06:26:36	4.9	Middle	2	1	17.77	8.08	32.80	88.10	6.1	2.7	3.0
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Fine	SR5(N)	06:25:50	4.9	Middle	2	2	17.78	8.07	32.83	87.80	6.0	2.7	2.4
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Fine	SR5(N)	06:25:38	8.7	Bottom	3	1	17.76	8.07	32.98	87.80	6.0	2.8	2.5
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Fine	SR5(N)	06:26:24	8.7	Bottom	3	2	17.77	8.07	32.95	88.10	6.1	3.0	2.0
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Fine	SR10A(N)	05:23:05	1	Surface	1	1	18.04	8.07	32.44	88.70	6.1	2.2	2.8
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Fine	SR10A(N)	05:23:51	1	Surface	1	2	18.04	8.07	32.44	88.80	6.1	2.1	2.2
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Fine	SR10A(N)	05:22:47	6.6	Middle	2	1	17.87	8.06	33.21	87.30	6.0	2.5	2.8

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Fine	SR10A(N)	05:23:33	6.6	Middle	2	2	17.87	8.06	33.21	86.70	5.9	2.5	2.5
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Fine	SR10A(N)	05:22:37	12.1	Bottom	3	1	17.88	8.06	33.33	87.00	5.9	2.8	2.6
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Fine	SR10A(N)	05:23:21	12.1	Bottom	3	2	17.89	8.05	33.34	86.90	5.9	2.8	3.5
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Fine	SR10B(N2)	05:12:53	1.0	Surface	1	1	18.05	8.07	32.42	92.50	6.3	2.1	2.1
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Fine	SR10B(N2)	05:12:12	1.0	Surface	1	2	18.05	8.06	32.40	92.50	6.3	2.1	1.9
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Fine	SR10B(N2)	05:11:56	3.8	Middle	2	1	17.92	8.05	32.97	89.50	6.1	2.5	2.4
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Fine	SR10B(N2)	05:12:39	3.8	Middle	2	2	17.93	8.06	32.95	88.80	6.1	2.4	2.6
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Fine	SR10B(N2)	05:12:26	6.5	Bottom	3	1	17.92	8.05	33.20	88.60	6.1	2.7	2.1
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Fine	SR10B(N2)	05:11:43	6.5	Bottom	3	2	17.85	8.05	33.25	88.50	6.1	2.8	2.7
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Fine	CS2(A)	07:18:41	1	Surface	1	1	17.85	8.10	32.13	90.00	6.2	2.5	5.9
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Fine	CS2(A)	07:18:01	1	Surface	1	2	17.85	8.11	32.14	90.30	6.2	2.4	4.6
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Fine	CS2(A)	07:18:27	3.3	Middle	2	1	17.77	8.10	32.60	89.10	6.1	2.9	2.3
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Fine	CS2(A)	07:17:48	3.3	Middle	2	2	17.77	8.10	32.61	89.20	6.1	3.1	3.6
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Fine	CS2(A)	07:18:16	5.6	Bottom	3	1	17.77	8.09	32.82	88.80	6.1	3.3	2.0
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Fine	CS2(A)	07:17:36	5.6	Bottom	3	2	17.75	8.10	32.81	89.20	6.1	3.3	1.8
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Cloudy	CS(Mf)5	05:04:03	1.0	Surface	1	1	17.94	7.98	30.60	91.10	5.9	3.4	2.3
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Cloudy	CS(Mf)5	05:04:55	1.0	Surface	1	2	17.90	8.01	30.65	92.70	6.0	3.4	3.5
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Cloudy	CS(Mf)5	05:03:47	6.0	Middle	2	1	17.66	7.96	31.30	90.90	5.9	3.5	3.5
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Cloudy	CS(Mf)5	05:04:32	6.0	Middle	2	2	17.67	7.99	31.26	92.20	5.9	3.5	2.6
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Cloudy	CS(Mf)5	05:03:23	11.0	Bottom	3	1	17.65	7.96	31.32	90.10	5.8	3.5	4.2
HKLR	HY/2011/03	2025-03-07	Mid-Flood	Cloudy	CS(Mf)5	05:04:20	11.0	Bottom	3	2	17.67	7.98	31.27	90.90	5.9	3.6	3.2
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	IS5	11:55:10	1.0	Surface	1	1	18.45	8.08	32.83	90.50	6.2	2.2	3.3
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	IS5	11:54:20	1.0	Surface	1	2	18.47	8.09	32.83	91.90	6.3	2.2	3.2
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	IS5	11:54:57	4.2	Middle	2	1	18.18	8.08	33.47	88.30	6.0	2.4	3.5
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	IS5	11:54:06	4.2	Middle	2	2	18.19	8.06	33.47	88.40	6.0	2.4	3.8
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	IS5	11:54:36	7.4	Bottom	3	1	18.14	8.07	33.61	87.30	6.0	2.5	2.5
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	IS5	11:53:55	7.4	Bottom	3	2	18.17	8.06	33.61	87.60	6.0	2.6	2.5
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	IS(Mf)6	11:44:51	1.0	Surface	1	1	18.51	8.08	32.78	93.50	6.4	2.1	4.4
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	IS(Mf)6	11:44:35	1.0	Surface	1	2	18.49	8.09	32.79	93.40	6.4	2.1	2.1
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	IS(Mf)6	11:44:22	2.2	Bottom	3	1	18.44	8.09	32.95	93.10	6.3	2.3	2.0
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	IS(Mf)6	11:44:42	2.2	Bottom	3	2	18.47	8.09	32.91	93.10	6.4	2.3	3.5
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	IS7	11:35:41	1.0	Surface	1	1	18.49	8.10	32.80	92.90	6.3	2.1	3.6
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	IS7	11:35:56	1.0	Surface	1	2	18.52	8.10	32.76	93.30	6.4	2.1	2.1
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	IS7	11:35:49	2.3	Bottom	3	1	18.48	8.09	32.89	92.80	6.3	2.3	2.6
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	IS7	11:35:33	2.3	Bottom	3	2	18.45	8.09	32.91	92.70	6.3	2.3	2.4
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	IS8(N)	11:04:24	1.0	Surface	1	1	18.47	8.09	32.72	93.50	6.4	2.3	3.3
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	IS8(N)	11:03:51	1.0	Surface	1	2	18.49	8.09	32.70	92.90	6.4	2.3	2.6
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	IS8(N)	11:03:59	3.0	Bottom	3	1	18.42	8.07	33.02	92.50	6.3	2.5	2.9
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	IS8(N)	11:03:40	3.0	Bottom	3	2	18.38	8.09	33.06	91.70	6.3	2.5	2.0
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	IS(Mf)9	11:26:17	1.0	Surface	1	1	18.52	8.09	32.72	93.10	6.4	2.2	3.4
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	IS(Mf)9	11:26:01	1.0	Surface	1	2	18.51	8.09	32.75	92.60	6.3	2.2	3.0
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	IS(Mf)9	11:26:08	2.5	Bottom	3	1	18.48	8.09	32.91	92.20	6.3	2.5	2.2
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	IS(Mf)9	11:25:51	2.5	Bottom	3	2	18.42	8.09	32.93	91.70	6.3	2.4	3.6
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	IS10(N)	11:15:22	1.0	Surface	1	1	18.40	8.09	32.63	90.60	6.2	2.1	2.9
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	IS10(N)	11:14:42	1.0	Surface	1	2	18.34	8.09	32.67	90.50	6.2	2.1	2.4
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	IS10(N)	11:15:06	5.4	Middle	2	1	18.16	8.08	33.31	88.60	6.1	2.1	3.2
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	IS10(N)	11:14:27	5.4	Middle	2	2	18.15	8.08	33.30	88.90	6.1	2.3	4.9
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	IS10(N)	11:14:57	9.8	Bottom	3	1	18.19	8.08	33.34	88.90	6.1	2.2	2.2
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	IS10(N)	11:14:16	9.8	Bottom	3	2	18.16	8.08	33.38	89.00	6.1	2.3	3.8
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	SR3(N)	12:08:54	1.0	Surface	1	1	18.50	8.09	32.80	92.30	6.3	2.2	2.6
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	SR3(N)	12:08:38	1.0	Surface	1	2	18.49	8.08	32.82	91.60	6.3	2.3	2.6
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	SR3(N)	12:08:45	2.3	Bottom	3	1	18.47	8.08	32.92	91.40	6.2	2.4	4.1
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	SR3(N)	12:08:29	2.3	Bottom	3	2	18.42	8.08	32.96	90.50	6.2	2.4	3.0
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	SR4(N3)	11:11:38	1.0	Surface	1	1	18.46	8.09	32.72	92.10	6.3	2.2	3.0
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	SR4(N3)	11:11:57	1.0	Surface	1	2	18.49	8.09	32.72	92.00	6.3	2.2	2.7
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	SR4(N3)	11:11:47	2.9	Bottom	3	1	18.41	8.07	33.02	91.50	6.3	2.4	3.1
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	SR4(N3)	11:11:28	2.9	Bottom	3	2	18.38	8.07	33.06	91.90	6.3	2.4	2.1
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	SR5(N)	11:26:36	1.0	Surface	1	1	18.36	8.09	32.66	89.70	6.1	2.2	2.8
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	SR5(N)	11:25:51	1.0	Surface	1	2	18.37	8.09	32.67	89.60	6.1	2.2	2.5
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	SR5(N)	11:26:20	4.8	Middle	2	1	18.20	8.08	33.18	88.40	6.1	2.3	1.6
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	SR5(N)	11:25:37	4.8	Middle	2	2	18.20	8.08	33.21	88.30	6.0	2.4	3.2
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	SR5(N)	11:25:25	8.6	Bottom	3	1	18.17	8.08	33.36	88.50	6.1	2.5	2.0
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	SR5(N)	11:26:09	8.6	Bottom	3	2	18.18	8.08	33.34	88.60	6.1	2.6	1.6
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	SR10A(N)	10:21:48	1.0	Surface	1	1	18.49	8.09	32.85	89.60	6.1	1.8	3.5
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	SR10A(N)	10:21:02	1.0	Surface	1	2	18.50	8.09	32.85	89.00	6.1	1.9	2.8
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	SR10A(N)	10:20:45	6.6	Middle	2	1	18.21	8.08	33.57	87.40	6.0	2.0	3.4
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	SR10A(N)	10:21:29	6.6	Middle	2	2	18.21	8.09	33.57	87.00	5.9	2.1	2.8
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	SR10A(N)	10:20:36	12.2	Bottom	3	1	18.22	8.09	33.66	87.50	6.0	2.3	3.0
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	SR10A(N)	10:21:18	12.2	Bottom	3	2	18.25	8.08	33.68	87.50	6.0	2.3	3.0
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	SR10B(N2)	10:09:33	1.0	Surface	1	1	18.52	8.10	32.83	93.20	6.3	1.9	3.2
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	SR10B(N2)	10:08:50	1.0	Surface	1	2	18.53	8.09	32.80	93.20	6.4	1.9	3.7
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	SR10B(N2)	10:08:32	3.8	Middle	2	1	18.29	8.08	33.30	90.20	6.2	2.1	2.8
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	SR10B(N2)	10:09:19	3.8	Middle	2	2	18.32	8.09	33.26	89.70	6.1	2.0	6.2
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	SR10B(N2)	10:09:05	6.6	Bottom	3	1	18.28	8.08	33.53	88.80	6.1	2.2	2.2
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	SR10B(N2)	10:08:20	6.6	Bottom	3	2	18.21	8.07	33.62	88.80	6.1	2.3	2.9
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	CS2(A)	12:21:41	1.0	Surface	1	1	18.34	8.10	32.68	90.40	6.2	2.2	2.7
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	CS2(A)	12:21:01	1.0	Surface	1	2	18.34	8.11	32.68	90.50	6.2	2.2	4.4
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	CS2(A)	12:21:28	3.3	Middle	2	1	18.22	8.10	33.07	89.30	6.1	2.3	2.6
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	CS2(A)	12:20:48	3.3	Middle	2	2	18.22	8.10	33.07	89.30	6.1	2.2	2.5
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	CS2(A)	12:20:36	5.6	Bottom	3	1	18.16	8.10	33.29	89.30	6.1	2.4	1.9
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	CS2(A)	12:21:16	5.6	Bottom	3	2	18.18	8.09	33.29	89.10	6.1	2.4	2.5
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	CS(Mf)5	10:27:00	1.0	Surface	1	1	18.50	8.10	32.80	92.20	6.3	1.9	3.3
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	CS(Mf)5	10:26:13	1.0	Surface	1	2	18.48	8.08	32.84	91.70	6.3	2.0	3.3
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	CS(Mf)5	10:26:42	6.3	Middle	2	1	18.18	8.08	33.65	89.10	6.1	2.1	3.2
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	CS(Mf)5	10:25:58	6.3	Middle	2	2	18.18	8.07	33.65	89.60	6.1	2.1	2.3
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	CS(Mf)5	10:25:46	11.6	Bottom	3	1	18.19	8.07	33.75	88.20	6.0	2.3	2.4
HKLR	HY/2011/03	2025-03-10	Mid-Ebb	Fine	CS(Mf)5	10:26:30	11.6	Bottom	3	2	18.18	8.07	33.78	87.70	6.0	2.4	2.4
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	IS5	15:28:08	1.0	Surface	1	1	18.55	8.08	32.80	93.70	6.5	2.2	2.3
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	IS5	15:28:47	1.0	Surface	1	2	18.59	8.09	32.80	94.20	6.5	2.2	1.8
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	IS5	15:27:57	4.3	Middle	2	1	18.38	8.07	33.36	92.50	6.4	2.4	3.4
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	IS5	15:28:33	4.3	Middle	2	2	18.40	8.07	33.34	92.60	6.4	2.4	2.8
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	IS5	15:28:23	7.6	Bottom	3	1	18.39	8.07	33.42	92.50	6.4	2.5	3.7
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	IS5	15:27:47	7.6	Bottom	3	2	18.37	8.07	33.45	92.30	6.4	2.5	3.4
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	IS(Mf)6	15:37:16	1.0	Surface	1	1	18.60	8.09	32.81	96.60	6.7	2.1	3.1
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	IS(Mf)6	15:36:58	1.0	Surface	1	2	18.58	8.09	32.80	95.70	6.6	2.1	4.4
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	IS(Mf)6	15:37:08	2.2	Bottom	3	1	18.57	8.09	32.90	95.00	6.6	2.4	3.7
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	IS(Mf)6	15:36:50	2.2	Bottom	3	2	18.52	8.09	32.92	94.10	6.5	2.4	3.1
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	IS7	15:45:56	1.0	Surface	1	1	18.61	8.09	32.80	96.10	6.7	2.1	2.9
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	IS7	15:45:40	1.0	Surface	1	2	18.58	8.09	32.81	95.80	6.6	2.2	2.4
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	IS7	15:45:31	2.3	Bottom	3	1	18.55	8.09	32.93	95.30	6.6	2.3	2.3
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	IS7	15:45:46	2.3	Bottom	3	2	18.57	8.09	32.90	95.50	6.6	2.2	2.4
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	IS8(N)	16:20:30	1.0	Surface	1	1	18.56	8.09	32.78	93.80	6.5	2.3	3.2
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	IS8(N)	16:20:49	1.0	Surface	1	2	18.58	8.10	32.76	94.40	6.6	2.3	2.7
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	IS8(N)	16:20:39	3.0	Bottom	3	1	18.55	8.09	32.89	93.80	6.5	2.4	2.9
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	IS8(N)	16:20:22	3.0	Bottom	3	2	18.49	8.08	32.98	93.20	6.5	2.5	3.2
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	IS(Mf)9	15:57:29	1.0	Surface	1	1	18.60	8.09	32.80	95.70	6.6	2.1	2.4
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	IS(Mf)9	15:57:08	1.0	Surface	1	2	18.59	8.08	32.80	95.20	6.6	2.2	2.7
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	IS(Mf)9	15:57:18	2.6	Bottom	3	1	18.57	8.08	32.93	95.20	6.6	2.3	5.2
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	IS(Mf)9	15:57:00	2.6	Bottom	3	2	18.54	8.08	32.93	95.00	6.6	2.2	4.0
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	IS10(N)	16:22:35	1.0	Surface	1	1	18.46	8.09	32.37	89.60	6.1	2.1	3.0
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	IS10(N)	16:23:15	1.0	Surface	1	2	18.50	8.09	32.35	90.30	6.2	2.1	4.0
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	IS10(N)	16:22:21	5.3	Middle	2	1	18.25	8.08	33.21	88.70	6.1	2.3	3.1
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	IS10(N)	16:23:01	5.3	Middle	2	2	18.26	8.08	33.20	88.70	6.1	2.3	2.6
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	IS10(N)	16:22:50	9.6	Bottom	3	1	18.29	8.08	33.25	88.50	6.1	2.4	2.2
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	IS10(N)	16:22:10	9.6	Bottom	3	2	18.24	8.07	33.31	88.50	6.0	2.4	6.2
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	SR3(N)	15:13:39	1.0	Surface	1	1	18.60	8.09	32.77	96.10	6.7	2.3	2.7
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	SR3(N)	15:13:56	1.0	Surface	1	2	18.61	8.09	32.77	97.00	6.7	2.3	12.0
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	SR3(N)	15:13:45	2.3	Bottom	3	1	18.59	8.09	32.82	95.50	6.6	2.4	3.4
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	SR3(N)	15:13:28	2.3	Bottom	3	2	18.56	8.09	32.86	94.60	6.5	2.4	2.8
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	SR4(N3)	16:11:35	1.0	Surface	1	1	18.57	8.10	32.78	94.20	6.5	2.3	3.1
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	SR4(N3)	16:11:19	1.0	Surface	1	2	18.57	8.09	32.78	93.90	6.5	2.3	3.0
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	SR4(N3)	16:11:28	2.9	Bottom	3	1	18.56	8.09	32.91	93.60	6.5	2.4	3.8
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	SR4(N3)	16:11:10	2.9	Bottom	3	2	18.43	8.08	32.93	93.00	6.5	2.4	2.6
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	SR5(N)	16:14:14	1	Surface	1	1	18.49	8.09	32.36	90.80	6.2	2.0	2.4
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	SR5(N)	16:13:36	1	Surface	1	2	18.45	8.09	32.38	90.40	6.2	2.0	3.5

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	SR5(N)	16:14:01	4.8	Middle	2	1	18.29	8.08	33.08	89.20	6.1	2.1	2.6
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	SR5(N)	16:13:22	4.8	Middle	2	2	18.28	8.08	33.07	89.40	6.1	2.2	4.1
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	SR5(N)	16:13:50	8.5	Bottom	3	1	18.28	8.08	33.28	89.40	6.1	2.4	1.8
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	SR5(N)	16:13:11	8.5	Bottom	3	2	18.26	8.09	33.29	89.40	6.1	2.4	3.0
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	SR10A(N)	17:16:03	1	Surface	1	1	18.45	8.09	33.18	90.60	6.2	2.0	2.6
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	SR10A(N)	17:15:17	1	Surface	1	2	18.45	8.10	33.14	90.20	6.2	2.0	3.6
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	SR10A(N)	17:15:00	6.7	Middle	2	1	18.23	8.09	33.87	88.20	6.0	2.2	3.4
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	SR10A(N)	17:15:44	6.7	Middle	2	2	18.23	8.08	33.85	87.50	6.0	2.2	3.8
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	SR10A(N)	17:14:47	12.3	Bottom	3	1	18.24	8.10	33.92	88.10	6.0	2.2	1.9
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	SR10A(N)	17:15:33	12.3	Bottom	3	2	18.24	8.09	33.88	87.70	6.0	2.2	2.8
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	SR10B(N2)	17:26:39	1.0	Surface	1	1	18.47	8.09	33.21	89.00	6.1	1.9	4.2
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	SR10B(N2)	17:26:04	1.0	Surface	1	2	18.45	8.09	33.20	88.90	6.1	1.9	2.5
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	SR10B(N2)	17:25:51	3.8	Middle	2	1	18.31	8.09	33.58	88.00	6.0	2.0	2.3
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	SR10B(N2)	17:26:28	3.8	Middle	2	2	18.31	8.09	33.52	87.80	6.0	2.0	2.9
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	SR10B(N2)	17:25:41	6.5	Bottom	3	1	18.31	8.09	33.73	88.40	6.0	2.2	2.6
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	SR10B(N2)	17:26:16	6.5	Bottom	3	2	18.30	8.08	33.72	88.10	6.0	2.2	2.8
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	CS2(A)	15:20:46	1	Surface	1	1	18.41	8.10	32.48	92.70	6.4	2.1	3.0
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	CS2(A)	15:21:17	1	Surface	1	2	18.42	8.09	32.46	92.40	6.3	2.0	4.4
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	CS2(A)	15:21:07	3.3	Middle	2	1	18.27	8.09	33.08	90.60	6.2	2.3	3.2
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	CS2(A)	15:20:36	3.3	Middle	2	2	18.25	8.10	33.08	90.80	6.2	2.3	3.0
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	CS2(A)	15:20:26	5.6	Bottom	3	1	18.23	8.10	33.34	90.70	6.2	2.4	3.4
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	CS2(A)	15:20:58	5.6	Bottom	3	2	18.29	8.09	33.25	90.70	6.2	2.4	3.0
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	CS(Mf)5	17:01:21	1.0	Surface	1	1	18.58	8.10	32.91	90.60	6.3	2.1	2.8
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	CS(Mf)5	17:02:02	1.0	Surface	1	2	18.57	8.10	32.92	91.10	6.3	2.0	2.4
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	CS(Mf)5	17:01:48	6.4	Middle	2	1	18.19	8.06	33.79	88.20	6.1	2.2	2.3
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	CS(Mf)5	17:01:07	6.4	Middle	2	2	18.18	8.07	33.79	88.30	6.1	2.2	2.8
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	CS(Mf)5	17:01:38	11.7	Bottom	3	1	18.19	8.07	33.38	87.10	6.0	2.4	3.6
HKLR	HY/2011/03	2025-03-10	Mid-Flood	Fine	CS(Mf)5	17:00:55	11.7	Bottom	3	2	18.15	8.07	33.91	87.10	6.0	2.3	3.3
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	IS5	11:31:43	1.0	Surface	1	1	18.46	8.11	33.06	92.80	6.9	2.5	3.2
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	IS5	11:31:08	1.0	Surface	1	2	18.44	8.11	33.06	92.30	6.8	2.5	2.8
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	IS5	11:30:57	4.2	Middle	2	1	18.36	8.10	33.34	91.90	6.8	2.6	4.0
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	IS5	11:31:31	4.2	Middle	2	2	18.37	8.10	33.34	92.10	6.8	2.6	3.5
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	IS5	11:30:48	7.4	Bottom	3	1	18.35	8.09	33.39	91.80	6.8	2.5	4.7
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	IS5	11:31:22	7.4	Bottom	3	2	18.36	8.10	33.38	92.00	6.8	2.7	3.1
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	IS(Mf)6	11:41:02	1.0	Surface	1	1	18.54	8.11	33.04	95.10	7.0	2.8	3.0
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	IS(Mf)6	11:40:42	1.0	Surface	1	2	18.54	8.11	33.01	94.50	7.0	2.7	2.3
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	IS(Mf)6	11:40:53	2.2	Bottom	3	1	18.53	8.11	33.07	94.20	6.9	3.3	2.7
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	IS(Mf)6	11:40:32	2.2	Bottom	3	2	18.50	8.11	33.08	93.40	6.9	3.3	3.2
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	IS7	11:51:49	1.0	Surface	1	1	18.56	8.10	33.03	95.40	7.0	2.0	3.4
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	IS7	11:51:34	1.0	Surface	1	2	18.54	8.10	33.04	95.20	7.0	2.1	4.4
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	IS7	11:51:41	2.4	Bottom	3	1	18.54	8.10	33.09	95.00	7.0	2.2	3.3
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	IS7	11:51:23	2.4	Bottom	3	2	18.51	8.10	33.10	94.80	7.0	2.3	3.8
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	IS8(N)	12:22:14	1.0	Surface	1	1	18.56	8.08	32.98	92.50	6.8	2.4	3.3
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	IS8(N)	12:22:35	1.0	Surface	1	2	18.59	8.09	32.96	92.80	6.8	2.3	3.4
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	IS8(N)	12:22:24	2.9	Bottom	3	1	18.55	8.07	33.03	92.30	6.8	2.6	3.0
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	IS8(N)	12:22:05	2.9	Bottom	3	2	18.52	8.07	33.08	92.20	6.8	2.7	4.6
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	IS(Mf)9	12:01:06	1.0	Surface	1	1	18.54	8.09	33.03	95.00	7.0	2.5	4.3
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	IS(Mf)9	12:00:49	1.0	Surface	1	2	18.54	8.09	33.03	94.80	7.0	2.6	2.8
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	IS(Mf)9	12:00:56	2.4	Bottom	3	1	18.53	8.09	33.10	94.80	7.0	2.6	5.1
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	IS(Mf)9	12:00:41	2.4	Bottom	3	2	18.51	8.08	33.10	94.70	7.0	2.6	4.0
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	IS10(N)	12:31:35	1.0	Surface	1	1	18.34	8.09	32.13	87.40	6.4	2.2	2.3
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	IS10(N)	12:30:53	1.0	Surface	1	2	18.36	8.09	32.12	87.20	6.4	2.3	2.4
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	IS10(N)	12:30:38	5.4	Middle	2	1	18.13	8.08	32.62	86.50	6.3	2.3	1.8
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	IS10(N)	12:31:20	5.4	Middle	2	2	18.13	8.08	32.61	86.40	6.3	2.4	2.4
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	IS10(N)	12:30:26	9.7	Bottom	3	1	18.14	8.08	32.67	86.60	6.3	2.4	4.2
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	IS10(N)	12:31:08	9.7	Bottom	3	2	18.15	8.08	32.65	86.40	6.3	2.6	2.4
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	SR3(N)	11:15:31	1.0	Surface	1	1	18.47	8.09	33.03	92.80	6.8	2.7	2.8
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	SR3(N)	11:15:48	1.0	Surface	1	2	18.47	8.10	33.04	93.60	6.9	2.7	3.3
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	SR3(N)	11:15:24	2.5	Bottom	3	1	18.46	8.09	33.07	92.20	6.8	2.7	3.2
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	SR3(N)	11:15:38	2.5	Bottom	3	2	18.46	8.10	33.07	92.80	6.8	2.6	2.3
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	SR4(N3)	12:14:53	1.0	Surface	1	1	18.56	8.09	32.98	92.20	6.8	1.9	3.8
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	SR4(N3)	12:14:39	1.0	Surface	1	2	18.56	8.08	32.98	91.80	6.8	2.0	2.2
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	SR4(N3)	12:14:48	2.8	Bottom	3	1	18.56	8.08	33.04	91.70	6.8	2.1	4.7
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	SR4(N3)	12:14:32	2.8	Bottom	3	2	18.49	8.07	33.05	91.50	6.7	2.1	3.2
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	SR5(N)	12:16:54	1.0	Surface	1	1	18.29	8.08	32.16	87.50	6.4	2.5	1.7
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	SR5(N)	12:17:38	1.0	Surface	1	2	18.40	8.09	32.10	88.00	6.4	2.4	2.2
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	SR5(N)	12:17:19	4.5	Middle	2	1	18.14	8.08	32.54	86.70	6.4	2.6	3.1
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	SR5(N)	12:16:42	4.5	Middle	2	2	18.14	8.08	32.53	86.90	6.4	2.7	2.3
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	SR5(N)	12:17:06	7.9	Bottom	3	1	18.17	8.08	32.65	86.80	6.4	2.7	3.4
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	SR5(N)	12:16:28	7.9	Bottom	3	2	18.13	8.09	32.68	86.90	6.4	2.8	3.2
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	SR10A(N)	13:20:07	1.0	Surface	1	1	18.44	8.08	33.10	86.10	6.2	2.0	1.8
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	SR10A(N)	13:19:24	1.0	Surface	1	2	18.45	8.09	33.06	86.20	6.3	2.0	2.3
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	SR10A(N)	13:19:04	6.4	Middle	2	1	18.31	8.08	33.48	85.10	6.2	2.2	2.0
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	SR10A(N)	13:19:52	6.4	Middle	2	2	18.31	8.07	33.46	84.50	6.1	2.1	2.5
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	SR10A(N)	13:18:52	11.8	Bottom	3	1	18.32	8.09	33.50	85.20	6.2	2.4	3.0
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	SR10A(N)	13:19:42	11.8	Bottom	3	2	18.32	8.08	33.47	84.60	6.1	2.4	3.8
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	SR10B(N2)	13:31:32	1.0	Surface	1	1	18.44	8.07	33.12	85.10	6.2	2.3	2.1
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	SR10B(N2)	13:30:56	1.0	Surface	1	2	18.43	8.07	33.12	85.00	6.2	2.3	3.9
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	SR10B(N2)	13:30:45	3.8	Middle	2	1	18.35	8.07	33.33	84.50	6.1	2.3	2.6
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	SR10B(N2)	13:31:18	3.8	Middle	2	2	18.36	8.07	33.29	84.40	6.1	2.2	2.4
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	SR10B(N2)	13:30:35	6.5	Bottom	3	1	18.35	8.07	33.43	84.70	6.1	2.3	2.5
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	SR10B(N2)	13:31:09	6.5	Bottom	3	2	18.35	8.07	33.40	84.50	6.1	2.3	3.0
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	CS2(A)	11:23:23	1.0	Surface	1	1	18.33	8.09	32.17	88.60	6.5	2.1	2.5
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	CS2(A)	11:22:48	1.0	Surface	1	2	18.29	8.09	32.22	88.20	6.4	2.0	2.1
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	CS2(A)	11:23:13	3.3	Middle	2	1	18.13	8.08	32.54	87.40	6.4	2.6	3.0
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	CS2(A)	11:22:39	3.3	Middle	2	2	18.12	8.08	32.56	86.70	6.4	2.5	1.8
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	CS2(A)	11:23:04	5.6	Bottom	3	1	18.16	8.08	32.66	87.40	6.4	2.5	3.3
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	CS2(A)	11:22:28	5.6	Bottom	3	2	18.13	8.11	32.72	86.10	6.3	2.3	2.3
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	CS(Mf)5	13:01:14	1.0	Surface	1	1	18.60	8.11	33.26	88.50	6.5	2.1	3.4
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	CS(Mf)5	13:00:37	1.0	Surface	1	2	18.60	8.11	33.27	88.40	6.5	2.2	5.3
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	CS(Mf)5	13:01:00	6.4	Middle	2	1	18.37	8.06	33.88	87.60	6.4	2.5	2.4
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	CS(Mf)5	13:00:26	6.4	Middle	2	2	18.37	8.05	33.88	87.70	6.4	2.5	3.1
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	CS(Mf)5	13:00:52	11.7	Bottom	3	1	18.38	8.08	33.65	87.50	6.4	2.4	2.7
HKLR	HY/2011/03	2025-03-12	Mid-Ebb	Fine	CS(Mf)5	13:00:14	11.7	Bottom	3	2	18.37	8.05	33.92	88.10	6.5	2.4	4.3
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	IS5	07:02:34	1.0	Surface	1	1	18.37	8.12	33.09	89.90	6.6	2.1	2.4
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	IS5	07:01:54	1.0	Surface	1	2	18.40	8.13	33.09	91.00	6.7	2.0	3.1
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	IS5	07:01:41	4.2	Middle	2	1	18.25	8.09	33.42	89.00	6.5	2.2	2.6
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	IS5	07:02:22	4.2	Middle	2	2	18.24	8.10	33.42	89.20	6.6	2.1	4.4
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	IS5	07:02:06	7.4	Bottom	3	1	18.22	8.09	33.49	88.80	6.5	2.2	2.8
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	IS5	07:01:32	7.4	Bottom	3	2	18.24	8.09	33.48	88.10	6.5	2.3	3.4
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	IS(Mf)6	06:51:29	1.0	Surface	1	1	18.40	8.11	33.06	91.00	6.7	2.1	3.8
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	IS(Mf)6	06:51:46	1.0	Surface	1	2	18.41	8.10	33.06	91.80	6.7	2.1	2.7
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	IS(Mf)6	06:51:19	2.3	Bottom	3	1	18.38	8.10	33.14	90.90	6.7	2.2	3.0
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	IS(Mf)6	06:51:37	2.3	Bottom	3	2	18.39	8.10	33.12	90.70	6.6	2.2	1.5
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	IS7	06:42:45	1.0	Surface	1	1	18.42	8.12	33.04	91.60	6.7	1.9	3.0
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	IS7	06:42:30	1.0	Surface	1	2	18.42	8.13	33.07	91.40	6.7	1.9	3.6
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	IS7	06:42:37	2.3	Bottom	3	1	18.41	8.11	33.11	91.30	6.7	2.1	2.8
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	IS7	06:42:23	2.3	Bottom	3	2	18.40	8.11	33.12	91.10	6.7	2.1	2.6
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	IS8(N)	06:09:48	1.0	Surface	1	1	18.42	8.10	33.00	91.20	6.7	2.1	2.9
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	IS8(N)	06:10:10	1.0	Surface	1	2	18.39	8.10	33.02	92.00	6.8	2.2	3.7
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	IS8(N)	06:09:54	3.0	Bottom	3	1	18.38	8.09	33.17	90.90	6.7	2.2	2.4
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	IS8(N)	06:09:37	3.0	Bottom	3	2	18.34	8.11	33.20	90.90	6.7	2.3	4.2
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	IS(Mf)9	06:32:49	1.0	Surface	1	1	18.42	8.11	33.04	91.30	6.7	2.0	2.0
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	IS(Mf)9	06:33:03	1.0	Surface	1	2	18.43	8.11	33.02	91.50	6.7	2.1	3.3
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	IS(Mf)9	06:32:55	2.5	Bottom	3	1	18.40	8.10	33.12	90.90	6.7	2.2	3.4
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	IS(Mf)9	06:32:40	2.5	Bottom	3	2	18.35	8.09	33.14	90.90	6.7	2.2	4.6
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	IS10(N)	06:27:07	1.0	Surface	1	1	18.18	8.09	32.46	87.60	6.4	2.1	2.5
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	IS10(N)	06:27:48	1.0	Surface	1	2	18.21	8.09	32.43	87.40	6.4	2.2	2.4
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	IS10(N)	06:26:53	5.4	Middle	2	1	18.08	8.09	32.79	86.80	6.4	2.6	3.4
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	IS10(N)	06:27:32	5.4	Middle	2	2	18.08	8.09	32.81	86.40	6.3	2.6	3.2
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	IS10(N)	06:27:21	9.7	Bottom	3	1	18.10	8.09	32.80	86.60	6.3	2.7	2.0
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	IS10(N)	06:26:43	9.7	Bottom	3	2	18.08	8.09	32.84	86.90	6.4	2.5	2.9
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	SR3(N)	07:13:42	1.0	Surface	1	1	18.39	8.12	33.07	90.50	6.6	2.0	2.6
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	SR3(N)	07:13:28	1.0	Surface	1	2	18.39	8.11	33.08	89.40	6.6	2.0	2.2
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	SR3(N)	07:13:17	2.6	Bottom	3	1	18.36	8.11	33.15	88.80	6.5	2.5	3.4

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	SR3(N)	07:13:34	2.6	Bottom	3	2	18.38	8.12	33.13	89.50	6.6	2.5	2.5
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	SR4(N3)	06:19:39	1.0	Surface	1	1	18.40	8.11	33.02	91.20	6.7	1.9	4.5
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	SR4(N3)	06:19:59	1.0	Surface	1	2	18.42	8.11	33.02	91.20	6.7	1.8	3.8
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	SR4(N3)	06:19:49	2.8	Bottom	3	1	18.37	8.09	33.18	90.90	6.7	2.0	2.2
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	SR4(N3)	06:19:30	2.8	Bottom	3	2	18.34	8.09	33.20	91.10	6.7	1.9	2.2
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	SR5(N)	06:38:44	1	Surface	1	1	18.20	8.09	32.45	86.80	6.4	2.2	5.7
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	SR5(N)	06:37:57	1	Surface	1	2	18.19	8.09	32.46	86.90	6.4	2.3	2.9
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	SR5(N)	06:38:29	4.6	Middle	2	1	18.11	8.08	32.72	86.10	6.3	2.6	3.2
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	SR5(N)	06:37:43	4.6	Middle	2	2	18.10	8.08	32.74	86.10	6.3	2.7	3.4
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	SR5(N)	06:38:16	8.1	Bottom	3	1	18.09	8.08	32.82	86.10	6.3	2.5	2.7
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	SR5(N)	06:37:31	8.1	Bottom	3	2	18.09	8.08	32.82	86.20	6.3	2.4	2.8
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	SR10A(N)	05:38:43	1	Surface	1	1	18.37	8.09	32.87	85.10	6.2	2.4	3.7
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	SR10A(N)	05:39:25	1	Surface	1	2	18.37	8.09	32.87	85.40	6.2	2.4	2.9
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	SR10A(N)	05:39:09	6.5	Middle	2	1	18.23	8.09	33.26	84.00	6.1	2.7	4.4
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	SR10A(N)	05:38:28	6.5	Middle	2	2	18.23	8.09	33.26	84.20	6.1	2.8	3.4
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	SR10A(N)	05:38:58	12.0	Bottom	3	1	18.25	8.08	33.32	84.20	6.1	2.9	2.4
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	SR10A(N)	05:38:20	12.0	Bottom	3	2	18.23	8.09	33.30	84.30	6.1	3.0	2.4
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	SR10B(N2)	05:29:35	1.0	Surface	1	1	18.39	8.09	32.86	87.30	6.3	2.1	2.0
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	SR10B(N2)	05:28:51	1.0	Surface	1	2	18.39	8.08	32.83	87.60	6.4	2.1	2.1
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	SR10B(N2)	05:28:34	3.8	Middle	2	1	18.27	8.07	33.11	86.30	6.3	2.2	1.8
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	SR10B(N2)	05:29:17	3.8	Middle	2	2	18.29	8.08	33.07	85.60	6.2	2.2	3.0
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	SR10B(N2)	05:29:03	6.5	Bottom	3	1	18.27	8.08	33.22	85.30	6.2	2.5	2.3
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	SR10B(N2)	05:28:22	6.5	Bottom	3	2	18.23	8.06	33.27	86.10	6.3	2.4	2.0
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	CS(2(A)	07:33:21	1	Surface	1	1	18.12	8.09	32.30	87.30	6.4	2.5	2.7
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	CS(2(A)	07:32:49	1	Surface	1	2	18.12	8.10	32.30	87.70	6.4	2.4	2.3
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	CS(2(A)	07:33:11	3.4	Middle	2	1	18.05	8.09	32.52	86.80	6.4	2.5	3.7
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	CS(2(A)	07:32:37	3.4	Middle	2	2	18.05	8.10	32.51	87.10	6.4	2.4	2.8
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	CS(2(A)	07:32:26	5.7	Bottom	3	1	18.01	8.10	32.65	87.40	6.4	2.5	3.1
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	CS(2(A)	07:33:01	5.7	Bottom	3	2	18.03	8.09	32.64	86.70	6.4	2.6	2.5
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	CS(Mf)5	05:34:52	1.0	Surface	1	1	18.40	8.12	33.07	91.90	6.7	2.2	2.4
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	CS(Mf)5	05:34:08	1.0	Surface	1	2	18.39	8.10	33.09	92.00	6.8	2.3	2.0
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	CS(Mf)5	05:34:36	6.3	Middle	2	1	18.22	8.10	33.51	90.70	6.7	2.4	3.2
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	CS(Mf)5	05:33:56	6.3	Middle	2	2	18.23	8.08	33.51	91.30	6.7	2.4	2.4
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	CS(Mf)5	05:33:46	11.6	Bottom	3	1	18.23	8.08	33.56	91.20	6.7	2.5	2.4
HKLR	HY/2011/03	2025-03-12	Mid-Flood	Fine	CS(Mf)5	05:34:24	11.6	Bottom	3	2	18.23	8.09	33.58	90.50	6.6	2.4	2.9
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	IS5	12:28:52	1.0	Surface	1	1	18.68	8.10	32.08	90.80	6.8	2.6	4.0
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	IS5	12:29:31	1.0	Surface	1	2	18.70	8.10	32.07	90.50	6.8	2.5	4.1
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	IS5	12:29:16	4.3	Middle	2	1	18.52	8.06	32.57	89.00	6.7	2.9	3.1
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	IS5	12:28:40	4.3	Middle	2	2	18.50	8.06	32.60	88.70	6.7	2.7	2.6
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	IS5	12:28:32	7.5	Bottom	3	1	18.47	8.06	32.67	87.50	6.6	2.7	3.8
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	IS5	12:29:08	7.5	Bottom	3	2	18.49	8.06	32.66	88.80	6.7	2.8	4.0
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	IS(Mf)6	12:38:09	1.0	Surface	1	1	18.72	8.09	32.05	92.10	6.9	2.4	3.0
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	IS(Mf)6	12:37:51	1.0	Surface	1	2	18.72	8.09	32.03	92.60	6.9	2.5	3.0
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	IS(Mf)6	12:38:00	2.2	Bottom	3	1	18.71	8.09	32.10	90.20	6.8	2.9	3.7
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	IS(Mf)6	12:37:41	2.2	Bottom	3	2	18.68	8.09	32.10	89.20	6.7	3.0	4.5
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	IS7	12:48:25	1.0	Surface	1	1	18.85	8.09	32.28	95.00	7.1	2.1	5.4
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	IS7	12:48:09	1.0	Surface	1	2	18.80	8.10	32.30	92.70	6.9	2.2	4.4
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	IS7	12:47:58	2.3	Bottom	3	1	18.79	8.10	32.32	90.10	6.7	2.4	2.8
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	IS7	12:48:16	2.3	Bottom	3	2	18.80	8.10	32.32	90.90	6.8	2.4	2.9
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	IS8(N)	13:18:38	1.0	Surface	1	1	18.82	8.09	32.22	90.30	6.8	2.5	3.3
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	IS8(N)	13:18:57	1.0	Surface	1	2	18.84	8.09	32.21	92.20	6.9	2.4	3.1
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	IS8(N)	13:18:28	2.9	Bottom	3	1	18.78	8.09	32.28	88.10	6.6	2.7	2.6
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	IS8(N)	13:18:47	2.9	Bottom	3	2	18.80	8.08	32.26	89.70	6.7	2.6	3.1
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	IS(Mf)9	12:57:10	1.0	Surface	1	1	18.72	8.09	32.22	90.70	6.8	2.5	2.2
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	IS(Mf)9	12:56:54	1.0	Surface	1	2	18.72	8.09	32.21	90.40	6.8	2.7	2.7
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	IS(Mf)9	12:57:01	2.5	Bottom	3	1	18.72	8.09	32.26	90.10	6.8	2.7	4.6
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	IS(Mf)9	12:56:45	2.5	Bottom	3	2	18.70	8.09	32.28	90.80	6.8	2.7	4.8
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	IS10(N)	13:26:11	1.0	Surface	1	1	18.60	8.09	31.57	88.20	6.1	2.3	3.6
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	IS10(N)	13:26:51	1.0	Surface	1	2	18.64	8.10	31.51	88.10	6.1	2.3	2.2
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	IS10(N)	13:25:56	5.4	Middle	2	1	18.25	8.05	32.56	85.00	5.9	2.8	2.8
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	IS10(N)	13:26:35	5.4	Middle	2	2	18.26	8.05	32.55	86.00	6.0	2.7	4.1
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	IS10(N)	13:26:23	9.7	Bottom	3	1	18.33	8.06	32.56	85.60	5.9	3.1	2.9
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	IS10(N)	13:25:45	9.7	Bottom	3	2	18.25	8.05	32.61	84.80	5.9	3.0	4.0
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	SR3(N)	12:12:38	1.0	Surface	1	1	18.75	8.09	32.04	90.40	6.8	2.7	2.7
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	SR3(N)	12:12:55	1.0	Surface	1	2	18.74	8.08	32.02	90.80	6.8	2.6	3.7
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	SR3(N)	12:12:30	2.3	Bottom	3	1	18.64	8.10	32.15	87.20	6.3	2.8	4.5
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	SR3(N)	12:12:45	2.3	Bottom	3	2	18.74	8.08	32.08	89.10	6.7	2.6	3.7
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	SR4(N3)	13:10:31	1.0	Surface	1	1	18.79	8.09	32.09	93.50	7.0	2.2	4.2
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	SR4(N3)	13:10:15	1.0	Surface	1	2	18.83	8.09	31.63	91.60	6.9	2.3	3.0
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	SR4(N3)	13:10:07	2.9	Bottom	3	1	18.68	8.08	32.26	89.40	6.7	2.5	4.3
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	SR4(N3)	13:10:23	2.9	Bottom	3	2	18.81	8.09	32.17	90.00	6.7	2.5	3.4
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	SR5(N)	13:16:37	1.0	Surface	1	1	18.55	8.09	31.66	87.70	6.1	2.5	2.5
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	SR5(N)	13:17:19	1.0	Surface	1	2	18.64	8.10	31.55	88.40	6.1	2.5	3.2
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	SR5(N)	13:16:26	4.5	Middle	2	1	18.29	8.05	32.37	84.90	5.9	3.0	4.0
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	SR5(N)	13:17:02	4.5	Middle	2	2	18.27	8.05	32.44	85.20	5.9	2.8	3.2
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	SR5(N)	13:16:50	8.0	Bottom	3	1	18.30	8.05	32.55	85.40	5.9	3.2	3.8
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	SR5(N)	13:16:12	8.0	Bottom	3	2	18.24	8.03	32.64	83.90	5.8	3.1	3.8
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	SR10A(N)	14:15:54	1.0	Surface	1	1	18.67	8.12	32.51	89.60	6.1	2.2	3.4
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	SR10A(N)	14:15:02	1.0	Surface	1	2	18.72	8.13	32.39	90.20	6.2	2.4	2.8
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	SR10A(N)	14:15:37	6.7	Middle	2	1	18.39	8.07	33.33	87.10	6.0	2.4	3.0
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	SR10A(N)	14:14:42	6.7	Middle	2	2	18.38	8.09	33.40	87.30	6.0	2.4	3.2
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	SR10A(N)	14:14:18	12.3	Bottom	3	1	18.39	8.11	33.39	87.30	6.0	2.8	3.4
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	SR10A(N)	14:15:25	12.3	Bottom	3	2	18.37	8.07	33.39	86.80	6.0	3.0	3.0
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	SR10B(N2)	14:25:31	1.0	Surface	1	1	18.75	8.09	32.29	89.90	6.2	2.1	2.9
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	SR10B(N2)	14:26:07	1.0	Surface	1	2	18.70	8.09	32.34	90.10	6.2	2.2	3.6
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	SR10B(N2)	14:25:19	3.9	Middle	2	1	18.38	8.07	33.33	86.90	6.0	2.2	2.8
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	SR10B(N2)	14:25:55	3.9	Middle	2	2	18.43	8.07	33.18	88.00	6.0	2.1	3.4
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	SR10B(N2)	14:25:09	6.7	Bottom	3	1	18.36	8.07	33.48	86.50	5.9	2.7	3.3
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	SR10B(N2)	14:25:46	6.7	Bottom	3	2	18.39	8.07	33.39	86.80	6.0	2.8	2.9
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	CS(2(A)	12:22:02	1.0	Surface	1	1	18.53	8.09	31.74	89.00	6.2	2.2	2.0
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	CS(2(A)	12:21:31	1.0	Surface	1	2	18.54	8.10	31.72	89.20	6.2	2.0	2.9
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	CS(2(A)	12:21:21	3.2	Middle	2	1	18.30	8.06	32.33	86.00	6.0	2.6	2.2
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	CS(2(A)	12:21:53	3.2	Middle	2	2	18.31	8.05	32.27	87.10	6.1	2.5	3.0
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	CS(2(A)	12:21:44	5.3	Bottom	3	1	18.34	8.06	32.38	86.10	6.0	2.9	3.7
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	CS(2(A)	12:21:10	5.3	Bottom	3	2	18.28	8.08	32.55	85.00	5.9	2.7	2.8
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	CS(Mf)5	11:41:41	1.0	Surface	1	1	18.14	8.09	31.75	87.30	6.6	1.8	3.2
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	CS(Mf)5	14:01:19	1.0	Surface	1	2	18.69	8.10	32.84	87.50	6.5	2.1	3.7
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	CS(Mf)5	14:01:42	6.4	Middle	2	1	18.30	8.04	34.02	85.50	6.4	2.3	5.1
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	CS(Mf)5	14:01:06	6.4	Middle	2	2	18.30	8.04	34.03	86.00	6.4	2.3	4.9
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	CS(Mf)5	14:01:33	11.8	Bottom	3	1	18.36	8.05	33.88	84.30	6.3	2.4	4.9
HKLR	HY/2011/03	2025-03-14	Mid-Ebb	Fine	CS(Mf)5	14:00:55	11.8	Bottom	3	2	18.30	8.04	34.13	84.20	6.3	2.3	4.5
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	IS5	08:41:39	1.0	Surface	1	1	18.56	8.10	32.10	87.30	6.1	2.4	5.2
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	IS5	08:41:00	1.0	Surface	1	2	18.57	8.11	32.10	88.90	6.2	2.4	4.5
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	IS5	08:40:46	4.3	Middle	2	1	18.36	8.05	32.79	84.20	5.9	2.7	4.2
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	IS5	08:41:25	4.3	Middle	2	2	18.37	8.05	32.76	84.50	5.9	2.6	4.8
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	IS5	08:41:13	7.6	Bottom	3	1	18.35	8.05	32.82	81.90	5.7	2.7	3.7
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	IS5	08:40:37	7.6	Bottom	3	2	18.35	8.05	32.90	81.90	5.7	2.8	3.8
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	IS(Mf)6	08:32:17	1.0	Surface	1	1	18.58	8.09	32.21	92.70	6.4	2.8	3.5
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	IS(Mf)6	08:32:00	1.0	Surface	1	2	18.57	8.10	32.21	90.80	6.3	2.8	3.7
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	IS(Mf)6	08:31:49	2.3	Bottom	3	1	18.52	8.08	32.33	90.10	6.2	2.9	4.0
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	IS(Mf)6	08:32:08	2.3	Bottom	3	2	18.54	8.08	32.31	89.50	6.2	2.9	2.8
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	IS7	08:22:28	1.0	Surface	1	1	18.60	8.10	32.25	90.70	6.3	2.4	4.4
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	IS7	08:22:09	1.0	Surface	1	2	18.60	8.11	32.24	89.20	6.2	2.4	3.8
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	IS7	08:22:17	2.3	Bottom	3	1	18.55	8.08	32.39	88.70	6.1	2.6	3.9
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	IS7	08:22:00	2.3	Bottom	3	2	18.53	8.08	32.46	87.50	6.1	2.6	3.8
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	IS8(N)	07:50:57	1.0	Surface	1	1	18.58	8.09	32.13	89.30	6.2	2.6	4.0
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	IS8(N)	07:50:34	1.0	Surface	1	2	18.57	8.09	32.17	89.90	6.2	2.6	4.2
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	IS8(N)	07:50:41	3.1	Bottom	3	1	18.49	8.06	32.42	88.20	6.1	2.7	4.7
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	IS8(N)	07:50:24	3.1	Bottom	3	2	18.48	8.08	32.43	89.80	6.2	2.9	3.8
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	IS(Mf)9	08:13:05	1.0	Surface	1	1	18.58	8.10	32.24	90.10	6.2	2.2	4.3
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	IS(Mf)9	08:12:45	1.0	Surface	1	2	18.58	8.10	32.25	88.50	6.1	2.2	3.5
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	IS(Mf)9	08:12:54	2.6	Bottom	3	1	18.51	8.07	32.43	87.90	6.1	2.4	3.1
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	IS(Mf)9	08:12:35	2.6	Bottom	3	2	18.47	8.06	32.47	86.90	6.0	2.5	3.4
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	IS10(N)	08:15:47	1.0	Surface	1	1	18.34	8.09	32.46	85.10	5.9	2.3	3.5
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	IS10(N)	08:15:03	1.0	Surface	1	2	18.32	8.09	32.53	85.30	5.9	2.3	3.4

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	IS10(N)	08:14:51	5.3	Middle	2	1	18.11	8.06	33.23	83.20	5.8	2.7	3.0
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	IS10(N)	08:15:29	5.3	Middle	2	2	18.12	8.06	33.25	82.50	5.7	2.8	2.9
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	IS10(N)	08:14:40	9.6	Bottom	3	1	18.13	8.06	33.22	81.80	5.7	2.8	3.9
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	IS10(N)	08:15:17	9.6	Bottom	3	2	18.14	8.06	33.15	81.90	5.7	2.9	3.0
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	SR3(N)	08:54:48	1.0	Surface	1	1	18.56	8.10	32.09	89.80	6.2	1.9	2.7
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	SR3(N)	08:54:31	1.0	Surface	1	2	18.56	8.10	32.11	90.10	6.2	2.1	3.6
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	SR3(N)	08:54:22	2.4	Bottom	3	1	18.52	8.09	32.23	88.40	6.1	2.7	3.7
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	SR3(N)	08:54:38	2.4	Bottom	3	2	18.55	8.10	32.17	88.10	6.1	2.7	3.0
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	SR4(N3)	07:58:38	1.0	Surface	1	1	18.56	8.09	32.11	89.30	6.2	2.3	4.0
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	SR4(N3)	07:58:59	1.0	Surface	1	2	18.55	8.09	32.12	89.80	6.2	2.2	3.1
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	SR4(N3)	07:58:48	2.9	Bottom	3	1	18.46	8.05	32.52	87.30	6.1	2.5	5.8
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	SR4(N3)	07:58:28	2.9	Bottom	3	2	18.45	8.06	32.62	86.90	6.0	2.4	4.6
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	SR5(N)	08:25:19	1	Surface	1	1	18.34	8.10	32.47	84.80	5.9	2.1	3.1
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	SR5(N)	08:24:35	1	Surface	1	2	18.34	8.10	32.47	85.30	5.9	2.2	2.3
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	SR5(N)	08:25:04	4.7	Middle	2	1	18.15	8.06	33.09	82.70	5.7	2.5	4.0
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	SR5(N)	08:24:21	4.7	Middle	2	2	18.14	8.06	33.08	82.90	5.8	2.5	2.7
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	SR5(N)	08:24:53	8.4	Bottom	3	1	18.12	8.05	33.24	81.50	5.7	2.8	3.3
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	SR5(N)	08:24:10	8.4	Bottom	3	2	18.12	8.05	33.26	81.70	5.7	2.8	3.4
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	SR10A(N)	07:20:42	1	Surface	1	1	18.43	8.09	32.68	85.50	5.9	2.0	4.1
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	SR10A(N)	07:21:39	1	Surface	1	2	18.41	8.09	32.73	85.80	5.9	1.8	2.8
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	SR10A(N)	07:21:23	6.8	Middle	2	1	18.17	8.05	33.52	82.20	5.7	2.1	3.8
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	SR10A(N)	07:20:25	6.8	Middle	2	2	18.17	8.05	33.54	82.30	5.7	2.2	3.5
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	SR10A(N)	07:20:16	12.6	Bottom	3	1	18.18	8.05	33.54	82.00	5.7	2.6	3.2
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	SR10A(N)	07:21:13	12.6	Bottom	3	2	18.18	8.04	33.55	81.20	5.6	2.4	3.5
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	SR10B(N2)	07:08:32	1.0	Surface	1	1	18.44	8.09	32.64	89.60	6.2	2.1	4.2
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	SR10B(N2)	07:07:51	1.0	Surface	1	2	18.45	8.08	32.65	88.90	6.1	2.1	3.3
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	SR10B(N2)	07:07:38	3.9	Middle	2	1	18.28	8.05	33.11	87.90	6.1	2.3	3.5
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	SR10B(N2)	07:08:17	3.9	Middle	2	2	18.29	8.05	33.10	86.80	6.0	2.2	2.8
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	SR10B(N2)	07:07:26	6.7	Bottom	3	1	18.21	8.03	33.44	84.00	5.8	2.7	2.7
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	SR10B(N2)	07:08:03	6.7	Bottom	3	2	18.25	8.05	33.41	84.40	5.8	2.7	3.4
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	CS(2A)	09:16:30	1	Surface	1	1	18.29	8.10	32.40	85.00	5.9	1.8	3.2
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	CS(2A)	09:15:56	1	Surface	1	2	18.29	8.10	32.41	85.10	5.9	1.8	3.8
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	CS(2A)	09:15:45	3.3	Middle	2	1	18.14	8.07	32.89	84.40	5.9	2.4	3.7
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	CS(2A)	09:16:20	3.3	Middle	2	2	18.14	8.07	32.87	84.10	5.8	2.3	3.5
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	CS(2A)	09:15:34	5.5	Bottom	3	1	18.09	8.07	33.13	83.20	5.8	2.5	3.0
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	CS(2A)	09:16:10	5.5	Bottom	3	2	18.11	8.06	33.10	82.50	5.7	2.3	3.4
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	CS(Mf)5	07:11:52	1.0	Surface	1	1	18.57	8.10	32.32	87.00	6.0	2.2	3.3
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	CS(Mf)5	07:12:34	1.0	Surface	1	2	18.56	8.10	32.32	87.70	6.1	2.2	2.5
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	CS(Mf)5	07:12:18	6.3	Middle	2	1	18.23	8.05	33.26	84.90	5.9	2.4	3.2
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	CS(Mf)5	07:11:38	6.3	Middle	2	2	18.27	8.05	33.22	84.40	5.9	2.3	3.6
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	CS(Mf)5	07:11:24	11.5	Bottom	3	1	18.21	8.04	33.79	83.10	5.8	2.4	4.8
HKLR	HY/2011/03	2025-03-14	Mid-Flood	Fine	CS(Mf)5	07:12:06	11.5	Bottom	3	2	18.31	8.05	33.82	81.90	5.7	2.4	4.4
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	IS5	13:34:04	1.0	Surface	1	1	18.84	8.09	32.12	94.10	6.9	2.6	4.0
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	IS5	13:34:42	1.0	Surface	1	2	18.85	8.09	32.11	94.10	6.9	2.7	4.9
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	IS5	13:34:28	4.3	Middle	2	1	18.69	8.06	32.59	92.70	6.8	3.3	4.3
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	IS5	13:33:51	4.3	Middle	2	2	18.68	8.06	32.61	92.50	6.8	3.4	3.9
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	IS5	13:33:44	7.5	Bottom	3	1	18.66	8.06	32.67	91.80	6.8	3.4	4.3
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	IS5	13:34:19	7.5	Bottom	3	2	18.68	8.06	32.66	92.50	6.8	3.3	4.9
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	IS(Mf)6	13:42:17	1.0	Surface	1	1	18.87	8.09	32.10	96.40	7.1	2.6	4.3
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	IS(Mf)6	13:41:59	1.0	Surface	1	2	18.87	8.09	32.08	96.20	7.1	2.7	5.2
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	IS(Mf)6	13:42:08	2.2	Bottom	3	1	18.86	8.09	32.16	94.60	7.0	3.3	4.5
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	IS(Mf)6	13:41:49	2.2	Bottom	3	2	18.83	8.09	32.16	93.60	6.9	3.2	4.6
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	IS7	13:50:51	1.0	Surface	1	1	18.94	8.09	32.23	97.40	7.2	1.8	5.4
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	IS7	13:50:34	1.0	Surface	1	2	18.91	8.10	32.24	96.10	7.1	2.2	4.4
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	IS7	13:50:25	2.3	Bottom	3	1	18.88	8.10	32.30	94.40	6.9	2.7	5.1
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	IS7	13:50:41	2.3	Bottom	3	2	18.90	8.10	32.28	95.00	7.0	2.7	6.0
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	IS8(N)	14:27:37	1.0	Surface	1	1	18.93	8.08	32.18	93.90	6.9	2.7	4.9
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	IS8(N)	14:27:55	1.0	Surface	1	2	18.94	8.08	32.16	95.10	7.0	2.3	5.8
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	IS8(N)	14:27:27	2.9	Bottom	3	1	18.88	8.07	32.27	92.50	6.8	3.2	4.9
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	IS8(N)	14:27:46	2.9	Bottom	3	2	18.90	8.07	32.24	93.60	6.9	3.1	5.3
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	IS(Mf)9	14:02:39	1.0	Surface	1	1	18.87	8.09	32.20	94.90	7.0	2.6	5.3
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	IS(Mf)9	14:02:21	1.0	Surface	1	2	18.87	8.09	32.19	94.60	7.0	2.8	4.9
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	IS(Mf)9	14:02:29	2.6	Bottom	3	1	18.86	8.09	32.27	94.40	6.9	3.2	5.0
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	IS(Mf)9	14:02:12	2.6	Bottom	3	2	18.84	8.08	32.28	94.70	7.0	3.0	4.8
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	IS10(N)	14:29:34	1.0	Surface	1	1	18.75	8.10	31.85	88.90	6.3	2.3	4.0
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	IS10(N)	14:30:14	1.0	Surface	1	2	18.78	8.10	31.81	89.00	6.3	2.1	5.0
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	IS10(N)	14:29:58	5.4	Middle	2	1	18.53	8.07	32.62	87.30	6.2	3.0	5.5
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	IS10(N)	14:29:20	5.4	Middle	2	2	18.52	8.07	32.62	86.80	6.1	3.2	4.7
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	IS10(N)	14:29:48	9.8	Bottom	3	1	18.58	8.08	32.66	87.00	6.1	3.4	4.5
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	IS10(N)	14:29:10	9.8	Bottom	3	2	18.53	8.07	32.69	86.80	6.1	3.3	3.8
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	SR3(N)	13:18:54	1.0	Surface	1	1	18.87	8.08	32.13	95.30	7.0	3.0	5.5
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	SR3(N)	13:18:37	1.0	Surface	1	2	18.88	8.08	32.14	94.60	7.0	3.0	5.9
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	SR3(N)	13:18:28	2.3	Bottom	3	1	18.81	8.09	32.23	92.20	6.6	3.2	4.8
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	SR3(N)	13:18:43	2.3	Bottom	3	2	18.86	8.08	32.19	93.60	6.9	3.1	4.6
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	SR4(N3)	14:18:32	1.0	Surface	1	1	18.91	8.08	32.12	95.50	7.0	2.2	4.7
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	SR4(N3)	14:18:15	1.0	Surface	1	2	18.93	8.08	31.87	94.40	6.9	2.1	5.0
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	SR4(N3)	14:18:07	2.9	Bottom	3	1	18.72	8.07	32.26	92.90	6.8	2.7	4.6
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	SR4(N3)	14:18:25	2.9	Bottom	3	2	18.91	8.07	32.21	93.40	6.9	2.6	4.6
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	SR5(N)	14:21:54	1.0	Surface	1	1	18.78	8.10	31.83	89.80	6.3	2.2	3.7
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	SR5(N)	14:21:14	1.0	Surface	1	2	18.72	8.10	31.90	89.10	6.3	2.2	4.7
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	SR5(N)	14:21:02	4.5	Middle	2	1	18.55	8.08	32.49	86.90	6.1	3.2	4.2
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	SR5(N)	14:21:40	4.5	Middle	2	2	18.54	8.07	32.53	87.20	6.2	3.0	5.3
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	SR5(N)	14:21:28	8.0	Bottom	3	1	18.55	8.07	32.67	87.20	6.2	3.3	4.4
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	SR5(N)	14:20:50	8.0	Bottom	3	2	18.51	8.07	32.71	86.30	6.1	3.4	3.7
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	SR10A(N)	15:29:38	1.0	Surface	1	1	18.80	8.12	32.75	90.00	6.3	2.1	4.0
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	SR10A(N)	15:28:46	1.0	Surface	1	2	18.83	8.12	32.68	90.60	6.3	2.3	4.0
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	SR10A(N)	15:29:17	6.6	Middle	2	1	18.62	8.09	33.39	87.50	6.1	2.9	4.4
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	SR10A(N)	15:28:28	6.6	Middle	2	2	18.60	8.10	33.45	88.10	6.2	2.7	4.3
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	SR10A(N)	15:28:11	12.2	Bottom	3	1	18.61	8.11	33.45	88.20	6.2	3.1	3.2
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	SR10A(N)	15:29:05	12.2	Bottom	3	2	18.62	8.09	33.42	87.40	6.1	3.2	4.5
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	SR10B(N2)	15:40:05	1.0	Surface	1	1	18.84	8.10	32.65	89.80	6.3	2.2	4.0
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	SR10B(N2)	15:40:45	1.0	Surface	1	2	18.82	8.10	32.68	89.60	6.3	2.2	4.1
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	SR10B(N2)	15:39:53	3.8	Middle	2	1	18.63	8.09	33.34	87.30	6.1	2.2	4.0
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	SR10B(N2)	15:40:33	3.8	Middle	2	2	18.64	8.09	33.27	87.80	6.1	2.2	4.8
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	SR10B(N2)	15:39:43	6.6	Bottom	3	1	18.61	8.09	33.46	87.10	6.1	3.0	3.8
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	SR10B(N2)	15:40:19	6.6	Bottom	3	2	18.64	8.09	33.40	87.20	6.1	2.9	3.8
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	CS(2A)	13:21:18	1.0	Surface	1	1	18.62	8.10	31.99	91.30	6.5	2.5	3.8
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	CS(2A)	13:20:47	1.0	Surface	1	2	18.62	8.10	32.00	91.70	6.5	2.6	3.7
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	CS(2A)	13:20:37	3.3	Middle	2	1	18.46	8.08	32.55	88.90	6.3	3.0	4.7
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	CS(2A)	13:21:09	3.3	Middle	2	2	18.47	8.08	32.52	89.20	6.3	3.2	5.5
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	CS(2A)	13:21:01	5.5	Bottom	3	1	18.48	8.08	32.65	88.60	6.3	3.0	4.5
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	CS(2A)	13:20:26	5.5	Bottom	3	2	18.45	8.08	32.75	88.10	6.2	3.0	4.6
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	CS(Mf)5	15:11:51	1.0	Surface	1	1	18.53	8.09	32.61	90.90	6.7	2.1	5.8
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	CS(Mf)5	15:11:08	1.0	Surface	1	2	18.88	8.09	32.63	90.70	6.6	2.0	5.8
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	CS(Mf)5	15:11:31	6.4	Middle	2	1	18.54	8.03	33.61	88.70	6.5	2.3	5.4
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	CS(Mf)5	15:10:54	6.4	Middle	2	2	18.54	8.03	33.62	89.00	6.5	2.3	4.2
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	CS(Mf)5	15:11:23	11.8	Bottom	3	1	18.57	8.04	33.26	87.90	6.4	2.7	4.4
HKLR	HY/2011/03	2025-03-17	Mid-Ebb	Fine	CS(Mf)5	15:10:43	11.8	Bottom	3	2	18.54	8.03	33.68	87.80	6.4	2.6	4.2
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	IS5	09:00:51	1.0	Surface	1	1	18.69	8.10	32.23	91.20	6.4	2.3	5.4
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	IS5	09:00:09	1.0	Surface	1	2	18.71	8.11	32.23	92.70	6.5	2.3	5.3
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	IS5	08:59:55	4.3	Middle	2	1	18.52	8.06	32.83	88.40	6.2	2.8	5.4
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	IS5	09:00:37	4.3	Middle	2	2	18.52	8.06	32.82	88.80	6.2	2.8	4.8
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	IS5	09:00:23	7.6	Bottom	3	1	18.49	8.06	32.89	87.00	6.1	3.2	6.4
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	IS5	08:59:46	7.6	Bottom	3	2	18.51	8.06	32.93	86.90	6.1	3.2	5.8
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	IS(Mf)6	08:51:15	1.0	Surface	1	1	18.72	8.10	32.28	95.00	6.6	2.4	7.2
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	IS(Mf)6	08:50:57	1.0	Surface	1	2	18.72	8.10	32.29	93.80	6.6	2.4	6.1
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	IS(Mf)6	08:50:45	2.3	Bottom	3	1	18.68	8.09	32.41	93.40	6.5	2.9	7.2
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	IS(Mf)6	08:51:05	2.3	Bottom	3	2	18.69	8.09	32.38	93.00	6.5	2.9	6.9
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	IS7	08:39:56	1.0	Surface	1	1	18.73	8.10	32.31	93.80	6.6	2.0	7.7
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	IS7	08:39:39	1.0	Surface	1	2	18.73	8.11	32.31	92.90	6.5	2.0	6.5
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	IS7	08:39:47	2.3	Bottom	3	1	18.69	8.09	32.42	92.60	6.5	2.6	7.8
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	IS7	08:39:31	2.3	Bottom	3	2	18.68	8.09	32.47	91.90	6.4	2.4	7.0
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	IS8(N)	08:08:06	1.0	Surface	1	1	18.71	8.09	32.24	93.70	6.6	2.1	5.8
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	IS8(N)	08:07:34	1.0	Surface	1	2	18.71	8.09	32.26	93.50	6.6	2.1	5.2
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	IS8(N)	08:07:41	3.1	Bottom	3	1	18.65	8.07	32.50	92.30	6.5	2.5	5.3

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	IS8(N)	08:07:24	3.1	Bottom	3	2	18.64	8.08	32.51	92.90	6.5	2.8	5.7
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	IS(Mf)9	08:31:03	1.0	Surface	1	1	18.73	8.10	32.29	93.40	6.5	1.9	4.6
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	IS(Mf)9	08:30:46	1.0	Surface	1	2	18.73	8.10	32.31	92.50	6.5	1.9	4.5
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	IS(Mf)9	08:30:53	2.6	Bottom	3	1	18.68	8.08	32.46	92.00	6.5	2.7	3.5
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	IS(Mf)9	08:30:35	2.6	Bottom	3	2	18.64	8.07	32.48	91.30	6.4	2.7	4.0
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	IS10(N)	08:33:23	1.0	Surface	1	1	18.51	8.10	32.42	88.40	6.2	2.3	4.8
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	IS10(N)	08:34:04	1.0	Surface	1	2	18.53	8.10	32.39	88.60	6.3	2.2	4.4
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	IS10(N)	08:33:10	5.4	Middle	2	1	18.40	8.08	33.02	86.20	6.1	2.8	4.4
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	IS10(N)	08:33:48	5.4	Middle	2	2	18.41	8.08	33.04	85.90	6.1	2.7	3.6
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	IS10(N)	08:33:36	9.8	Bottom	3	1	18.43	8.08	33.00	85.30	6.0	3.5	4.2
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	IS10(N)	08:32:59	9.8	Bottom	3	2	18.42	8.08	33.04	85.40	6.0	3.4	4.5
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	SR3(N)	09:12:46	1.0	Surface	1	1	18.71	8.10	32.27	92.90	6.5	2.1	4.6
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	SR3(N)	09:12:29	1.0	Surface	1	2	18.70	8.10	32.28	92.60	6.5	2.4	4.1
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	SR3(N)	09:12:20	2.4	Bottom	3	1	18.66	8.09	32.39	91.30	6.4	3.0	4.8
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	SR3(N)	09:12:36	2.4	Bottom	3	2	18.69	8.10	32.35	91.60	6.4	3.1	6.0
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	SR4(N3)	08:16:34	1.0	Surface	1	1	18.70	8.09	32.23	92.80	6.5	1.9	4.7
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	SR4(N3)	08:16:54	1.0	Surface	1	2	18.71	8.09	32.24	92.90	6.5	2.0	4.9
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	SR4(N3)	08:16:44	2.9	Bottom	3	1	18.63	8.06	32.55	91.60	6.4	2.2	4.8
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	SR4(N3)	08:16:23	2.9	Bottom	3	2	18.61	8.07	32.62	91.50	6.4	2.0	4.3
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	SR5(N)	08:43:49	1	Surface	1	1	18.55	8.11	32.44	86.90	6.1	2.0	4.7
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	SR5(N)	08:43:05	1	Surface	1	2	18.55	8.11	32.44	87.20	6.2	2.1	4.3
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	SR5(N)	08:43:34	4.6	Middle	2	1	18.43	8.08	32.94	85.30	6.0	2.7	4.6
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	SR5(N)	08:42:52	4.6	Middle	2	2	18.43	8.08	32.94	85.50	6.0	2.7	3.7
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	SR5(N)	08:42:40	8.2	Bottom	3	1	18.41	8.08	33.08	85.00	6.0	3.4	5.2
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	SR5(N)	08:43:23	8.2	Bottom	3	2	18.42	8.07	33.06	84.70	6.0	3.3	5.7
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	SR10A(N)	07:41:14	1	Surface	1	1	18.63	8.09	32.72	87.20	6.1	2.0	4.8
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	SR10A(N)	07:40:24	1	Surface	1	2	18.65	8.09	32.68	87.40	6.2	2.0	4.7
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	SR10A(N)	07:40:58	6.7	Middle	2	1	18.47	8.06	33.34	84.50	5.9	2.2	4.4
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	SR10A(N)	07:40:08	6.7	Middle	2	2	18.48	8.06	33.35	85.00	6.0	2.1	4.9
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	SR10A(N)	07:39:58	12.4	Bottom	3	1	18.49	8.06	33.37	84.90	6.0	3.0	4.6
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	SR10A(N)	07:40:48	12.4	Bottom	3	2	18.49	8.06	33.39	84.10	5.9	2.7	4.2
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	SR10B(N2)	07:31:49	1.0	Surface	1	1	18.65	8.09	32.67	91.00	6.4	2.1	6.0
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	SR10B(N2)	07:31:07	1.0	Surface	1	2	18.66	8.07	32.67	90.80	6.4	2.1	5.2
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	SR10B(N2)	07:30:53	3.8	Middle	2	1	18.54	8.07	33.07	88.90	6.2	2.3	5.1
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	SR10B(N2)	07:31:33	3.8	Middle	2	2	18.55	8.06	33.05	87.60	6.2	2.1	4.2
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	SR10B(N2)	07:30:42	6.5	Bottom	3	1	18.46	8.07	33.31	86.30	6.1	3.0	5.2
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	SR10B(N2)	07:31:20	6.5	Bottom	3	2	18.53	8.06	33.29	86.30	6.1	2.8	3.8
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	CS(2A)	09:40:19	1	Surface	1	1	18.45	8.11	32.39	88.20	6.3	2.3	5.2
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	CS(2A)	09:39:43	1	Surface	1	2	18.45	8.12	32.42	88.40	6.3	2.4	4.9
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	CS(2A)	09:39:31	3.3	Middle	2	1	18.36	8.10	32.82	87.30	6.2	3.3	4.0
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	CS(2A)	09:40:08	3.3	Middle	2	2	18.36	8.10	32.82	87.10	6.2	3.3	5.5
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	CS(2A)	09:39:20	5.6	Bottom	3	1	18.33	8.10	33.02	86.40	6.1	3.4	5.3
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	CS(2A)	09:39:58	5.6	Bottom	3	2	18.34	8.09	33.00	86.00	6.1	3.4	4.4
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	CS(Mf)5	07:26:02	1.0	Surface	1	1	18.72	8.09	32.40	91.90	6.5	2.1	4.0
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	CS(Mf)5	07:26:46	1.0	Surface	1	2	18.72	8.09	32.39	92.30	6.5	2.2	5.0
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	CS(Mf)5	07:26:29	6.3	Middle	2	1	18.46	8.05	33.17	89.60	6.3	2.5	5.0
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	CS(Mf)5	07:25:48	6.3	Middle	2	2	18.48	8.05	33.14	89.60	6.3	2.5	6.0
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	CS(Mf)5	07:25:36	11.5	Bottom	3	1	18.46	8.05	33.44	88.50	6.2	2.7	6.0
HKLR	HY/2011/03	2025-03-17	Mid-Flood	Fine	CS(Mf)5	07:26:17	11.5	Bottom	3	2	18.50	8.05	33.48	87.60	6.2	2.9	6.6
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	IS5	14:55:53	1.0	Surface	1	1	18.97	8.08	32.40	87.60	6.2	3.1	3.1
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	IS5	14:56:34	1.0	Surface	1	2	18.98	8.08	32.41	86.60	6.2	3.2	3.5
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	IS5	14:56:19	4.3	Middle	2	1	18.68	8.05	33.52	85.60	6.1	3.3	2.8
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	IS5	14:55:38	4.3	Middle	2	2	18.65	8.05	33.43	86.00	6.1	3.2	2.8
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	IS5	14:55:30	7.5	Bottom	3	1	18.64	8.05	33.91	85.00	6.0	3.5	2.2
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	IS5	14:56:07	7.5	Bottom	3	2	18.66	8.05	33.87	84.90	6.0	3.6	3.1
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	IS(Mf)6	15:03:56	1.0	Surface	1	1	18.99	8.08	32.21	88.80	6.3	3.1	2.4
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	IS(Mf)6	15:04:13	1.0	Surface	1	2	18.99	8.08	32.24	88.70	6.3	3.0	3.3
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	IS(Mf)6	15:04:04	2.2	Bottom	3	1	18.92	8.08	32.47	87.90	6.2	3.4	3.0
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	IS(Mf)6	15:03:45	2.2	Bottom	3	2	18.91	8.09	32.48	88.00	6.2	3.4	3.6
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	IS7	15:15:51	1.0	Surface	1	1	19.01	8.08	32.44	88.60	6.3	2.4	2.9
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	IS7	15:15:33	1.0	Surface	1	2	18.98	8.08	32.46	88.30	6.2	2.7	3.6
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	IS7	15:15:40	2.3	Bottom	3	1	18.92	8.08	32.58	87.40	6.2	3.1	2.8
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	IS7	15:15:24	2.3	Bottom	3	2	18.89	8.08	32.63	87.70	6.2	3.0	2.7
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	IS8(N)	15:57:10	1.0	Surface	1	1	19.03	8.07	32.38	87.20	6.2	3.0	3.7
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	IS8(N)	15:56:51	1.0	Surface	1	2	19.01	8.07	32.42	86.90	6.1	3.2	4.0
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	IS8(N)	15:57:00	3.0	Bottom	3	1	18.95	8.06	32.56	86.40	6.1	3.4	3.1
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	IS8(N)	15:56:40	3.0	Bottom	3	2	18.89	8.06	32.63	85.80	6.1	3.3	2.8
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	IS(Mf)9	15:25:16	1.0	Surface	1	1	18.98	8.07	32.45	86.80	6.1	3.0	2.5
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	IS(Mf)9	15:24:56	1.0	Surface	1	2	18.98	8.08	32.44	87.00	6.2	3.1	2.1
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	IS(Mf)9	15:25:05	2.7	Bottom	3	1	18.88	8.07	32.64	86.60	6.1	3.4	2.9
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	IS(Mf)9	15:24:46	2.7	Bottom	3	2	18.87	8.07	32.63	87.00	6.1	3.3	3.0
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	IS10(N)	16:06:00	1.0	Surface	1	1	19.09	8.08	28.31	97.20	6.8	2.6	3.2
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	IS10(N)	16:06:41	1.0	Surface	1	2	19.15	8.08	28.21	98.50	6.9	2.5	2.2
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	IS10(N)	16:05:46	5.4	Middle	2	1	18.69	8.06	30.09	80.20	5.6	3.1	3.0
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	IS10(N)	16:06:25	5.4	Middle	2	2	18.70	8.08	30.06	80.90	5.7	3.3	3.1
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	IS10(N)	16:05:35	9.7	Bottom	3	1	18.67	8.06	30.75	81.30	5.7	3.3	3.0
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	IS10(N)	16:06:15	9.7	Bottom	3	2	18.73	8.07	30.37	81.60	5.7	3.3	2.9
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	SR3(N)	14:41:54	1.0	Surface	1	1	18.98	8.06	32.32	89.90	6.4	3.1	3.0
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	SR3(N)	14:41:38	1.0	Surface	1	2	18.99	8.07	32.30	88.90	6.3	3.1	2.4
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	SR3(N)	14:41:28	2.3	Bottom	3	1	18.91	8.07	32.86	87.70	6.2	3.2	2.8
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	SR3(N)	14:41:44	2.3	Bottom	3	2	18.96	8.06	32.72	88.30	6.3	3.2	2.9
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	SR4(N3)	15:40:07	1.0	Surface	1	1	18.97	8.06	32.41	86.20	6.1	2.6	1.8
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	SR4(N3)	15:39:49	1.0	Surface	1	2	19.01	8.06	32.25	85.70	6.0	2.6	3.0
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	SR4(N3)	15:39:59	2.9	Bottom	3	1	18.91	8.05	32.58	85.00	6.0	2.9	4.2
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	SR4(N3)	15:39:39	2.9	Bottom	3	2	18.85	8.05	32.57	85.20	6.0	2.9	4.5
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	SR5(N)	15:58:39	1.0	Surface	1	1	19.08	8.08	28.34	98.30	6.9	2.2	3.4
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	SR5(N)	15:58:02	1.0	Surface	1	2	19.06	8.09	28.33	98.10	6.9	2.1	2.5
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	SR5(N)	15:57:49	4.2	Middle	2	1	18.74	8.06	29.83	81.00	5.7	2.8	3.3
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	SR5(N)	15:58:26	4.2	Middle	2	2	18.73	8.05	29.86	81.20	5.7	2.7	2.2
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	SR5(N)	15:58:15	7.3	Bottom	3	1	18.74	8.05	30.39	82.30	5.8	3.2	3.2
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	SR5(N)	15:57:36	7.3	Bottom	3	2	18.71	8.07	30.51	82.00	5.7	3.0	4.4
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	SR10A(N)	17:01:52	1.0	Surface	1	1	18.76	8.10	31.29	97.90	6.8	2.8	3.6
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	SR10A(N)	17:01:05	1.0	Surface	1	2	18.75	8.11	31.28	97.40	6.8	3.0	3.4
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	SR10A(N)	17:00:49	6.7	Middle	2	1	18.43	8.10	32.96	81.50	5.7	2.9	3.2
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	SR10A(N)	17:01:33	6.7	Middle	2	2	18.44	8.08	32.98	80.60	5.6	3.0	2.5
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	SR10A(N)	17:00:36	12.3	Bottom	3	1	18.44	8.10	33.06	81.80	5.7	3.0	2.6
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	SR10A(N)	17:01:22	12.3	Bottom	3	2	18.46	8.08	33.01	81.10	5.6	3.0	3.6
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	SR10B(N2)	17:12:35	1.0	Surface	1	1	18.76	8.09	31.27	96.70	6.7	2.7	2.5
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	SR10B(N2)	17:13:11	1.0	Surface	1	2	18.75	8.09	31.26	96.50	6.7	2.6	2.2
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	SR10B(N2)	17:12:24	3.7	Middle	2	1	18.53	8.08	32.34	80.70	5.6	3.1	4.0
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	SR10B(N2)	17:13:00	3.7	Middle	2	2	18.54	8.08	32.27	81.10	5.6	3.1	2.9
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	SR10B(N2)	17:12:14	6.4	Bottom	3	1	18.46	8.07	32.88	80.90	5.6	3.2	3.7
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	SR10B(N2)	17:12:48	6.4	Bottom	3	2	18.52	8.07	32.79	81.20	5.6	3.3	2.4
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	CS(2A)	14:57:08	1.0	Surface	1	1	18.96	8.11	28.49	100.30	7.1	3.2	2.7
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	CS(2A)	14:57:48	1.0	Surface	1	2	18.96	8.09	28.53	99.70	7.0	3.0	2.2
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	CS(2A)	14:56:58	3.3	Middle	2	1	18.56	8.10	30.52	83.30	5.9	3.3	2.6
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	CS(2A)	14:57:37	3.3	Middle	2	2	18.61	8.08	30.84	83.40	5.9	3.2	3.0
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	CS(2A)	14:56:48	5.5	Bottom	3	1	18.50	8.10	31.34	82.10	5.8	3.3	4.3
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	CS(2A)	14:57:25	5.5	Bottom	3	2	18.45	8.08	31.53	82.20	5.8	3.4	3.0
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	CS(Mf)5	16:41:43	1.0	Surface	1	1	18.95	8.08	33.22	84.60	6.0	2.6	2.9
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	CS(Mf)5	16:40:59	1.0	Surface	1	2	18.97	8.08	33.21	84.90	5.9	2.5	2.2
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	CS(Mf)5	16:40:42	6.4	Middle	2	1	18.50	8.04	34.62	82.80	5.8	2.7	3.8
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	CS(Mf)5	16:41:24	6.4	Middle	2	2	18.50	8.03	34.71	83.00	5.8	2.8	2.7
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	CS(Mf)5	16:41:14	11.7	Bottom	3	1	18.54	8.02	34.01	82.10	5.7	3.1	4.1
HKLR	HY/2011/03	2025-03-19	Mid-Ebb	Fine	CS(Mf)5	16:40:30	11.7	Bottom	3	2	18.51	8.04	34.99	81.80	5.7	3.0	3.0
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	IS5	09:45:51	1.0	Surface	1	1	18.92	8.08	32.36	85.40	5.9	2.8	3.2
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	IS5	09:45:08	1.0	Surface	1	2	18.93	8.09	32.28	87.80	6.1	2.8	2.2
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	IS5	09:44:52	4.3	Middle	2	1	18.69	8.05	33.83	84.00	5.8	3.3	2.8
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	IS5	09:45:35	4.3	Middle	2	2	18.70	8.05	33.84	83.20	5.8	3.4	3.1
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	IS5	09:45:23	7.5	Bottom	3	1	18.68	8.04	34.02	82.60	5.7	3.4	3.2
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	IS5	09:44:43	7.5	Bottom	3	2	18.68	8.05	34.07	83.30	5.8	3.3	2.9
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	IS(Mf)6	09:33:31	1.0	Surface	1	1	18.93	8.08	32.36	86.60	6.0	2.8	2.6
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	IS(Mf)6	09:33:49	1.0	Surface	1	2	18.93	8.08	32.36	86.60	6.0	2.7	3.6
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	IS(Mf)6	09:33:19	2.3	Bottom	3	1	18.84	8.07	32.68	86.60	6.0	3.2	3.7
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	IS(Mf)6	09:33:40	2.3	Bottom	3	2	18.86	8.07	32.66	85.90	5.9	3.2	2.4

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	IS7	09:24:19	1.0	Surface	1	1	18.92	8.08	32.38	87.40	6.0	2.5	2.6
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	IS7	09:24:00	1.0	Surface	1	2	18.87	8.09	32.42	87.60	6.0	2.6	1.9
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	IS7	09:24:07	2.3	Bottom	3	1	18.83	8.07	32.55	87.00	6.0	2.9	3.1
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	IS7	09:23:44	2.3	Bottom	3	2	18.81	8.08	32.58	88.00	6.1	2.8	2.1
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	IS8(N)	08:53:11	1.0	Surface	1	1	18.94	8.08	32.40	87.00	6.0	2.7	3.1
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	IS8(N)	08:53:39	1.0	Surface	1	2	18.92	8.08	32.49	86.40	6.0	2.6	2.4
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	IS8(N)	08:53:21	3.1	Bottom	3	1	18.77	8.06	33.61	85.90	6.0	2.9	2.4
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	IS8(N)	08:52:59	3.1	Bottom	3	2	18.76	8.07	33.55	86.80	6.0	3.1	1.7
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	IS(Mf)9	09:14:42	1.0	Surface	1	1	18.93	8.08	32.46	86.50	6.0	2.5	2.4
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	IS(Mf)9	09:15:00	1.0	Surface	1	2	18.94	8.08	32.44	86.60	6.0	2.4	2.2
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	IS(Mf)9	09:14:31	2.7	Bottom	3	1	18.82	8.07	32.70	86.40	6.0	2.8	3.0
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	IS(Mf)9	09:14:50	2.7	Bottom	3	2	18.83	8.07	32.77	86.10	5.9	2.9	2.9
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	IS10(N)	09:11:49	1.0	Surface	1	1	18.98	8.09	29.81	97.70	6.8	2.6	2.3
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	IS10(N)	09:11:10	1.0	Surface	1	2	18.98	8.08	29.80	97.50	6.8	2.8	2.9
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	IS10(N)	09:10:58	5.3	Middle	2	1	18.73	8.08	31.03	81.50	5.7	3.0	2.6
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	IS10(N)	09:11:35	5.3	Middle	2	2	18.75	8.08	31.05	81.10	5.7	2.9	2.5
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	IS10(N)	09:10:47	9.6	Bottom	3	1	18.68	8.07	31.34	79.70	5.6	3.3	2.4
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	IS10(N)	09:11:23	9.6	Bottom	3	2	18.77	8.08	31.31	79.60	5.6	3.4	2.6
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	SR3(N)	10:00:39	1.0	Surface	1	1	18.92	8.07	32.23	88.00	6.1	2.7	2.2
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	SR3(N)	10:01:00	1.0	Surface	1	2	18.93	8.07	32.17	87.80	6.1	2.5	3.0
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	SR3(N)	10:00:48	2.4	Bottom	3	1	18.87	8.07	32.65	87.20	6.1	3.3	3.3
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	SR3(N)	10:00:29	2.4	Bottom	3	2	18.85	8.06	32.54	87.70	6.1	3.2	2.1
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	SR4(N3)	09:01:05	1.0	Surface	1	1	18.94	8.07	32.76	86.70	6.0	2.6	3.1
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	SR4(N3)	09:01:25	1.0	Surface	1	2	18.94	8.06	32.80	87.10	6.0	2.6	3.4
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	SR4(N3)	09:01:15	2.9	Bottom	3	1	18.81	8.04	33.33	85.30	5.9	2.8	4.0
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	SR4(N3)	09:00:52	2.9	Bottom	3	2	18.76	8.05	33.46	85.60	5.9	2.7	3.7
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	SR5(N)	09:20:43	1	Surface	1	1	18.98	8.10	29.85	97.40	6.8	2.3	3.0
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	SR5(N)	09:20:05	1	Surface	1	2	19.01	8.10	29.87	97.60	6.8	2.4	2.5
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	SR5(N)	09:20:31	4.3	Middle	2	1	18.79	8.08	30.89	81.60	5.7	2.9	2.9
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	SR5(N)	09:19:52	4.3	Middle	2	2	18.80	8.08	30.83	81.50	5.7	2.9	2.5
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	SR5(N)	09:19:42	7.5	Bottom	3	1	18.75	8.08	31.22	81.70	5.7	3.2	4.2
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	SR5(N)	09:20:21	7.5	Bottom	3	2	18.82	8.08	31.07	81.70	5.7	3.3	3.2
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	SR10A(N)	08:20:52	1	Surface	1	1	18.90	8.09	31.32	97.00	6.7	2.0	1.8
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	SR10A(N)	08:21:48	1	Surface	1	2	18.77	8.08	31.83	95.70	6.7	2.1	2.1
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	SR10A(N)	08:20:36	6.0	Middle	2	1	18.51	8.06	33.42	79.70	5.5	2.4	2.8
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	SR10A(N)	08:21:30	6.0	Middle	2	2	18.53	8.06	33.32	79.10	5.5	2.3	3.4
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	SR10A(N)	08:21:20	11.0	Bottom	3	1	18.53	8.06	33.39	79.00	5.5	2.9	4.5
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	SR10A(N)	08:20:24	11.0	Bottom	3	2	18.51	8.06	33.47	80.30	5.6	3.0	3.3
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	SR10B(N2)	08:08:49	1.0	Surface	1	1	18.74	8.08	32.14	97.20	6.7	2.1	2.3
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	SR10B(N2)	08:08:07	1.0	Surface	1	2	18.77	8.07	32.06	98.80	6.8	2.2	2.6
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	SR10B(N2)	08:07:53	3.7	Middle	2	1	18.60	8.05	33.07	82.40	5.7	2.2	3.8
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	SR10B(N2)	08:08:33	3.7	Middle	2	2	18.58	8.06	33.07	81.20	5.6	2.2	3.3
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	SR10B(N2)	08:07:36	6.3	Bottom	3	1	18.51	8.05	33.39	81.60	5.7	3.1	3.9
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	SR10B(N2)	08:08:21	6.3	Bottom	3	2	18.55	8.06	33.32	80.80	5.6	3.0	2.7
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	CS(2(A)	10:11:26	1	Surface	1	1	19.07	8.11	29.76	98.10	6.9	3.0	3.8
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	CS(2(A)	10:10:52	1	Surface	1	2	19.07	8.13	29.73	97.30	6.8	2.8	2.9
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	CS(2(A)	10:10:40	3.4	Middle	2	1	18.57	8.10	32.03	81.30	5.7	2.9	2.7
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	CS(2(A)	10:11:15	3.4	Middle	2	2	18.56	8.09	32.01	81.70	5.7	2.9	2.8
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	CS(2(A)	10:10:29	5.7	Bottom	3	1	18.54	8.11	32.28	81.60	5.7	3.3	2.2
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	CS(2(A)	10:11:05	5.7	Bottom	3	2	18.55	8.09	32.26	81.80	5.7	3.4	2.9
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	CS(Mf)5	08:12:05	1.0	Surface	1	1	18.83	8.08	31.76	86.80	6.0	2.4	2.2
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	CS(Mf)5	08:12:59	1.0	Surface	1	2	18.89	8.07	31.71	87.20	6.0	2.4	2.8
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	CS(Mf)5	08:12:35	6.2	Middle	2	1	18.44	8.04	33.38	84.40	5.8	2.8	2.4
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	CS(Mf)5	08:11:51	6.2	Middle	2	2	18.45	8.05	33.25	85.20	5.9	2.8	3.3
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	CS(Mf)5	08:11:38	11.3	Bottom	3	1	18.41	8.04	33.63	83.40	5.8	3.1	4.4
HKLR	HY/2011/03	2025-03-19	Mid-Flood	Fine	CS(Mf)5	08:12:22	11.3	Bottom	3	2	18.44	8.04	33.64	82.50	5.7	3.2	3.4
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	IS5	16:13:11	1.0	Surface	1	1	18.84	8.09	32.88	90.30	6.5	3.0	4.8
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	IS5	16:13:50	1.0	Surface	1	2	18.85	8.09	32.83	89.70	6.5	3.0	4.6
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	IS5	16:13:36	4.3	Middle	2	1	18.67	8.07	33.51	88.70	6.4	3.2	5.1
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	IS5	16:12:59	4.3	Middle	2	2	18.66	8.07	33.51	88.90	6.4	3.2	5.0
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	IS5	16:12:50	7.6	Bottom	3	1	18.65	8.07	33.77	88.10	6.3	3.3	5.1
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	IS5	16:13:25	7.6	Bottom	3	2	18.67	8.07	33.74	88.20	6.3	3.4	4.4
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	IS(Mf)6	16:31:56	1.0	Surface	1	1	18.84	8.10	32.69	92.90	6.7	2.9	5.0
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	IS(Mf)6	16:31:39	1.0	Surface	1	2	18.84	8.10	32.67	92.20	6.6	3.0	4.5
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	IS(Mf)6	16:31:47	2.2	Bottom	3	1	18.81	8.10	32.84	91.60	6.6	3.2	4.4
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	IS(Mf)6	16:31:28	2.2	Bottom	3	2	18.79	8.11	32.87	91.20	6.5	3.2	5.1
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	IS7	16:43:00	1.0	Surface	1	1	18.87	8.11	32.79	93.20	6.7	2.8	4.9
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	IS7	16:42:41	1.0	Surface	1	2	18.85	8.10	32.79	92.60	6.6	2.9	5.1
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	IS7	16:42:49	2.3	Bottom	3	1	18.82	8.10	32.87	92.10	6.6	3.1	3.3
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	IS7	16:42:31	2.3	Bottom	3	2	18.79	8.11	32.91	91.60	6.6	3.0	4.3
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	IS8(N)	17:20:46	1.0	Surface	1	1	18.90	8.09	32.91	89.80	6.4	2.9	4.8
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	IS8(N)	17:21:04	1.0	Surface	1	2	18.91	8.09	32.89	90.20	6.5	2.8	3.9
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	IS8(N)	17:20:55	3.0	Bottom	3	1	18.86	8.09	33.05	89.50	6.4	3.1	4.7
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	IS8(N)	17:20:35	3.0	Bottom	3	2	18.82	8.09	33.10	88.90	6.4	3.1	4.2
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	IS(Mf)9	16:52:45	1.0	Surface	1	1	18.86	8.10	32.92	90.80	6.5	2.8	4.3
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	IS(Mf)9	16:52:24	1.0	Surface	1	2	18.86	8.11	32.90	90.60	6.5	2.9	4.4
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	IS(Mf)9	16:52:34	2.7	Bottom	3	1	18.81	8.10	33.08	90.30	6.5	3.1	5.5
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	IS(Mf)9	16:52:14	2.7	Bottom	3	2	18.80	8.11	33.07	90.20	6.5	3.1	4.4
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	IS10(N)	17:11:28	1.0	Surface	1	1	18.91	8.09	31.56	95.50	6.7	2.8	4.5
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	IS10(N)	17:12:06	1.0	Surface	1	2	18.96	8.09	31.49	96.40	6.7	2.8	5.6
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	IS10(N)	17:11:14	5.4	Middle	2	1	18.63	8.07	32.95	86.60	6.0	3.1	4.4
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	IS10(N)	17:11:51	5.4	Middle	2	2	18.64	8.08	32.93	87.00	6.1	3.2	5.0
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	IS10(N)	17:11:04	9.7	Bottom	3	1	18.62	8.07	33.36	87.20	6.1	3.2	5.0
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	IS10(N)	17:11:42	9.7	Bottom	3	2	18.66	8.07	33.13	87.20	6.1	3.3	3.8
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	SR3(N)	15:58:56	1.0	Surface	1	1	18.87	8.08	32.73	93.20	6.7	3.0	4.6
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	SR3(N)	15:58:37	1.0	Surface	1	2	18.87	8.09	32.65	91.20	6.6	3.0	5.0
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	SR3(N)	15:58:26	2.4	Bottom	3	1	18.82	8.09	32.97	90.00	6.4	3.1	5.9
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	SR3(N)	15:58:45	2.4	Bottom	3	2	18.84	8.08	32.93	90.90	6.6	3.1	4.9
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	SR4(N3)	17:09:03	1.0	Surface	1	1	18.84	8.09	32.85	90.00	6.4	2.7	3.1
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	SR4(N3)	17:08:46	1.0	Surface	1	2	18.86	8.09	32.77	89.50	6.4	2.7	4.3
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	SR4(N3)	17:08:55	2.9	Bottom	3	1	18.80	8.08	33.01	89.00	6.4	2.9	3.3
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	SR4(N3)	17:08:36	2.9	Bottom	3	2	18.78	8.08	33.02	88.70	6.4	2.9	3.5
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	SR5(N)	17:01:09	1.0	Surface	1	1	18.91	8.09	31.55	96.70	6.8	2.5	3.8
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	SR5(N)	17:00:33	1.0	Surface	1	2	18.89	8.10	31.55	96.40	6.7	2.5	4.6
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	SR5(N)	17:00:20	4.5	Middle	2	1	18.66	8.07	32.74	87.10	6.1	2.9	4.2
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	SR5(N)	17:00:57	4.5	Middle	2	2	18.66	8.06	32.77	87.30	6.1	2.8	4.2
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	SR5(N)	17:00:46	7.9	Bottom	3	1	18.66	8.06	33.16	87.80	6.1	3.3	4.6
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	SR5(N)	17:00:08	7.9	Bottom	3	2	18.63	8.08	33.23	87.70	6.1	3.2	3.8
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	SR10A(N)	17:59:31	1.0	Surface	1	1	18.72	8.11	32.39	96.30	6.7	2.6	5.0
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	SR10A(N)	18:00:18	1.0	Surface	1	2	18.72	8.10	32.40	96.70	6.7	2.6	4.3
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	SR10A(N)	17:59:58	6.7	Middle	2	1	18.48	8.09	33.53	86.70	6.0	2.8	5.3
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	SR10A(N)	17:59:16	6.7	Middle	2	2	18.46	8.10	33.58	87.60	6.1	2.7	4.9
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	SR10A(N)	17:59:03	12.3	Bottom	3	1	18.47	8.10	33.64	87.70	6.1	2.8	4.5
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	SR10A(N)	17:59:47	12.3	Bottom	3	2	18.51	8.09	33.55	86.90	6.0	2.8	3.8
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	SR10B(N2)	18:15:24	1.0	Surface	1	1	18.72	8.10	32.41	95.60	6.6	2.5	3.1
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	SR10B(N2)	18:16:03	1.0	Surface	1	2	18.71	8.10	32.42	95.20	6.6	2.5	3.1
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	SR10B(N2)	18:15:12	3.7	Middle	2	1	18.56	8.09	33.12	86.60	6.0	2.8	4.9
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	SR10B(N2)	18:15:51	3.7	Middle	2	2	18.55	8.09	33.08	86.80	6.0	2.8	5.4
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	SR10B(N2)	18:15:01	6.4	Bottom	3	1	18.51	8.08	33.47	86.60	6.0	2.9	4.4
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	SR10B(N2)	18:15:35	6.4	Bottom	3	2	18.55	8.08	33.39	86.70	6.0	3.0	3.8
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	CS(2(A)	16:03:14	1.0	Surface	1	1	18.79	8.11	31.40	99.50	7.0	2.9	3.5
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	CS(2(A)	16:03:51	1.0	Surface	1	2	18.80	8.10	31.40	98.90	6.9	2.8	4.5
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	CS(2(A)	16:03:05	3.4	Middle	2	1	18.53	8.09	32.83	89.90	6.3	3.2	4.1
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	CS(2(A)	16:03:40	3.4	Middle	2	2	18.57	8.09	33.00	89.60	6.3	3.1	4.3
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	CS(2(A)	16:02:54	5.7	Bottom	3	1	18.50	8.09	33.39	89.10	6.2	3.3	4.5
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	CS(2(A)	16:03:29	5.7	Bottom	3	2	18.49	8.08	33.49	89.10	6.2	3.4	4.9
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	CS(Mf)5	18:01:09	1.0	Surface	1	1	18.84	8.10	33.33	88.00	6.3	2.5	5.4
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	CS(Mf)5	18:00:18	1.0	Surface	1	2	18.86	8.10	33.34	88.30	6.3	2.4	4.6
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	CS(Mf)5	18:00:02	6.4	Middle	2	1	18.57	8.07	34.34	86.20	6.2	2.8	5.4
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	CS(Mf)5	18:00:44	6.4	Middle	2	2	18.59	8.06	34.37	86.20	6.2	2.8	4.3
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	CS(Mf)5	18:00:34	11.7	Bottom	3	1	18.57	8.06	33.96	85.70	6.1	3.0	5.2
HKLR	HY/2011/03	2025-03-21	Mid-Ebb	Fine	CS(Mf)5	17:59:50	11.7	Bottom	3	2	18.56	8.07	34.58	85.10	6.1	3.0	5.5
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	IS5	10:18:21	1.0	Surface	1	1	18.77	8.09	32.71	88.10	6.3	2.9	5.0
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	IS5	10:17:38	1.0	Surface	1	2	18.78	8.10	32.64	89.90	6.4	2.8	4.3
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	IS5	10:17:24	4.3	Middle	2	1	18.64	8.07	33.62	86.80	6.2	3.2	5.6

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	IS5	10:18:06	4.3	Middle	2	2	18.64	8.06	33.63	86.20	6.1	3.2	5.0
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	IS5	10:17:52	7.5	Bottom	3	1	18.62	8.06	33.73	85.60	6.1	3.2	5.5
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	IS5	10:17:14	7.5	Bottom	3	2	18.63	8.07	33.76	86.00	6.1	3.2	5.3
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	IS(Mf)6	10:06:45	1.0	Surface	1	1	18.79	8.09	32.67	90.40	6.4	2.8	5.2
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	IS(Mf)6	10:06:27	1.0	Surface	1	2	18.79	8.10	32.66	90.20	6.4	2.8	4.2
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	IS(Mf)6	10:06:35	2.2	Bottom	3	1	18.75	8.09	32.86	89.70	6.3	3.0	5.6
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	IS(Mf)6	10:06:12	2.2	Bottom	3	2	18.75	8.08	32.92	89.20	6.3	3.0	5.1
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	IS7	09:57:37	1.0	Surface	1	1	18.81	8.09	32.66	89.80	6.4	2.8	4.4
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	IS7	09:57:19	1.0	Surface	1	2	18.78	8.10	32.70	89.50	6.3	2.9	4.8
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	IS7	09:57:26	2.3	Bottom	3	1	18.76	8.09	32.80	89.30	6.3	3.1	3.7
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	IS7	09:57:07	2.3	Bottom	3	2	18.75	8.09	32.82	89.60	6.3	3.0	4.0
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	IS8(N)	09:21:03	1.0	Surface	1	1	18.80	8.09	32.70	90.20	6.4	2.5	4.2
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	IS8(N)	09:20:33	1.0	Surface	1	2	18.82	8.09	32.66	89.80	6.4	2.6	4.4
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	IS8(N)	09:20:42	3.1	Bottom	3	1	18.73	8.08	33.35	89.50	6.4	2.8	4.5
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	IS8(N)	09:20:22	3.1	Bottom	3	2	18.72	8.08	33.34	89.00	6.3	3.0	4.9
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	IS(Mf)9	09:48:13	1.0	Surface	1	1	18.81	8.10	32.72	90.10	6.4	2.6	4.6
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	IS(Mf)9	09:48:31	1.0	Surface	1	2	18.81	8.09	32.71	90.60	6.4	2.5	3.7
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	IS(Mf)9	09:48:20	2.6	Bottom	3	1	18.75	8.09	32.92	90.00	6.4	2.8	4.6
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	IS(Mf)9	09:48:02	2.6	Bottom	3	2	18.74	8.09	32.89	89.40	6.3	2.8	5.4
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	IS10(N)	09:36:22	1.0	Surface	1	1	18.77	8.09	32.14	96.30	6.7	2.8	3.7
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	IS10(N)	09:37:01	1.0	Surface	1	2	18.78	8.10	32.15	96.50	6.7	2.7	4.5
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	IS10(N)	09:36:48	5.4	Middle	2	1	18.63	8.09	33.02	87.40	6.1	2.9	5.1
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	IS10(N)	09:36:09	5.4	Middle	2	2	18.62	8.09	33.00	87.60	6.1	3.0	5.1
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	IS10(N)	09:36:36	9.7	Bottom	3	1	18.64	8.09	33.19	86.40	6.0	3.4	4.4
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	IS10(N)	09:35:59	9.7	Bottom	3	2	18.59	8.08	33.19	86.70	6.0	3.3	4.1
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	SR3(N)	10:33:01	1.0	Surface	1	1	18.78	8.08	32.62	89.40	6.4	2.7	5.3
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	SR3(N)	10:33:20	1.0	Surface	1	2	18.78	8.08	32.57	89.60	6.4	2.6	5.7
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	SR3(N)	10:32:52	2.2	Bottom	3	1	18.74	8.08	32.82	89.10	6.3	3.0	5.0
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	SR3(N)	10:33:10	2.2	Bottom	3	2	18.76	8.08	32.89	88.90	6.3	3.0	4.6
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	SR4(N3)	09:30:21	1.0	Surface	1	1	18.80	8.09	32.85	90.20	6.4	2.5	3.4
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	SR4(N3)	09:30:38	1.0	Surface	1	2	18.81	8.08	32.88	90.60	6.4	2.5	4.2
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	SR4(N3)	09:30:29	2.9	Bottom	3	1	18.73	8.07	33.20	89.60	6.4	2.6	5.8
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	SR4(N3)	09:30:08	2.9	Bottom	3	2	18.71	8.07	33.29	89.30	6.3	2.6	5.2
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	SR5(N)	09:47:07	1	Surface	1	1	18.78	8.11	32.20	95.50	6.7	2.5	5.0
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	SR5(N)	09:46:26	1	Surface	1	2	18.80	8.11	32.21	95.50	6.7	2.6	4.2
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	SR5(N)	09:46:54	4.5	Middle	2	1	18.65	8.09	32.91	87.10	6.1	2.8	3.2
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	SR5(N)	09:46:13	4.5	Middle	2	2	18.66	8.09	32.89	87.10	6.1	2.9	4.0
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	SR5(N)	09:46:02	7.9	Bottom	3	1	18.62	8.09	33.15	87.20	6.1	3.2	3.4
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	SR5(N)	09:46:43	7.9	Bottom	3	2	18.66	8.09	33.06	87.20	6.1	3.3	4.4
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	SR10A(N)	08:38:53	1	Surface	1	1	18.69	8.09	32.46	94.70	6.6	2.1	5.1
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	SR10A(N)	08:38:04	1	Surface	1	2	18.78	8.10	32.16	95.40	6.6	2.1	5.1
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	SR10A(N)	08:37:48	6.4	Middle	2	1	18.52	8.07	33.49	86.20	6.0	2.4	5.8
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	SR10A(N)	08:38:36	6.4	Middle	2	2	18.53	8.07	33.45	85.50	5.9	2.3	5.5
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	SR10A(N)	08:38:26	11.7	Bottom	3	1	18.55	8.07	33.49	85.60	5.9	2.8	4.3
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	SR10A(N)	08:37:38	11.7	Bottom	3	2	18.53	8.07	33.54	86.40	6.0	2.8	3.4
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	SR10B(N2)	08:28:51	1.0	Surface	1	1	18.70	8.09	32.60	98.00	6.8	2.1	4.6
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	SR10B(N2)	08:28:09	1.0	Surface	1	2	18.72	8.07	32.55	98.40	6.8	2.2	4.8
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	SR10B(N2)	08:27:54	3.8	Middle	2	1	18.59	8.06	33.19	89.10	6.2	2.3	5.3
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	SR10B(N2)	08:28:35	3.8	Middle	2	2	18.58	8.07	33.19	87.70	6.1	2.2	5.2
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	SR10B(N2)	08:28:24	6.5	Bottom	3	1	18.56	8.06	33.41	87.30	6.0	2.7	4.4
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	SR10B(N2)	08:27:40	6.5	Bottom	3	2	18.53	8.06	33.45	87.70	6.1	2.8	5.1
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	CS2(A)	10:41:07	1	Surface	1	1	18.80	8.11	32.14	96.60	6.7	3.0	5.2
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	CS2(A)	10:40:29	1	Surface	1	2	18.79	8.12	32.14	96.20	6.7	2.9	5.3
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	CS2(A)	10:40:18	3.4	Middle	2	1	18.52	8.11	33.49	87.80	6.1	3.1	3.8
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	CS2(A)	10:40:55	3.4	Middle	2	2	18.51	8.10	33.50	88.00	6.1	3.0	4.8
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	CS2(A)	10:40:07	5.8	Bottom	3	1	18.50	8.11	33.71	87.90	6.1	3.3	4.4
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	CS2(A)	10:40:45	5.8	Bottom	3	2	18.51	8.10	33.71	88.00	6.1	3.4	5.1
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	CS(Mf)5	08:38:41	1.0	Surface	1	1	18.77	8.07	32.27	89.60	6.4	2.3	4.4
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	CS(Mf)5	08:37:54	1.0	Surface	1	2	18.74	8.07	32.31	89.20	6.3	2.3	4.0
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	CS(Mf)5	08:38:22	6.2	Middle	2	1	18.52	8.05	33.37	87.40	6.2	2.6	3.4
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	CS(Mf)5	08:37:39	6.2	Middle	2	2	18.52	8.05	33.29	87.60	6.2	2.6	3.9
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	CS(Mf)5	08:37:26	11.4	Bottom	3	1	18.51	8.04	33.59	86.00	6.1	2.9	4.4
HKLR	HY/2011/03	2025-03-21	Mid-Flood	Fine	CS(Mf)5	08:38:10	11.4	Bottom	3	2	18.51	8.05	33.59	86.00	6.1	2.9	4.1
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	IS5	20:28:42	1.0	Surface	1	1	18.72	8.08	32.72	89.00	6.5	3.1	2.6
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	IS5	20:29:19	1.0	Surface	1	2	18.74	8.09	32.69	88.70	6.5	3.1	1.8
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	IS5	20:29:06	4.3	Middle	2	1	18.58	8.05	33.16	87.70	6.5	3.3	2.2
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	IS5	20:28:31	4.3	Middle	2	2	18.56	8.05	33.17	87.60	6.4	3.2	2.1
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	IS5	20:28:21	7.6	Bottom	3	1	18.53	8.05	33.51	86.50	6.4	3.4	2.8
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	IS5	20:28:55	7.6	Bottom	3	2	18.54	8.04	33.50	87.40	6.4	3.4	2.6
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	IS(Mf)6	20:42:48	1.0	Surface	1	1	18.73	8.09	32.70	91.60	6.7	2.9	2.0
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	IS(Mf)6	20:42:30	1.0	Surface	1	2	18.75	8.09	32.43	91.20	6.7	2.9	1.6
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	IS(Mf)6	20:42:38	2.2	Bottom	3	1	18.71	8.09	32.80	90.00	6.6	3.1	2.1
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	IS(Mf)6	20:42:08	2.2	Bottom	3	2	18.69	8.10	32.73	89.00	6.5	3.2	2.5
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	IS7	20:52:53	1.0	Surface	1	1	18.78	8.10	32.71	92.40	6.8	2.7	4.1
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	IS7	20:52:36	1.0	Surface	1	2	18.75	8.10	32.83	90.80	6.7	2.8	3.6
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	IS7	20:52:27	2.4	Bottom	3	1	18.73	8.10	32.79	89.00	6.5	2.9	3.8
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	IS7	20:52:43	2.4	Bottom	3	2	18.73	8.10	32.87	89.80	6.6	2.9	3.0
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	IS8(N)	21:29:19	1.0	Surface	1	1	18.78	8.09	32.73	88.80	6.5	2.9	2.3
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	IS8(N)	21:29:37	1.0	Surface	1	2	18.79	8.08	32.71	90.00	6.6	2.8	3.1
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	IS8(N)	21:29:28	3.0	Bottom	3	1	18.76	8.08	32.84	88.70	6.5	3.0	2.7
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	IS8(N)	21:29:09	3.0	Bottom	3	2	18.72	8.08	32.88	87.50	6.4	3.0	4.0
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	IS(Mf)9	21:02:47	1.0	Surface	1	1	18.74	8.09	32.85	89.20	6.6	2.7	2.0
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	IS(Mf)9	21:02:27	1.0	Surface	1	2	18.74	8.10	32.81	88.60	6.5	2.8	2.6
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	IS(Mf)9	21:02:37	2.6	Bottom	3	1	18.73	8.09	32.87	88.70	6.5	2.9	2.6
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	IS(Mf)9	21:02:18	2.6	Bottom	3	2	18.71	8.10	32.95	88.30	6.5	2.9	1.5
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	IS10(N)	21:33:30	1.0	Surface	1	1	19.05	8.09	31.52	90.40	6.3	2.6	1.3
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	IS10(N)	21:34:11	1.0	Surface	1	2	19.09	8.09	31.48	91.10	6.3	2.6	1.1
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	IS10(N)	21:33:56	5.4	Middle	2	1	18.79	8.07	32.89	85.40	5.9	2.9	1.5
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	IS10(N)	21:33:17	5.4	Middle	2	2	18.78	8.06	32.90	84.80	5.9	2.9	1.6
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	IS10(N)	21:33:06	9.7	Bottom	3	1	18.78	8.06	33.16	85.00	5.9	3.0	2.3
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	IS10(N)	21:33:45	9.7	Bottom	3	2	18.82	8.06	33.04	85.10	5.9	3.1	2.2
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	SR3(N)	20:14:54	1.0	Surface	1	1	18.76	8.09	32.64	91.20	6.7	3.0	2.1
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	SR3(N)	20:14:35	1.0	Surface	1	2	18.75	8.09	32.57	89.90	6.6	3.1	2.9
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	SR3(N)	20:14:24	2.3	Bottom	3	1	18.69	8.09	32.85	87.30	6.2	3.2	2.1
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	SR3(N)	20:14:43	2.3	Bottom	3	2	18.75	8.09	32.58	89.30	6.6	3.1	1.5
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	SR4(N3)	21:19:10	1.0	Surface	1	1	18.74	8.09	32.66	90.40	6.6	2.7	2.5
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	SR4(N3)	21:18:52	1.0	Surface	1	2	18.77	8.09	32.53	89.30	6.6	2.7	1.8
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	SR4(N3)	21:18:42	2.9	Bottom	3	1	17.98	8.07	32.92	87.40	6.4	2.9	2.1
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	SR4(N3)	21:19:01	2.9	Bottom	3	2	18.73	8.08	32.81	88.70	6.5	2.9	2.0
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	SR5(N)	21:23:51	1.0	Surface	1	1	19.06	8.10	31.50	91.50	6.3	2.6	2.4
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	SR5(N)	21:23:12	1.0	Surface	1	2	19.03	8.10	31.53	91.10	6.3	2.6	1.5
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	SR5(N)	21:22:59	4.6	Middle	2	1	18.82	8.07	32.72	85.00	5.9	3.0	1.9
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	SR5(N)	21:23:39	4.6	Middle	2	2	18.82	8.06	32.74	85.20	5.9	2.9	2.2
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	SR5(N)	21:23:26	8.1	Bottom	3	1	18.81	8.06	33.07	85.60	5.9	3.3	2.8
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	SR5(N)	21:22:47	8.1	Bottom	3	2	18.78	8.06	33.13	85.00	5.9	3.2	1.5
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	SR10A(N)	22:22:14	1.0	Surface	1	1	18.94	8.11	32.44	92.00	6.3	2.4	1.8
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	SR10A(N)	22:21:25	1.0	Surface	1	2	18.96	8.12	32.40	91.80	6.3	2.4	1.8
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	SR10A(N)	22:21:55	6.8	Middle	2	1	18.72	8.09	33.53	85.50	5.9	2.6	2.0
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	SR10A(N)	22:21:09	6.8	Middle	2	2	18.70	8.10	33.65	86.10	5.9	2.6	2.1
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	SR10A(N)	22:20:53	12.5	Bottom	3	1	18.71	8.11	33.67	86.10	5.9	2.7	2.2
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	SR10A(N)	22:21:43	12.5	Bottom	3	2	18.73	8.09	33.60	85.60	5.9	2.8	3.0
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	SR10B(N2)	22:34:36	1.0	Surface	1	1	18.96	8.11	32.39	91.10	6.3	2.3	3.6
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	SR10B(N2)	22:35:16	1.0	Surface	1	2	18.95	8.11	32.41	91.00	6.3	2.3	2.4
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	SR10B(N2)	22:34:24	3.8	Middle	2	1	18.78	8.09	33.21	85.50	5.9	2.5	3.1
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	SR10B(N2)	22:35:03	3.8	Middle	2	2	18.78	8.09	33.16	85.80	5.9	2.5	2.2
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	SR10B(N2)	22:34:13	6.5	Bottom	3	1	18.73	8.08	33.50	85.20	5.9	2.7	1.7
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	SR10B(N2)	22:34:48	6.5	Bottom	3	2	18.77	8.08	33.43	85.30	5.9	2.8	2.0
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	CS2(A)	20:20:57	1.0	Surface	1	1	18.96	8.11	31.50	94.00	6.5	2.7	1.9
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	CS2(A)	20:21:30	1.0	Surface	1	2	18.97	8.10	31.50	93.60	6.5	2.7	2.3
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	CS2(A)	20:20:44	3.3	Middle	2	1	18.76	8.08	32.69	87.50	6.1	3.1	2.1
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	CS2(A)	20:21:19	3.3	Middle	2	2	18.79	8.08	32.78	87.70	6.1	3.0	3.0
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	CS2(A)	20:20:34	5.6	Bottom	3	1	18.73	8.09	33.17	86.80	6.0	3.2	1.5
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	CS2(A)	20:21:10	5.6	Bottom	3	2	18.75	8.08	33.17	87.20	6.0	3.3	1.1
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	CS(Mf)5	22:10:21	1.0	Surface	1	1	18.73	8.09	33.10	87.50	6.4	2.5	3.3
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	CS(Mf)5	22:09:36	1.0	Surface	1	2	18.73	8.09	33.10	87.10	6.4	2.5	3.6

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	CS(Mf)5	22:09:21	6.4	Middle	2	1	18.41	8.04	34.28	85.10	6.3	2.8	2.6
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	CS(Mf)5	22:10:02	6.4	Middle	2	2	18.43	8.03	34.28	84.80	6.2	2.7	1.8
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	CS(Mf)5	22:09:52	11.8	Bottom	3	1	18.43	8.04	34.00	83.60	6.1	2.9	3.0
HKLR	HY/2011/03	2025-03-24	Mid-Ebb	Fine	CS(Mf)5	22:09:10	11.8	Bottom	3	2	18.41	8.04	34.49	82.90	6.1	2.9	2.0
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	IS5	09:38:07	1.0	Surface	1	1	18.66	8.09	32.57	86.60	6.0	3.0	3.3
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	IS5	09:37:23	1.0	Surface	1	2	18.67	8.09	32.54	87.80	6.1	2.9	2.4
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	IS5	09:37:10	4.3	Middle	2	1	18.47	8.04	33.49	83.70	5.8	3.3	2.5
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	IS5	09:37:53	4.3	Middle	2	2	18.48	8.04	33.48	83.70	5.8	3.3	3.5
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	IS5	09:37:37	7.5	Bottom	3	1	18.47	8.04	33.42	82.10	5.7	3.3	2.5
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	IS5	09:36:59	7.5	Bottom	3	2	18.47	8.04	33.46	82.30	5.7	3.3	3.4
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	IS(Mf)6	09:27:40	1.0	Surface	1	1	18.68	8.09	32.48	89.50	6.2	2.9	2.2
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	IS(Mf)6	09:27:58	1.0	Surface	1	2	18.67	8.09	32.59	89.90	6.2	2.9	3.4
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	IS(Mf)6	09:27:48	2.3	Bottom	3	1	18.63	8.08	32.80	88.70	6.1	3.1	2.9
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	IS(Mf)6	09:27:27	2.3	Bottom	3	2	18.62	8.07	32.82	88.60	6.1	3.1	1.7
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	IS7	09:18:54	1.0	Surface	1	1	18.69	8.08	32.66	88.60	6.1	2.9	2.4
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	IS7	09:18:36	1.0	Surface	1	2	18.67	8.09	32.65	88.00	6.1	3.0	1.6
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	IS7	09:18:43	2.3	Bottom	3	1	18.65	8.07	32.63	87.80	6.1	3.1	2.4
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	IS7	09:18:26	2.3	Bottom	3	2	18.62	8.07	32.85	87.20	6.0	3.1	1.7
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	IS8(N)	08:45:15	1.0	Surface	1	1	18.68	8.08	32.71	88.70	6.1	2.8	2.4
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	IS8(N)	08:44:29	1.0	Surface	1	2	18.68	8.08	32.72	88.50	6.1	2.9	2.0
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	IS8(N)	08:44:37	3.1	Bottom	3	1	18.61	8.06	33.02	87.60	6.1	3.0	1.7
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	IS8(N)	08:44:18	3.1	Bottom	3	2	18.59	8.06	33.21	87.60	6.1	3.2	1.4
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	IS(Mf)9	09:10:11	1.0	Surface	1	1	18.69	8.09	32.51	89.10	6.2	2.7	1.2
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	IS(Mf)9	09:09:54	1.0	Surface	1	2	18.68	8.09	32.69	88.00	6.1	2.8	1.8
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	IS(Mf)9	09:10:02	2.6	Bottom	3	1	18.62	8.07	32.90	87.90	6.1	3.0	2.2
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	IS(Mf)9	09:09:44	2.6	Bottom	3	2	18.60	8.06	32.75	87.20	6.0	2.9	1.8
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	IS10(N)	09:03:33	1.0	Surface	1	1	18.91	8.10	32.10	90.60	6.3	2.5	1.6
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	IS10(N)	09:02:53	1.0	Surface	1	2	18.89	8.09	32.11	90.40	6.3	2.5	1.6
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	IS10(N)	09:03:20	5.4	Middle	2	1	18.75	8.08	33.13	84.60	5.9	2.8	1.8
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	IS10(N)	09:02:40	5.4	Middle	2	2	18.74	8.07	33.12	84.90	5.9	2.8	2.5
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	IS10(N)	09:03:09	9.7	Bottom	3	1	18.76	8.07	33.24	84.00	5.8	3.1	1.6
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	IS10(N)	09:02:28	9.7	Bottom	3	2	18.73	8.07	33.26	84.00	5.8	3.1	2.2
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	SR3(N)	09:51:12	1.0	Surface	1	1	18.68	8.08	32.38	89.00	6.2	2.7	1.6
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	SR3(N)	09:50:55	1.0	Surface	1	2	18.67	8.08	32.59	88.40	6.1	2.8	2.0
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	SR3(N)	09:50:46	2.3	Bottom	3	1	18.64	8.08	32.58	87.80	6.1	3.1	2.1
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	SR3(N)	09:51:03	2.3	Bottom	3	2	18.65	8.08	32.72	87.90	6.1	3.0	1.7
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	SR4(N3)	08:53:38	1.0	Surface	1	1	18.68	8.08	32.60	88.40	6.1	2.7	2.2
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	SR4(N3)	08:53:56	1.0	Surface	1	2	18.67	8.08	32.73	88.20	6.1	2.7	1.9
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	SR4(N3)	08:53:47	2.9	Bottom	3	1	18.58	8.05	33.11	86.90	6.0	2.9	1.6
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	SR4(N3)	08:53:26	2.9	Bottom	3	2	18.56	8.05	33.27	86.80	6.0	2.8	2.1
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	SR5(N)	09:14:01	1	Surface	1	1	18.89	8.10	32.15	89.50	6.2	2.4	2.7
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	SR5(N)	09:13:20	1	Surface	1	2	18.90	8.10	32.14	89.70	6.2	2.4	2.2
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	SR5(N)	09:13:47	4.6	Middle	2	1	18.76	8.08	32.97	84.30	5.8	2.6	1.7
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	SR5(N)	09:13:06	4.6	Middle	2	2	18.77	8.08	32.99	84.40	5.8	2.7	1.1
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	SR5(N)	09:12:56	8.2	Bottom	3	1	18.74	8.07	33.26	84.20	5.8	3.0	1.7
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	SR5(N)	09:13:36	8.2	Bottom	3	2	18.76	8.07	33.19	84.10	5.8	3.0	1.8
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	SR10A(N)	08:10:57	1	Surface	1	1	18.87	8.09	32.43	89.30	6.2	2.1	2.5
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	SR10A(N)	08:10:07	1	Surface	1	2	18.92	8.09	32.26	89.70	6.2	2.2	1.7
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	SR10A(N)	08:10:40	6.6	Middle	2	1	18.70	8.06	33.56	83.30	5.7	2.3	2.3
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	SR10A(N)	08:09:51	6.6	Middle	2	2	18.69	8.06	33.58	83.70	5.8	2.4	2.7
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	SR10A(N)	08:10:30	12.1	Bottom	3	1	18.73	8.06	33.64	83.10	5.7	2.7	1.3
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	SR10A(N)	08:09:40	12.1	Bottom	3	2	18.71	8.06	33.67	83.80	5.8	2.7	1.7
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	SR10B(N2)	08:01:41	1.0	Surface	1	1	18.89	8.09	32.49	93.20	6.4	2.2	1.5
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	SR10B(N2)	08:01:00	1.0	Surface	1	2	18.90	8.07	32.46	93.20	6.4	2.2	1.9
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	SR10B(N2)	08:00:45	3.8	Middle	2	1	18.77	8.05	33.16	87.20	6.0	2.4	3.0
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	SR10B(N2)	08:01:26	3.8	Middle	2	2	18.77	8.06	33.14	86.10	5.9	2.3	2.2
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	SR10B(N2)	08:01:16	6.5	Bottom	3	1	18.75	8.05	33.47	85.10	5.9	2.7	1.5
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	SR10B(N2)	08:00:32	6.5	Bottom	3	2	18.54	8.04	33.53	85.20	5.9	2.7	2.0
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	CS2(A)	10:12:14	1	Surface	1	1	18.90	8.10	32.10	90.40	6.3	2.6	2.2
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	CS2(A)	10:11:37	1	Surface	1	2	18.89	8.11	32.12	90.20	6.3	2.5	2.0
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	CS2(A)	10:12:02	3.4	Middle	2	1	18.71	8.09	33.16	85.50	5.9	2.7	1.5
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	CS2(A)	10:11:26	3.4	Middle	2	2	18.72	8.10	33.16	85.30	5.9	2.8	1.8
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	CS2(A)	10:11:14	5.7	Bottom	3	1	18.69	8.09	33.49	85.00	5.9	3.0	2.7
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	CS2(A)	10:11:53	5.7	Bottom	3	2	18.71	8.09	33.47	85.00	5.9	3.1	1.7
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	CS(Mf)5	07:52:34	1.0	Surface	1	1	18.67	8.07	32.36	87.50	6.1	2.6	2.4
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	CS(Mf)5	07:51:49	1.0	Surface	1	2	18.66	8.07	32.38	86.70	6.0	2.6	1.6
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	CS(Mf)5	07:52:17	6.3	Middle	2	1	18.40	8.02	33.50	84.30	5.8	2.8	2.3
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	CS(Mf)5	07:51:34	6.3	Middle	2	2	18.41	8.02	33.45	83.90	5.8	2.8	2.1
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	CS(Mf)5	07:51:22	11.5	Bottom	3	1	18.40	8.01	33.72	82.40	5.7	3.0	1.7
HKLR	HY/2011/03	2025-03-24	Mid-Flood	Fine	CS(Mf)5	07:52:05	11.5	Bottom	3	2	18.44	8.03	33.77	81.80	5.6	3.1	2.0
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	IS5	10:29:19	1.0	Surface	1	1	19.72	8.00	32.02	91.10	6.1	3.3	4.2
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	IS5	10:30:04	1.0	Surface	1	2	19.72	8.00	31.95	90.50	6.0	3.3	3.4
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	IS5	10:29:08	4.1	Middle	2	1	19.65	7.99	31.91	90.80	6.1	3.3	3.7
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	IS5	10:29:44	4.1	Middle	2	2	19.69	8.02	32.46	89.80	6.0	3.2	3.5
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	IS5	10:28:52	7.2	Bottom	3	1	19.42	8.00	32.41	90.80	6.1	3.3	3.8
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	IS5	10:29:33	7.2	Bottom	3	2	19.74	8.01	32.45	89.70	6.0	3.3	3.3
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	IS(Mf)6	10:40:55	1.0	Surface	1	1	19.64	7.97	31.90	90.50	6.0	3.3	3.9
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	IS(Mf)6	10:41:18	1.0	Surface	1	2	19.64	7.97	31.89	90.80	6.0	3.3	4.0
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	IS(Mf)6	10:40:38	2.0	Bottom	3	1	19.50	7.97	32.13	90.40	6.0	3.3	3.6
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	IS(Mf)6	10:41:07	2.0	Bottom	3	2	19.54	7.97	32.10	90.10	6.0	3.3	3.4
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	IS7	10:49:34	1.0	Surface	1	1	19.68	8.00	32.02	91.50	6.1	3.2	4.7
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	IS7	10:49:49	1.0	Surface	1	2	19.75	8.01	31.98	91.70	6.1	3.3	3.6
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	IS7	10:49:16	2.0	Bottom	3	1	19.57	7.99	32.26	91.70	6.1	3.2	2.6
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	IS7	10:49:42	2.0	Bottom	3	2	19.58	8.00	32.25	91.60	6.1	3.3	3.0
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	IS8(N)	11:24:30	1.0	Surface	1	1	19.72	7.98	31.90	91.90	6.2	3.3	3.9
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	IS8(N)	11:24:54	1.0	Surface	1	2	19.71	7.98	31.95	91.70	6.1	3.2	5.4
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	IS8(N)	11:24:13	2.8	Bottom	3	1	19.69	7.97	32.43	91.70	6.1	3.2	4.0
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	IS8(N)	11:24:42	2.8	Bottom	3	2	19.66	7.97	32.11	91.60	6.1	3.2	4.8
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	IS(Mf)9	11:01:19	1.0	Surface	1	1	19.68	7.98	31.94	91.80	6.1	3.2	4.0
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	IS(Mf)9	11:01:57	1.0	Surface	1	2	19.67	7.98	31.94	91.60	6.1	3.4	5.0
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	IS(Mf)9	11:01:09	2.6	Bottom	3	1	19.65	7.98	32.09	91.70	6.1	3.3	2.6
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	IS(Mf)9	11:01:28	2.6	Bottom	3	2	19.62	7.98	32.13	91.80	6.1	3.3	3.4
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	IS10(N)	11:17:03	1.0	Surface	1	1	19.51	8.11	32.10	82.90	6.0	3.3	4.0
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	IS10(N)	11:17:47	1.0	Surface	1	2	19.51	8.11	32.11	82.60	5.9	3.3	3.2
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	IS10(N)	11:16:49	4.5	Middle	2	1	19.26	8.10	32.14	82.80	6.0	3.2	3.4
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	IS10(N)	11:17:32	4.5	Middle	2	2	19.22	8.10	32.13	82.30	5.9	3.3	4.3
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	IS10(N)	11:16:37	8.0	Bottom	3	1	19.30	8.10	31.66	83.60	6.0	3.2	4.3
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	IS10(N)	11:17:24	8.0	Bottom	3	2	19.29	8.10	31.69	82.10	5.9	3.3	4.5
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	SR3(N)	10:16:21	1.0	Surface	1	1	19.41	8.00	31.85	91.40	6.1	3.2	4.2
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	SR3(N)	10:16:44	1.0	Surface	1	2	19.44	8.00	31.81	91.70	6.1	3.4	4.0
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	SR3(N)	10:16:05	2.0	Bottom	3	1	19.43	8.00	32.13	91.30	6.1	3.2	3.6
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	SR3(N)	10:16:28	2.0	Bottom	3	2	19.63	8.01	31.96	91.00	6.1	3.3	3.4
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	SR4(N3)	11:15:07	1.0	Surface	1	1	19.74	8.02	32.05	91.10	6.1	3.3	3.8
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	SR4(N3)	11:15:37	1.0	Surface	1	2	19.75	8.02	32.06	90.90	6.1	3.3	3.2
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	SR4(N3)	11:14:46	2.6	Bottom	3	1	19.67	8.01	32.26	90.90	6.1	3.3	3.7
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	SR4(N3)	11:15:17	2.6	Bottom	3	2	19.70	8.02	32.32	90.80	6.0	3.3	3.0
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	SR5(N)	11:06:02	1.0	Surface	1	1	19.44	8.10	31.99	82.90	6.0	3.2	3.3
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	SR5(N)	11:06:30	1.0	Surface	1	2	19.45	8.11	31.97	82.40	5.9	3.4	4.3
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	SR5(N)	11:05:54	4.5	Middle	2	1	19.18	8.10	31.61	82.60	5.9	3.3	3.0
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	SR5(N)	11:06:21	4.5	Middle	2	2	19.19	8.10	31.60	82.10	5.9	3.3	3.1
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	SR5(N)	11:05:43	8.0	Bottom	3	1	19.23	8.10	32.09	81.90	5.9	3.2	3.3
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	SR5(N)	11:06:13	8.0	Bottom	3	2	19.25	8.10	31.97	81.80	5.9	3.4	3.5
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	SR10A(N)	12:09:34	1.0	Surface	1	1	19.33	8.11	31.71	82.80	6.0	3.4	3.1
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	SR10A(N)	12:10:07	1.0	Surface	1	2	19.36	8.11	31.66	82.40	5.9	3.3	3.1
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	SR10A(N)	12:09:24	5.7	Middle	2	1	19.10	8.11	32.15	82.70	5.9	3.3	3.4
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	SR10A(N)	12:09:56	5.7	Middle	2	2	19.10	8.11	32.15	82.30	5.9	3.3	4.0
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	SR10A(N)	12:09:06	10.4	Bottom	3	1	19.12	8.11	32.06	82.00	5.9	3.3	3.8
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	SR10A(N)	12:09:46	10.4	Bottom	3	2	19.14	8.10	32.04	81.90	5.9	3.3	4.7
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	SR10B(N2)	12:21:45	1.0	Surface	1	1	19.49	8.11	32.15	83.60	6.0	3.1	3.3
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	SR10B(N2)	12:22:26	1.0	Surface	1	2	19.50	8.11	32.15	83.40	6.0	3.1	2.4
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	SR10B(N2)	12:21:34	3.8	Middle	2	1	19.23	8.10	32.10	83.60	6.0	3.3	3.2
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	SR10B(N2)	12:22:03	3.8	Middle	2	2	19.24	8.11	32.09	83.20	6.0	3.2	3.2
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	SR10B(N2)	12:21:24	6.6	Bottom	3	1	19.31	8.10	31.58	83.00	6.0	3.2	2.8
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	SR10B(N2)	12:21:55	6.6	Bottom	3	2	19.32	8.11	31.46	82.80	6.0	3.2	3.2
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	CS2(A)	10:20:06	1.0	Surface	1	1	19.55	8.11	31.56	83.30	6.0	3.1	3.3

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	CS2(A)	10:20:33	1.0	Surface	1	2	19.55	8.11	31.60	83.30	6.0	3.3	3.6
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	CS2(A)	10:19:56	3.1	Middle	2	1	19.55	8.10	32.05	82.50	6.0	3.1	3.4
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	CS2(A)	10:20:23	3.1	Middle	2	2	19.55	8.10	32.07	82.90	6.0	3.2	3.6
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	CS2(A)	10:19:45	5.2	Bottom	3	1	19.54	8.11	32.05	82.40	6.0	3.1	3.9
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	CS2(A)	10:20:15	5.2	Bottom	3	2	19.54	8.11	32.11	82.80	6.0	3.2	2.9
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	CS(Mf)5	12:06:28	1.0	Surface	1	1	19.71	7.98	32.03	89.20	5.9	3.3	4.3
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	CS(Mf)5	12:07:10	1.0	Surface	1	2	19.64	7.99	31.90	89.00	5.9	3.3	4.4
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	CS(Mf)5	12:06:11	6.0	Middle	2	1	19.46	7.98	32.51	88.60	5.9	3.3	4.6
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	CS(Mf)5	12:06:56	6.0	Middle	2	2	19.44	7.98	32.50	88.90	5.9	3.2	4.0
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	CS(Mf)5	12:05:56	11.0	Bottom	3	1	19.43	7.98	32.49	88.20	5.9	3.3	3.5
HKLR	HY/2011/03	2025-03-26	Mid-Ebb	Sunny	CS(Mf)5	12:06:38	11.0	Bottom	3	2	19.42	7.98	32.44	88.60	5.9	3.3	3.2
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	IS5	06:46:56	1.0	Surface	1	1	19.68	8.00	31.89	93.60	6.2	3.2	4.4
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	IS5	06:47:42	1.0	Surface	1	2	19.56	8.01	31.75	93.20	6.2	3.2	3.4
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	IS5	06:46:37	4.2	Middle	2	1	19.68	8.00	32.35	93.50	6.2	3.2	2.5
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	IS5	06:47:21	4.2	Middle	2	2	19.70	8.00	32.34	92.20	6.2	3.3	2.6
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	IS5	06:46:19	7.4	Bottom	3	1	19.60	8.00	32.39	93.40	6.2	3.2	3.0
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	IS5	06:47:09	7.4	Bottom	3	2	19.42	8.00	32.39	91.70	6.1	3.2	2.5
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	IS(Mf)6	06:37:02	1.0	Surface	1	1	19.64	8.02	31.73	90.50	6.0	3.3	4.4
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	IS(Mf)6	06:37:29	1.0	Surface	1	2	19.51	8.02	31.74	90.40	6.0	3.4	3.0
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	IS(Mf)6	06:36:53	2.2	Bottom	3	1	19.44	8.01	31.93	90.40	6.0	3.3	2.4
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	IS(Mf)6	06:37:19	2.2	Bottom	3	2	19.45	8.01	31.99	90.20	6.0	3.4	2.4
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	IS7	06:27:56	1.0	Surface	1	1	19.67	8.04	31.75	91.00	6.1	3.2	3.0
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	IS7	06:28:23	1.0	Surface	1	2	19.69	8.04	31.74	91.00	6.1	3.2	3.8
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	IS7	06:27:32	2.0	Bottom	3	1	19.58	8.03	32.07	90.60	6.1	3.2	4.3
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	IS7	06:28:06	2.0	Bottom	3	2	19.62	8.04	32.02	90.90	6.1	3.3	4.7
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	IS8(N)	05:57:41	1.0	Surface	1	1	19.58	8.03	31.83	90.60	6.0	3.4	2.8
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	IS8(N)	05:58:06	1.0	Surface	1	2	19.63	8.03	31.80	90.40	6.0	3.3	2.3
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	IS8(N)	05:57:22	3.0	Bottom	3	1	19.36	8.02	32.11	90.60	6.0	3.4	2.6
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	IS8(N)	05:57:51	3.0	Bottom	3	2	19.55	8.02	32.06	90.30	6.0	3.3	3.2
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	IS(Mf)9	06:18:00	1.0	Surface	1	1	19.75	8.01	31.89	91.60	6.1	3.4	1.7
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	IS(Mf)9	06:18:23	1.0	Surface	1	2	19.74	8.01	31.81	91.40	6.1	3.3	2.5
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	IS(Mf)9	06:17:36	2.6	Bottom	3	1	19.68	8.00	32.14	91.50	6.1	3.4	3.4
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	IS(Mf)9	06:18:12	2.6	Bottom	3	2	19.68	8.00	32.10	91.20	6.1	3.3	3.6
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	IS10(N)	05:30:00	1.0	Surface	1	1	19.50	8.12	32.00	83.10	6.0	3.2	3.0
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	IS10(N)	05:30:36	1.0	Surface	1	2	19.53	8.12	32.03	83.20	6.0	3.2	3.7
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	IS10(N)	05:29:47	4.5	Middle	2	1	19.50	8.11	31.61	82.80	6.0	3.2	3.2
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	IS10(N)	05:30:25	4.5	Middle	2	2	19.50	8.11	31.57	82.40	6.0	3.2	3.3
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	IS10(N)	05:29:37	8.0	Bottom	3	1	19.46	8.12	32.09	82.40	6.0	3.2	4.5
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	IS10(N)	05:30:14	8.0	Bottom	3	2	19.46	8.12	32.08	81.80	5.9	3.2	4.2
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	SR3(N)	06:56:33	1.0	Surface	1	1	19.63	8.00	31.88	89.50	6.0	3.3	3.0
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	SR3(N)	06:57:05	1.0	Surface	1	2	19.63	8.00	31.88	89.50	6.0	3.3	2.8
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	SR3(N)	06:56:02	2.2	Bottom	3	1	19.56	7.99	32.05	89.10	6.0	3.2	3.7
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	SR3(N)	06:56:45	2.2	Bottom	3	2	19.60	8.00	32.14	90.10	6.0	3.4	2.9
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	SR4(N3)	06:07:01	1.0	Surface	1	1	19.76	7.99	31.78	90.40	6.1	3.2	2.7
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	SR4(N3)	06:07:27	1.0	Surface	1	2	19.78	7.99	31.76	90.40	6.1	3.3	2.8
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	SR4(N3)	06:06:45	2.6	Bottom	3	1	19.65	7.98	32.10	89.60	6.0	3.4	2.8
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	SR4(N3)	06:07:10	2.6	Bottom	3	2	19.65	7.98	32.11	90.60	6.1	3.3	3.0
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	SR5(N)	05:38:44	1	Surface	1	1	19.54	8.11	32.01	84.00	6.0	3.2	3.0
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	SR5(N)	05:39:19	1	Surface	1	2	19.51	8.11	32.09	82.80	5.9	3.1	4.1
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	SR5(N)	05:38:33	4.6	Middle	2	1	19.25	8.10	31.56	82.90	6.0	3.2	5.1
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	SR5(N)	05:39:08	4.6	Middle	2	2	19.23	8.10	31.57	82.70	5.9	3.2	5.2
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	SR5(N)	05:38:23	8.2	Bottom	3	1	19.31	8.10	31.95	82.50	5.9	3.2	3.3
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	SR5(N)	05:38:56	8.2	Bottom	3	2	19.24	8.10	32.09	82.30	5.9	3.2	3.3
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	SR10A(N)	04:42:14	1	Surface	1	1	19.56	8.11	31.54	83.30	6.0	3.2	3.5
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	SR10A(N)	04:42:51	1	Surface	1	2	19.57	8.10	31.53	82.80	6.0	3.3	3.6
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	SR10A(N)	04:42:02	5.6	Middle	2	1	19.56	8.10	32.04	82.90	6.0	3.4	3.2
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	SR10A(N)	04:42:42	5.6	Middle	2	2	19.57	8.10	31.98	81.60	5.9	3.4	3.1
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	SR10A(N)	04:41:51	10.2	Bottom	3	1	19.50	8.10	31.96	82.50	6.0	3.4	2.9
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	SR10A(N)	04:42:25	10.2	Bottom	3	2	19.50	8.10	31.95	81.60	5.9	3.3	2.5
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	SR10B(N2)	04:31:49	1.0	Surface	1	1	19.78	8.12	32.14	83.10	6.0	3.2	2.3
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	SR10B(N2)	04:32:29	1.0	Surface	1	2	19.54	8.12	32.15	83.20	6.0	3.2	3.0
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	SR10B(N2)	04:31:37	3.8	Middle	2	1	19.53	8.11	32.09	82.70	5.9	3.2	4.2
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	SR10B(N2)	04:32:19	3.8	Middle	2	2	19.57	8.11	32.12	83.00	6.0	3.2	3.1
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	SR10B(N2)	04:31:16	6.6	Bottom	3	1	19.53	8.11	31.72	82.40	5.9	3.2	3.8
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	SR10B(N2)	04:32:02	6.6	Bottom	3	2	19.54	8.11	31.67	83.40	6.0	3.3	4.7
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	CS(2A)	06:45:11	1	Surface	1	1	19.46	8.14	32.13	83.30	6.0	3.2	3.2
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	CS(2A)	06:45:46	1	Surface	1	2	19.41	8.14	32.13	83.30	6.0	3.2	3.0
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	CS(2A)	06:45:00	3.2	Middle	2	1	19.23	8.13	32.06	82.90	6.0	3.3	2.8
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	CS(2A)	06:45:34	3.2	Middle	2	2	19.21	8.13	32.04	83.00	6.0	3.3	2.9
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	CS(2A)	06:44:45	5.4	Bottom	3	1	19.25	8.14	31.61	82.90	6.0	3.3	3.2
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	CS(2A)	06:45:27	5.4	Bottom	3	2	19.24	8.14	31.59	82.70	6.0	3.4	2.4
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	CS(Mf)5	05:13:42	1.0	Surface	1	1	19.46	8.05	31.75	93.40	6.2	3.2	1.8
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	CS(Mf)5	05:14:39	1.0	Surface	1	2	19.63	8.02	31.70	91.80	6.1	3.3	2.4
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	CS(Mf)5	05:13:26	6.0	Middle	2	1	19.59	8.03	32.36	92.90	6.2	3.3	3.0
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	CS(Mf)5	05:14:11	6.0	Middle	2	2	19.35	8.00	32.40	91.60	6.1	3.2	2.3
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	CS(Mf)5	05:13:02	11.0	Bottom	3	1	19.36	8.02	32.37	91.60	6.1	3.3	4.0
HKLR	HY/2011/03	2025-03-26	Mid-Flood	Cloudy	CS(Mf)5	05:13:59	11.0	Bottom	3	2	19.34	8.00	32.42	90.80	6.0	3.3	5.3
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	IS5	11:21:00	1.0	Surface	1	1	19.45	8.01	31.77	91.10	6.1	3.4	2.4
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	IS5	11:21:47	1.0	Surface	1	2	19.45	8.01	31.84	91.70	6.2	3.4	2.7
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	IS5	11:20:49	4.1	Middle	2	1	19.42	8.00	32.28	90.40	6.1	3.4	3.0
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	IS5	11:21:25	4.1	Middle	2	2	19.38	8.03	31.73	91.40	6.1	3.4	3.4
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	IS5	11:20:33	7.2	Bottom	3	1	19.47	8.01	32.27	90.30	6.1	3.4	2.8
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	IS5	11:21:14	7.2	Bottom	3	2	19.15	8.02	32.23	91.40	6.1	3.4	2.6
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	IS(Mf)6	11:30:36	1.0	Surface	1	1	19.41	8.01	31.84	92.10	6.2	3.2	2.4
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	IS(Mf)6	11:30:59	1.0	Surface	1	2	19.48	8.02	31.80	92.30	6.2	3.2	2.3
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	IS(Mf)6	11:30:19	2.0	Bottom	3	1	19.30	8.00	32.08	92.30	6.2	3.2	2.4
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	IS(Mf)6	11:30:48	2.0	Bottom	3	2	19.31	8.01	32.07	92.20	6.2	3.3	3.6
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	IS7	11:40:26	1.0	Surface	1	1	19.41	8.01	31.76	92.40	6.2	3.5	3.4
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	IS7	11:40:40	1.0	Surface	1	2	19.40	8.01	31.76	92.20	6.2	3.4	3.4
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	IS7	11:40:07	2.0	Bottom	3	1	19.38	8.01	31.91	92.30	6.2	3.5	2.9
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	IS7	11:40:33	2.0	Bottom	3	2	19.35	8.01	31.95	92.40	6.2	3.5	3.0
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	IS8(N)	12:12:21	1.0	Surface	1	1	19.37	7.98	31.72	91.10	6.1	3.1	2.9
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	IS8(N)	12:12:45	1.0	Surface	1	2	19.37	7.98	31.71	91.40	6.1	3.2	3.4
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	IS8(N)	12:12:05	2.8	Bottom	3	1	19.23	7.98	31.95	91.00	6.1	3.1	2.3
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	IS8(N)	12:12:33	2.8	Bottom	3	2	19.27	7.98	31.92	90.70	6.1	3.1	3.2
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	IS(Mf)9	11:49:10	1.0	Surface	1	1	19.47	8.05	31.87	91.70	6.1	3.2	2.6
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	IS(Mf)9	11:49:49	1.0	Surface	1	2	19.48	8.05	31.88	91.50	6.1	3.3	3.2
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	IS(Mf)9	11:49:00	2.6	Bottom	3	1	19.40	8.04	32.08	91.50	6.1	3.2	2.8
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	IS(Mf)9	11:49:19	2.6	Bottom	3	2	19.43	8.05	32.14	91.40	6.1	3.3	3.7
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	IS10(N)	12:25:25	1.0	Surface	1	1	19.17	8.07	32.09	83.30	6.0	3.1	3.5
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	IS10(N)	12:26:09	1.0	Surface	1	2	19.20	8.07	32.04	82.90	6.0	3.1	3.2
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	IS10(N)	12:25:11	4.6	Middle	2	1	18.94	8.07	32.53	83.20	6.0	3.1	3.2
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	IS10(N)	12:25:54	4.6	Middle	2	2	18.94	8.07	32.53	82.80	6.0	3.2	3.0
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	IS10(N)	12:24:59	8.2	Bottom	3	1	18.96	8.07	32.44	82.50	6.0	3.1	4.0
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	IS10(N)	12:25:46	8.2	Bottom	3	2	18.98	8.06	32.42	82.40	6.0	3.2	3.8
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	SR3(N)	11:06:32	1.0	Surface	1	1	19.36	8.02	31.70	90.10	6.0	3.4	3.9
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	SR3(N)	11:06:54	1.0	Surface	1	2	19.36	8.02	31.70	90.10	6.0	3.3	3.8
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	SR3(N)	11:06:16	2.0	Bottom	3	1	19.29	8.01	31.87	89.70	6.0	3.4	2.6
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	SR3(N)	11:06:39	2.0	Bottom	3	2	19.33	8.02	31.96	90.70	6.1	3.3	3.0
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	SR4(N3)	12:02:58	1.0	Surface	1	1	19.45	8.01	31.72	92.50	6.2	3.3	2.5
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	SR4(N3)	12:03:28	1.0	Surface	1	2	19.44	8.01	31.77	92.30	6.2	3.2	2.6
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	SR4(N3)	12:02:37	2.6	Bottom	3	1	19.42	8.00	32.25	92.30	6.2	3.2	3.1
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	SR4(N3)	12:03:08	2.6	Bottom	3	2	19.39	8.00	31.93	92.20	6.2	3.2	2.7
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	SR5(N)	12:15:24	1.0	Surface	1	1	19.26	8.11	32.39	84.90	6.1	3.3	4.5
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	SR5(N)	12:15:52	1.0	Surface	1	2	19.26	8.11	32.47	83.70	6.0	3.3	4.7
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	SR5(N)	12:15:16	4.5	Middle	2	1	19.01	8.10	31.94	83.80	6.1	3.3	4.4
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	SR5(N)	12:15:43	4.5	Middle	2	2	18.97	8.10	31.95	83.60	6.0	3.3	3.9
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	SR5(N)	12:15:05	8.0	Bottom	3	1	19.05	8.11	32.33	83.40	6.0	3.3	3.6
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	SR5(N)	12:15:35	8.0	Bottom	3	2	19.04	8.11	32.47	83.20	6.0	3.2	2.8
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	SR10A(N)	13:16:56	1.0	Surface	1	1	19.33	8.07	32.53	84.10	6.1	3.3	3.8
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	SR10A(N)	13:17:29	1.0	Surface	1	2	19.34	8.07	32.53	83.90	6.1	3.3	2.6
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	SR10A(N)	13:16:46	5.6	Middle	2	1	19.07	8.06	32.48	84.10	6.1	3.2	2.6
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	SR10A(N)	13:17:18	5.6	Middle	2	2	19.08	8.07	32.47	83.70	6.1	3.2	2.6
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	SR10A(N)	13:16:28	10.2	Bottom	3	1	19.15	8.06	31.96	83.50	6.0	3.2	3.3
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	SR10A(N)	13:17:08	10.2	Bottom	3	2	19.16	8.07	31.84	83.30	6.0	3.3	3.2

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	SR10B(N2)	13:29:07	1.0	Surface	1	1	19.19	8.07	32.48	83.40	6.0	3.2	2.7
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	SR10B(N2)	13:29:48	1.0	Surface	1	2	19.20	8.07	32.49	83.10	6.0	3.1	2.9
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	SR10B(N2)	13:28:56	3.7	Middle	2	1	18.93	8.06	32.52	83.30	6.0	3.1	3.5
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	SR10B(N2)	13:29:25	3.7	Middle	2	2	18.94	8.06	32.51	82.80	6.0	3.1	3.6
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	SR10B(N2)	13:28:46	6.4	Bottom	3	1	18.98	8.06	32.04	84.10	6.1	3.1	4.9
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	SR10B(N2)	13:29:17	6.4	Bottom	3	2	19.00	8.06	32.07	82.60	6.0	3.3	4.7
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	CS2(A)	11:20:58	1.0	Surface	1	1	19.32	8.07	32.37	83.40	6.0	3.2	2.7
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	CS2(A)	11:21:25	1.0	Surface	1	2	19.29	8.08	32.35	82.90	6.0	3.2	3.5
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	CS2(A)	11:20:48	3.1	Middle	2	1	19.03	8.07	31.99	83.10	6.0	3.3	2.7
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	CS2(A)	11:21:15	3.1	Middle	2	2	19.01	8.07	31.98	82.60	6.0	3.2	3.8
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	CS2(A)	11:20:37	5.2	Bottom	3	1	19.09	8.07	32.47	82.40	6.0	3.2	3.8
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	CS2(A)	11:21:07	5.2	Bottom	3	2	19.02	8.07	32.35	82.30	6.0	3.3	4.2
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	CS(Mf)5	12:57:19	1.0	Surface	1	1	19.37	8.01	31.72	89.60	6.0	3.2	2.8
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	CS(Mf)5	12:58:01	1.0	Surface	1	2	19.44	8.02	31.85	89.80	6.0	3.1	2.6
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	CS(Mf)5	12:57:04	5.8	Middle	2	1	19.17	8.01	32.32	89.50	6.0	3.1	2.8
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	CS(Mf)5	12:57:47	5.8	Middle	2	2	19.19	8.01	32.33	89.20	6.0	3.2	2.6
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	CS(Mf)5	12:56:47	10.6	Bottom	3	1	19.15	8.01	32.26	89.20	6.0	3.1	2.8
HKLR	HY/2011/03	2025-03-28	Mid-Ebb	Sunny	CS(Mf)5	12:57:29	10.6	Bottom	3	2	19.16	8.01	32.31	88.80	5.9	3.2	3.1
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	IS5	06:42:52	1.0	Surface	1	1	19.29	8.02	31.57	93.80	6.3	3.2	3.0
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	IS5	06:43:38	1.0	Surface	1	2	19.41	8.03	31.71	94.20	6.3	3.1	2.8
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	IS5	06:42:33	4.3	Middle	2	1	19.43	8.02	32.16	92.80	6.3	3.1	3.4
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	IS5	06:43:17	4.3	Middle	2	2	19.41	8.02	32.17	94.10	6.3	3.3	2.7
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	IS5	06:42:15	7.6	Bottom	3	1	19.15	8.02	32.21	92.30	6.2	3.1	3.4
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	IS5	06:43:06	7.6	Bottom	3	2	19.33	8.02	32.21	94.00	6.3	3.1	4.0
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	IS(Mf)6	06:32:56	1.0	Surface	1	1	19.31	8.06	31.65	91.30	6.1	3.1	3.1
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	IS(Mf)6	06:33:25	1.0	Surface	1	2	19.36	8.06	31.62	91.10	6.1	3.2	3.1
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	IS(Mf)6	06:32:49	2.2	Bottom	3	1	19.09	8.05	31.93	91.30	6.1	3.1	2.6
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	IS(Mf)6	06:33:15	2.2	Bottom	3	2	19.28	8.05	31.88	91.00	6.1	3.1	2.4
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	IS7	06:22:12	1.0	Surface	1	1	19.37	8.04	31.55	91.20	6.1	3.2	2.9
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	IS7	06:22:39	1.0	Surface	1	2	19.24	8.04	31.56	91.10	6.1	3.2	3.4
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	IS7	06:21:47	2.0	Bottom	3	1	19.17	8.03	31.75	91.10	6.1	3.2	3.6
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	IS7	06:22:22	2.0	Bottom	3	2	19.18	8.03	31.81	90.90	6.1	3.2	3.1
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	IS8(N)	05:53:25	1.0	Surface	1	1	19.49	8.02	31.60	91.10	6.1	3.2	3.7
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	IS8(N)	05:53:52	1.0	Surface	1	2	19.51	8.02	31.58	91.10	6.1	3.2	3.3
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	IS8(N)	05:53:08	3.0	Bottom	3	1	19.38	8.01	31.92	90.30	6.1	3.2	3.5
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	IS8(N)	05:53:37	3.0	Bottom	3	2	19.38	8.01	31.93	91.30	6.2	3.3	3.7
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	IS(Mf)9	06:12:16	1.0	Surface	1	1	19.40	8.06	31.57	91.70	6.2	3.3	2.6
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	IS(Mf)9	06:12:39	1.0	Surface	1	2	19.42	8.06	31.56	91.70	6.2	3.3	3.1
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	IS(Mf)9	06:11:52	2.6	Bottom	3	1	19.31	8.05	31.89	91.30	6.2	3.3	2.8
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	IS(Mf)9	06:12:28	2.6	Bottom	3	2	19.35	8.06	31.84	91.60	6.2	3.3	2.2
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	IS10(N)	06:13:12	1.0	Surface	1	1	19.54	8.08	32.52	84.00	6.1	3.1	3.2
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	IS10(N)	06:13:48	1.0	Surface	1	2	19.30	8.08	32.53	84.10	6.1	3.2	2.9
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	IS10(N)	06:12:59	4.5	Middle	2	1	19.29	8.07	32.47	83.60	6.0	3.2	3.2
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	IS10(N)	06:13:37	4.5	Middle	2	2	19.33	8.07	32.50	83.90	6.1	3.1	3.8
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	IS10(N)	06:12:49	8.0	Bottom	3	1	19.29	8.07	32.10	83.30	6.0	3.2	2.7
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	IS10(N)	06:13:26	8.0	Bottom	3	2	19.30	8.07	32.05	84.30	6.1	3.1	2.9
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	SR3(N)	06:55:29	1.0	Surface	1	1	19.14	8.02	31.67	92.00	6.2	3.2	3.2
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	SR3(N)	06:56:01	1.0	Surface	1	2	19.17	8.02	31.63	92.30	6.2	3.3	2.6
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	SR3(N)	06:54:58	2.2	Bottom	3	1	19.16	8.02	31.95	91.90	6.2	3.2	3.4
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	SR3(N)	06:55:42	2.2	Bottom	3	2	19.36	8.03	31.78	91.60	6.1	3.3	3.9
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	SR4(N3)	06:01:47	1.0	Surface	1	1	19.48	8.04	31.71	92.30	6.2	3.2	2.7
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	SR4(N3)	06:02:13	1.0	Surface	1	2	19.47	8.04	31.63	92.10	6.2	3.2	3.8
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	SR4(N3)	06:01:31	2.6	Bottom	3	1	19.41	8.03	31.96	92.20	6.2	3.3	2.4
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	SR4(N3)	06:01:54	2.6	Bottom	3	2	19.41	8.03	31.92	91.90	6.2	3.3	2.9
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	SR5(N)	06:22:36	1	Surface	1	1	19.24	8.08	32.51	83.80	6.1	3.2	3.7
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	SR5(N)	06:23:11	1	Surface	1	2	19.19	8.08	32.51	83.80	6.1	3.2	2.5
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	SR5(N)	06:22:25	4.5	Middle	2	1	19.01	8.07	32.44	83.40	6.1	3.3	2.8
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	SR5(N)	06:23:00	4.5	Middle	2	2	18.99	8.07	32.42	83.50	6.1	3.3	4.1
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	SR5(N)	06:22:15	8.0	Bottom	3	1	19.03	8.07	31.99	83.40	6.1	3.3	3.9
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	SR5(N)	06:22:48	8.0	Bottom	3	2	19.02	8.07	31.97	83.20	6.0	3.3	4.6
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	SR10A(N)	05:21:56	1	Surface	1	1	19.28	8.08	32.38	84.00	6.1	3.2	3.6
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	SR10A(N)	05:22:33	1	Surface	1	2	19.31	8.08	32.41	84.10	6.1	3.3	3.6
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	SR10A(N)	05:21:44	5.7	Middle	2	1	19.28	8.07	31.99	83.70	6.1	3.3	3.5
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	SR10A(N)	05:22:24	5.7	Middle	2	2	19.28	8.07	31.95	83.30	6.0	3.3	4.2
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	SR10A(N)	05:21:33	10.4	Bottom	3	1	19.24	8.08	32.47	83.30	6.0	3.2	5.1
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	SR10A(N)	05:22:07	10.4	Bottom	3	2	19.24	8.08	32.46	82.70	6.0	3.3	4.4
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	SR10B(N2)	05:11:11	1.0	Surface	1	1	19.32	8.07	31.92	84.20	6.1	3.3	4.0
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	SR10B(N2)	05:11:51	1.0	Surface	1	2	19.33	8.06	31.91	83.70	6.1	3.4	4.7
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	SR10B(N2)	05:10:59	3.8	Middle	2	1	19.32	8.06	32.42	83.80	6.1	3.3	3.8
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	SR10B(N2)	05:11:41	3.8	Middle	2	2	19.33	8.06	32.36	82.50	6.0	3.4	4.1
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	SR10B(N2)	05:10:38	6.6	Bottom	3	1	19.26	8.06	32.34	83.40	6.1	3.3	3.2
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	SR10B(N2)	05:11:24	6.6	Bottom	3	2	19.26	8.06	32.33	82.50	6.0	3.4	3.4
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	CS2(A)	07:11:03	1	Surface	1	1	19.30	8.08	31.94	83.80	6.1	3.2	3.7
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	CS2(A)	07:11:38	1	Surface	1	2	19.30	8.08	31.98	83.80	6.1	3.2	4.2
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	CS2(A)	07:10:52	3.1	Middle	2	1	19.30	8.07	32.43	83.00	6.0	3.2	4.3
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	CS2(A)	07:11:26	3.1	Middle	2	2	19.30	8.07	32.45	83.40	6.1	3.2	4.0
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	CS2(A)	07:10:37	5.2	Bottom	3	1	19.29	8.08	32.43	82.90	6.0	3.2	4.6
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	CS2(A)	07:11:19	5.2	Bottom	3	2	19.29	8.08	32.49	83.30	6.1	3.3	4.6
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	CS(Mf)5	05:16:26	1.0	Surface	1	1	19.36	8.05	31.57	92.50	6.2	3.3	3.0
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	CS(Mf)5	05:17:23	1.0	Surface	1	2	19.19	8.08	31.52	94.10	6.3	3.3	3.5
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	CS(Mf)5	05:16:10	5.9	Middle	2	1	19.08	8.03	32.18	92.30	6.2	3.3	2.8
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	CS(Mf)5	05:16:56	5.9	Middle	2	2	19.32	8.06	32.22	93.60	6.2	3.3	3.0
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	CS(Mf)5	05:15:42	10.8	Bottom	3	1	19.07	8.03	32.19	91.50	6.1	3.3	2.8
HKLR	HY/2011/03	2025-03-28	Mid-Flood	Cloudy	CS(Mf)5	05:16:43	10.8	Bottom	3	2	19.09	8.05	32.24	92.30	6.2	3.3	2.7
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	IS5	13:00:58	1.0	Surface	1	1	19.39	8.00	32.64	91.30	6.1	3.2	3.3
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	IS5	13:01:45	1.0	Surface	1	2	19.39	8.00	32.71	90.70	6.1	3.2	2.6
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	IS5	13:00:47	4.1	Middle	2	1	19.36	7.99	33.15	91.00	6.1	3.2	2.4
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	IS5	13:01:26	4.1	Middle	2	2	19.32	8.02	32.60	90.00	6.0	3.2	3.2
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	IS5	13:00:31	7.2	Bottom	3	1	19.41	8.00	33.14	91.00	6.1	3.2	2.4
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	IS5	13:01:12	7.2	Bottom	3	2	19.09	8.01	33.10	89.90	6.0	3.2	2.5
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	IS(Mf)6	13:11:34	1.0	Surface	1	1	19.35	8.00	32.63	92.00	6.2	3.0	2.2
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	IS(Mf)6	13:11:58	1.0	Surface	1	2	19.34	8.00	32.63	91.80	6.2	3.0	2.3
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	IS(Mf)6	13:11:17	2.0	Bottom	3	1	19.32	8.00	32.78	91.90	6.2	3.0	2.8
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	IS(Mf)6	13:11:46	2.0	Bottom	3	2	19.29	8.00	32.82	92.00	6.2	3.1	3.6
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	IS7	13:23:24	1.0	Surface	1	1	19.41	8.04	32.74	91.30	6.1	3.3	1.6
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	IS7	13:23:39	1.0	Surface	1	2	19.42	8.04	32.75	91.10	6.1	3.2	2.5
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	IS7	13:23:05	2.0	Bottom	3	1	19.34	8.03	32.95	91.10	6.1	3.3	2.1
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	IS7	13:23:31	2.0	Bottom	3	2	19.37	8.04	33.01	91.00	6.1	3.3	1.7
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	IS8(N)	13:53:19	1.0	Surface	1	1	19.35	8.00	32.71	91.70	6.2	3.0	5.0
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	IS8(N)	13:53:43	1.0	Surface	1	2	19.42	8.01	32.67	91.90	6.2	3.1	4.0
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	IS8(N)	13:53:04	2.6	Bottom	3	1	19.24	7.99	32.95	91.90	6.2	3.0	4.3
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	IS8(N)	13:53:31	2.6	Bottom	3	2	19.25	8.00	32.94	91.80	6.2	3.0	3.6
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	IS(Mf)9	13:32:08	1.0	Surface	1	1	19.39	8.00	32.59	92.10	6.2	3.1	2.9
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	IS(Mf)9	13:32:47	1.0	Surface	1	2	19.38	8.00	32.64	91.90	6.2	3.2	3.8
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	IS(Mf)9	13:31:58	2.6	Bottom	3	1	19.36	7.99	33.12	91.90	6.2	3.1	3.8
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	IS(Mf)9	13:32:23	2.6	Bottom	3	2	19.33	7.99	32.80	91.80	6.2	3.2	3.5
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	IS10(N)	13:46:16	1.0	Surface	1	1	19.12	8.04	33.42	85.30	6.1	3.0	2.6
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	IS10(N)	13:47:00	1.0	Surface	1	2	19.13	8.04	33.42	85.10	6.1	3.0	3.5
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	IS10(N)	13:46:05	4.4	Middle	2	1	18.86	8.03	33.37	85.30	6.1	3.0	2.4
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	IS10(N)	13:46:45	4.4	Middle	2	2	18.87	8.04	33.36	84.90	6.1	3.0	3.4
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	IS10(N)	13:45:50	7.8	Bottom	3	1	18.94	8.03	32.85	84.70	6.1	3.0	2.7
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	IS10(N)	13:46:37	7.8	Bottom	3	2	18.95	8.04	32.73	84.50	6.1	3.1	2.2
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	SR3(N)	12:51:14	1.0	Surface	1	1	19.06	8.01	32.54	91.60	6.1	3.3	2.0
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	SR3(N)	12:51:36	1.0	Surface	1	2	19.09	8.01	32.50	91.90	6.2	3.2	3.0
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	SR3(N)	12:50:53	2.2	Bottom	3	1	19.08	8.01	32.82	91.50	6.1	3.3	1.9
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	SR3(N)	12:51:21	2.2	Bottom	3	2	19.28	8.02	32.65	91.20	6.1	3.2	2.6
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	SR4(N3)	13:43:52	1.0	Surface	1	1	19.31	7.97	32.59	90.70	6.1	3.2	3.0
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	SR4(N3)	13:44:26	1.0	Surface	1	2	19.31	7.97	32.58	91.00	6.1	3.1	2.4
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	SR4(N3)	13:43:35	2.6	Bottom	3	1	19.17	7.97	32.82	90.60	6.1	3.1	2.2
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	SR4(N3)	13:44:06	2.6	Bottom	3	2	19.21	7.97	32.79	90.30	6.0	3.1	2.1
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	SR5(N)	13:36:15	1.0	Surface	1	1	19.09	8.04	32.98	85.00	6.1	2.9	3.2
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	SR5(N)	13:36:43	1.0	Surface	1	2	19.09	8.04	32.93	85.00	6.1	2.9	2.9
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	SR5(N)	13:36:07	4.4	Middle	2	1	19.09	8.04	33.42	84.60	6.1	2.9	2.7
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	SR5(N)	13:36:34	4.4	Middle	2	2	19.09	8.04	33.42	84.70	6.1	3.0	2.8
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	SR5(N)	13:35:52	7.8	Bottom	3	1	19.08	8.04	33.33	84.60	6.1	2.9	1.4

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	SR5(N)	13:36:24	7.8	Bottom	3	2	19.08	8.03	33.31	84.40	6.1	3.0	1.1
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	SR10A(N)	14:38:43	1.0	Surface	1	1	18.98	8.04	33.37	84.60	6.1	3.0	2.0
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	SR10A(N)	14:39:16	1.0	Surface	1	2	18.99	8.04	33.38	84.30	6.0	2.9	1.8
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	SR10A(N)	14:38:33	5.5	Middle	2	1	18.72	8.03	33.41	84.50	6.1	2.9	1.8
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	SR10A(N)	14:39:02	5.5	Middle	2	2	18.73	8.03	33.40	84.00	6.0	2.9	2.0
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	SR10A(N)	14:38:18	10.0	Bottom	3	1	18.77	8.03	32.93	85.30	6.1	2.9	1.8
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	SR10A(N)	14:38:55	10.0	Bottom	3	2	18.79	8.03	32.96	83.80	6.0	3.1	2.0
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	SR10B(N2)	14:48:52	1.0	Surface	1	1	18.96	8.08	32.83	84.50	6.1	3.1	2.8
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	SR10B(N2)	14:49:39	1.0	Surface	1	2	18.99	8.08	32.87	84.10	6.0	3.1	2.0
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	SR10B(N2)	14:48:43	3.8	Middle	2	1	18.73	8.07	33.32	84.40	6.0	3.0	1.4
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	SR10B(N2)	14:49:12	3.8	Middle	2	2	18.73	8.07	33.34	84.00	6.0	3.0	2.5
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	SR10B(N2)	14:48:33	6.6	Bottom	3	1	18.75	8.08	33.32	83.70	6.0	3.0	1.9
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	SR10B(N2)	14:49:04	6.6	Bottom	3	2	18.77	8.08	33.38	83.60	6.0	3.1	2.7
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	CS2(A)	12:41:49	1.0	Surface	1	1	19.05	8.05	33.28	86.10	6.1	3.1	2.2
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	CS2(A)	12:42:16	1.0	Surface	1	2	19.05	8.05	33.36	84.90	6.1	3.1	1.5
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	CS2(A)	12:41:39	3.1	Middle	2	1	18.80	8.04	32.83	85.00	6.1	3.1	2.8
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	CS2(A)	12:42:05	3.1	Middle	2	2	18.76	8.04	32.84	84.80	6.1	3.1	2.2
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	CS2(A)	12:41:21	5.2	Bottom	3	1	18.84	8.04	33.22	84.60	6.1	3.1	3.5
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	CS2(A)	12:41:58	5.2	Bottom	3	2	18.83	8.04	33.36	84.40	6.0	3.0	2.6
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	CS(Mf)5	14:41:17	1.0	Surface	1	1	19.38	8.01	32.72	89.40	6.0	3.1	2.7
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	CS(Mf)5	14:41:58	1.0	Surface	1	2	19.31	8.00	32.59	89.20	6.0	3.0	3.5
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	CS(Mf)5	14:41:04	5.7	Middle	2	1	19.13	8.00	33.20	88.80	5.9	3.0	2.0
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	CS(Mf)5	14:41:45	5.7	Middle	2	2	19.11	8.00	33.19	89.10	6.0	3.1	2.5
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	CS(Mf)5	14:40:45	10.4	Bottom	3	1	19.10	8.00	33.18	88.40	5.9	3.0	2.1
HKLR	HY/2011/03	2025-03-31	Mid-Ebb	Sunny	CS(Mf)5	14:41:29	10.4	Bottom	3	2	19.09	8.00	33.13	88.80	5.9	3.1	2.9
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	IS5	08:42:58	1.0	Surface	1	1	19.33	8.01	32.58	93.80	6.3	3.1	2.9
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	IS5	08:43:40	1.0	Surface	1	2	19.21	8.02	32.44	93.40	6.2	3.0	2.8
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	IS5	08:42:35	4.2	Middle	2	1	19.33	8.01	33.04	93.70	6.2	3.0	2.2
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	IS5	08:43:19	4.2	Middle	2	2	19.35	8.01	33.03	92.40	6.2	3.2	2.8
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	IS5	08:42:17	7.4	Bottom	3	1	19.25	8.01	33.08	93.60	6.2	3.0	1.5
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	IS5	08:43:08	7.4	Bottom	3	2	19.07	8.01	33.08	91.90	6.2	3.0	2.7
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	IS(Mf)6	08:32:58	1.0	Surface	1	1	19.45	8.00	32.47	90.70	6.1	3.0	2.7
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	IS(Mf)6	08:33:27	1.0	Surface	1	2	19.47	8.00	32.45	90.70	6.1	3.1	3.5
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	IS(Mf)6	08:32:51	2.2	Bottom	3	1	19.34	7.99	32.79	89.90	6.1	3.0	2.6
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	IS(Mf)6	08:33:03	2.2	Bottom	3	2	19.34	7.99	32.80	90.90	6.1	3.0	3.0
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	IS7	08:22:52	1.0	Surface	1	1	19.23	8.05	32.52	90.90	6.1	3.1	2.2
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	IS7	08:23:23	1.0	Surface	1	2	19.28	8.05	32.49	90.70	6.1	3.1	3.0
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	IS7	08:22:31	2.0	Bottom	3	1	19.01	8.04	32.80	90.90	6.1	3.1	2.5
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	IS7	08:23:06	2.0	Bottom	3	2	19.20	8.04	32.75	90.60	6.1	3.1	2.0
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	IS8(N)	07:53:27	1.0	Surface	1	1	19.44	8.02	32.58	91.90	6.2	3.0	3.0
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	IS8(N)	07:53:58	1.0	Surface	1	2	19.43	8.02	32.50	91.70	6.2	3.0	2.9
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	IS8(N)	07:53:17	3.0	Bottom	3	1	19.37	8.01	32.83	91.80	6.2	3.0	3.0
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	IS8(N)	07:53:39	3.0	Bottom	3	2	19.37	8.01	32.79	91.50	6.1	3.1	2.1
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	IS(Mf)9	08:13:00	1.0	Surface	1	1	19.29	8.03	32.42	90.80	6.1	3.1	2.9
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	IS(Mf)9	08:13:23	1.0	Surface	1	2	19.16	8.03	32.43	90.70	6.1	3.1	2.4
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	IS(Mf)9	08:12:36	2.6	Bottom	3	1	19.09	8.02	32.62	90.70	6.1	3.1	2.9
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	IS(Mf)9	08:13:11	2.6	Bottom	3	2	19.10	8.02	32.68	90.50	6.1	3.1	3.1
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	IS10(N)	08:21:05	1.0	Surface	1	1	19.03	8.04	33.40	85.40	6.1	3.0	3.6
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	IS10(N)	08:21:38	1.0	Surface	1	2	18.98	8.03	33.40	84.90	6.1	3.0	3.1
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	IS10(N)	08:20:50	4.5	Middle	2	1	18.80	8.03	33.33	85.00	6.1	3.1	2.1
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	IS10(N)	08:21:28	4.5	Middle	2	2	18.78	8.03	33.31	83.70	6.0	3.1	2.1
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	IS10(N)	08:20:40	8.0	Bottom	3	1	18.82	8.03	32.88	84.60	6.1	3.1	3.6
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	IS10(N)	08:21:17	8.0	Bottom	3	2	18.81	8.03	32.86	83.70	6.0	3.1	3.7
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	SR3(N)	08:53:11	1.0	Surface	1	1	19.30	8.01	32.57	89.70	6.0	3.1	2.4
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	SR3(N)	08:53:43	1.0	Surface	1	2	19.30	8.01	32.57	89.70	6.0	3.2	2.7
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	SR3(N)	08:52:42	2.2	Bottom	3	1	19.23	8.00	32.74	89.30	6.0	3.1	3.1
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	SR3(N)	08:53:24	2.2	Bottom	3	2	19.27	8.01	32.83	90.30	6.0	3.2	2.2
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	SR4(N3)	08:02:31	1.0	Surface	1	1	19.32	8.04	32.44	91.30	6.2	3.0	2.4
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	SR4(N3)	08:02:57	1.0	Surface	1	2	19.34	8.04	32.43	91.30	6.2	3.0	2.6
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	SR4(N3)	08:02:15	2.6	Bottom	3	1	19.23	8.03	32.76	90.90	6.1	3.1	2.9
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	SR4(N3)	08:02:39	2.6	Bottom	3	2	19.27	8.04	32.71	91.20	6.1	3.1	2.4
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	SR5(N)	08:31:28	1	Surface	1	1	19.11	8.05	32.81	85.00	6.1	3.1	3.0
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	SR5(N)	08:32:02	1	Surface	1	2	19.12	8.05	32.80	85.00	6.1	3.2	2.4
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	SR5(N)	08:31:16	4.4	Middle	2	1	19.11	8.04	33.31	84.20	6.1	3.1	2.7
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	SR5(N)	08:31:51	4.4	Middle	2	2	19.12	8.04	33.25	84.60	6.1	3.2	2.1
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	SR5(N)	08:31:06	7.8	Bottom	3	1	19.05	8.05	33.23	84.10	6.1	3.1	1.9
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	SR5(N)	08:31:39	7.8	Bottom	3	2	19.05	8.05	33.22	84.50	6.1	3.2	1.6
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	SR10A(N)	07:20:07	1	Surface	1	1	19.33	8.05	33.41	85.20	6.1	2.9	2.7
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	SR10A(N)	07:20:45	1	Surface	1	2	19.09	8.05	33.42	85.30	6.1	3.0	1.8
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	SR10A(N)	07:19:58	5.6	Middle	2	1	19.08	8.04	33.36	84.80	6.1	3.0	1.4
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	SR10A(N)	07:20:35	5.6	Middle	2	2	19.12	8.04	33.39	85.10	6.1	2.9	1.9
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	SR10A(N)	07:19:44	10.2	Bottom	3	1	19.08	8.04	32.99	84.50	6.0	3.0	1.7
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	SR10A(N)	07:20:18	10.2	Bottom	3	2	19.09	8.04	32.94	85.50	6.1	2.9	2.6
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	SR10B(N2)	07:10:22	1.0	Surface	1	1	19.07	8.05	33.27	85.20	6.1	3.0	2.4
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	SR10B(N2)	07:11:02	1.0	Surface	1	2	19.10	8.05	33.30	85.30	6.1	3.1	2.4
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	SR10B(N2)	07:10:10	3.8	Middle	2	1	19.07	8.04	32.88	84.90	6.1	3.1	2.3
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	SR10B(N2)	07:10:52	3.8	Middle	2	2	19.07	8.04	32.84	84.50	6.1	3.1	2.6
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	SR10B(N2)	07:09:42	6.6	Bottom	3	1	19.03	8.05	33.36	84.50	6.1	3.0	2.9
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	SR10B(N2)	07:10:34	6.6	Bottom	3	2	19.03	8.05	33.35	83.90	6.0	3.1	2.5
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	CS(2A)	09:25:54	1	Surface	1	1	19.11	8.04	33.26	84.60	6.1	3.0	2.7
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	CS(2A)	09:26:29	1	Surface	1	2	19.08	8.05	33.24	84.10	6.0	3.0	3.4
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	CS(2A)	09:25:43	3.1	Middle	2	1	18.82	8.04	32.88	84.30	6.0	3.1	3.0
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	CS(2A)	09:26:19	3.1	Middle	2	2	18.80	8.04	32.87	83.80	6.0	3.0	2.1
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	CS(2A)	09:25:26	5.2	Bottom	3	1	18.88	8.04	33.36	83.60	6.0	3.0	2.5
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	CS(2A)	09:26:10	5.2	Bottom	3	2	18.81	8.04	33.24	83.50	6.0	3.1	2.2
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	CS(Mf)5	07:06:48	1.0	Surface	1	1	19.32	8.06	32.39	92.10	6.1	3.1	2.4
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	CS(Mf)5	07:07:45	1.0	Surface	1	2	19.15	8.03	32.44	93.70	6.3	3.1	2.5
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	CS(Mf)5	07:06:32	5.8	Middle	2	1	19.04	8.04	33.09	91.90	6.1	3.1	2.7
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	CS(Mf)5	07:07:18	5.8	Middle	2	2	19.28	8.01	33.05	93.20	6.2	3.1	2.5
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	CS(Mf)5	07:06:01	10.6	Bottom	3	1	19.03	8.03	33.11	91.10	6.1	3.1	1.6
HKLR	HY/2011/03	2025-03-31	Mid-Flood	Fine	CS(Mf)5	07:07:05	10.6	Bottom	3	2	19.05	8.01	33.06	91.90	6.1	3.1	2.2

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	IS5	14:21:55	1.0	Surface	1	1	19.31	7.99	32.63	89.40	6.0	3.4	3.8
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	IS5	14:22:42	1.0	Surface	1	2	19.31	7.99	32.56	90.00	6.0	3.4	4.7
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	IS5	14:21:44	4.2	Middle	2	1	19.24	7.98	32.52	88.70	6.0	3.4	4.5
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	IS5	14:22:22	4.2	Middle	2	2	19.28	8.01	33.07	89.70	6.0	3.4	4.5
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	IS5	14:21:29	7.4	Bottom	3	1	19.01	7.99	33.02	88.60	5.9	3.4	4.5
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	IS5	14:22:09	7.4	Bottom	3	2	19.33	8.00	33.06	89.70	6.0	3.4	4.4
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	IS(Mf)6	14:33:11	1.0	Surface	1	1	19.33	8.02	32.66	90.00	6.0	3.2	4.6
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	IS(Mf)6	14:33:36	1.0	Surface	1	2	19.34	8.02	32.67	89.80	6.0	3.2	4.2
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	IS(Mf)6	14:32:54	2.0	Bottom	3	1	19.26	8.01	32.87	89.80	6.0	3.2	4.3
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	IS(Mf)6	14:33:23	2.0	Bottom	3	2	19.29	8.02	32.93	89.70	6.0	3.3	4.4
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	IS7	14:42:01	1.0	Surface	1	1	19.31	7.98	32.51	90.80	6.1	3.5	4.6
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	IS7	14:42:15	1.0	Surface	1	2	19.30	7.98	32.56	90.60	6.1	3.4	4.1
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	IS7	14:41:42	2.0	Bottom	3	1	19.28	7.97	33.04	90.60	6.1	3.5	4.7
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	IS7	14:42:08	2.0	Bottom	3	2	19.25	7.97	32.72	90.50	6.1	3.5	4.7
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	IS8(N)	15:12:56	1.0	Surface	1	1	19.27	7.99	32.55	90.70	6.1	3.3	4.7
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	IS8(N)	15:13:20	1.0	Surface	1	2	19.26	7.99	32.55	90.50	6.1	3.4	4.5
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	IS8(N)	15:12:45	2.8	Bottom	3	1	19.24	7.99	32.70	90.60	6.1	3.3	4.7
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	IS8(N)	15:13:08	2.8	Bottom	3	2	19.21	7.99	32.74	90.70	6.1	3.3	4.7
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	IS(Mf)9	14:51:45	1.0	Surface	1	1	19.23	7.95	32.51	89.40	6.0	3.4	5.3
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	IS(Mf)9	14:52:24	1.0	Surface	1	2	19.23	7.95	32.50	89.70	6.0	3.5	4.8
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	IS(Mf)9	14:51:35	2.4	Bottom	3	1	19.09	7.95	32.74	89.30	6.0	3.4	4.5
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	IS(Mf)9	14:52:00	2.4	Bottom	3	2	19.13	7.95	32.71	89.00	6.0	3.5	5.0
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	IS10(N)	15:16:23	1.0	Surface	1	1	18.97	8.03	33.18	83.90	6.0	3.1	3.7
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	IS10(N)	15:17:07	1.0	Surface	1	2	18.98	8.03	33.16	83.60	6.0	3.1	3.7
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	IS10(N)	15:16:14	4.3	Middle	2	1	18.71	8.02	32.80	83.80	6.0	3.2	3.9
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	IS10(N)	15:16:52	4.3	Middle	2	2	18.72	8.03	32.79	83.30	6.0	3.1	3.8
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	IS10(N)	15:15:57	7.6	Bottom	3	1	18.76	8.02	33.28	84.60	6.1	3.1	4.6
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	IS10(N)	15:16:44	7.6	Bottom	3	2	18.78	8.03	33.16	83.10	6.0	3.2	4.0
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	SR3(N)	14:11:17	1.0	Surface	1	1	19.22	8.00	32.49	88.40	5.9	3.5	5.2
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	SR3(N)	14:11:43	1.0	Surface	1	2	19.22	8.00	32.49	88.40	5.9	3.4	4.9
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	SR3(N)	14:11:00	2.0	Bottom	3	1	19.15	8.00	32.66	88.00	5.9	3.5	3.8
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	SR3(N)	14:11:28	2.0	Bottom	3	2	19.19	8.01	32.75	89.00	6.0	3.4	4.3
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	SR4(N3)	15:03:29	1.0	Surface	1	1	19.27	7.98	32.63	90.40	6.1	3.5	4.6
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	SR4(N3)	15:04:03	1.0	Surface	1	2	19.34	7.99	32.59	90.60	6.1	3.4	4.7
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	SR4(N3)	15:03:14	2.6	Bottom	3	1	19.16	7.97	32.87	90.60	6.1	3.4	4.2
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	SR4(N3)	15:03:43	2.6	Bottom	3	2	19.17	7.98	32.86	90.50	6.1	3.4	4.4
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	SR5(N)	15:06:22	1.0	Surface	1	1	19.11	8.01	33.34	83.90	6.0	3.2	5.1
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	SR5(N)	15:06:50	1.0	Surface	1	2	19.12	8.01	33.34	83.40	6.0	3.2	4.4
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	SR5(N)	15:06:14	4.3	Middle	2	1	18.85	8.01	33.29	83.60	6.0	3.2	4.6
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	SR5(N)	15:06:41	4.3	Middle	2	2	18.86	8.01	33.28	83.10	6.0	3.2	4.6
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	SR5(N)	15:05:54	7.6	Bottom	3	1	18.93	8.01	32.77	82.90	6.0	3.2	4.4
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	SR5(N)	15:06:33	7.6	Bottom	3	2	18.94	8.00	32.65	82.80	6.0	3.3	4.1
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	SR10A(N)	16:10:50	1.0	Surface	1	1	18.95	8.03	32.75	83.80	6.0	3.3	4.1
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	SR10A(N)	16:11:23	1.0	Surface	1	2	18.98	8.03	32.79	83.40	6.0	3.3	4.0
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	SR10A(N)	16:10:40	5.5	Middle	2	1	18.72	8.02	33.24	83.70	6.0	3.2	3.7
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	SR10A(N)	16:11:11	5.5	Middle	2	2	18.72	8.02	33.26	83.30	6.0	3.2	3.7
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	SR10A(N)	16:10:22	10.0	Bottom	3	1	18.74	8.02	33.24	83.00	6.0	3.2	3.8
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	SR10A(N)	16:11:02	10.0	Bottom	3	2	18.76	8.02	33.30	82.90	6.0	3.3	3.9
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	SR10B(N2)	16:20:58	1.0	Surface	1	1	19.08	8.04	33.29	84.60	6.1	3.2	3.8
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	SR10B(N2)	16:21:55	1.0	Surface	1	2	19.08	8.04	33.30	84.40	6.0	3.1	3.8
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	SR10B(N2)	16:20:50	3.8	Middle	2	1	19.08	8.03	33.33	84.60	6.1	3.1	4.4
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	SR10B(N2)	16:21:19	3.8	Middle	2	2	19.08	8.03	33.32	84.20	6.0	3.1	4.2
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	SR10B(N2)	16:20:40	6.6	Bottom	3	1	19.07	8.04	32.85	84.00	6.0	3.1	3.9
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	SR10B(N2)	16:21:11	6.6	Bottom	3	2	19.07	8.04	32.88	83.80	6.0	3.3	4.6
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	CS2(A)	14:11:55	1.0	Surface	1	1	19.08	8.02	32.90	84.30	6.1	3.0	4.5
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	CS2(A)	14:12:23	1.0	Surface	1	2	19.09	8.02	32.85	84.30	6.1	3.0	4.6
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	CS2(A)	14:11:46	3.1	Middle	2	1	19.08	8.01	33.34	83.90	6.1	3.0	4.6
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	CS2(A)	14:12:12	3.1	Middle	2	2	19.09	8.01	33.34	84.00	6.1	3.1	4.3
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	CS2(A)	14:11:28	5.2	Bottom	3	1	19.02	8.01	33.25	83.90	6.1	3.0	3.7
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	CS2(A)	14:12:05	5.2	Bottom	3	2	19.02	8.01	33.23	83.70	6.0	3.1	4.2
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	CS(Mf)5	16:05:54	1.0	Surface	1	1	19.23	7.99	32.51	87.90	5.9	3.4	4.2
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	CS(Mf)5	16:06:39	1.0	Surface	1	2	19.30	7.98	32.64	88.10	5.9	3.3	4.8
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	CS(Mf)5	16:05:43	5.7	Middle	2	1	19.03	7.98	33.11	87.80	5.9	3.3	4.7
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	CS(Mf)5	16:06:22	5.7	Middle	2	2	19.05	7.98	33.12	87.50	5.9	3.4	5.0
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	CS(Mf)5	16:05:22	10.4	Bottom	3	1	19.01	7.98	33.05	87.50	5.9	3.3	5.0
HKLR	HY/2011/03	2025-04-02	Mid-Ebb	Sunny	CS(Mf)5	16:06:06	10.4	Bottom	3	2	19.02	7.98	33.10	87.10	5.8	3.4	5.1
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	IS5	09:13:46	1.0	Surface	1	1	19.13	7.99	32.36	92.10	6.1	3.4	5.0
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	IS5	09:14:28	1.0	Surface	1	2	19.25	8.00	32.50	92.50	6.2	3.3	5.0
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	IS5	09:13:23	4.3	Middle	2	1	19.27	7.99	32.95	91.10	6.1	3.3	4.9
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	IS5	09:14:09	4.3	Middle	2	2	19.25	7.99	32.96	92.40	6.2	3.5	5.4
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	IS5	09:13:03	7.6	Bottom	3	1	18.99	7.99	33.00	90.60	6.1	3.3	5.6
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	IS5	09:13:56	7.6	Bottom	3	2	19.17	7.99	33.00	92.30	6.2	3.3	5.2
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	IS(Mf)6	09:02:56	1.0	Surface	1	1	19.36	8.01	32.50	90.60	6.1	3.3	4.8
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	IS(Mf)6	09:03:25	1.0	Surface	1	2	19.35	8.01	32.42	90.40	6.1	3.4	4.8
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	IS(Mf)6	09:02:47	2.0	Bottom	3	1	19.29	8.00	32.75	90.50	6.1	3.3	4.9
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	IS(Mf)6	09:03:01	2.0	Bottom	3	2	19.29	8.00	32.71	90.20	6.1	3.3	4.4
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	IS7	08:52:56	1.0	Surface	1	1	19.37	7.98	32.39	89.40	6.0	3.4	4.0
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	IS7	08:53:21	1.0	Surface	1	2	19.39	7.98	32.37	89.40	6.0	3.4	4.1
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	IS7	08:52:29	2.0	Bottom	3	1	19.26	7.97	32.71	88.60	6.0	3.4	5.0
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	IS7	08:53:04	2.0	Bottom	3	2	19.26	7.97	32.72	89.60	6.0	3.4	4.9
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	IS8(N)	08:22:58	1.0	Surface	1	1	19.24	8.03	32.36	90.00	6.1	3.2	4.7
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	IS8(N)	08:23:26	1.0	Surface	1	2	19.26	8.03	32.35	90.00	6.1	3.2	4.2
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	IS8(N)	08:22:45	2.8	Bottom	3	1	19.15	8.02	32.68	89.60	6.0	3.2	4.0
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	IS8(N)	08:23:07	2.8	Bottom	3	2	19.19	8.03	32.63	89.90	6.1	3.3	4.4
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	IS(Mf)9	08:42:25	1.0	Surface	1	1	19.15	8.03	32.44	89.60	6.0	3.4	4.8
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	IS(Mf)9	08:42:51	1.0	Surface	1	2	19.20	8.03	32.41	89.40	6.0	3.4	4.4
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	IS(Mf)9	08:42:04	2.6	Bottom	3	1	18.93	8.02	32.72	89.60	6.0	3.4	5.0
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	IS(Mf)9	08:42:39	2.6	Bottom	3	2	19.12	8.02	32.67	89.30	6.0	3.4	4.2
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	IS10(N)	08:25:12	1.0	Surface	1	1	19.05	8.02	32.73	84.50	6.1	3.2	4.0
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	IS10(N)	08:25:45	1.0	Surface	1	2	19.08	8.01	32.72	84.60	6.1	3.3	3.7
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	IS10(N)	08:24:57	4.4	Middle	2	1	19.05	8.01	33.23	84.10	6.0	3.2	3.4
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	IS10(N)	08:25:35	4.4	Middle	2	2	19.05	8.01	33.17	84.40	6.0	3.3	4.0
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	IS10(N)	08:24:47	7.8	Bottom	3	1	19.01	8.01	33.15	83.80	6.0	3.2	4.2
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	IS10(N)	08:25:23	7.8	Bottom	3	2	19.01	8.01	33.14	84.80	6.1	3.3	4.3
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	SR3(N)	09:23:55	1.0	Surface	1	1	18.98	8.00	32.46	90.30	6.1	3.3	4.4
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	SR3(N)	09:24:31	1.0	Surface	1	2	19.01	8.00	32.42	90.60	6.1	3.4	4.4
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	SR3(N)	09:23:30	2.2	Bottom	3	1	19.00	7.99	32.74	90.20	6.1	3.3	4.6
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	SR3(N)	09:24:12	2.2	Bottom	3	2	19.20	8.00	32.57	89.90	6.0	3.4	4.1
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	SR4(N3)	08:33:54	1.0	Surface	1	1	19.21	8.02	32.34	89.50	6.0	3.2	4.4
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	SR4(N3)	08:34:25	1.0	Surface	1	2	19.08	8.02	32.35	89.40	6.0	3.2	4.4
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	SR4(N3)	08:33:43	2.6	Bottom	3	1	19.01	8.01	32.54	89.40	6.0	3.3	4.7
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	SR4(N3)	08:34:07	2.6	Bottom	3	2	19.02	8.01	32.60	89.20	6.0	3.3	4.5
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	SR5(N)	08:35:35	1	Surface	1	1	19.08	8.02	33.19	84.70	6.1	3.2	4.2
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	SR5(N)	08:36:07	1	Surface	1	2	19.05	8.02	33.22	84.20	6.1	3.3	4.2

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	SR5(N)	08:35:25	4.5	Middle	2	1	18.79	8.01	32.80	84.30	6.1	3.3	4.2
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	SR5(N)	08:35:58	4.5	Middle	2	2	18.77	8.01	32.76	83.00	6.0	3.3	4.4
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	SR5(N)	08:35:13	8.0	Bottom	3	1	18.85	8.02	33.28	83.90	6.0	3.2	4.5
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	SR5(N)	08:35:46	8.0	Bottom	3	2	18.78	8.02	33.27	83.00	6.0	3.3	4.4
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	SR10A(N)	07:31:16	1	Surface	1	1	19.01	8.03	33.32	84.30	6.1	3.2	3.8
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	SR10A(N)	07:31:58	1	Surface	1	2	18.96	8.03	33.32	84.30	6.1	3.2	3.8
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	SR10A(N)	07:31:08	5.5	Middle	2	1	18.78	8.02	33.25	83.50	6.0	3.3	4.1
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	SR10A(N)	07:31:42	5.5	Middle	2	2	18.76	8.02	33.23	83.90	6.1	3.3	4.7
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	SR10A(N)	07:30:51	10.0	Bottom	3	1	18.80	8.02	32.80	83.40	6.0	3.3	4.4
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	SR10A(N)	07:31:25	10.0	Bottom	3	2	18.79	8.02	32.78	83.80	6.0	3.3	4.0
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	SR10B(N2)	07:21:29	1.0	Surface	1	1	19.31	8.03	33.33	84.60	6.1	3.1	4.7
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	SR10B(N2)	07:22:09	1.0	Surface	1	2	19.07	8.03	33.34	84.50	6.1	3.2	4.3
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	SR10B(N2)	07:21:17	3.9	Middle	2	1	19.06	8.02	33.28	83.80	6.0	3.2	4.8
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	SR10B(N2)	07:21:56	3.9	Middle	2	2	19.10	8.02	33.31	84.20	6.1	3.1	5.0
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	SR10B(N2)	07:20:41	6.8	Bottom	3	1	19.06	8.03	32.91	83.20	6.0	3.2	5.0
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	SR10B(N2)	07:21:41	6.8	Bottom	3	2	19.07	8.03	32.86	83.80	6.0	3.1	4.9
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	CS2(A)	09:41:01	1	Surface	1	1	19.02	8.01	33.20	85.40	6.1	3.2	4.7
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	CS2(A)	09:41:36	1	Surface	1	2	19.02	8.02	33.28	84.20	6.0	3.2	4.8
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	CS2(A)	09:40:50	3.1	Middle	2	1	18.77	8.01	32.75	84.30	6.0	3.2	4.4
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	CS2(A)	09:41:27	3.1	Middle	2	2	18.73	8.01	32.76	84.10	6.0	3.2	4.4
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	CS2(A)	09:40:33	5.2	Bottom	3	1	18.81	8.01	33.14	83.90	6.0	3.2	4.3
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	CS2(A)	09:41:17	5.2	Bottom	3	2	18.80	8.01	33.28	83.70	6.0	3.1	4.5
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	CS(Mf)5	07:31:16	1.0	Surface	1	1	19.07	8.02	32.36	92.40	6.2	3.3	5.4
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	CS(Mf)5	07:32:13	1.0	Surface	1	2	19.24	8.05	32.31	90.80	6.1	3.3	4.6
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	CS(Mf)5	07:31:00	5.9	Middle	2	1	19.20	8.00	32.97	91.90	6.1	3.3	5.2
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	CS(Mf)5	07:31:45	5.9	Middle	2	2	18.96	8.03	33.01	90.60	6.0	3.3	4.9
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	CS(Mf)5	07:30:27	10.8	Bottom	3	1	18.97	8.00	32.98	90.60	6.0	3.3	5.3
HKLR	HY/2011/03	2025-04-02	Mid-Flood	Sunny	CS(Mf)5	07:31:33	10.8	Bottom	3	2	18.95	8.02	33.03	89.80	6.0	3.3	5.0
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Fine	IS5	16:21:48	1.0	Surface	1	1	19.32	8.00	32.83	88.30	5.8	3.2	3.2
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Fine	IS5	16:22:37	1.0	Surface	1	2	19.33	8.00	32.70	87.70	5.8	3.2	3.3
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Fine	IS5	16:21:35	4.0	Middle	2	1	19.30	8.02	33.31	88.00	5.8	3.2	3.3
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Fine	IS5	16:22:15	4.0	Middle	2	2	19.26	7.99	33.30	87.00	5.7	3.2	3.2
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Fine	IS5	16:21:22	7.0	Bottom	3	1	19.35	8.01	33.29	88.00	5.8	3.2	2.5
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Fine	IS5	16:22:02	7.0	Bottom	3	2	19.03	8.00	33.24	86.90	5.7	3.2	2.9
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Fine	IS(Mf)6	16:31:04	1.0	Surface	1	1	19.33	8.00	32.70	87.70	5.8	3.4	3.8
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Fine	IS(Mf)6	16:31:26	1.0	Surface	1	2	19.32	8.00	32.75	88.00	5.8	3.3	2.7
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Fine	IS(Mf)6	16:30:47	2.0	Bottom	3	1	19.31	7.99	33.23	87.60	5.7	3.4	2.8
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Fine	IS(Mf)6	16:31:16	2.0	Bottom	3	2	19.27	7.99	32.91	87.30	5.7	3.4	2.9
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Fine	IS7	16:40:44	1.0	Surface	1	1	19.25	7.97	32.85	88.70	5.9	3.3	2.6
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Fine	IS7	16:40:59	1.0	Surface	1	2	19.25	7.97	32.86	88.90	5.9	3.4	2.6
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Fine	IS7	16:40:25	2.0	Bottom	3	1	19.14	7.97	33.06	88.90	5.9	3.3	3.7
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Fine	IS7	16:40:51	2.0	Bottom	3	2	19.15	7.97	33.12	88.80	5.9	3.4	4.0
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Fine	IS8(N)	17:12:48	1.0	Surface	1	1	19.35	8.04	32.70	88.30	5.8	3.1	3.1
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Fine	IS8(N)	17:13:12	1.0	Surface	1	2	19.33	8.04	32.69	88.10	5.8	3.1	3.0
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Fine	IS8(N)	17:12:37	2.8	Bottom	3	1	19.27	8.03	32.93	88.10	5.8	3.1	3.1
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Fine	IS8(N)	17:13:02	2.8	Bottom	3	2	19.31	8.04	32.90	88.00	5.8	3.2	2.9
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Fine	IS(Mf)9	16:51:07	1.0	Surface	1	1	19.29	8.00	32.82	89.00	5.9	3.4	3.0
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Fine	IS(Mf)9	16:51:45	1.0	Surface	1	2	19.36	8.01	32.78	88.80	5.8	3.3	3.5
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Fine	IS(Mf)9	16:50:57	2.6	Bottom	3	1	19.15	7.99	33.06	88.90	5.9	3.3	3.6
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Fine	IS(Mf)9	16:51:22	2.6	Bottom	3	2	19.19	8.00	33.05	89.00	5.9	3.3	3.6
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Sunny	IS10(N)	16:54:47	1.0	Surface	1	1	19.24	8.10	31.80	93.80	6.5	2.5	3.8
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Sunny	IS10(N)	16:55:25	1.0	Surface	1	2	19.28	8.09	31.76	94.30	6.5	2.5	2.8
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Sunny	IS10(N)	16:55:10	5.4	Middle	2	1	19.00	8.07	32.93	90.60	6.2	2.8	2.4
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Sunny	IS10(N)	16:54:34	5.4	Middle	2	2	18.99	8.07	32.94	89.90	6.2	2.8	3.0
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Sunny	IS10(N)	16:54:23	9.7	Bottom	3	1	18.99	8.07	33.11	90.00	6.2	2.9	3.2
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Sunny	IS10(N)	16:55:00	9.7	Bottom	3	2	19.04	8.07	33.02	90.30	6.2	2.9	3.9
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Fine	SR3(N)	16:10:41	1.0	Surface	1	1	19.08	8.01	32.65	88.60	5.8	3.1	3.0
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Fine	SR3(N)	16:11:06	1.0	Surface	1	2	19.08	8.01	32.61	88.90	5.8	3.2	3.0
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Fine	SR3(N)	16:10:23	2.0	Bottom	3	1	19.07	8.00	32.93	88.50	5.8	3.1	2.6
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Fine	SR3(N)	16:10:51	2.0	Bottom	3	2	19.27	8.01	32.76	88.20	5.8	3.2	2.7
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Fine	SR4(N3)	17:02:51	1.0	Surface	1	1	19.32	8.01	32.74	89.10	5.9	3.1	2.6
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Fine	SR4(N3)	17:03:26	1.0	Surface	1	2	19.31	8.01	32.74	88.90	5.9	3.2	2.6
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Fine	SR4(N3)	17:02:36	2.6	Bottom	3	1	19.26	8.01	32.89	88.90	5.9	3.1	2.7
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Fine	SR4(N3)	17:03:05	2.6	Bottom	3	2	19.26	8.01	32.93	88.80	5.9	3.1	3.3
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Sunny	SR5(N)	16:45:30	1.0	Surface	1	1	19.26	8.09	31.78	94.80	6.5	2.6	3.4
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Sunny	SR5(N)	16:44:53	1.0	Surface	1	2	19.22	8.09	31.81	94.30	6.5	2.6	3.3
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Sunny	SR5(N)	16:44:40	4.7	Middle	2	1	19.03	8.08	32.77	90.10	6.2	2.9	2.9
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Sunny	SR5(N)	16:45:18	4.7	Middle	2	2	19.03	8.07	32.80	90.40	6.2	2.8	3.0
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Sunny	SR5(N)	16:45:07	8.3	Bottom	3	1	19.02	8.07	33.04	90.60	6.2	3.2	2.3
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Sunny	SR5(N)	16:44:28	8.3	Bottom	3	2	18.99	8.06	33.09	89.80	6.2	3.2	3.0
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Sunny	SR10A(N)	17:41:34	1.0	Surface	1	1	19.19	8.09	32.71	96.00	6.6	2.2	2.7
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Sunny	SR10A(N)	17:40:44	1.0	Surface	1	2	19.22	8.10	32.67	95.90	6.6	2.2	3.6
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Sunny	SR10A(N)	17:41:14	6.8	Middle	2	1	18.97	8.07	33.58	91.00	6.2	2.4	2.8
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Sunny	SR10A(N)	17:40:27	6.8	Middle	2	2	18.95	8.08	33.69	91.60	6.3	2.4	3.1
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Sunny	SR10A(N)	17:40:10	12.5	Bottom	3	1	18.96	8.09	33.69	91.60	6.3	2.5	3.3
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Sunny	SR10A(N)	17:41:02	12.5	Bottom	3	2	18.98	8.07	33.63	91.00	6.2	2.6	2.7
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Sunny	SR10B(N2)	17:50:54	1.0	Surface	1	1	19.23	8.09	32.64	95.10	6.5	2.1	2.9
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Sunny	SR10B(N2)	17:51:34	1.0	Surface	1	2	19.21	8.09	32.68	94.90	6.5	2.1	2.8
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Sunny	SR10B(N2)	17:50:42	3.8	Middle	2	1	19.02	8.07	33.37	90.90	6.2	2.2	2.0
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Sunny	SR10B(N2)	17:51:22	3.8	Middle	2	2	19.02	8.07	33.32	91.40	6.3	2.2	2.6
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Sunny	SR10B(N2)	17:50:32	6.6	Bottom	3	1	18.98	8.06	33.59	90.60	6.2	2.5	2.4
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Sunny	SR10B(N2)	17:51:06	6.6	Bottom	3	2	19.01	8.06	33.52	90.70	6.2	2.5	3.0
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Sunny	CS2(A)	15:56:05	1.0	Surface	1	1	19.14	8.11	31.83	97.70	6.8	2.6	2.6
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Sunny	CS2(A)	15:56:37	1.0	Surface	1	2	19.15	8.10	31.83	97.00	6.7	2.6	3.0
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Sunny	CS2(A)	15:55:53	3.4	Middle	2	1	18.97	8.08	32.74	92.70	6.4	3.0	2.7
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Sunny	CS2(A)	15:56:26	3.4	Middle	2	2	18.99	8.08	32.78	92.80	6.4	2.9	3.2
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Sunny	CS2(A)	15:55:42	5.7	Bottom	3	1	18.94	8.09	33.09	92.10	6.4	3.1	2.8
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Sunny	CS2(A)	15:56:17	5.7	Bottom	3	2	18.97	8.08	33.06	92.40	6.4	3.2	2.8
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Fine	CS(Mf)5	17:59:06	1.0	Surface	1	1	19.35	8.00	32.75	86.40	5.7	3.1	2.9
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Fine	CS(Mf)5	17:59:58	1.0	Surface	1	2	19.28	8.01	32.82	86.20	5.6	3.2	2.4
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Fine	CS(Mf)5	17:58:56	5.8	Middle	2	1	19.10	8.00	33.26	85.80	5.6	3.2	3.0
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Fine	CS(Mf)5	17:59:34	5.8	Middle	2	2	19.09	8.00	32.71	86.10	5.6	3.1	3.1
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Fine	CS(Mf)5	17:58:34	10.6	Bottom	3	1	19.07	8.00	33.25	85.40	5.6	3.2	4.8
HKLR	HY/2011/03	2025-04-04	Mid-Ebb	Fine	CS(Mf)5	17:59:18	10.6	Bottom	3	2	19.06	8.00	33.21	85.80	5.6	3.1	5.0
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Fine	IS5	10:02:13	1.0	Surface	1	1	19.33	8.01	32.69	90.80	5.9	3.2	3.4
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Fine	IS5	10:02:55	1.0	Surface	1	2	19.20	8.00	32.55	90.40	5.9	3.3	2.6
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Fine	IS5	10:01:50	4.1	Middle	2	1	19.32	8.00	33.15	90.70	5.9	3.4	2.9
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Fine	IS5	10:02:34	4.1	Middle	2	2	19.34	8.00	33.14	89.40	5.9	3.2	2.8
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Fine	IS5	10:01:32	7.2	Bottom	3	1	19.24	8.00	33.19	90.60	5.9	3.2	2.3
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Fine	IS5	10:02:23	7.2	Bottom	3	2	19.06	8.00	33.19	88.90	5.9	3.2	2.1
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Fine	IS(Mf)6	09:51:23	1.0	Surface	1	1	19.42	8.04	32.58	88.30	5.8	3.0	2.6
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Fine	IS(Mf)6	09:51:52	1.0	Surface	1	2	19.44	8.04	32.56	88.30	5.8	3.0	2.3
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Fine	IS(Mf)6	09:51:12	2.0	Bottom	3	1	19.33	8.03	32.54	87.90	5.8	3.0	2.3
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Fine	IS(Mf)6	09:51:28	2.0	Bottom	3	2	19.36	8.04	32.91	88.20	5.8	3.1	2.1

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Fine	IS7	09:42:33	1.0	Surface	1	1	19.43	8.03	32.69	88.90	5.9	3.0	2.9
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Fine	IS7	09:42:58	1.0	Surface	1	2	19.42	8.03	32.61	88.70	5.8	3.1	3.2
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Fine	IS7	09:42:08	2.0	Bottom	3	1	19.36	8.02	32.94	88.80	5.9	3.0	3.1
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Fine	IS7	09:42:41	2.0	Bottom	3	2	19.36	8.02	32.90	88.50	5.8	3.0	3.2
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Fine	IS8(N)	09:12:18	1.0	Surface	1	1	19.37	8.03	32.53	87.80	5.8	3.0	2.2
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Fine	IS8(N)	09:12:43	1.0	Surface	1	2	19.26	8.03	32.54	87.70	5.8	3.0	3.1
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Fine	IS8(N)	09:12:02	3.0	Bottom	3	1	19.19	8.02	32.73	87.70	5.8	3.1	2.7
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Fine	IS8(N)	09:12:24	3.0	Bottom	3	2	19.20	8.02	32.79	87.50	5.7	3.1	3.5
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Fine	IS(Mf)9	09:32:02	1.0	Surface	1	1	19.44	8.00	32.87	87.70	5.8	3.1	2.6
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Fine	IS(Mf)9	09:32:28	1.0	Surface	1	2	19.44	8.00	32.82	87.70	5.8	3.1	2.5
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Fine	IS(Mf)9	09:31:46	2.6	Bottom	3	1	19.33	7.99	32.90	86.90	5.7	3.1	2.8
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Fine	IS(Mf)9	09:32:16	2.6	Bottom	3	2	19.33	7.99	32.55	87.90	5.8	3.1	2.6
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Sunny	IS10(N)	09:21:39	1.0	Surface	1	1	19.06	8.09	32.36	93.90	6.5	2.4	3.0
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Sunny	IS10(N)	09:20:58	1.0	Surface	1	2	19.04	8.10	32.38	93.80	6.5	2.4	2.4
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Sunny	IS10(N)	09:21:24	5.4	Middle	2	1	18.91	8.08	33.17	89.40	6.2	2.7	1.8
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Sunny	IS10(N)	09:20:45	5.4	Middle	2	2	18.90	8.08	33.16	89.80	6.2	2.6	2.6
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Sunny	IS10(N)	09:21:14	9.7	Bottom	3	1	18.92	8.08	33.22	88.80	6.1	2.9	2.0
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Sunny	IS10(N)	09:20:34	9.7	Bottom	3	2	18.90	8.08	33.24	88.90	6.1	2.9	2.8
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Fine	SR3(N)	10:12:52	1.0	Surface	1	1	19.25	8.01	32.68	86.70	5.7	3.3	2.3
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Fine	SR3(N)	10:13:28	1.0	Surface	1	2	19.24	8.01	32.68	86.70	5.7	3.2	2.6
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Fine	SR3(N)	10:12:27	2.0	Bottom	3	1	19.17	8.01	32.85	86.30	5.7	3.3	3.3
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Fine	SR3(N)	10:13:07	2.0	Bottom	3	2	19.21	8.02	32.94	87.30	5.7	3.2	2.8
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Fine	SR4(N3)	09:22:31	1.0	Surface	1	1	19.33	8.05	32.63	87.90	5.8	3.1	3.5
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Fine	SR4(N3)	09:23:02	1.0	Surface	1	2	19.38	8.05	32.60	87.70	5.8	3.1	2.7
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Fine	SR4(N3)	09:22:22	2.8	Bottom	3	1	19.11	8.04	32.91	87.90	5.8	3.1	2.5
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Fine	SR4(N3)	09:22:44	2.8	Bottom	3	2	19.31	8.04	32.86	87.60	5.8	3.1	3.6
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Sunny	SR5(N)	09:32:38	1	Surface	1	1	19.05	8.10	32.41	92.40	6.4	2.3	2.5
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Sunny	SR5(N)	09:31:56	1	Surface	1	2	19.06	8.10	32.40	92.60	6.4	2.3	2.7
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Sunny	SR5(N)	09:32:23	4.7	Middle	2	1	18.92	8.09	33.04	89.00	6.1	2.5	3.4
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Sunny	SR5(N)	09:31:43	4.7	Middle	2	2	18.93	8.09	33.06	89.10	6.2	2.6	4.3
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Sunny	SR5(N)	09:31:32	8.4	Bottom	3	1	18.90	8.08	33.26	88.70	6.1	2.9	4.3
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Sunny	SR5(N)	09:32:13	8.4	Bottom	3	2	18.91	8.08	33.21	88.60	6.1	2.9	3.3
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Sunny	SR10A(N)	08:26:39	1	Surface	1	1	19.09	8.09	32.66	92.70	6.4	2.0	3.1
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Sunny	SR10A(N)	08:25:49	1	Surface	1	2	19.13	8.08	32.54	92.80	6.4	2.1	2.3
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Sunny	SR10A(N)	08:26:22	6.7	Middle	2	1	18.92	8.07	33.52	88.20	6.1	2.2	2.5
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Sunny	SR10A(N)	08:25:33	6.7	Middle	2	2	18.91	8.07	33.53	88.70	6.1	2.2	2.5
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Sunny	SR10A(N)	08:26:12	12.3	Bottom	3	1	18.94	8.07	33.57	88.00	6.0	2.5	2.1
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Sunny	SR10A(N)	08:25:22	12.3	Bottom	3	2	18.93	8.07	33.59	88.60	6.1	2.5	2.4
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Sunny	SR10B(N2)	08:16:23	1.0	Surface	1	1	19.12	8.10	32.65	97.60	6.7	2.1	2.4
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Sunny	SR10B(N2)	08:15:42	1.0	Surface	1	2	19.13	8.08	32.64	97.30	6.7	2.1	3.0
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Sunny	SR10B(N2)	08:15:27	3.8	Middle	2	1	18.99	8.06	33.16	93.00	6.4	2.3	2.4
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Sunny	SR10B(N2)	08:16:08	3.8	Middle	2	2	19.00	8.06	33.14	91.60	6.3	2.2	3.3
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Sunny	SR10B(N2)	08:15:57	6.6	Bottom	3	1	18.97	8.06	33.43	90.20	6.2	2.5	3.6
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Sunny	SR10B(N2)	08:15:16	6.6	Bottom	3	2	18.85	8.05	33.47	90.20	6.2	2.5	3.0
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Sunny	CS2(A)	10:21:54	1	Surface	1	1	19.03	8.10	32.37	93.20	6.5	2.4	3.0
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Sunny	CS2(A)	10:21:15	1	Surface	1	2	19.03	8.09	32.40	93.20	6.5	2.4	2.4
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Sunny	CS2(A)	10:21:05	3.4	Middle	2	1	18.90	8.10	33.09	90.30	6.2	2.7	2.3
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Sunny	CS2(A)	10:21:41	3.4	Middle	2	2	18.89	8.10	33.09	90.30	6.2	2.6	3.4
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Sunny	CS2(A)	10:20:53	5.7	Bottom	3	1	18.86	8.10	33.36	89.70	6.2	2.8	2.8
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Sunny	CS2(A)	10:21:33	5.7	Bottom	3	2	18.88	8.10	33.35	89.70	6.2	2.9	3.0
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Fine	CS(Mf)5	08:29:33	1.0	Surface	1	1	19.42	8.03	32.50	89.10	5.8	3.1	2.8
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Fine	CS(Mf)5	08:30:30	1.0	Surface	1	2	19.25	8.03	32.55	90.70	5.9	3.1	3.6
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Fine	CS(Mf)5	08:29:17	6.0	Middle	2	1	19.14	8.01	33.20	88.90	5.8	3.1	3.0
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Fine	CS(Mf)5	08:30:02	6.0	Middle	2	2	19.38	8.02	33.16	90.20	5.9	3.1	2.8
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Fine	CS(Mf)5	08:28:42	11.0	Bottom	3	1	19.11	8.01	33.22	88.10	5.8	3.1	2.3
HKLR	HY/2011/03	2025-04-04	Mid-Flood	Fine	CS(Mf)5	08:29:51	11.0	Bottom	3	2	19.15	8.02	33.17	88.90	5.8	3.1	2.7
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	IS5	20:35:05	1.0	Surface	1	1	19.04	8.08	32.80	92.40	6.7	2.8	4.5
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	IS5	20:35:41	1.0	Surface	1	2	19.07	8.08	32.79	92.60	6.7	2.8	4.3
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	IS5	20:34:54	4.3	Middle	2	1	18.93	8.06	33.16	91.40	6.6	3.2	5.2
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	IS5	20:35:29	4.3	Middle	2	2	18.94	8.05	33.15	91.60	6.6	3.3	5.0
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	IS5	20:34:45	7.5	Bottom	3	1	18.91	8.06	33.34	90.90	6.5	3.4	4.6
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	IS5	20:35:19	7.5	Bottom	3	2	18.92	8.05	33.33	91.40	6.6	3.4	5.4
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	IS(Mf)6	20:46:25	1.0	Surface	1	1	19.06	8.08	32.78	94.90	6.8	2.6	6.4
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	IS(Mf)6	20:46:08	1.0	Surface	1	2	19.06	8.08	32.64	94.30	6.8	2.6	5.4
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	IS(Mf)6	20:46:16	2.2	Bottom	3	1	19.03	8.08	32.87	93.30	6.7	3.1	4.9
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	IS(Mf)6	20:45:52	2.2	Bottom	3	2	19.00	8.09	32.84	92.20	6.6	3.2	5.6
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	IS7	20:57:21	1.0	Surface	1	1	19.09	8.09	32.79	95.10	6.8	2.3	5.4
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	IS7	20:57:04	1.0	Surface	1	2	19.07	8.09	32.85	94.20	6.8	2.5	5.2
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	IS7	20:56:55	2.3	Bottom	3	1	19.03	8.09	32.90	93.00	6.7	2.7	5.2
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	IS7	20:57:11	2.3	Bottom	3	2	19.04	8.09	32.92	93.50	6.7	2.7	4.6
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	IS8(N)	21:34:14	1.0	Surface	1	1	19.07	8.07	32.79	92.30	6.6	2.6	5.5
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	IS8(N)	21:34:32	1.0	Surface	1	2	19.09	8.07	32.77	93.10	6.7	2.5	5.5
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	IS8(N)	21:34:23	3.0	Bottom	3	1	19.06	8.07	32.90	92.10	6.6	2.9	5.0
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	IS8(N)	21:34:04	3.0	Bottom	3	2	19.02	8.07	32.94	91.30	6.6	3.0	6.1
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	IS(Mf)9	21:08:17	1.0	Surface	1	1	19.06	8.08	32.86	93.20	6.7	2.4	7.9
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	IS(Mf)9	21:07:57	1.0	Surface	1	2	19.06	8.08	32.84	92.70	6.7	2.5	9.4
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	IS(Mf)9	21:08:07	2.6	Bottom	3	1	19.03	8.08	32.94	92.80	6.7	2.7	6.2
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	IS(Mf)9	21:07:49	2.6	Bottom	3	2	19.01	8.08	32.98	92.40	6.6	2.7	5.2
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	IS10(N)	21:39:10	1.0	Surface	1	1	19.09	8.07	32.33	93.20	6.5	2.6	3.8
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	IS10(N)	21:39:48	1.0	Surface	1	2	19.11	8.07	32.30	93.70	6.6	2.4	4.4
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	IS10(N)	21:38:57	5.3	Middle	2	1	18.93	8.05	33.15	91.00	6.4	3.0	4.2
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	IS10(N)	21:39:33	5.3	Middle	2	2	18.93	8.05	33.15	91.40	6.4	3.0	3.4
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	IS10(N)	21:39:23	9.6	Bottom	3	1	18.96	8.05	33.22	91.10	6.4	3.2	3.2
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	IS10(N)	21:38:46	9.6	Bottom	3	2	18.93	8.05	33.27	91.10	6.4	3.0	3.8
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	SR3(N)	20:22:41	1.0	Surface	1	1	19.08	8.08	32.76	94.70	6.8	2.8	5.8
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	SR3(N)	20:22:23	1.0	Surface	1	2	19.08	8.08	32.71	93.60	6.7	2.9	6.6
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	SR3(N)	20:22:12	2.3	Bottom	3	1	19.04	8.08	32.88	91.60	6.5	3.2	5.1
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	SR3(N)	20:22:30	2.3	Bottom	3	2	19.06	8.08	32.74	93.00	6.7	3.0	5.1
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	SR4(N3)	21:24:19	1.0	Surface	1	1	19.06	8.08	32.76	93.10	6.7	2.4	4.8
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	SR4(N3)	21:24:00	1.0	Surface	1	2	19.08	8.08	32.68	92.50	6.7	2.4	5.6
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	SR4(N3)	21:24:09	2.8	Bottom	3	1	19.05	8.07	32.89	92.00	6.6	2.6	5.2
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	SR4(N3)	21:23:50	2.8	Bottom	3	2	18.66	8.06	32.94	91.10	6.6	2.6	4.7
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	SR5(N)	21:30:17	1.0	Surface	1	1	19.11	8.07	32.33	94.30	6.6	2.7	3.0
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	SR5(N)	21:29:39	1.0	Surface	1	2	19.08	8.07	32.35	93.80	6.6	2.8	3.0
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	SR5(N)	21:29:26	4.6	Middle	2	1	18.96	8.06	33.03	91.00	6.4	3.1	4.0
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	SR5(N)	21:30:05	4.6	Middle	2	2	18.96	8.05	33.04	91.30	6.4	3.0	3.5
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	SR5(N)	21:29:54	8.2	Bottom	3	1	18.94	8.05	33.25	91.50	6.4	3.4	2.2
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	SR5(N)	21:29:14	8.2	Bottom	3	2	18.92	8.05	33.27	91.00	6.4	3.2	2.7
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	SR10A(N)	22:28:40	1.0	Surface	1	1	19.06	8.07	33.07	94.70	6.6	2.5	3.1
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	SR10A(N)	22:27:51	1.0	Surface	1	2	19.09	8.08	33.03	94.60	6.6	2.5	3.9
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	SR10A(N)	22:28:20	6.6	Middle	2	1	18.93	8.06	33.69	91.20	6.4	3.0	2.9
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	SR10A(N)	22:27:36	6.6	Middle	2	2	18.92	8.06	33.75	91.80	6.4	3.0	2.8
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	SR10A(N)	22:27:21	12.1	Bottom	3	1	18.93	8.07	33.76	92.00	6.4	3.1	3.8
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	SR10A(N)	22:28:08	12.1	Bottom	3	2	18.95	8.06	33.72	91.50	6.4	3.3	3.4

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	SR10B(N2)	22:38:56	1.0	Surface	1	1	19.10	8.07	33.04	93.80	6.5	2.4	3.9
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	SR10B(N2)	22:39:34	1.0	Surface	1	2	19.08	8.07	33.07	93.80	6.5	2.4	2.9
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	SR10B(N2)	22:38:44	3.8	Middle	2	1	18.98	8.06	33.53	91.40	6.4	2.7	3.2
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	SR10B(N2)	22:39:22	3.8	Middle	2	2	18.98	8.06	33.49	91.60	6.4	2.7	4.0
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	SR10B(N2)	22:38:34	6.6	Bottom	3	1	18.94	8.05	33.68	91.20	6.4	3.2	3.9
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	SR10B(N2)	22:39:09	6.6	Bottom	3	2	18.97	8.05	33.62	91.20	6.4	3.2	4.1
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	CS2(A)	20:41:44	1.0	Surface	1	1	18.99	8.08	32.41	96.90	6.8	3.2	4.3
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	CS2(A)	20:42:17	1.0	Surface	1	2	19.00	8.08	32.39	96.40	6.8	3.0	4.2
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	CS2(A)	20:41:33	3.3	Middle	2	1	18.89	8.06	33.04	93.40	6.6	3.2	4.6
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	CS2(A)	20:42:06	3.3	Middle	2	2	18.91	8.06	33.07	93.50	6.6	3.1	4.6
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	CS2(A)	20:41:22	5.6	Bottom	3	1	18.87	8.06	33.31	93.10	6.5	3.3	4.6
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	CS2(A)	20:41:56	5.6	Bottom	3	2	18.88	8.06	33.29	93.40	6.5	3.3	5.0
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	CS(Mf)5	22:16:39	1.0	Surface	1	1	19.05	8.08	33.07	89.90	6.5	2.0	5.2
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	CS(Mf)5	22:15:57	1.0	Surface	1	2	19.06	8.08	33.07	89.50	6.4	2.0	5.4
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	CS(Mf)5	22:15:42	6.4	Middle	2	1	18.78	8.05	33.95	87.70	6.3	2.5	5.7
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	CS(Mf)5	22:16:23	6.4	Middle	2	2	18.79	8.07	33.94	87.60	6.3	2.3	5.3
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	CS(Mf)5	22:16:14	11.7	Bottom	3	1	18.79	8.06	33.48	86.80	6.2	2.6	5.7
HKLR	HY/2011/03	2025-04-07	Mid-Ebb	Fine	CS(Mf)5	22:15:32	11.7	Bottom	3	2	18.77	8.05	34.05	86.50	6.2	2.6	5.1
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	IS5	09:53:17	1.0	Surface	1	1	18.92	8.09	32.82	89.90	6.3	2.6	4.3
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	IS5	09:52:33	1.0	Surface	1	2	18.94	8.09	32.80	91.10	6.4	2.5	3.6
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	IS5	09:52:21	4.2	Middle	2	1	18.79	8.07	33.43	87.60	6.1	3.0	4.8
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	IS5	09:53:04	4.2	Middle	2	2	18.79	8.05	33.43	87.90	6.1	3.0	5.3
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	IS5	09:52:48	7.4	Bottom	3	1	18.77	8.05	33.43	86.70	6.0	3.2	5.0
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	IS5	09:52:10	7.4	Bottom	3	2	18.79	8.06	33.44	86.60	6.0	3.3	4.0
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	IS(Mf)6	09:43:12	1.0	Surface	1	1	18.95	8.09	32.83	92.60	6.4	2.7	4.8
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	IS(Mf)6	09:42:55	1.0	Surface	1	2	18.95	8.09	32.78	92.30	6.4	2.7	4.8
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	IS(Mf)6	09:43:03	2.2	Bottom	3	1	18.92	8.08	32.97	91.80	6.4	3.1	4.6
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	IS(Mf)6	09:42:44	2.2	Bottom	3	2	18.91	8.08	32.99	91.70	6.4	3.1	4.4
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	IS7	09:33:15	1.0	Surface	1	1	18.97	8.08	32.85	91.90	6.4	2.7	4.0
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	IS7	09:33:00	1.0	Surface	1	2	18.95	8.09	32.86	91.40	6.4	2.7	4.6
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	IS7	09:33:06	2.3	Bottom	3	1	18.94	8.08	32.87	91.30	6.4	3.1	4.2
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	IS7	09:32:50	2.3	Bottom	3	2	18.92	8.08	32.99	90.90	6.3	3.0	4.5
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	IS8(N)	08:59:15	1.0	Surface	1	1	18.94	8.08	32.87	92.40	6.5	2.7	4.8
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	IS8(N)	08:58:30	1.0	Surface	1	2	18.94	8.08	32.87	91.80	6.4	2.7	4.7
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	IS8(N)	08:58:39	3.1	Bottom	3	1	18.90	8.07	33.11	91.30	6.4	2.9	5.4
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	IS8(N)	08:58:20	3.1	Bottom	3	2	18.88	8.07	33.22	90.70	6.3	3.1	4.9
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	IS(Mf)9	09:23:58	1.0	Surface	1	1	18.96	8.09	32.77	92.10	6.4	2.5	4.0
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	IS(Mf)9	09:23:42	1.0	Surface	1	2	18.96	8.09	32.87	91.40	6.4	2.6	3.2
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	IS(Mf)9	09:23:49	2.6	Bottom	3	1	18.92	8.08	33.02	91.20	6.4	3.0	3.5
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	IS(Mf)9	09:23:32	2.6	Bottom	3	2	18.90	8.07	32.94	90.50	6.3	2.9	4.5
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	IS10(N)	09:32:19	1.0	Surface	1	1	18.95	8.07	32.67	93.90	6.6	2.9	5.5
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	IS10(N)	09:32:59	1.0	Surface	1	2	18.96	8.07	32.67	93.90	6.6	2.9	4.4
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	IS10(N)	09:32:44	5.4	Middle	2	1	18.87	8.05	33.28	90.80	6.4	3.4	4.6
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	IS10(N)	09:32:06	5.4	Middle	2	2	18.87	8.05	33.27	91.20	6.4	3.3	4.8
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	IS10(N)	09:32:34	9.7	Bottom	3	1	18.88	8.05	33.32	90.70	6.4	3.5	4.1
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	IS10(N)	09:31:55	9.7	Bottom	3	2	18.87	8.06	33.34	90.90	6.4	3.4	5.0
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	SR3(N)	10:05:05	1.0	Surface	1	1	18.95	8.08	32.83	90.90	6.3	2.6	4.6
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	SR3(N)	10:05:21	1.0	Surface	1	2	18.95	8.08	32.71	91.50	6.4	2.5	5.2
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	SR3(N)	10:05:13	2.3	Bottom	3	1	18.93	8.08	32.93	90.50	6.3	2.9	3.4
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	SR3(N)	10:04:56	2.3	Bottom	3	2	18.91	8.08	32.86	89.90	6.3	3.1	4.1
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	SR4(N3)	09:08:00	1.0	Surface	1	1	18.95	8.08	32.87	91.30	6.4	2.4	3.5
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	SR4(N3)	09:07:43	1.0	Surface	1	2	18.94	8.08	32.81	91.50	6.4	2.4	4.5
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	SR4(N3)	09:07:52	2.9	Bottom	3	1	18.89	8.06	33.15	90.60	6.3	2.7	4.4
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	SR4(N3)	09:07:31	2.9	Bottom	3	2	18.87	8.06	33.26	90.60	6.3	2.6	4.0
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	SR5(N)	09:42:41	1	Surface	1	1	18.96	8.07	32.71	92.30	6.5	2.9	3.9
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	SR5(N)	09:41:59	1	Surface	1	2	18.96	8.07	32.70	92.50	6.5	2.9	4.7
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	SR5(N)	09:42:27	4.7	Middle	2	1	18.88	8.06	33.18	90.20	6.3	3.0	6.3
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	SR5(N)	09:41:47	4.7	Middle	2	2	18.89	8.06	33.19	90.40	6.3	3.0	6.1
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	SR5(N)	09:41:35	8.4	Bottom	3	1	18.86	8.05	33.36	90.50	6.3	3.4	4.7
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	SR5(N)	09:42:17	8.4	Bottom	3	2	18.87	8.05	33.33	90.30	6.3	3.3	5.8
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	SR10A(N)	08:39:53	1	Surface	1	1	19.01	8.06	32.97	92.60	6.5	2.3	5.6
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	SR10A(N)	08:39:05	1	Surface	1	2	19.03	8.06	32.90	92.40	6.5	2.4	5.7
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	SR10A(N)	08:39:34	6.5	Middle	2	1	18.90	8.04	33.58	89.30	6.2	2.6	4.5
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	SR10A(N)	08:38:49	6.5	Middle	2	2	18.90	8.04	33.59	89.90	6.3	2.6	5.2
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	SR10A(N)	08:39:24	12.0	Bottom	3	1	18.92	8.04	33.64	89.50	6.2	3.2	4.7
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	SR10A(N)	08:38:38	12.0	Bottom	3	2	18.90	8.04	33.65	90.10	6.3	3.2	5.5
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	SR10B(N2)	08:29:29	1.0	Surface	1	1	19.03	8.06	32.96	96.80	6.8	2.4	5.7
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	SR10B(N2)	08:28:48	1.0	Surface	1	2	19.04	8.05	32.95	96.50	6.8	2.4	4.8
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	SR10B(N2)	08:28:31	3.8	Middle	2	1	18.95	8.03	33.35	93.50	6.5	2.7	4.1
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	SR10B(N2)	08:29:14	3.8	Middle	2	2	18.96	8.04	33.30	92.00	6.4	2.6	4.4
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	SR10B(N2)	08:29:03	6.6	Bottom	3	1	18.93	8.04	33.56	91.10	6.4	3.1	4.8
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	SR10B(N2)	08:28:20	6.6	Bottom	3	2	18.86	8.03	33.59	91.10	6.4	3.1	4.7
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	CS2(A)	10:31:48	1	Surface	1	1	18.92	8.08	32.68	93.40	6.6	2.5	3.8
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	CS2(A)	10:31:10	1	Surface	1	2	18.92	8.07	32.70	93.40	6.6	2.7	4.7
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	CS2(A)	10:31:36	3.3	Middle	2	1	18.84	8.07	33.16	91.60	6.4	3.0	4.2
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	CS2(A)	10:31:00	3.3	Middle	2	2	18.85	8.08	33.16	91.40	6.4	2.9	3.9
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	CS2(A)	10:30:48	5.6	Bottom	3	1	18.82	8.07	33.39	91.10	6.4	3.2	3.8
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	CS2(A)	10:31:26	5.6	Bottom	3	2	18.83	8.07	33.38	91.20	6.4	3.4	4.8
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	CS(Mf)5	08:12:48	1.0	Surface	1	1	18.95	8.07	32.74	91.30	6.3	2.3	4.5
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	CS(Mf)5	08:12:05	1.0	Surface	1	2	18.94	8.06	32.77	90.90	6.3	2.4	3.5
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	CS(Mf)5	08:12:31	6.3	Middle	2	1	18.75	8.06	33.49	88.60	6.2	2.7	3.3
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	CS(Mf)5	08:11:50	6.3	Middle	2	2	18.77	8.05	33.47	88.80	6.2	2.7	2.5
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	CS(Mf)5	08:11:38	11.5	Bottom	3	1	18.77	8.04	33.64	87.50	6.1	3.1	2.2
HKLR	HY/2011/03	2025-04-07	Mid-Flood	Fine	CS(Mf)5	08:12:21	11.5	Bottom	3	2	18.77	8.05	33.66	87.10	6.1	3.1	2.4
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	IS5	10:20:20	1.0	Surface	1	1	19.07	8.06	33.09	90.90	6.6	2.8	2.4
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	IS5	10:20:56	1.0	Surface	1	2	19.09	8.06	33.03	91.00	6.6	2.8	3.0
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	IS5	10:20:10	4.3	Middle	2	1	19.00	8.04	33.36	89.90	6.5	3.0	2.9
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	IS5	10:20:44	4.3	Middle	2	2	19.00	8.04	33.31	90.00	6.5	3.0	3.4
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	IS5	10:20:00	7.5	Bottom	3	1	18.98	8.05	33.47	89.40	6.5	3.0	3.8
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	IS5	10:20:34	7.5	Bottom	3	2	18.99	8.04	33.45	89.70	6.5	3.0	3.4
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	IS(Mf)6	10:31:33	1.0	Surface	1	1	19.07	8.07	32.97	94.20	6.8	2.8	3.7
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	IS(Mf)6	10:31:16	1.0	Surface	1	2	19.07	8.07	32.90	93.20	6.7	2.8	2.6
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	IS(Mf)6	10:31:25	2.2	Bottom	3	1	19.06	8.07	33.05	92.60	6.7	2.9	3.7
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	IS(Mf)6	10:31:02	2.2	Bottom	3	2	19.03	8.08	33.06	91.50	6.6	2.9	3.4
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	IS7	10:41:36	1.0	Surface	1	1	19.10	8.08	32.97	94.70	6.8	2.8	3.2
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	IS7	10:41:18	1.0	Surface	1	2	19.09	8.08	33.00	93.70	6.8	2.8	2.9
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	IS7	10:41:07	2.3	Bottom	3	1	19.06	8.08	33.05	92.50	6.7	2.9	3.8
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	IS7	10:41:25	2.3	Bottom	3	2	19.07	8.08	33.05	93.40	6.7	2.9	3.9
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	IS8(N)	11:16:18	1.0	Surface	1	1	19.12	8.06	33.10	90.80	6.6	2.7	3.0
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	IS8(N)	11:16:36	1.0	Surface	1	2	19.13	8.06	33.10	91.40	6.6	2.7	3.9
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	IS8(N)	11:16:27	3.0	Bottom	3	1	19.11	8.06	33.23	90.60	6.5	2.8	5.0
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	IS8(N)	11:16:07	3.0	Bottom	3	2	19.08	8.06	33.27	89.90	6.5	2.9	3.9
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	IS(Mf)9	10:52:06	1.0	Surface	1	1	19.10	8.08	33.13	92.30	6.7	2.7	3.4
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	IS(Mf)9	10:51:45	1.0	Surface	1	2	19.09	8.08	33.11	91.70	6.6	2.7	4.2

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	IS(Mf)9	10:51:55	2.6	Bottom	3	1	19.08	8.08	33.24	91.70	6.6	2.8	4.0
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	IS(Mf)9	10:51:36	2.6	Bottom	3	2	19.06	8.09	33.25	91.10	6.6	2.8	4.9
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	IS10(N)	11:10:24	1.0	Surface	1	1	19.01	8.05	32.48	93.50	6.5	2.8	4.4
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	IS10(N)	11:11:00	1.0	Surface	1	2	19.04	8.06	32.45	94.00	6.6	2.8	4.0
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	IS10(N)	11:10:11	5.3	Middle	2	1	18.85	8.04	33.29	92.00	6.4	2.9	4.3
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	IS10(N)	11:10:47	5.3	Middle	2	2	18.85	8.03	33.28	92.20	6.4	2.9	3.3
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	IS10(N)	11:10:01	9.6	Bottom	3	1	18.85	8.03	33.39	92.10	6.4	3.0	4.9
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	IS10(N)	11:10:37	9.6	Bottom	3	2	18.88	8.03	33.34	92.00	6.4	3.0	4.1
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	SR3(N)	10:09:08	1.0	Surface	1	1	19.11	8.06	32.97	93.80	6.8	2.9	3.9
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	SR3(N)	10:08:48	1.0	Surface	1	2	19.11	8.06	32.87	91.80	6.6	2.9	3.8
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	SR3(N)	10:08:56	2.4	Bottom	3	1	19.09	8.06	32.94	91.50	6.6	2.9	4.5
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	SR3(N)	10:08:36	2.4	Bottom	3	2	19.08	8.06	32.99	90.20	6.5	3.0	4.3
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	SR4(N3)	11:07:20	1.0	Surface	1	1	19.08	8.07	33.03	91.70	6.6	2.7	3.7
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	SR4(N3)	11:07:02	1.0	Surface	1	2	19.09	8.07	33.00	91.10	6.6	2.7	3.3
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	SR4(N3)	11:07:10	2.8	Bottom	3	1	19.07	8.06	33.17	90.80	6.6	2.8	3.8
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	SR4(N3)	11:06:51	2.8	Bottom	3	2	18.88	8.06	33.22	90.00	6.5	2.8	3.9
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	SR5(N)	11:00:53	1.0	Surface	1	1	19.03	8.05	32.45	94.70	6.6	2.8	3.1
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	SR5(N)	11:00:15	1.0	Surface	1	2	19.00	8.06	32.47	94.20	6.6	2.8	3.7
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	SR5(N)	11:00:41	4.7	Middle	2	1	18.87	8.03	33.18	92.30	6.4	2.9	4.3
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	SR5(N)	11:00:03	4.7	Middle	2	2	18.87	8.04	33.16	92.10	6.4	2.9	4.7
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	SR5(N)	11:00:30	8.3	Bottom	3	1	18.86	8.03	33.38	92.40	6.4	3.1	2.9
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	SR5(N)	10:59:51	8.3	Bottom	3	2	18.84	8.04	33.40	92.20	6.4	3.0	3.8
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	SR10A(N)	11:58:44	1.0	Surface	1	1	18.99	8.07	33.34	94.90	6.6	2.6	3.9
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	SR10A(N)	11:59:32	1.0	Surface	1	2	18.97	8.06	33.37	95.10	6.6	2.6	3.3
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	SR10A(N)	11:59:11	6.6	Middle	2	1	18.83	8.05	33.92	92.00	6.4	2.8	3.6
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	SR10A(N)	11:58:29	6.6	Middle	2	2	18.80	8.05	34.01	92.70	6.4	2.8	3.6
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	SR10A(N)	11:58:16	12.1	Bottom	3	1	18.82	8.06	34.02	92.80	6.4	2.8	3.7
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	SR10A(N)	11:59:00	12.1	Bottom	3	2	18.85	8.05	33.93	92.10	6.4	2.9	4.0
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	SR10B(N2)	12:09:44	1.0	Surface	1	1	18.99	8.06	33.37	94.10	6.5	2.6	3.6
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	SR10B(N2)	12:10:25	1.0	Surface	1	2	18.98	8.06	33.41	93.80	6.5	2.6	3.8
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	SR10B(N2)	12:09:32	3.8	Middle	2	1	18.88	8.05	33.77	91.90	6.4	2.7	3.0
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	SR10B(N2)	12:10:13	3.8	Middle	2	2	18.87	8.05	33.74	92.10	6.4	2.7	3.8
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	SR10B(N2)	12:09:21	6.5	Bottom	3	1	18.85	8.04	33.91	91.70	6.4	2.9	3.3
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	SR10B(N2)	12:09:56	6.5	Bottom	3	2	18.88	8.04	33.84	91.70	6.4	2.9	3.2
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	CS2(A)	10:11:12	1.0	Surface	1	1	18.92	8.06	32.50	97.20	6.8	2.8	3.3
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	CS2(A)	10:10:40	1.0	Surface	1	2	18.90	8.06	32.54	97.80	6.8	2.9	3.2
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	CS2(A)	10:10:30	3.4	Middle	2	1	18.80	8.04	33.15	94.90	6.6	3.0	3.9
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	CS2(A)	10:11:01	3.4	Middle	2	2	18.82	8.05	33.16	94.70	6.6	2.9	3.8
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	CS2(A)	10:10:18	5.7	Bottom	3	1	18.78	8.04	33.39	94.60	6.6	3.1	4.6
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	CS2(A)	10:10:52	5.7	Bottom	3	2	18.80	8.04	33.37	94.70	6.6	3.1	5.2
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	CS(Mf)5	11:57:52	1.0	Surface	1	1	19.10	8.07	33.28	89.00	6.4	2.5	3.2
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	CS(Mf)5	11:57:11	1.0	Surface	1	2	19.10	8.07	33.27	88.90	6.4	2.5	3.5
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	CS(Mf)5	11:56:55	6.3	Middle	2	1	18.91	8.04	33.98	87.00	6.3	2.7	4.0
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	CS(Mf)5	11:57:38	6.3	Middle	2	2	18.93	8.05	33.96	86.80	6.3	2.7	3.6
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	CS(Mf)5	11:57:28	11.6	Bottom	3	1	18.89	8.05	33.67	86.40	6.2	2.8	4.1
HKLR	HY/2011/03	2025-04-09	Mid-Ebb	Fine	CS(Mf)5	11:56:45	11.6	Bottom	3	2	18.88	8.04	34.07	85.80	6.2	2.8	3.4
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	IS5	06:06:10	1.0	Surface	1	1	18.97	8.06	32.95	88.70	6.3	2.8	3.1
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	IS5	06:05:26	1.0	Surface	1	2	18.98	8.07	32.92	89.80	6.4	2.8	3.4
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	IS5	06:05:15	4.2	Middle	2	1	18.88	8.05	33.40	86.90	6.2	2.9	3.4
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	IS5	06:05:57	4.2	Middle	2	2	18.88	8.03	33.41	86.90	6.2	2.9	4.3
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	IS5	06:05:40	7.4	Bottom	3	1	18.86	8.03	33.42	86.00	6.1	3.0	3.5
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	IS5	06:05:04	7.4	Bottom	3	2	18.88	8.04	33.42	86.00	6.1	3.0	3.6
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	IS(Mf)6	05:56:07	1.0	Surface	1	1	18.99	8.07	32.92	91.60	6.5	2.8	3.2
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	IS(Mf)6	05:55:50	1.0	Surface	1	2	18.99	8.07	32.89	91.30	6.5	2.8	4.2
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	IS(Mf)6	05:55:57	2.2	Bottom	3	1	18.97	8.06	33.03	90.90	6.5	2.9	3.6
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	IS(Mf)6	05:55:35	2.2	Bottom	3	2	18.98	8.06	33.08	90.00	6.4	2.9	3.7
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	IS7	05:46:46	1.0	Surface	1	1	19.03	8.06	32.91	90.30	6.4	2.8	3.4
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	IS7	05:46:30	1.0	Surface	1	2	19.01	8.07	32.93	89.70	6.4	2.9	3.7
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	IS7	05:46:37	2.3	Bottom	3	1	19.01	8.06	32.97	89.70	6.4	3.0	4.9
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	IS7	05:46:20	2.3	Bottom	3	2	19.00	8.06	33.04	89.30	6.3	3.0	4.5
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	IS8(N)	05:13:35	1.0	Surface	1	1	19.01	8.06	32.90	91.40	6.5	2.7	4.4
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	IS8(N)	05:12:57	1.0	Surface	1	2	19.01	8.06	32.91	90.50	6.5	2.7	3.3
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	IS8(N)	05:13:05	3.0	Bottom	3	1	18.99	8.05	33.09	90.40	6.4	2.8	3.5
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	IS8(N)	05:12:47	3.0	Bottom	3	2	18.98	8.05	33.17	89.30	6.4	2.9	3.1
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	IS(Mf)9	05:37:41	1.0	Surface	1	1	19.02	8.07	32.89	91.60	6.5	2.7	3.1
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	IS(Mf)9	05:37:24	1.0	Surface	1	2	19.02	8.07	32.94	90.80	6.5	2.7	3.4
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	IS(Mf)9	05:37:31	2.6	Bottom	3	1	18.99	8.06	33.05	90.80	6.5	2.8	3.7
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	IS(Mf)9	05:37:14	2.6	Bottom	3	2	18.98	8.06	33.02	89.70	6.4	2.8	3.0
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	IS10(N)	05:20:36	1.0	Surface	1	1	18.86	8.06	32.82	94.50	6.6	2.8	3.5
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	IS10(N)	05:21:16	1.0	Surface	1	2	18.87	8.06	32.83	94.60	6.6	2.8	4.3
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	IS10(N)	05:21:01	5.3	Middle	2	1	18.79	8.04	33.33	92.20	6.4	3.0	3.8
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	IS10(N)	05:20:22	5.3	Middle	2	2	18.79	8.04	33.32	92.40	6.5	2.9	3.8
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	IS10(N)	05:20:52	9.6	Bottom	3	1	18.80	8.04	33.38	92.00	6.4	3.1	4.0
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	IS10(N)	05:20:12	9.6	Bottom	3	2	18.79	8.05	33.38	92.30	6.4	3.1	3.2
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	SR3(N)	06:16:45	1.0	Surface	1	1	18.99	8.06	32.94	89.10	6.3	2.7	4.9
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	SR3(N)	06:17:01	1.0	Surface	1	2	18.99	8.06	32.86	89.70	6.4	2.7	4.9
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	SR3(N)	06:16:53	2.3	Bottom	3	1	18.98	8.06	33.04	88.90	6.3	2.8	4.4
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	SR3(N)	06:16:35	2.3	Bottom	3	2	18.97	8.06	33.00	88.50	6.3	2.9	4.0
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	SR4(N3)	05:22:20	1.0	Surface	1	1	19.01	8.06	32.92	90.90	6.5	2.6	4.1
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	SR4(N3)	05:22:04	1.0	Surface	1	2	19.00	8.06	32.87	90.90	6.5	2.6	3.8
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	SR4(N3)	05:22:12	2.8	Bottom	3	1	18.97	8.05	33.11	90.50	6.4	2.7	4.5
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	SR4(N3)	05:21:52	2.8	Bottom	3	2	18.96	8.05	33.18	90.10	6.4	2.7	3.9
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	SR5(N)	05:31:17	1	Surface	1	1	18.87	8.06	32.87	92.90	6.5	2.8	3.5
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	SR5(N)	05:30:33	1	Surface	1	2	18.87	8.06	32.87	93.00	6.5	2.8	3.3
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	SR5(N)	05:31:02	4.7	Middle	2	1	18.80	8.05	33.25	91.40	6.4	2.8	3.5
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	SR5(N)	05:30:21	4.7	Middle	2	2	18.80	8.05	33.28	91.60	6.4	2.9	3.6
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	SR5(N)	05:30:09	8.3	Bottom	3	1	18.78	8.04	33.42	91.60	6.4	3.0	4.1
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	SR5(N)	05:30:51	8.3	Bottom	3	2	18.79	8.04	33.39	91.50	6.4	3.0	3.4
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	SR10A(N)	04:29:20	1	Surface	1	1	18.91	8.05	33.08	93.20	6.5	2.5	4.2
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	SR10A(N)	04:28:34	1	Surface	1	2	18.94	8.05	33.02	93.10	6.5	2.5	4.6
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	SR10A(N)	04:28:18	6.6	Middle	2	1	18.81	8.03	33.58	91.30	6.3	2.6	3.0
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	SR10A(N)	04:29:01	6.6	Middle	2	2	18.81	8.03	33.59	90.60	6.3	2.6	2.9
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	SR10A(N)	04:28:08	12.1	Bottom	3	1	18.83	8.03	33.64	91.30	6.4	2.9	3.1
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	SR10A(N)	04:28:51	12.1	Bottom	3	2	18.84	8.03	33.63	90.90	6.3	2.9	3.7
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	SR10B(N2)	04:18:31	1.0	Surface	1	1	18.94	8.05	33.05	97.80	6.8	2.5	3.8
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	SR10B(N2)	04:17:49	1.0	Surface	1	2	18.95	8.03	33.03	97.20	6.8	2.5	4.4
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	SR10B(N2)	04:17:33	3.8	Middle	2	1	18.87	8.02	33.35	94.60	6.6	2.6	3.8
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	SR10B(N2)	04:18:15	3.8	Middle	2	2	18.87	8.03	33.32	93.10	6.5	2.6	3.8
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	SR10B(N2)	04:18:04	6.6	Bottom	3	1	18.85	8.02	33.54	92.40	6.4	2.8	4.0
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	SR10B(N2)	04:17:22	6.6	Bottom	3	2	18.80	8.02	33.56	92.40	6.4	2.8	4.6
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	CS2(A)	06:20:56	1	Surface	1	1	18.82	8.07	32.85	94.20	6.6	2.8	3.5
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	CS2(A)	06:20:17	1	Surface	1	2	18.82	8.06	32.87	94.30	6.6	2.8	3.0
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	CS2(A)	06:20:44	3.4	Middle	2	1	18.75	8.06	33.21	92.90	6.5	2.9	4.0
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	CS2(A)	06:20:06	3.4	Middle	2	2	18.76	8.07	33.19	92.80	6.5	2.9	3.4

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	CS2(A)	06:19:55	5.7	Bottom	3	1	18.74	8.06	33.40	92.60	6.5	3.0	4.7
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	CS2(A)	06:20:34	5.7	Bottom	3	2	18.75	8.06	33.40	92.70	6.5	3.1	5.5
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	CS(Mf)5	04:31:33	1.0	Surface	1	1	19.00	8.06	32.82	89.90	6.4	2.5	3.8
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	CS(Mf)5	04:30:51	1.0	Surface	1	2	18.99	8.05	32.85	89.50	6.4	2.6	3.1
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	CS(Mf)5	04:31:18	6.2	Middle	2	1	18.87	8.05	33.43	87.80	6.3	2.7	2.6
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	CS(Mf)5	04:30:37	6.2	Middle	2	2	18.88	8.04	33.41	87.70	6.2	2.7	3.2
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	CS(Mf)5	04:30:24	11.4	Bottom	3	1	18.88	8.04	33.60	86.40	6.2	2.8	2.6
HKLR	HY/2011/03	2025-04-09	Mid-Flood	Fine	CS(Mf)5	04:31:07	11.4	Bottom	3	2	18.87	8.04	33.60	86.60	6.2	2.8	2.9
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	IS5	11:20:24	1.0	Surface	1	1	19.09	8.05	33.08	92.70	6.6	2.8	1.7
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	IS5	11:20:58	1.0	Surface	1	2	19.11	8.04	33.03	92.70	6.6	2.8	1.8
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	IS5	11:20:14	4.3	Middle	2	1	19.01	8.03	33.31	91.60	6.5	3.3	2.2
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	IS5	11:20:47	4.3	Middle	2	2	19.02	8.03	33.26	91.60	6.5	3.3	2.0
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	IS5	11:20:04	7.5	Bottom	3	1	18.99	8.04	33.38	91.00	6.5	3.4	1.9
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	IS5	11:20:37	7.5	Bottom	3	2	19.02	8.03	33.35	91.40	6.5	3.4	3.2
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	IS(Mf)6	11:31:33	1.0	Surface	1	1	19.10	8.06	32.94	96.20	6.8	2.8	1.8
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	IS(Mf)6	11:31:16	1.0	Surface	1	2	19.10	8.06	32.91	95.10	6.7	2.8	2.8
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	IS(Mf)6	11:31:25	2.2	Bottom	3	1	19.08	8.06	33.01	94.60	6.7	3.2	1.8
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	IS(Mf)6	11:31:03	2.2	Bottom	3	2	19.04	8.06	33.04	93.30	6.6	3.2	2.2
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	IS7	11:41:16	1.0	Surface	1	1	19.11	8.07	32.92	96.30	6.8	2.8	2.5
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	IS7	11:40:58	1.0	Surface	1	2	19.10	8.06	32.93	95.50	6.8	2.9	4.1
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	IS7	11:40:48	2.3	Bottom	3	1	19.06	8.07	33.00	94.60	6.7	3.2	3.2
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	IS7	11:41:05	2.3	Bottom	3	2	19.08	8.06	32.99	95.30	6.8	3.1	2.9
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	IS8(N)	12:15:06	1.0	Surface	1	1	19.09	8.05	33.06	92.10	6.5	2.7	4.2
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	IS8(N)	12:15:24	1.0	Surface	1	2	19.11	8.05	33.06	92.80	6.6	2.7	3.2
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	IS8(N)	12:15:16	3.0	Bottom	3	1	19.08	8.05	33.19	92.00	6.5	2.9	3.6
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	IS8(N)	12:14:55	3.0	Bottom	3	2	19.04	8.05	33.25	91.40	6.5	3.1	2.9
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	IS(Mf)9	11:51:31	1.0	Surface	1	1	19.14	8.07	33.05	94.70	6.7	2.5	2.5
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	IS(Mf)9	11:51:10	1.0	Surface	1	2	19.13	8.07	33.04	94.10	6.7	2.6	2.2
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	IS(Mf)9	11:51:20	2.6	Bottom	3	1	19.12	8.07	33.17	94.10	6.7	2.8	2.3
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	IS(Mf)9	11:51:01	2.6	Bottom	3	2	19.09	8.08	33.17	93.40	6.6	2.9	2.9
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	IS10(N)	12:09:15	1.0	Surface	1	1	19.01	8.05	32.48	90.70	6.3	2.9	2.2
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	IS10(N)	12:09:50	1.0	Surface	1	2	19.04	8.06	32.45	91.20	6.4	2.9	2.0
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	IS10(N)	12:09:37	5.1	Middle	2	1	18.89	8.04	33.21	89.80	6.3	3.0	2.2
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	IS10(N)	12:09:01	5.1	Middle	2	2	18.89	8.04	33.22	89.60	6.2	3.0	3.0
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	IS10(N)	12:09:27	9.2	Bottom	3	1	18.92	8.04	33.25	89.70	6.2	3.0	2.2
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	IS10(N)	12:08:51	9.2	Bottom	3	2	18.89	8.04	33.29	89.80	6.3	3.0	1.8
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	SR3(N)	11:05:18	1.0	Surface	1	1	19.14	8.05	32.96	95.80	6.8	3.0	2.8
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	SR3(N)	11:04:59	1.0	Surface	1	2	19.13	8.05	32.87	93.90	6.7	2.9	2.9
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	SR3(N)	11:05:07	2.4	Bottom	3	1	19.12	8.05	32.94	93.60	6.7	3.2	2.2
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	SR3(N)	11:04:46	2.4	Bottom	3	2	19.11	8.05	32.96	92.50	6.5	3.4	2.2
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	SR4(N3)	12:06:07	1.0	Surface	1	1	19.08	8.06	32.95	93.10	6.6	2.7	2.0
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	SR4(N3)	12:05:50	1.0	Surface	1	2	19.08	8.06	32.96	92.50	6.6	2.7	2.6
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	SR4(N3)	12:05:39	2.8	Bottom	3	1	18.94	8.05	33.14	91.80	6.5	2.9	2.4
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	SR4(N3)	12:05:57	2.8	Bottom	3	2	19.07	8.05	33.10	92.40	6.6	2.9	2.5
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	SR5(N)	11:59:19	1.0	Surface	1	1	19.02	8.05	32.44	91.90	6.4	2.8	2.5
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	SR5(N)	11:58:42	1.0	Surface	1	2	19.00	8.06	32.46	91.40	6.4	2.8	3.6
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	SR5(N)	11:58:30	4.6	Middle	2	1	18.90	8.04	33.10	89.90	6.3	2.9	3.1
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	SR5(N)	11:59:07	4.6	Middle	2	2	18.90	8.04	33.11	90.10	6.3	2.9	2.1
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	SR5(N)	11:58:57	8.1	Bottom	3	1	18.90	8.04	33.28	90.10	6.3	3.1	1.8
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	SR5(N)	11:58:18	8.1	Bottom	3	2	18.88	8.04	33.30	90.10	6.3	3.0	3.1
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	SR10A(N)	12:58:03	1.0	Surface	1	1	18.99	8.07	33.49	91.90	6.4	2.7	1.9
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	SR10A(N)	12:58:51	1.0	Surface	1	2	18.98	8.07	33.51	92.10	6.4	2.7	2.4
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	SR10A(N)	12:58:29	6.7	Middle	2	1	18.87	8.05	33.94	89.20	6.2	2.8	2.5
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	SR10A(N)	12:57:48	6.7	Middle	2	2	18.84	8.06	34.06	90.10	6.3	2.7	2.0
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	SR10A(N)	12:57:35	12.4	Bottom	3	1	18.85	8.07	34.05	90.10	6.3	2.8	1.9
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	SR10A(N)	12:58:18	12.4	Bottom	3	2	18.89	8.05	33.95	89.20	6.2	2.8	2.2
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	SR10B(N2)	13:09:09	1.0	Surface	1	1	19.00	8.06	33.52	91.00	6.3	2.6	1.9
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	SR10B(N2)	13:09:51	1.0	Surface	1	2	18.98	8.06	33.57	90.50	6.3	2.6	2.0
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	SR10B(N2)	13:09:39	3.6	Middle	2	1	18.90	8.05	33.81	89.20	6.2	2.7	2.0
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	SR10B(N2)	13:08:58	3.6	Middle	2	2	18.91	8.06	33.82	89.00	6.2	2.7	2.0
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	SR10B(N2)	13:08:47	6.2	Bottom	3	1	18.89	8.05	33.94	89.00	6.2	2.8	1.4
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	SR10B(N2)	13:09:21	6.2	Bottom	3	2	18.91	8.05	33.87	89.00	6.2	2.8	2.5
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	CS2(A)	11:07:12	1.0	Surface	1	1	18.90	8.06	32.49	94.40	6.6	2.8	2.1
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	CS2(A)	11:06:40	1.0	Surface	1	2	18.87	8.06	32.54	95.20	6.7	2.8	2.1
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	CS2(A)	11:07:01	3.4	Middle	2	1	18.81	8.05	33.11	92.20	6.5	3.0	2.1
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	CS2(A)	11:06:30	3.4	Middle	2	2	18.79	8.04	33.11	92.70	6.5	3.0	2.0
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	CS2(A)	11:06:18	5.8	Bottom	3	1	18.78	8.04	33.32	92.40	6.5	3.1	2.2
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	CS2(A)	11:06:52	5.8	Bottom	3	2	18.80	8.04	33.29	92.30	6.5	3.1	3.5
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	CS(Mf)5	12:55:19	1.0	Surface	1	1	19.06	8.06	33.14	89.40	6.3	2.4	2.3
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	CS(Mf)5	12:54:39	1.0	Surface	1	2	19.06	8.06	33.11	89.50	6.4	2.5	2.1
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	CS(Mf)5	12:55:05	6.3	Middle	2	1	18.91	8.03	33.77	87.30	6.2	3.0	3.0
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	CS(Mf)5	12:54:24	6.3	Middle	2	2	18.88	8.03	33.80	87.50	6.2	3.1	2.8
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	CS(Mf)5	12:54:55	11.6	Bottom	3	1	18.87	8.03	33.54	86.90	6.2	3.4	2.2
HKLR	HY/2011/03	2025-04-11	Mid-Ebb	Fine	CS(Mf)5	12:54:12	11.6	Bottom	3	2	18.84	8.02	33.89	86.40	6.1	3.4	2.8
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	IS5	06:22:58	1.0	Surface	1	1	18.97	8.05	32.91	89.80	6.3	2.8	2.6
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	IS5	06:22:17	1.0	Surface	1	2	18.97	8.06	32.89	91.00	6.4	2.9	2.7
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	IS5	06:22:06	4.2	Middle	2	1	18.87	8.03	33.33	88.20	6.2	3.0	3.1
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	IS5	06:22:46	4.2	Middle	2	2	18.87	8.02	33.34	88.10	6.2	3.1	2.9
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	IS5	06:22:31	7.4	Bottom	3	1	18.85	8.02	33.35	87.50	6.2	3.0	2.2
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	IS5	06:21:55	7.4	Bottom	3	2	18.86	8.03	33.36	87.60	6.1	3.0	2.8
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	IS(Mf)6	06:12:22	1.0	Surface	1	1	18.99	8.06	32.87	92.90	6.5	2.6	2.2
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	IS(Mf)6	06:12:05	1.0	Surface	1	2	18.99	8.06	32.85	92.60	6.5	2.8	2.1
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	IS(Mf)6	06:12:12	2.2	Bottom	3	1	18.96	8.05	32.99	92.30	6.5	3.0	2.0
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	IS(Mf)6	06:11:50	2.2	Bottom	3	2	18.97	8.04	33.05	91.40	6.4	3.0	2.3
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	IS7	06:03:07	1.0	Surface	1	1	19.01	8.05	32.80	91.40	6.4	3.0	2.2
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	IS7	06:02:51	1.0	Surface	1	2	18.99	8.05	32.83	90.80	6.4	3.1	2.9
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	IS7	06:02:57	2.2	Bottom	3	1	18.99	8.05	32.89	90.80	6.4	3.2	2.1
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	IS7	06:02:41	2.2	Bottom	3	2	18.98	8.04	32.93	90.70	6.4	3.3	2.0
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	IS8(N)	05:30:08	1.0	Surface	1	1	18.98	8.05	32.76	91.80	6.5	2.9	1.7
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	IS8(N)	05:29:30	1.0	Surface	1	2	18.99	8.05	32.75	91.10	6.4	3.0	1.9
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	IS8(N)	05:29:39	3.0	Bottom	3	1	18.97	8.04	32.96	91.00	6.4	3.3	2.6
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	IS8(N)	05:29:20	3.0	Bottom	3	2	18.95	8.04	33.03	90.40	6.4	3.2	2.3
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	IS(Mf)9	05:53:34	1.0	Surface	1	1	18.99	8.05	32.80	92.70	6.5	3.0	2.6
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	IS(Mf)9	05:53:17	1.0	Surface	1	2	19.00	8.06	32.82	92.00	6.5	3.0	3.0
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	IS(Mf)9	05:53:24	2.6	Bottom	3	1	18.97	8.05	32.92	91.90	6.5	3.1	2.6
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	IS(Mf)9	05:53:08	2.6	Bottom	3	2	18.96	8.05	32.92	90.90	6.4	3.2	2.0
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	IS10(N)	05:55:22	1.0	Surface	1	1	18.85	8.06	32.82	91.80	6.4	2.8	2.4
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	IS10(N)	05:56:01	1.0	Surface	1	2	18.86	8.06	32.83	92.10	6.5	2.8	1.9
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	IS10(N)	05:55:09	5.2	Middle	2	1	18.81	8.05	33.21	90.00	6.3	2.9	1.6
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	IS10(N)	05:55:47	5.2	Middle	2	2	18.82	8.05	33.22	90.00	6.3	2.9	2.6
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	IS10(N)	05:55:38	9.3	Bottom	3	1	18.83	8.05	33.25	89.70	6.3	3.1	2.3
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	IS10(N)	05:54:58	9.3	Bottom	3	2	18.82	8.05	33.25	90.00	6.3	3.0	2.6
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	SR3(N)	06:33:21	1.0	Surface	1	1	19.00	8.05	32.90	90.60	6.4	2.7	3.4
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	SR3(N)	06:33:38	1.0	Surface	1	2	19.00	8.05	32.85	91.20	6.4	2.7	3.0

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	SR3(N)	06:33:30	2.3	Bottom	3	1	18.99	8.05	33.02	90.50	6.4	2.9	2.7
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	SR3(N)	06:33:12	2.3	Bottom	3	2	18.97	8.05	33.00	90.10	6.3	3.1	3.4
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	SR4(N3)	05:38:56	1.0	Surface	1	1	18.98	8.04	32.76	91.20	6.5	2.8	2.8
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	SR4(N3)	05:38:40	1.0	Surface	1	2	18.97	8.04	32.71	91.50	6.5	2.7	2.8
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	SR4(N3)	05:38:48	2.8	Bottom	3	1	18.95	8.03	32.97	91.10	6.4	3.1	2.6
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	SR4(N3)	05:38:28	2.8	Bottom	3	2	18.94	8.03	33.00	91.20	6.4	3.0	2.8
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	SR5(N)	06:06:28	1	Surface	1	1	18.88	8.06	32.88	90.20	6.3	2.8	2.8
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	SR5(N)	06:05:44	1	Surface	1	2	18.88	8.06	32.89	90.30	6.3	2.8	2.4
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	SR5(N)	06:06:13	4.6	Middle	2	1	18.83	8.06	33.16	89.10	6.2	2.9	2.5
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	SR5(N)	06:05:31	4.6	Middle	2	2	18.83	8.06	33.19	89.30	6.2	2.9	2.6
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	SR5(N)	06:05:19	8.2	Bottom	3	1	18.82	8.05	33.29	89.40	6.2	3.0	3.1
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	SR5(N)	06:06:01	8.2	Bottom	3	2	18.82	8.05	33.27	89.20	6.2	3.0	2.1
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	SR10A(N)	05:04:30	1	Surface	1	1	18.93	8.05	33.08	90.20	6.3	2.5	2.6
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	SR10A(N)	05:03:46	1	Surface	1	2	18.95	8.05	33.04	90.40	6.3	2.5	3.8
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	SR10A(N)	05:03:30	6.6	Middle	2	1	18.86	8.03	33.45	89.00	6.2	2.6	2.8
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	SR10A(N)	05:04:12	6.6	Middle	2	2	18.85	8.03	33.47	88.20	6.1	2.6	2.4
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	SR10A(N)	05:03:21	12.2	Bottom	3	1	18.87	8.04	33.50	89.10	6.2	2.8	1.6
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	SR10A(N)	05:04:02	12.2	Bottom	3	2	18.88	8.04	33.49	88.60	6.2	2.8	1.6
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	SR10B(N2)	04:53:35	1.0	Surface	1	1	18.95	8.05	33.04	94.80	6.6	2.5	1.7
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	SR10B(N2)	04:52:52	1.0	Surface	1	2	18.96	8.02	33.02	94.40	6.6	2.6	1.9
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	SR10B(N2)	04:52:37	3.8	Middle	2	1	18.90	8.02	33.25	92.00	6.4	2.6	1.9
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	SR10B(N2)	04:53:19	3.8	Middle	2	2	18.90	8.03	33.24	90.50	6.3	2.6	2.0
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	SR10B(N2)	04:53:07	6.5	Bottom	3	1	18.89	8.02	33.40	89.80	6.3	2.7	2.5
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	SR10B(N2)	04:52:26	6.5	Bottom	3	2	18.85	8.01	33.41	89.90	6.3	2.7	3.2
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	CS2(A)	06:56:53	1	Surface	1	1	18.79	8.08	32.88	91.70	6.4	2.9	1.3
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	CS2(A)	06:56:13	1	Surface	1	2	18.79	8.07	32.90	91.90	6.4	2.9	1.1
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	CS2(A)	06:56:41	3.2	Middle	2	1	18.74	8.07	33.14	90.70	6.4	3.0	2.2
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	CS2(A)	06:56:01	3.2	Middle	2	2	18.75	8.07	33.12	90.80	6.4	3.0	1.8
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	CS2(A)	06:56:31	5.3	Bottom	3	1	18.74	8.07	33.28	90.50	6.3	3.1	1.9
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	CS2(A)	06:55:51	5.3	Bottom	3	2	18.73	8.07	33.27	90.50	6.3	3.1	1.5
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	CS(Mf)5	04:50:17	1.0	Surface	1	1	18.98	8.04	32.76	90.00	6.3	2.2	2.2
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	CS(Mf)5	04:49:36	1.0	Surface	1	2	18.96	8.03	32.80	89.50	6.3	2.4	1.8
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	CS(Mf)5	04:50:03	6.3	Middle	2	1	18.84	8.02	33.35	87.80	6.2	2.7	2.7
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	CS(Mf)5	04:49:21	6.3	Middle	2	2	18.83	8.01	33.34	88.00	6.2	2.8	2.0
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	CS(Mf)5	04:49:08	11.5	Bottom	3	1	18.85	8.01	33.53	86.60	6.1	3.2	1.5
HKLR	HY/2011/03	2025-04-11	Mid-Flood	Fine	CS(Mf)5	04:49:52	11.5	Bottom	3	2	18.84	8.01	33.54	86.60	6.1	3.2	2.4
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	IS5	12:40:55	1.0	Surface	1	1	19.51	8.09	32.07	94.90	6.8	3.0	3.6
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	IS5	12:41:32	1.0	Surface	1	2	19.55	8.08	32.02	95.30	6.8	3.1	4.0
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	IS5	12:41:19	4.3	Middle	2	1	19.38	8.06	32.35	91.80	6.6	3.5	4.6
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	IS5	12:40:44	4.3	Middle	2	2	19.36	8.06	32.36	91.70	6.6	3.5	3.8
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	IS5	12:40:34	7.5	Bottom	3	1	19.34	8.06	32.56	91.20	6.5	3.6	4.4
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	IS5	12:41:09	7.5	Bottom	3	2	19.37	8.06	32.56	91.80	6.6	3.6	3.6
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	IS(Mf)6	12:50:12	1.0	Surface	1	1	19.55	8.09	32.08	98.10	7.0	3.0	4.4
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	IS(Mf)6	12:49:55	1.0	Surface	1	2	19.54	8.09	31.81	97.10	7.0	3.0	4.1
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	IS(Mf)6	12:50:04	2.2	Bottom	3	1	19.52	8.09	32.14	96.50	6.9	3.5	4.0
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	IS(Mf)6	12:49:44	2.2	Bottom	3	2	19.48	8.09	32.05	95.00	6.8	3.6	4.6
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	IS7	13:01:10	1.0	Surface	1	1	19.55	8.10	31.98	98.20	7.0	2.9	3.8
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	IS7	13:00:52	1.0	Surface	1	2	19.54	8.10	32.07	97.50	7.0	3.1	4.3
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	IS7	13:00:43	2.3	Bottom	3	1	19.50	8.10	32.06	96.30	6.9	3.3	4.1
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	IS7	13:00:59	2.3	Bottom	3	2	19.52	8.10	32.12	97.10	7.0	3.3	4.2
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	IS8(N)	13:33:56	1.0	Surface	1	1	19.53	8.08	31.90	94.70	6.8	3.0	3.6
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	IS8(N)	13:34:13	1.0	Surface	1	2	19.54	8.08	31.90	95.60	6.9	3.0	3.6
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	IS8(N)	13:34:05	3.0	Bottom	3	1	19.52	8.07	32.01	94.80	6.8	3.3	3.8
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	IS8(N)	13:33:45	3.0	Bottom	3	2	19.47	8.07	32.06	94.00	6.7	3.4	4.4
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	IS(Mf)9	13:10:50	1.0	Surface	1	1	19.56	8.10	32.11	97.00	7.0	2.8	4.9
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	IS(Mf)9	13:10:30	1.0	Surface	1	2	19.55	8.10	32.11	96.20	6.9	2.9	4.6
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	IS(Mf)9	13:10:39	2.6	Bottom	3	1	19.53	8.10	32.16	96.30	6.9	3.2	3.0
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	IS(Mf)9	13:10:21	2.6	Bottom	3	2	19.50	8.10	32.22	95.60	6.9	3.1	3.8
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	IS10(N)	13:30:43	1.0	Surface	1	1	19.45	8.07	32.05	90.50	6.4	3.0	5.5
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	IS10(N)	13:31:20	1.0	Surface	1	2	19.47	8.08	32.07	91.10	6.4	3.0	4.7
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	IS10(N)	13:31:07	5.3	Middle	2	1	19.21	8.06	33.06	88.50	6.2	3.3	3.7
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	IS10(N)	13:30:30	5.3	Middle	2	2	19.20	8.06	33.12	88.40	6.2	3.3	4.8
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	IS10(N)	13:30:57	9.5	Bottom	3	1	19.27	8.06	33.13	88.10	6.2	3.4	3.8
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	IS10(N)	13:30:20	9.5	Bottom	3	2	19.22	8.06	33.15	88.10	6.2	3.4	4.5
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	SR3(N)	12:25:33	1.0	Surface	1	1	19.55	8.08	32.13	96.20	6.9	3.2	5.0
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	SR3(N)	12:25:51	1.0	Surface	1	2	19.56	8.08	32.19	97.70	7.0	3.2	5.1
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	SR3(N)	12:25:40	2.3	Bottom	3	1	19.54	8.09	32.05	95.80	6.9	3.4	4.2
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	SR3(N)	12:25:22	2.3	Bottom	3	2	19.51	8.08	32.23	94.20	6.7	3.6	4.8
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	SR4(N3)	13:25:05	1.0	Surface	1	1	19.52	8.09	31.85	95.60	6.9	2.9	3.6
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	SR4(N3)	13:24:49	1.0	Surface	1	2	19.52	8.08	32.02	95.10	6.8	3.0	4.0
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	SR4(N3)	13:24:56	2.8	Bottom	3	1	19.51	8.08	31.97	94.80	6.8	3.2	3.7
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	SR4(N3)	13:24:40	2.8	Bottom	3	2	19.19	8.07	32.18	93.90	6.7	3.2	3.8
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	SR5(N)	13:22:25	1.0	Surface	1	1	19.45	8.08	31.87	92.00	6.5	3.0	4.2
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	SR5(N)	13:21:44	1.0	Surface	1	2	19.40	8.08	31.81	91.30	6.4	3.0	3.7
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	SR5(N)	13:22:13	4.8	Middle	2	1	19.23	8.06	32.89	88.90	6.3	3.2	4.0
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	SR5(N)	13:21:32	4.8	Middle	2	2	19.23	8.06	32.79	88.60	6.2	3.2	3.8
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	SR5(N)	13:22:03	8.5	Bottom	3	1	19.22	8.06	33.09	88.70	6.3	3.5	2.9
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	SR5(N)	13:21:20	8.5	Bottom	3	2	19.23	8.06	32.87	88.50	6.2	3.4	3.8
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	SR10A(N)	14:24:07	1.0	Surface	1	1	19.44	8.09	32.93	91.60	6.4	2.9	4.4
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	SR10A(N)	14:23:18	1.0	Surface	1	2	19.44	8.09	32.85	91.40	6.4	2.9	3.8
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	SR10A(N)	14:23:46	6.7	Middle	2	1	19.20	8.07	33.80	87.70	6.1	3.1	5.4
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	SR10A(N)	14:23:03	6.7	Middle	2	2	19.18	8.07	33.86	88.30	6.2	3.1	5.2
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	SR10A(N)	14:22:51	12.4	Bottom	3	1	19.19	8.08	33.91	88.10	6.2	3.2	4.2
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	SR10A(N)	14:23:34	12.4	Bottom	3	2	19.25	8.07	33.88	87.40	6.1	3.2	4.3
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	SR10B(N2)	14:34:52	1.0	Surface	1	1	19.46	8.08	32.77	91.20	6.4	2.8	5.3
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	SR10B(N2)	14:35:33	1.0	Surface	1	2	19.47	8.08	32.81	91.00	6.4	2.8	6.9
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	SR10B(N2)	14:35:21	3.7	Middle	2	1	19.18	8.07	33.69	88.50	6.2	2.9	5.6
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	SR10B(N2)	14:34:41	3.7	Middle	2	2	19.26	8.07	33.75	88.40	6.2	2.9	5.0
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	SR10B(N2)	14:34:30	6.3	Bottom	3	1	19.25	8.07	33.90	88.00	6.2	3.1	3.6
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	SR10B(N2)	14:35:05	6.3	Bottom	3	2	19.28	8.06	33.74	87.90	6.2	3.1	4.6
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	CS2(A)	12:34:13	1.0	Surface	1	1	19.41	8.08	32.33	94.50	6.7	2.9	3.1
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	CS2(A)	12:33:36	1.0	Surface	1	2	19.37	8.08	32.18	94.80	6.7	2.9	3.4
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	CS2(A)	12:34:01	3.4	Middle	2	1	19.16	8.07	33.29	90.40	6.4	3.2	4.8
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	CS2(A)	12:33:25	3.4	Middle	2	2	19.17	8.07	33.21	90.80	6.4	3.2	3.9
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	CS2(A)	12:33:12	5.8	Bottom	3	1	19.13	8.06	33.47	90.60	6.4	3.5	4.0
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	CS2(A)	12:33:52	5.8	Bottom	3	2	19.16	8.07	33.43	90.80	6.4	3.5	4.1
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	CS(Mf)5	14:16:32	1.0	Surface	1	1	19.51	8.09	31.99	91.10	6.5	2.7	1.8
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	CS(Mf)5	14:17:12	1.0	Surface	1	2	19.50	8.09	32.01	91.50	6.6	2.5	3.0
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	CS(Mf)5	14:16:57	6.3	Middle	2	1	19.19	8.04	32.88	87.00	6.3	3.1	3.2
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	CS(Mf)5	14:16:17	6.3	Middle	2	2	19.18	8.04	32.90	87.20	6.3	3.1	3.8
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	CS(Mf)5	14:16:47	11.6	Bottom	3	1	19.18	8.04	32.59	86.40	6.2	3.4	4.9
HKLR	HY/2011/03	2025-04-14	Mid-Ebb	Fine	CS(Mf)5	14:16:06	11.6	Bottom	3	2	19.16	8.03	32.94	86.20	6.2	3.4	3.7
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	IS5	08:30:07	1.0	Surface	1	1	19.39	8.09	32.70	91.60	6.4	2.9	4.2
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	IS5	08:29:21	1.0	Surface	1	2	19.41	8.10	32.69	92.70	6.5	2.9	4.4

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	IS5	08:29:09	4.3	Middle	2	1	19.19	8.05	33.30	87.50	6.1	3.2	4.3
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	IS5	08:29:54	4.3	Middle	2	2	19.19	8.05	33.30	87.50	6.1	3.3	3.6
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	IS5	08:29:35	7.5	Bottom	3	1	19.15	8.04	33.33	86.50	6.1	3.4	3.9
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	IS5	08:28:58	7.5	Bottom	3	2	19.18	8.05	33.33	86.70	6.1	3.4	4.5
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	IS(Mf)6	08:20:13	1.0	Surface	1	1	19.45	8.10	32.67	95.30	6.7	2.8	4.9
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	IS(Mf)6	08:19:55	1.0	Surface	1	2	19.44	8.10	32.66	94.90	6.6	2.9	4.0
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	IS(Mf)6	08:20:04	2.2	Bottom	3	1	19.40	8.09	32.77	94.60	6.6	3.2	3.8
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	IS(Mf)6	08:19:41	2.2	Bottom	3	2	19.38	8.08	32.82	94.20	6.6	3.2	3.8
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	IS7	08:10:06	1.0	Surface	1	1	19.47	8.09	32.63	94.10	6.6	3.0	4.1
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	IS7	08:09:50	1.0	Surface	1	2	19.44	8.09	32.66	93.60	6.5	3.0	4.3
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	IS7	08:09:58	2.3	Bottom	3	1	19.42	8.08	32.72	93.50	6.5	3.3	4.0
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	IS7	08:09:41	2.3	Bottom	3	2	19.40	8.07	32.74	93.30	6.5	3.4	4.6
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	IS8(N)	07:34:20	1.0	Surface	1	1	19.42	8.08	32.60	94.30	6.6	3.0	3.2
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	IS8(N)	07:33:43	1.0	Surface	1	2	19.45	8.08	32.59	93.60	6.6	3.1	3.9
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	IS8(N)	07:33:51	3.0	Bottom	3	1	19.37	8.07	32.79	93.20	6.5	3.4	3.2
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	IS8(N)	07:33:32	3.0	Bottom	3	2	19.35	8.07	32.84	92.60	6.5	3.4	3.8
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	IS(Mf)9	08:00:41	1.0	Surface	1	1	19.46	8.09	32.62	94.70	6.6	2.9	5.0
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	IS(Mf)9	08:00:25	1.0	Surface	1	2	19.45	8.10	32.64	94.00	6.6	3.0	5.2
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	IS(Mf)9	08:00:31	2.6	Bottom	3	1	19.41	8.08	32.74	93.80	6.6	3.4	5.0
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	IS(Mf)9	08:00:15	2.6	Bottom	3	2	19.36	8.08	32.75	92.90	6.5	3.4	4.7
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	IS10(N)	07:47:42	1.0	Surface	1	1	19.30	8.10	32.46	91.90	6.5	2.9	5.6
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	IS10(N)	07:48:24	1.0	Surface	1	2	19.33	8.10	32.45	92.40	6.5	2.9	4.8
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	IS10(N)	07:48:08	5.3	Middle	2	1	19.19	8.08	33.33	89.00	6.3	3.1	3.6
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	IS10(N)	07:47:27	5.3	Middle	2	2	19.17	8.08	33.33	88.70	6.2	3.2	4.4
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	IS10(N)	07:47:57	9.6	Bottom	3	1	19.23	8.08	33.34	88.40	6.2	3.5	4.0
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	IS10(N)	07:47:16	9.6	Bottom	3	2	19.16	8.08	33.41	88.50	6.2	3.4	3.4
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	SR3(N)	08:44:43	1.0	Surface	1	1	19.43	8.09	32.91	92.70	6.5	3.0	4.6
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	SR3(N)	08:44:59	1.0	Surface	1	2	19.43	8.09	32.88	93.50	6.5	2.9	4.0
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	SR3(N)	08:44:51	2.4	Bottom	3	1	19.41	8.09	33.00	92.60	6.5	3.2	4.6
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	SR3(N)	08:44:33	2.4	Bottom	3	2	19.37	8.08	33.00	91.70	6.4	3.4	4.6
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	SR4(N3)	07:43:01	1.0	Surface	1	1	19.44	8.08	32.60	93.30	6.5	2.8	4.8
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	SR4(N3)	07:42:43	1.0	Surface	1	2	19.40	8.08	32.58	93.60	6.6	2.7	4.7
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	SR4(N3)	07:42:51	2.9	Bottom	3	1	19.36	8.06	32.81	93.00	6.5	3.1	4.1
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	SR4(N3)	07:42:32	2.9	Bottom	3	2	19.33	8.06	32.84	93.20	6.5	3.0	4.6
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	SR5(N)	07:57:36	1	Surface	1	1	19.37	8.10	32.35	90.90	6.4	2.9	3.6
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	SR5(N)	07:58:22	1	Surface	1	2	19.37	8.10	32.35	90.60	6.4	2.9	3.6
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	SR5(N)	07:58:07	4.7	Middle	2	1	19.20	8.09	33.28	87.80	6.2	3.1	3.4
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	SR5(N)	07:57:23	4.7	Middle	2	2	19.21	8.09	33.30	88.10	6.2	3.1	4.0
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	SR5(N)	07:57:11	8.3	Bottom	3	1	19.17	8.08	33.44	88.40	6.2	3.3	3.6
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	SR5(N)	07:57:55	8.3	Bottom	3	2	19.17	8.08	33.44	88.10	6.2	3.3	3.6
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	SR10A(N)	06:56:26	1	Surface	1	1	19.38	8.09	32.70	90.30	6.3	2.7	4.1
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	SR10A(N)	06:55:42	1	Surface	1	2	19.40	8.08	32.62	90.60	6.4	2.7	4.6
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	SR10A(N)	06:55:24	6.7	Middle	2	1	19.19	8.06	33.59	87.90	6.2	2.9	3.9
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	SR10A(N)	06:56:08	6.7	Middle	2	2	19.19	8.07	33.60	87.10	6.1	2.9	4.0
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	SR10A(N)	06:55:14	12.3	Bottom	3	1	19.20	8.07	33.65	87.50	6.1	3.2	4.0
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	SR10A(N)	06:55:58	12.3	Bottom	3	2	19.23	8.07	33.64	87.30	6.1	3.1	3.6
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	SR10B(N2)	06:45:38	1.0	Surface	1	1	19.41	8.08	32.66	95.00	6.6	2.7	4.4
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	SR10B(N2)	06:44:55	1.0	Surface	1	2	19.42	8.07	32.65	95.20	6.7	2.8	4.0
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	SR10B(N2)	06:44:40	3.7	Middle	2	1	19.32	8.07	33.29	91.20	6.4	2.9	4.2
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	SR10B(N2)	06:45:22	3.7	Middle	2	2	19.30	8.06	33.28	90.30	6.3	2.9	3.6
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	SR10B(N2)	06:45:11	6.4	Bottom	3	1	19.28	8.07	33.50	89.30	6.3	3.1	4.2
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	SR10B(N2)	06:44:28	6.4	Bottom	3	2	19.16	8.07	33.58	89.30	6.2	3.0	4.4
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	CS2(A)	08:52:00	1	Surface	1	1	19.29	8.10	32.33	92.10	6.5	3.1	4.0
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	CS2(A)	08:51:16	1	Surface	1	2	19.30	8.09	32.36	92.50	6.5	3.1	3.6
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	CS2(A)	08:51:46	3.3	Middle	2	1	19.15	8.09	33.21	89.50	6.3	3.2	4.3
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	CS2(A)	08:51:01	3.3	Middle	2	2	19.18	8.09	33.17	89.60	6.3	3.2	3.7
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	CS2(A)	08:51:35	5.6	Bottom	3	1	19.10	8.08	33.44	89.20	6.3	3.5	3.5
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	CS2(A)	08:50:49	5.6	Bottom	3	2	19.13	8.09	33.40	89.50	6.3	3.4	4.1
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	CS(Mf)5	06:51:25	1.0	Surface	1	1	19.42	8.07	32.61	92.40	6.5	2.6	5.5
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	CS(Mf)5	06:50:42	1.0	Surface	1	2	19.40	8.06	32.65	91.70	6.4	2.7	5.1
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	CS(Mf)5	06:51:11	6.3	Middle	2	1	19.17	8.05	33.34	87.60	6.1	3.0	5.0
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	CS(Mf)5	06:50:28	6.3	Middle	2	2	19.18	8.04	33.33	87.70	6.1	3.1	4.1
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	CS(Mf)5	06:50:16	11.5	Bottom	3	1	19.19	8.04	33.41	86.50	6.1	3.4	3.6
HKLR	HY/2011/03	2025-04-14	Mid-Flood	Fine	CS(Mf)5	06:50:59	11.5	Bottom	3	2	19.18	8.04	33.44	86.40	6.0	3.4	4.0
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	IS5	13:43:03	1.0	Surface	1	1	19.66	8.07	32.13	95.70	6.8	2.9	2.9
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	IS5	13:43:41	1.0	Surface	1	2	19.70	8.07	32.10	96.20	6.9	3.0	3.5
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	IS5	13:42:52	4.3	Middle	2	1	19.51	8.05	32.45	93.70	6.7	3.4	2.7
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	IS5	13:43:28	4.3	Middle	2	2	19.52	8.05	32.44	93.90	6.7	3.4	3.6
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	IS5	13:42:42	7.5	Bottom	3	1	19.49	8.05	32.57	93.30	6.7	3.5	3.8
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	IS5	13:43:17	7.5	Bottom	3	2	19.52	8.05	32.55	93.80	6.7	3.5	4.0
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	IS(Mf)6	13:51:32	1.0	Surface	1	1	19.69	8.08	32.12	98.60	7.1	2.9	2.8
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	IS(Mf)6	13:51:15	1.0	Surface	1	2	19.68	8.08	31.98	97.60	7.0	2.9	3.4
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	IS(Mf)6	13:51:24	2.2	Bottom	3	1	19.65	8.07	32.21	96.80	6.9	3.3	3.6
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	IS(Mf)6	13:51:05	2.2	Bottom	3	2	19.60	8.08	32.17	95.30	6.8	3.4	2.8
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	IS7	14:01:05	1.0	Surface	1	1	19.69	8.09	32.07	98.60	7.0	2.9	3.4
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	IS7	14:00:47	1.0	Surface	1	2	19.68	8.08	32.11	98.00	7.0	3.1	3.2
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	IS7	14:00:54	2.3	Bottom	3	1	19.64	8.08	32.21	97.60	7.0	3.3	3.3
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	IS7	14:00:38	2.3	Bottom	3	2	19.62	8.08	32.20	97.00	6.9	3.2	2.6
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	IS8(N)	14:37:42	1.0	Surface	1	1	19.68	8.06	32.01	95.60	6.8	3.0	2.8
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	IS8(N)	14:38:00	1.0	Surface	1	2	19.69	8.07	32.00	96.40	6.9	3.0	3.7
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	IS8(N)	14:37:51	3.0	Bottom	3	1	19.66	8.06	32.13	95.50	6.8	3.2	3.6
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	IS8(N)	14:37:32	3.0	Bottom	3	2	19.60	8.06	32.20	94.80	6.8	3.4	4.4
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	IS(Mf)9	14:11:51	1.0	Surface	1	1	19.69	8.08	32.14	97.50	7.0	2.8	4.1
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	IS(Mf)9	14:11:31	1.0	Surface	1	2	19.68	8.08	32.13	96.80	6.9	2.9	3.7
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	IS(Mf)9	14:11:41	2.6	Bottom	3	1	19.64	8.08	32.26	96.90	6.9	3.2	3.8
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	IS(Mf)9	14:11:23	2.6	Bottom	3	2	19.61	8.08	32.28	96.30	6.9	3.1	3.2
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	IS10(N)	14:31:15	1.0	Surface	1	1	19.55	8.07	32.22	91.00	6.5	3.2	3.1
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	IS10(N)	14:31:53	1.0	Surface	1	2	19.57	8.08	32.22	91.40	6.5	3.1	3.7
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	IS10(N)	14:31:39	5.3	Middle	2	1	19.36	8.06	32.98	89.70	6.4	3.4	3.9
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	IS10(N)	14:31:02	5.3	Middle	2	2	19.35	8.06	33.01	89.70	6.4	3.4	3.5
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	IS10(N)	14:31:30	9.5	Bottom	3	1	19.39	8.06	33.03	89.40	6.4	3.5	3.8
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	IS10(N)	14:30:52	9.5	Bottom	3	2	19.36	8.06	33.04	89.60	6.4	3.4	3.0
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	SR3(N)	13:28:46	1.0	Surface	1	1	19.71	8.07	32.18	98.60	7.0	3.1	3.3
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	SR3(N)	13:28:27	1.0	Surface	1	2	19.70	8.07	32.13	97.20	6.9	3.1	2.6
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	SR3(N)	13:28:35	2.3	Bottom	3	1	19.67	8.07	32.13	96.70	6.9	3.3	2.3
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	SR3(N)	13:28:16	2.3	Bottom	3	2	19.64	8.07	32.22	95.20	6.8	3.4	2.6
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	SR4(N3)	14:27:52	1.0	Surface	1	1	19.67	8.07	32.00	96.30	6.9	2.9	3.0
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	SR4(N3)	14:27:35	1.0	Surface	1	2	19.68	8.07	32.06	95.90	6.9	3.0	2.7
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	SR4(N3)	14:27:42	2.8	Bottom	3	1	19.65	8.06	32.13	95.50	6.8	3.2	3.1
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	SR4(N3)	14:27:25	2.8	Bottom	3	2	19.47	8.06	32.23	94.80	6.8	3.2	3.8
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	SR5(N)	14:22:17	1.0	Surface	1	1	19.55	8.08	32.13	92.50	6.6	3.0	4.2
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	SR5(N)	14:21:37	1.0	Surface	1	2	19.52	8.08	32.10	91.90	6.6	3.0	3.6
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	SR5(N)	14:22:05	4.7	Middle	2	1	19.38	8.06	32.86	90.10	6.4	3.2	3.6
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	SR5(N)	14:21:24	4.7	Middle	2	2	19.38	8.06	32.81	89.90	6.4	3.2	4.3

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	SR5(N)	14:21:55	8.3	Bottom	3	1	19.35	8.06	33.02	90.10	6.4	3.6	3.4
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	SR5(N)	14:21:12	8.3	Bottom	3	2	19.36	8.06	32.90	90.00	6.4	3.5	3.5
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	SR10A(N)	15:20:02	1.0	Surface	1	1	19.56	8.08	32.81	92.40	6.6	2.9	3.7
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	SR10A(N)	15:20:51	1.0	Surface	1	2	19.54	8.08	32.85	92.30	6.6	2.9	3.7
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	SR10A(N)	15:20:31	6.6	Middle	2	1	19.37	8.07	33.50	89.40	6.3	3.1	4.2
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	SR10A(N)	15:19:49	6.6	Middle	2	2	19.37	8.07	33.52	90.10	6.4	3.1	4.9
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	SR10A(N)	15:19:36	12.1	Bottom	3	1	19.37	8.08	33.56	90.10	6.4	3.2	5.3
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	SR10A(N)	15:20:19	12.1	Bottom	3	2	19.41	8.07	33.54	89.40	6.3	3.2	4.6
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	SR10B(N2)	15:32:53	1.0	Surface	1	1	19.56	8.08	32.78	91.60	6.5	2.8	3.2
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	SR10B(N2)	15:33:30	1.0	Surface	1	2	19.57	8.08	32.82	91.50	6.5	2.8	3.0
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	SR10B(N2)	15:33:19	3.7	Middle	2	1	19.39	8.07	33.39	89.80	6.4	2.9	3.8
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	SR10B(N2)	15:32:41	3.7	Middle	2	2	19.43	8.07	33.44	89.90	6.4	2.9	3.6
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	SR10B(N2)	15:32:31	6.3	Bottom	3	1	19.41	8.07	33.54	89.60	6.4	3.1	3.2
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	SR10B(N2)	15:33:05	6.3	Bottom	3	2	19.44	8.06	33.43	89.50	6.4	3.1	3.8
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	CS2(A)	13:33:47	1.0	Surface	1	1	19.43	8.08	32.31	95.40	6.8	3.0	4.0
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	CS2(A)	13:34:22	1.0	Surface	1	2	19.45	8.08	32.38	94.90	6.8	2.9	4.4
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	CS2(A)	13:34:11	3.4	Middle	2	1	19.29	8.07	33.05	92.20	6.6	3.2	3.6
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	CS2(A)	13:33:36	3.4	Middle	2	2	19.28	8.06	33.01	92.50	6.6	3.3	4.4
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	CS2(A)	13:33:24	5.7	Bottom	3	1	19.26	8.06	33.21	92.50	6.6	3.6	3.3
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	CS2(A)	13:34:01	5.7	Bottom	3	2	19.27	8.06	33.18	92.60	6.6	3.5	3.3
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	CS(Mf)5	15:19:09	1.0	Surface	1	1	19.68	8.07	32.14	91.60	6.5	2.7	3.5
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	CS(Mf)5	15:19:49	1.0	Surface	1	2	19.66	8.07	32.16	92.10	6.6	2.6	4.3
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	CS(Mf)5	15:18:53	6.3	Middle	2	1	19.28	8.02	32.94	88.50	6.3	2.9	4.9
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	CS(Mf)5	15:19:35	6.3	Middle	2	2	19.29	8.02	32.93	88.70	6.3	2.9	3.9
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	CS(Mf)5	15:19:25	11.6	Bottom	3	1	19.27	8.02	32.32	88.10	6.3	3.2	3.3
HKLR	HY/2011/03	2025-04-16	Mid-Ebb	Fine	CS(Mf)5	15:18:43	11.6	Bottom	3	2	19.26	8.02	32.97	87.90	6.3	3.2	4.2
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	IS5	08:40:49	1.0	Surface	1	1	19.42	8.07	32.64	92.60	6.5	2.9	3.6
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	IS5	08:40:03	1.0	Surface	1	2	19.44	8.08	32.63	93.70	6.6	2.9	4.2
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	IS5	08:39:51	4.2	Middle	2	1	19.22	8.04	33.11	89.40	6.3	3.1	3.4
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	IS5	08:40:37	4.2	Middle	2	2	19.21	8.04	33.11	89.80	6.3	3.2	3.4
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	IS5	08:40:18	7.4	Bottom	3	1	19.15	8.03	33.17	88.90	6.3	3.3	3.6
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	IS5	08:39:40	7.4	Bottom	3	2	19.21	8.04	33.17	88.70	6.2	3.3	3.7
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	IS(Mf)6	08:29:21	1.0	Surface	1	1	19.48	8.08	32.63	95.70	6.7	2.8	3.2
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	IS(Mf)6	08:29:04	1.0	Surface	1	2	19.47	8.08	32.63	95.40	6.7	2.9	3.1
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	IS(Mf)6	08:29:12	2.2	Bottom	3	1	19.44	8.08	32.72	95.10	6.7	3.1	2.7
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	IS(Mf)6	08:28:51	2.2	Bottom	3	2	19.43	8.07	32.76	94.80	6.7	3.1	3.9
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	IS7	08:18:46	1.0	Surface	1	1	19.51	8.08	32.59	95.10	6.7	2.9	3.9
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	IS7	08:18:31	1.0	Surface	1	2	19.47	8.08	32.62	94.60	6.7	2.9	3.1
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	IS7	08:18:38	2.3	Bottom	3	1	19.46	8.07	32.68	94.50	6.7	3.2	3.8
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	IS7	08:18:22	2.3	Bottom	3	2	19.44	8.06	32.69	94.20	6.6	3.2	4.3
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	IS8(N)	07:46:24	1.0	Surface	1	1	19.45	8.07	32.55	95.60	6.8	2.9	4.2
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	IS8(N)	07:45:43	1.0	Surface	1	2	19.48	8.07	32.54	94.60	6.7	3.0	4.4
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	IS8(N)	07:45:51	3.1	Bottom	3	1	19.41	8.06	32.76	94.30	6.7	3.2	4.0
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	IS8(N)	07:45:32	3.1	Bottom	3	2	19.40	8.07	32.79	93.40	6.6	3.3	3.8
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	IS(Mf)9	08:10:06	1.0	Surface	1	1	19.51	8.08	32.57	95.40	6.7	2.8	3.5
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	IS(Mf)9	08:09:50	1.0	Surface	1	2	19.50	8.09	32.59	94.80	6.7	2.9	4.1
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	IS(Mf)9	08:09:56	2.5	Bottom	3	1	19.47	8.07	32.69	94.50	6.7	3.3	4.3
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	IS(Mf)9	08:09:39	2.5	Bottom	3	2	19.42	8.08	32.69	93.50	6.6	3.2	3.5
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	IS10(N)	08:20:49	1.0	Surface	1	1	19.40	8.09	32.41	92.70	6.6	3.0	3.7
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	IS10(N)	08:21:31	1.0	Surface	1	2	19.42	8.09	32.41	93.20	6.7	3.0	3.8
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	IS10(N)	08:21:15	5.3	Middle	2	1	19.32	8.07	33.08	90.50	6.5	3.2	3.1
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	IS10(N)	08:20:34	5.3	Middle	2	2	19.31	8.07	33.07	90.30	6.4	3.3	3.5
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	IS10(N)	08:21:04	9.6	Bottom	3	1	19.35	8.07	33.10	90.20	6.4	3.5	4.6
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	IS10(N)	08:20:24	9.6	Bottom	3	2	19.31	8.07	33.14	90.30	6.4	3.5	3.8
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	SR3(N)	08:55:09	1.0	Surface	1	1	19.46	8.07	32.74	93.30	6.6	3.1	4.0
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	SR3(N)	08:55:25	1.0	Surface	1	2	19.47	8.08	32.72	94.10	6.6	3.0	4.7
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	SR3(N)	08:55:17	2.3	Bottom	3	1	19.45	8.07	32.83	93.10	6.6	3.2	3.5
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	SR3(N)	08:55:00	2.3	Bottom	3	2	19.39	8.07	32.84	92.00	6.5	3.4	3.9
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	SR4(N3)	07:55:39	1.0	Surface	1	1	19.49	8.07	32.54	94.20	6.6	2.7	6.2
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	SR4(N3)	07:55:21	1.0	Surface	1	2	19.44	8.07	32.53	94.30	6.7	2.6	5.4
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	SR4(N3)	07:55:30	2.9	Bottom	3	1	19.41	8.05	32.76	93.90	6.6	3.0	3.4
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	SR4(N3)	07:55:10	2.9	Bottom	3	2	19.39	8.06	32.79	94.00	6.6	2.9	2.8
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	SR5(N)	08:31:23	1	Surface	1	1	19.45	8.09	32.39	91.10	6.5	3.0	2.8
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	SR5(N)	08:30:40	1	Surface	1	2	19.45	8.09	32.39	91.30	6.5	3.0	2.7
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	SR5(N)	08:31:09	4.6	Middle	2	1	19.34	8.07	33.02	89.30	6.4	3.2	3.6
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	SR5(N)	08:30:27	4.6	Middle	2	2	19.35	8.07	33.03	89.60	6.4	3.2	3.2
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	SR5(N)	08:30:15	8.2	Bottom	3	1	19.30	8.07	33.18	89.90	6.4	3.4	3.4
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	SR5(N)	08:30:58	8.2	Bottom	3	2	19.31	8.07	33.16	89.60	6.4	3.5	3.6
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	SR10A(N)	07:25:59	1	Surface	1	1	19.50	8.08	32.66	90.70	6.5	2.7	3.1
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	SR10A(N)	07:25:15	1	Surface	1	2	19.52	8.07	32.61	91.10	6.5	2.7	3.2
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	SR10A(N)	07:24:58	6.6	Middle	2	1	19.36	8.05	33.31	89.30	6.3	2.9	3.1
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	SR10A(N)	07:25:42	6.6	Middle	2	2	19.36	8.06	33.31	88.60	6.3	2.9	3.6
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	SR10A(N)	07:24:48	12.1	Bottom	3	1	19.36	8.06	33.38	89.20	6.3	3.2	2.4
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	SR10A(N)	07:25:32	12.1	Bottom	3	2	19.40	8.06	33.37	88.90	6.3	3.1	3.5
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	SR10B(N2)	07:12:50	1.0	Surface	1	1	19.53	8.07	32.64	95.20	6.7	2.7	2.4
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	SR10B(N2)	07:12:08	1.0	Surface	1	2	19.53	8.06	32.63	95.00	6.8	2.7	3.3
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	SR10B(N2)	07:11:51	3.7	Middle	2	1	19.44	8.05	33.12	92.20	6.6	2.9	3.1
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	SR10B(N2)	07:12:35	3.7	Middle	2	2	19.43	8.05	33.08	91.00	6.5	2.9	3.1
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	SR10B(N2)	07:12:24	6.4	Bottom	3	1	19.41	8.06	33.28	90.30	6.4	3.1	3.2
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	SR10B(N2)	07:11:40	6.4	Bottom	3	2	19.34	8.05	33.33	90.40	6.4	3.0	3.9
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	CS2(A)	09:23:21	1	Surface	1	1	19.35	8.09	32.35	92.60	6.6	3.2	3.7
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	CS2(A)	09:22:42	1	Surface	1	2	19.35	8.08	32.38	93.00	6.7	3.1	3.1
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	CS2(A)	09:23:09	3.3	Middle	2	1	19.26	8.08	32.94	91.00	6.5	3.3	3.3
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	CS2(A)	09:22:28	3.3	Middle	2	2	19.29	8.08	32.91	91.10	6.5	3.3	3.5
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	CS2(A)	09:22:58	5.6	Bottom	3	1	19.23	8.08	33.13	91.00	6.5	3.6	2.8
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	CS2(A)	09:22:16	5.6	Bottom	3	2	19.24	8.08	33.10	91.20	6.5	3.5	3.6
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	CS(Mf)5	07:04:19	1.0	Surface	1	1	19.48	8.05	32.63	93.60	6.6	2.6	4.5
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	CS(Mf)5	07:03:36	1.0	Surface	1	2	19.46	8.05	32.68	93.00	6.6	2.7	4.2
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	CS(Mf)5	07:04:04	6.3	Middle	2	1	19.24	8.04	33.21	90.10	6.4	2.9	3.5
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	CS(Mf)5	07:03:22	6.3	Middle	2	2	19.26	8.03	33.22	90.30	6.4	3.0	3.7
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	CS(Mf)5	07:03:10	11.5	Bottom	3	1	19.27	8.02	33.30	89.10	6.3	3.2	3.6
HKLR	HY/2011/03	2025-04-16	Mid-Flood	Fine	CS(Mf)5	07:03:52	11.5	Bottom	3	2	19.24	8.03	33.30	89.00	6.3	3.2	3.4
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	IS5	14:59:57	1.0	Surface	1	1	19.93	8.06	32.00	96.20	6.8	2.7	2.9
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	IS5	15:00:35	1.0	Surface	1	2	19.96	8.06	31.99	96.50	6.9	2.8	3.5
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	IS5	14:59:44	4.3	Middle	2	1	19.76	8.05	32.35	94.80	6.7	3.0	2.7
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	IS5	15:00:22	4.3	Middle	2	2	19.77	8.05	32.34	94.90	6.7	3.0	3.6
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	IS5	15:00:10	7.5	Bottom	3	1	19.77	8.05	32.40	94.60	6.7	3.1	3.8
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	IS5	14:59:34	7.5	Bottom	3	2	19.75	8.05	32.42	94.50	6.7	3.1	4.0
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	IS(Mf)6	15:10:28	1.0	Surface	1	1	19.94	8.07	31.93	98.40	7.0	2.7	2.8
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	IS(Mf)6	15:10:45	1.0	Surface	1	2	19.95	8.07	32.01	99.30	7.1	2.7	3.4
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	IS(Mf)6	15:10:36	2.2	Bottom	3	1	19.90	8.06	32.12	97.50	6.9	2.9	3.6
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	IS(Mf)6	15:10:17	2.2	Bottom	3	2	19.86	8.08	32.10	96.10	6.8	2.9	2.8
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	IS7	15:21:05	1.0	Surface	1	1	19.95	8.08	31.99	98.20	7.0	2.6	3.4
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	IS7	15:20:47	1.0	Surface	1	2	19.93	8.07	32.02	97.90	7.0	2.8	3.2

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	IS7	15:20:54	2.3	Bottom	3	1	19.88	8.07	32.13	97.50	6.9	2.9	3.3
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	IS7	15:20:38	2.3	Bottom	3	2	19.85	8.07	32.16	97.30	6.9	2.9	2.6
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	IS8(N)	15:55:52	1.0	Surface	1	1	19.96	8.06	31.93	96.70	6.9	2.7	2.8
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	IS8(N)	15:55:33	1.0	Surface	1	2	19.94	8.05	31.95	96.10	6.8	2.7	3.7
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	IS8(N)	15:55:43	3.0	Bottom	3	1	19.90	8.05	32.07	96.10	6.8	2.9	3.6
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	IS8(N)	15:55:24	3.0	Bottom	3	2	19.84	8.05	32.15	95.50	6.8	3.0	4.4
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	IS(Mf)9	15:30:04	1.0	Surface	1	1	19.95	8.07	32.03	97.40	6.9	2.6	4.1
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	IS(Mf)9	15:29:43	1.0	Surface	1	2	19.94	8.07	32.02	97.10	6.9	2.7	3.7
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	IS(Mf)9	15:29:54	2.6	Bottom	3	1	19.87	8.07	32.19	97.00	6.9	2.9	3.8
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	IS(Mf)9	15:29:36	2.6	Bottom	3	2	19.85	8.06	32.19	96.80	6.9	2.8	3.2
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	IS10(N)	16:08:29	1.0	Surface	1	1	19.81	8.09	32.45	92.50	6.6	3.0	3.1
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	IS10(N)	16:09:06	1.0	Surface	1	2	19.83	8.09	32.45	92.80	6.7	3.0	3.7
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	IS10(N)	16:08:52	5.2	Middle	2	1	19.67	8.08	33.08	91.70	6.6	3.1	3.9
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	IS10(N)	16:08:16	5.2	Middle	2	2	19.66	8.08	33.10	91.70	6.6	3.1	3.5
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	IS10(N)	16:08:05	9.4	Bottom	3	1	19.67	8.08	33.12	91.90	6.6	3.2	3.8
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	IS10(N)	16:08:44	9.4	Bottom	3	2	19.68	8.08	33.10	91.70	6.6	3.3	3.0
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	SR3(N)	14:44:49	1.0	Surface	1	1	19.95	8.06	32.05	99.00	7.0	2.8	3.3
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	SR3(N)	14:44:31	1.0	Surface	1	2	19.95	8.06	32.01	97.80	6.9	2.8	2.6
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	SR3(N)	14:44:20	2.3	Bottom	3	1	19.89	8.06	32.10	96.10	6.8	3.0	2.3
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	SR3(N)	14:44:39	2.3	Bottom	3	2	19.92	8.06	32.05	97.20	6.9	2.9	2.6
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	SR4(N3)	15:45:37	1.0	Surface	1	1	19.93	8.06	31.96	96.30	6.8	2.7	3.0
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	SR4(N3)	15:45:20	1.0	Surface	1	2	19.94	8.06	31.97	96.20	6.8	2.8	2.7
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	SR4(N3)	15:45:27	2.9	Bottom	3	1	19.88	8.05	32.11	95.70	6.8	2.9	3.1
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	SR4(N3)	15:45:09	2.9	Bottom	3	2	19.80	8.05	32.14	95.30	6.8	2.9	3.8
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	SR5(N)	15:59:40	1.0	Surface	1	1	19.82	8.09	32.42	93.70	6.7	2.7	4.2
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	SR5(N)	15:59:00	1.0	Surface	1	2	19.79	8.09	32.40	93.30	6.7	2.7	3.6
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	SR5(N)	15:59:27	4.7	Middle	2	1	19.69	8.08	33.00	91.90	6.6	2.9	3.6
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	SR5(N)	15:58:46	4.7	Middle	2	2	19.69	8.08	32.97	92.00	6.6	2.9	4.3
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	SR5(N)	15:59:17	8.3	Bottom	3	1	19.66	8.08	33.12	92.20	6.6	3.2	3.4
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	SR5(N)	15:58:34	8.3	Bottom	3	2	19.66	8.08	33.05	92.30	6.6	3.1	3.5
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	SR10A(N)	17:01:14	1.0	Surface	1	1	19.83	8.09	32.87	94.00	6.7	2.7	3.7
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	SR10A(N)	17:02:00	1.0	Surface	1	2	19.81	8.09	32.89	94.10	6.7	2.7	3.7
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	SR10A(N)	17:01:43	6.5	Middle	2	1	19.69	8.09	33.43	91.70	6.5	2.9	4.2
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	SR10A(N)	17:01:01	6.5	Middle	2	2	19.70	8.09	33.42	92.20	6.6	2.9	4.9
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	SR10A(N)	17:00:49	12.0	Bottom	3	1	19.69	8.09	33.45	92.40	6.6	2.9	5.3
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	SR10A(N)	17:01:31	12.0	Bottom	3	2	19.72	8.09	33.44	91.90	6.6	2.9	4.6
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	SR10B(N2)	17:11:20	1.0	Surface	1	1	19.83	8.09	32.86	93.10	6.7	2.6	3.2
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	SR10B(N2)	17:11:55	1.0	Surface	1	2	19.84	8.09	32.91	93.10	6.7	2.7	3.0
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	SR10B(N2)	17:11:07	3.7	Middle	2	1	19.74	8.09	33.37	92.10	6.6	2.8	3.8
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	SR10B(N2)	17:11:44	3.7	Middle	2	2	19.72	8.09	33.33	92.00	6.6	2.8	3.6
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	SR10B(N2)	17:10:58	6.3	Bottom	3	1	19.72	8.09	33.43	92.10	6.6	2.9	3.2
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	SR10B(N2)	17:11:32	6.3	Bottom	3	2	19.74	8.08	33.35	91.90	6.6	2.9	3.8
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	CS2(A)	15:00:50	1.0	Surface	1	1	19.71	8.09	32.51	96.20	6.9	2.8	4.0
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	CS2(A)	15:01:23	1.0	Surface	1	2	19.72	8.09	32.54	95.70	6.9	2.7	4.4
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	CS2(A)	15:01:12	3.4	Middle	2	1	19.62	8.08	33.06	93.80	6.7	2.9	3.6
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	CS2(A)	15:00:39	3.4	Middle	2	2	19.61	8.07	33.03	94.00	6.8	3.0	4.4
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	CS2(A)	15:00:28	5.7	Bottom	3	1	19.59	8.07	33.19	94.40	6.8	3.2	3.3
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	CS2(A)	15:01:02	5.7	Bottom	3	2	19.60	8.07	33.16	94.30	6.8	3.2	3.3
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	CS(Mf)5	16:38:23	1.0	Surface	1	1	19.98	8.08	32.15	92.90	6.6	2.6	3.5
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	CS(Mf)5	16:39:03	1.0	Surface	1	2	19.97	8.08	32.16	93.50	6.6	2.6	4.3
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	CS(Mf)5	16:38:06	6.3	Middle	2	1	19.59	8.07	32.87	90.30	6.4	2.7	4.9
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	CS(Mf)5	16:38:49	6.3	Middle	2	2	19.59	8.06	32.87	90.60	6.4	2.7	3.9
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	CS(Mf)5	16:37:56	11.6	Bottom	3	1	19.58	8.07	32.88	89.80	6.4	2.9	3.3
HKLR	HY/2011/03	2025-04-18	Mid-Ebb	Fine	CS(Mf)5	16:38:39	11.6	Bottom	3	2	19.58	8.05	32.03	90.00	6.4	2.9	4.2
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	IS5	09:12:10	1.0	Surface	1	1	19.57	8.07	32.68	94.20	6.6	2.6	3.6
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	IS5	09:11:23	1.0	Surface	1	2	19.58	8.08	32.67	95.60	6.7	2.7	4.2
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	IS5	09:11:11	4.2	Middle	2	1	19.39	8.05	33.04	91.30	6.4	2.8	3.4
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	IS5	09:11:57	4.2	Middle	2	2	19.38	8.05	33.04	92.00	6.5	2.8	3.4
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	IS5	09:11:39	7.4	Bottom	3	1	19.32	8.04	33.11	91.20	6.4	2.9	3.6
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	IS5	09:11:00	7.4	Bottom	3	2	19.38	8.05	33.11	90.90	6.4	2.9	3.7
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	IS(Mf)6	09:01:03	1.0	Surface	1	1	19.62	8.08	32.67	96.10	6.8	2.6	3.2
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	IS(Mf)6	09:00:46	1.0	Surface	1	2	19.61	8.08	32.68	95.90	6.7	2.6	3.1
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	IS(Mf)6	09:00:53	2.2	Bottom	3	1	19.59	8.08	32.75	95.70	6.7	2.8	2.7
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	IS(Mf)6	09:00:33	2.2	Bottom	3	2	19.58	8.07	32.78	95.60	6.7	2.8	3.9
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	IS7	08:52:17	1.0	Surface	1	1	19.60	8.08	32.68	95.40	6.7	2.5	3.9
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	IS7	08:52:32	1.0	Surface	1	2	19.63	8.08	32.65	95.70	6.7	2.5	3.1
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	IS7	08:52:24	2.3	Bottom	3	1	19.59	8.07	32.73	95.40	6.7	2.8	3.8
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	IS7	08:52:09	2.3	Bottom	3	2	19.58	8.07	32.74	95.20	6.7	2.7	4.3
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	IS8(N)	08:20:40	1.0	Surface	1	1	19.59	8.08	32.64	97.20	6.9	2.6	4.2
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	IS8(N)	08:19:48	1.0	Surface	1	2	19.61	8.08	32.63	96.10	6.8	2.6	4.4
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	IS8(N)	08:19:56	3.1	Bottom	3	1	19.55	8.07	32.83	95.70	6.7	2.8	4.0
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	IS8(N)	08:19:38	3.1	Bottom	3	2	19.55	8.08	32.85	94.80	6.7	2.9	3.8
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	IS(Mf)9	08:43:23	1.0	Surface	1	1	19.64	8.08	32.63	95.80	6.7	2.5	3.5
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	IS(Mf)9	08:43:07	1.0	Surface	1	2	19.63	8.09	32.65	95.50	6.7	2.6	4.1
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	IS(Mf)9	08:43:13	2.5	Bottom	3	1	19.61	8.07	32.75	95.10	6.7	2.9	4.3
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	IS(Mf)9	08:42:56	2.5	Bottom	3	2	19.57	8.08	32.75	94.50	6.6	2.8	3.5
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	IS10(N)	08:35:26	1.0	Surface	1	1	19.69	8.10	32.55	94.20	6.8	2.8	3.7
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	IS10(N)	08:36:07	1.0	Surface	1	2	19.70	8.10	32.55	94.40	6.8	2.8	3.8
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	IS10(N)	08:35:50	5.3	Middle	2	1	19.61	8.08	33.09	92.40	6.6	2.9	3.1
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	IS10(N)	08:35:10	5.3	Middle	2	2	19.61	8.08	33.07	92.60	6.7	3.0	3.5
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	IS10(N)	08:35:40	9.5	Bottom	3	1	19.64	8.08	33.11	92.60	6.6	3.2	4.6
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	IS10(N)	08:35:00	9.5	Bottom	3	2	19.61	8.08	33.13	92.60	6.7	3.2	3.8
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	SR3(N)	09:28:03	1.0	Surface	1	1	19.60	8.07	32.73	94.20	6.6	2.8	4.0
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	SR3(N)	09:28:19	1.0	Surface	1	2	19.61	8.08	32.71	94.80	6.7	2.8	4.7
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	SR3(N)	09:28:10	2.3	Bottom	3	1	19.59	8.07	32.80	94.00	6.6	2.9	3.5
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	SR3(N)	09:27:55	2.3	Bottom	3	2	19.54	8.07	32.82	93.10	6.5	3.0	3.9
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	SR4(N3)	08:28:32	1.0	Surface	1	1	19.62	8.08	32.63	95.00	6.7	2.5	6.2
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	SR4(N3)	08:28:12	1.0	Surface	1	2	19.57	8.07	32.62	95.20	6.7	2.4	5.4
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	SR4(N3)	08:28:23	2.9	Bottom	3	1	19.55	8.06	32.82	94.90	6.7	2.7	3.4
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	SR4(N3)	08:28:01	2.9	Bottom	3	2	19.54	8.07	32.85	95.10	6.7	2.6	2.8
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	SR5(N)	08:46:13	1	Surface	1	1	19.71	8.10	32.54	92.90	6.7	2.8	2.8
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	SR5(N)	08:45:30	1	Surface	1	2	19.71	8.10	32.54	93.00	6.7	2.7	2.7
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	SR5(N)	08:45:59	4.7	Middle	2	1	19.64	8.08	33.00	91.60	6.6	2.9	3.6
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	SR5(N)	08:45:17	4.7	Middle	2	2	19.64	8.08	33.01	92.00	6.6	2.9	3.2
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	SR5(N)	08:45:05	8.3	Bottom	3	1	19.60	8.08	33.15	92.30	6.6	3.1	3.4
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	SR5(N)	08:45:48	8.3	Bottom	3	2	19.61	8.08	33.12	92.00	6.6	3.2	3.6
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	SR10A(N)	07:41:30	1	Surface	1	1	19.78	8.09	32.76	92.50	6.6	2.5	3.1
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	SR10A(N)	07:40:46	1	Surface	1	2	19.80	8.08	32.72	92.50	6.6	2.5	3.2
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	SR10A(N)	07:40:29	6.6	Middle	2	1	19.68	8.07	33.28	91.40	6.5	2.7	3.1
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	SR10A(N)	07:41:13	6.6	Middle	2	2	19.67	8.07	33.28	90.90	6.5	2.7	3.6
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	SR10A(N)	07:40:18	12.2	Bottom	3	1	19.67	8.07	33.34	91.60	6.6	2.9	2.4
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	SR10A(N)	07:41:03	12.2	Bottom	3	2	19.70	8.07	33.33	91.30	6.5	2.9	3.5
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	SR10B(N2)	07:28:47	1.0	Surface	1	1	19.81	8.08	32.75	97.30	7.0	2.5	2.4
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	SR10B(N2)	07:28:05	1.0	Surface	1	2	19.81	8.07	32.75	96.30	6.9	2.5	3.3

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	SR10B(N2)	07:27:47	3.7	Middle	2	1	19.73	8.07	33.16	94.40	6.8	2.7	3.1
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	SR10B(N2)	07:28:32	3.7	Middle	2	2	19.73	8.07	33.12	93.00	6.7	2.7	3.1
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	SR10B(N2)	07:28:20	6.4	Bottom	3	1	19.70	8.07	33.27	92.60	6.6	2.8	3.2
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	SR10B(N2)	07:27:36	6.4	Bottom	3	2	19.67	8.07	33.31	92.50	6.6	2.8	3.9
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	CS2(A)	09:40:41	1	Surface	1	1	19.65	8.10	32.48	93.80	6.8	2.9	3.7
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	CS2(A)	09:40:02	1	Surface	1	2	19.65	8.09	32.50	93.90	6.8	2.9	3.1
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	CS2(A)	09:40:27	3.3	Middle	2	1	19.59	8.09	32.92	92.70	6.7	3.0	3.3
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	CS2(A)	09:39:48	3.3	Middle	2	2	19.62	8.09	32.89	92.70	6.7	3.0	3.5
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	CS2(A)	09:40:17	5.6	Bottom	3	1	19.57	8.09	33.07	93.00	6.7	3.3	2.8
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	CS2(A)	09:39:37	5.6	Bottom	3	2	19.57	8.09	33.05	93.20	6.7	3.2	3.6
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	CS(Mf)5	07:38:38	1.0	Surface	1	1	19.64	8.06	32.77	95.40	6.7	2.5	4.5
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	CS(Mf)5	07:37:54	1.0	Surface	1	2	19.63	8.07	32.80	95.00	6.7	2.6	4.2
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	CS(Mf)5	07:38:22	6.3	Middle	2	1	19.45	8.05	33.22	92.70	6.5	2.7	3.5
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	CS(Mf)5	07:37:39	6.3	Middle	2	2	19.47	8.06	33.22	93.00	6.5	2.7	3.7
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	CS(Mf)5	07:37:28	11.5	Bottom	3	1	19.48	8.06	33.27	91.90	6.5	2.9	3.6
HKLR	HY/2011/03	2025-04-18	Mid-Flood	Fine	CS(Mf)5	07:38:11	11.5	Bottom	3	2	19.44	8.05	33.28	91.60	6.4	2.9	3.4
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Cloudy	IS5	18:10:07	1.0	Surface	1	1	26.60	8.08	29.86	120.20	8.0	3.3	1.2
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Cloudy	IS5	18:10:54	1.0	Surface	1	2	26.59	8.08	29.73	120.00	8.0	3.3	1.7
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Cloudy	IS5	18:09:52	4.1	Middle	2	1	26.53	8.10	30.34	119.60	8.0	3.3	1.4
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Cloudy	IS5	18:10:32	4.1	Middle	2	2	26.57	8.07	30.33	119.90	8.0	3.3	2.1
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Cloudy	IS5	18:09:39	7.2	Bottom	3	1	26.30	8.09	30.32	119.20	7.9	3.3	1.7
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Cloudy	IS5	18:10:19	7.2	Bottom	3	2	26.62	8.08	30.27	119.60	8.0	3.4	2.7
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Cloudy	IS(Mf)6	18:18:31	1.0	Surface	1	1	26.52	8.08	29.88	122.80	8.2	3.4	1.6
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Cloudy	IS(Mf)6	18:18:58	1.0	Surface	1	2	26.52	8.08	29.89	122.60	8.2	3.3	2.2
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Cloudy	IS(Mf)6	18:18:11	2.0	Bottom	3	1	26.41	8.07	30.09	122.70	8.2	3.4	2.1
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Cloudy	IS(Mf)6	18:18:43	2.0	Bottom	3	2	26.42	8.07	30.15	122.80	8.2	3.4	1.7
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Cloudy	IS7	18:29:11	1.0	Surface	1	1	26.56	8.05	29.85	122.90	8.2	3.4	1.6
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Cloudy	IS7	18:29:27	1.0	Surface	1	2	26.63	8.05	29.81	122.70	8.2	3.3	1.8
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Cloudy	IS7	18:28:52	2.0	Bottom	3	1	26.42	8.05	30.09	122.70	8.2	3.4	1.7
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Cloudy	IS7	18:29:18	2.0	Bottom	3	2	26.46	8.05	30.08	122.60	8.2	3.3	2.0
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Cloudy	IS8(N)	19:01:45	1.0	Surface	1	1	26.60	8.12	29.73	122.50	8.2	3.4	1.8
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Cloudy	IS8(N)	19:02:09	1.0	Surface	1	2	26.59	8.12	29.78	122.70	8.2	3.4	2.5
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Cloudy	IS8(N)	19:01:34	3.0	Bottom	3	1	26.58	8.11	30.26	122.70	8.2	3.4	1.9
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Cloudy	IS8(N)	19:01:57	3.0	Bottom	3	2	26.54	8.12	29.94	122.60	8.2	3.4	1.3
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Cloudy	IS(Mf)9	18:39:34	1.0	Surface	1	1	26.59	8.08	29.77	122.10	8.1	3.3	2.0
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Cloudy	IS(Mf)9	18:40:13	1.0	Surface	1	2	26.58	8.09	29.77	121.90	8.1	3.3	1.6
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Cloudy	IS(Mf)9	18:39:24	2.6	Bottom	3	1	26.53	8.07	29.92	121.90	8.1	3.4	1.3
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Cloudy	IS(Mf)9	18:39:49	2.6	Bottom	3	2	26.53	8.08	29.96	121.80	8.1	3.3	1.8
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Fine	IS10(N)	19:26:00	1.0	Surface	1	1	25.54	8.09	29.80	90.30	6.3	3.0	1.6
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Fine	IS10(N)	19:26:36	1.0	Surface	1	2	25.55	8.09	29.80	90.90	6.3	3.0	2.4
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Fine	IS10(N)	19:26:23	5.3	Middle	2	1	25.37	8.07	30.36	89.50	6.2	3.0	2.0
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Fine	IS10(N)	19:25:48	5.3	Middle	2	2	25.36	8.07	30.38	89.40	6.2	3.0	1.7
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Fine	IS10(N)	19:26:10	9.6	Bottom	3	1	25.37	8.07	30.39	89.20	6.2	3.1	2.5
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Fine	IS10(N)	19:26:14	9.6	Bottom	3	2	25.40	8.07	30.37	89.40	6.2	3.1	1.8
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Cloudy	SR3(N)	17:58:58	1.0	Surface	1	1	26.52	8.09	29.71	120.50	8.0	3.4	2.0
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Cloudy	SR3(N)	17:59:23	1.0	Surface	1	2	26.51	8.09	29.71	120.50	8.0	3.3	2.1
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Cloudy	SR3(N)	17:58:40	2.2	Bottom	3	1	26.44	8.08	29.88	120.10	8.0	3.4	1.4
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Cloudy	SR3(N)	17:59:09	2.2	Bottom	3	2	26.48	8.09	29.97	121.10	8.1	3.4	1.8
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Cloudy	SR4(N3)	18:51:18	1.0	Surface	1	1	26.62	8.09	29.73	121.50	8.1	3.3	2.0
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Cloudy	SR4(N3)	18:51:53	1.0	Surface	1	2	26.60	8.09	29.72	121.80	8.1	3.3	1.3
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Cloudy	SR4(N3)	18:51:03	2.8	Bottom	3	1	26.54	8.09	29.96	121.40	8.1	3.3	2.0
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Cloudy	SR4(N3)	18:51:35	2.8	Bottom	3	2	26.58	8.09	29.93	121.10	8.1	3.3	2.1
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Fine	SR5(N)	19:18:05	1.0	Surface	1	1	25.55	8.09	29.80	91.30	6.4	2.9	1.3
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Fine	SR5(N)	19:17:26	1.0	Surface	1	2	25.51	8.09	29.80	90.60	6.3	2.9	2.0
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Fine	SR5(N)	19:17:53	4.7	Middle	2	1	25.39	8.07	30.30	89.60	6.2	2.9	2.4
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Fine	SR5(N)	19:17:13	4.7	Middle	2	2	25.38	8.07	30.29	89.40	6.2	2.9	2.3
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Fine	SR5(N)	19:17:02	8.4	Bottom	3	1	25.37	8.07	30.39	89.50	6.2	3.0	2.1
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Fine	SR5(N)	19:17:43	8.4	Bottom	3	2	25.37	8.07	30.42	89.70	6.2	3.1	1.5
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Fine	SR10A(N)	20:20:55	1.0	Surface	1	1	25.54	8.09	30.32	91.80	6.4	2.8	1.4
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Fine	SR10A(N)	20:20:09	1.0	Surface	1	2	25.55	8.09	30.31	91.10	6.3	2.8	1.6
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Fine	SR10A(N)	20:20:37	6.7	Middle	2	1	25.38	8.07	30.79	88.80	6.2	2.9	1.8
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Fine	SR10A(N)	20:19:53	6.7	Middle	2	2	25.39	8.08	30.78	89.50	6.2	2.9	1.9
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Fine	SR10A(N)	20:19:41	12.3	Bottom	3	1	25.40	8.08	30.79	89.30	6.2	2.9	1.6
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Fine	SR10A(N)	20:20:26	12.3	Bottom	3	2	25.41	8.08	30.79	89.30	6.2	2.9	1.8
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Fine	SR10B(N2)	20:30:41	1.0	Surface	1	1	25.55	8.09	30.36	91.20	6.3	2.8	1.3
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Fine	SR10B(N2)	20:30:06	1.0	Surface	1	2	25.55	8.09	30.33	90.90	6.3	2.8	1.7
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Fine	SR10B(N2)	20:29:53	3.7	Middle	2	1	25.44	8.08	30.69	90.00	6.3	2.8	1.7
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Fine	SR10B(N2)	20:30:30	3.7	Middle	2	2	25.41	8.08	30.70	89.90	6.2	2.8	1.3
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Fine	SR10B(N2)	20:30:19	6.3	Bottom	3	1	25.43	8.07	30.74	89.90	6.2	2.9	1.3
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Fine	SR10B(N2)	20:29:44	6.3	Bottom	3	2	25.44	8.08	30.74	89.90	6.2	2.9	1.2
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Fine	CS2(A)	18:18:54	1.0	Surface	1	1	25.45	8.09	29.98	93.70	6.5	2.9	2.0
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Fine	CS2(A)	18:19:25	1.0	Surface	1	2	25.46	8.09	29.90	93.00	6.5	2.8	3.0
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Fine	CS2(A)	18:18:42	3.4	Middle	2	1	25.31	8.07	30.46	91.50	6.4	3.0	3.1
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Fine	CS2(A)	18:19:14	3.4	Middle	2	2	25.32	8.08	30.49	91.30	6.4	2.9	1.7
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Fine	CS2(A)	18:18:32	5.7	Bottom	3	1	25.30	8.07	30.61	91.50	6.4	3.0	2.8
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Fine	CS2(A)	18:19:05	5.7	Bottom	3	2	25.32	8.07	30.58	91.40	6.4	3.1	3.2
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Cloudy	CS(Mf)5	19:48:03	1.0	Surface	1	1	26.55	8.08	29.85	122.10	8.1	3.3	2.1
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Cloudy	CS(Mf)5	19:48:55	1.0	Surface	1	2	26.62	8.09	29.78	121.50	8.1	3.3	1.7
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Cloudy	CS(Mf)5	19:47:52	6.0	Middle	2	1	26.36	8.08	29.74	121.80	8.1	3.3	2.6
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Cloudy	CS(Mf)5	19:48:33	6.0	Middle	2	2	26.37	8.08	30.29	120.80	8.1	3.4	2.7
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Cloudy	CS(Mf)5	19:47:31	11.0	Bottom	3	1	26.33	8.08	30.24	121.80	8.1	3.3	1.6
HKLR	HY/2011/03	2025-04-21	Mid-Ebb	Cloudy	CS(Mf)5	19:48:15	11.0	Bottom	3	2	26.34	8.08	30.28	120.70	8.0	3.3	1.5
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Cloudy	IS5	06:34:04	1.0	Surface	1	1	26.60	8.09	29.58	122.90	8.2	3.4	3.1
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Cloudy	IS5	06:34:46	1.0	Surface	1	2	26.47	8.08	29.72	124.50	8.3	3.5	2.2
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Cloudy	IS5	06:33:41	4.2	Middle	2	1	26.59	8.08	30.17	122.70	8.1	3.4	1.6
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Cloudy	IS5	06:34:25	4.2	Middle	2	2	26.61	8.08	30.18	124.00	8.2	3.5	2.3
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Cloudy	IS5	06:33:23	7.4	Bottom	3	1	26.51	8.08	30.22	121.90	8.1	3.5	1.3
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Cloudy	IS5	06:34:12	7.4	Bottom	3	2	26.33	8.08	30.22	122.70	8.1	3.4	1.4
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Cloudy	IS(Mf)6	06:22:14	1.0	Surface	1	1	26.64	8.12	29.56	121.60	8.1	3.3	1.4
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Cloudy	IS(Mf)6	06:22:44	1.0	Surface	1	2	26.53	8.12	29.57	121.50	8.1	3.3	1.6
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Cloudy	IS(Mf)6	06:22:03	2.0	Bottom	3	1	26.46	8.11	29.76	121.50	8.1	3.3	1.9
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Cloudy	IS(Mf)6	06:22:19	2.0	Bottom	3	2	26.47	8.12	29.82	121.30	8.1	3.3	2.7
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Cloudy	IS7	06:13:24	1.0	Surface	1	1	26.69	8.11	29.61	122.10	8.2	3.4	2.1
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Cloudy	IS7	06:13:49	1.0	Surface	1	2	26.71	8.11	29.59	122.10	8.2	3.3	1.7
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Cloudy	IS7	06:12:59	2.0	Bottom	3	1	26.60	8.10	29.57	121.70	8.1	3.4	1.9
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Cloudy	IS7	06:13:33	2.0	Bottom	3	2	26.63	8.10	29.94	122.00	8.2	3.3	2.2
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Cloudy	IS8(N)	05:42:09	1.0	Surface	1	1	26.60	8.11	29.66	121.70	8.1	3.3	2.4
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Cloudy	IS8(N)	05:42:34	1.0	Surface	1	2	26.65	8.11	29.63	121.50	8.1	3.3	2.1
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Cloudy	IS8(N)	05:41:52	3.1	Bottom	3	1	26.38	8.10	29.94	121.70	8.1	3.3	2.0
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Cloudy	IS8(N)	05:42:15	3.1	Bottom	3	2	26.58	8.10	29.89	121.40	8.1	3.3	1.8
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Cloudy	IS(Mf)9	06:01:55	1.0	Surface	1	1	26.70	8.08	29.72	122.70	8.2	3.5	2.3
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Cloudy	IS(Mf)9	06:02:19	1.0	Surface	1	2	26.69	8.08	29.64	122.50	8.2	3.4	2.8
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Cloudy	IS(Mf)9	06:01:37	2.5	Bottom	3	1	26.63	8.07	29.97	122.60	8.2	3.5	2.5
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Cloudy	IS(Mf)9	06:02:07	2.5	Bottom	3	2	26.63	8.07	29.93	122.30	8.2	3.4	1.9

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Fine	IS10(N)	06:13:17	1.0	Surface	1	1	25.41	8.09	29.97	91.10	6.4	2.8	2.4
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Fine	IS10(N)	06:13:57	1.0	Surface	1	2	25.43	8.09	29.97	91.20	6.4	2.9	3.0
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Fine	IS10(N)	06:13:42	5.3	Middle	2	1	25.29	8.07	30.43	89.10	6.2	2.9	2.2
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Fine	IS10(N)	06:13:02	5.3	Middle	2	2	25.28	8.07	30.43	89.40	6.2	3.0	2.7
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Fine	IS10(N)	06:13:32	9.6	Bottom	3	1	25.31	8.07	30.44	89.60	6.3	3.1	2.9
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Fine	IS10(N)	06:12:52	9.6	Bottom	3	2	25.29	8.07	30.47	89.90	6.3	3.1	3.4
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Cloudy	SR3(N)	06:44:41	1.0	Surface	1	1	26.35	8.09	29.68	122.40	8.2	3.4	3.8
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Cloudy	SR3(N)	06:45:19	1.0	Surface	1	2	26.35	8.09	29.64	122.70	8.2	3.4	4.0
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Cloudy	SR3(N)	06:44:18	2.2	Bottom	3	1	26.34	8.09	29.96	122.30	8.2	3.4	1.7
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Cloudy	SR3(N)	06:44:58	2.2	Bottom	3	2	26.54	8.10	29.79	122.00	8.1	3.4	2.6
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Cloudy	SR4(N3)	05:52:22	1.0	Surface	1	1	26.71	8.13	29.90	121.50	8.1	3.4	2.4
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Cloudy	SR4(N3)	05:52:53	1.0	Surface	1	2	26.71	8.13	29.85	121.50	8.1	3.4	1.8
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Cloudy	SR4(N3)	05:52:12	2.9	Bottom	3	1	26.60	8.12	29.93	120.70	8.1	3.5	3.0
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Cloudy	SR4(N3)	05:52:35	2.9	Bottom	3	2	26.60	8.12	29.58	121.70	8.1	3.4	3.8
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Fine	SR5(N)	06:23:58	1	Surface	1	1	25.43	8.09	29.96	90.20	6.3	2.9	2.2
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Fine	SR5(N)	06:23:15	1	Surface	1	2	25.43	8.09	29.95	90.20	6.3	2.8	2.5
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Fine	SR5(N)	06:23:43	4.7	Middle	2	1	25.32	8.07	30.36	88.80	6.2	2.9	2.2
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Fine	SR5(N)	06:23:02	4.7	Middle	2	2	25.32	8.07	30.36	89.00	6.2	2.9	1.7
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Fine	SR5(N)	06:22:51	8.4	Bottom	3	1	25.28	8.07	30.48	88.90	6.2	3.0	2.2
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Fine	SR5(N)	06:23:33	8.4	Bottom	3	2	25.30	8.07	30.46	88.80	6.2	3.1	2.2
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Fine	SR10A(N)	05:18:39	1	Surface	1	1	25.51	8.08	30.14	89.80	6.3	2.7	3.2
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Fine	SR10A(N)	05:17:54	1	Surface	1	2	25.52	8.07	30.10	89.60	6.2	2.7	2.2
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Fine	SR10A(N)	05:17:37	6.7	Middle	2	1	25.34	8.05	30.67	88.40	6.2	2.8	1.4
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Fine	SR10A(N)	05:18:21	6.7	Middle	2	2	25.33	8.06	30.67	88.30	6.1	2.8	1.6
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Fine	SR10A(N)	05:17:26	12.4	Bottom	3	1	25.34	8.06	30.71	88.20	6.1	2.9	1.9
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Fine	SR10A(N)	05:18:11	12.4	Bottom	3	2	25.36	8.06	30.70	88.10	6.1	2.9	2.2
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Fine	SR10B(N2)	05:06:50	1.0	Surface	1	1	25.53	8.08	30.12	94.00	6.5	2.7	2.0
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Fine	SR10B(N2)	05:06:10	1.0	Surface	1	2	25.54	8.07	30.09	93.30	6.5	2.7	2.8
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Fine	SR10B(N2)	05:05:51	3.8	Middle	2	1	25.39	8.05	30.48	91.20	6.4	2.8	2.0
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Fine	SR10B(N2)	05:06:35	3.8	Middle	2	2	25.40	8.06	30.44	90.20	6.3	2.8	3.0
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Fine	SR10B(N2)	05:06:23	6.6	Bottom	3	1	25.38	8.05	30.59	89.20	6.2	2.9	2.7
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Fine	SR10B(N2)	05:05:40	6.6	Bottom	3	2	25.35	8.05	30.60	89.40	6.2	2.9	2.4
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Fine	CS2(A)	07:18:46	1	Surface	1	1	25.39	8.09	29.94	90.90	6.4	2.9	1.8
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Fine	CS2(A)	07:18:05	1	Surface	1	2	25.39	8.09	29.94	91.00	6.4	2.9	2.2
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Fine	CS2(A)	07:17:52	3.4	Middle	2	1	25.33	8.08	30.24	89.90	6.3	3.0	2.3
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Fine	CS2(A)	07:18:33	3.4	Middle	2	2	25.31	8.08	30.26	89.90	6.3	2.9	2.1
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Fine	CS2(A)	07:18:19	5.7	Bottom	3	1	25.29	8.08	30.40	90.00	6.3	3.1	2.7
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Fine	CS2(A)	07:17:40	5.7	Bottom	3	2	25.28	8.08	30.38	89.80	6.3	3.0	2.7
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Cloudy	CS(Mf)5	04:59:14	1.0	Surface	1	1	26.52	8.11	29.58	124.60	8.3	3.5	1.6
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Cloudy	CS(Mf)5	05:00:11	1.0	Surface	1	2	26.69	8.11	29.53	124.20	8.2	3.6	1.8
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Cloudy	CS(Mf)5	04:58:55	6.0	Middle	2	1	26.65	8.09	30.19	124.50	8.3	3.5	2.2
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Cloudy	CS(Mf)5	04:59:43	6.0	Middle	2	2	26.41	8.10	30.23	123.20	8.2	3.5	1.8
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Cloudy	CS(Mf)5	04:58:23	11.0	Bottom	3	1	26.42	8.09	30.20	124.40	8.3	3.6	2.1
HKLR	HY/2011/03	2025-04-21	Mid-Flood	Cloudy	CS(Mf)5	04:59:32	11.0	Bottom	3	2	26.38	8.10	30.25	122.70	8.2	3.5	1.8
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	IS5	10:32:02	1.0	Surface	1	1	26.33	8.06	29.89	119.40	7.9	3.3	2.7
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	IS5	10:32:44	1.0	Surface	1	2	26.46	8.07	29.75	119.20	7.9	3.3	2.7
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	IS5	10:31:38	4.2	Middle	2	1	26.47	8.06	30.35	118.80	7.9	3.4	2.8
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	IS5	10:32:23	4.2	Middle	2	2	26.45	8.06	30.34	119.10	7.9	3.4	3.8
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	IS5	10:31:21	7.4	Bottom	3	1	26.19	8.06	30.39	118.40	7.8	3.4	3.2
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	IS5	10:32:10	7.4	Bottom	3	2	26.37	8.06	30.39	118.80	7.9	3.4	2.8
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	IS(Mf)6	10:22:01	1.0	Surface	1	1	26.44	8.08	29.83	121.30	8.1	3.4	3.1
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	IS(Mf)6	10:22:31	1.0	Surface	1	2	26.49	8.08	29.80	121.30	8.1	3.4	3.1
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	IS(Mf)6	10:21:50	2.0	Bottom	3	1	26.22	8.07	30.11	120.90	8.1	3.4	3.0
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	IS(Mf)6	10:22:06	2.0	Bottom	3	2	26.42	8.07	30.06	121.20	8.1	3.4	2.8
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	IS7	10:13:14	1.0	Surface	1	1	26.50	8.10	29.73	120.80	8.0	3.3	2.9
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	IS7	10:13:36	1.0	Surface	1	2	26.39	8.10	29.74	120.70	8.0	3.3	3.9
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	IS7	10:12:46	2.0	Bottom	3	1	26.32	8.09	29.93	120.70	8.0	3.3	3.9
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	IS7	10:13:24	2.0	Bottom	3	2	26.33	8.10	29.99	120.50	8.0	3.3	3.4
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	IS8(N)	09:39:55	1.0	Surface	1	1	26.55	8.10	30.07	120.70	8.1	3.4	4.5
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	IS8(N)	09:40:21	1.0	Surface	1	2	26.55	8.10	30.02	120.70	8.1	3.5	4.1
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	IS8(N)	09:39:39	3.0	Bottom	3	1	26.44	8.09	30.10	119.90	8.0	3.5	3.7
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	IS8(N)	09:40:02	3.0	Bottom	3	2	26.44	8.09	29.75	120.90	8.1	3.4	3.1
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	IS(Mf)9	10:01:41	1.0	Surface	1	1	26.55	8.09	29.78	120.90	8.0	3.3	4.0
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	IS(Mf)9	10:02:06	1.0	Surface	1	2	26.57	8.09	29.76	120.70	8.0	3.3	4.7
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	IS(Mf)9	10:01:24	2.6	Bottom	3	1	26.46	8.08	29.74	120.90	8.0	3.3	3.0
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	IS(Mf)9	10:01:54	2.6	Bottom	3	2	26.49	8.08	30.11	120.60	8.0	3.4	3.7
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	IS10(N)	09:42:54	1.0	Surface	1	1	26.47	8.12	30.15	123.50	8.2	3.4	3.1
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	IS10(N)	09:43:29	1.0	Surface	1	2	26.23	8.12	30.16	123.40	8.1	3.4	3.0
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	IS10(N)	09:42:41	4.4	Middle	2	1	26.22	8.11	30.10	122.70	8.1	3.4	3.9
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	IS10(N)	09:43:19	4.4	Middle	2	2	26.26	8.11	30.13	123.10	8.1	3.4	3.0
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	IS10(N)	09:42:31	7.8	Bottom	3	1	26.22	8.12	29.73	122.10	8.1	3.4	4.3
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	IS10(N)	09:43:07	7.8	Bottom	3	2	26.23	8.12	29.68	122.70	8.1	3.5	3.6
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	SR3(N)	10:43:39	1.0	Surface	1	1	26.34	8.06	29.88	119.70	8.0	3.3	3.4
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	SR3(N)	10:44:17	1.0	Surface	1	2	26.33	8.06	29.88	119.70	8.0	3.3	3.1
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	SR3(N)	10:43:14	2.0	Bottom	3	1	26.26	8.05	30.05	119.30	7.9	3.3	3.4
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	SR3(N)	10:43:56	2.0	Bottom	3	2	26.30	8.06	30.14	120.30	8.0	3.3	3.1
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	SR4(N3)	09:51:07	1.0	Surface	1	1	26.54	8.06	29.89	121.90	8.1	3.4	3.7
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	SR4(N3)	09:51:40	1.0	Surface	1	2	26.53	8.06	29.81	121.70	8.1	3.3	3.8
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	SR4(N3)	09:50:59	3.0	Bottom	3	1	26.47	8.05	30.14	121.80	8.1	3.4	5.0
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	SR4(N3)	09:51:22	3.0	Bottom	3	2	26.47	8.05	30.10	121.50	8.1	3.4	4.1
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	SR5(N)	09:54:19	1.0	Surface	1	1	26.18	8.10	30.02	124.30	8.2	3.4	2.7
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	SR5(N)	09:54:51	1.0	Surface	1	2	26.18	8.11	30.10	123.10	8.1	3.4	2.7
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	SR5(N)	09:54:06	4.4	Middle	2	1	25.93	8.10	29.57	123.20	8.1	3.4	3.5
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	SR5(N)	09:54:42	4.4	Middle	2	2	25.89	8.10	29.58	123.00	8.1	3.4	3.3
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	SR5(N)	09:53:57	7.8	Bottom	3	1	25.97	8.10	29.96	122.80	8.1	3.4	2.7
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	SR5(N)	09:54:30	7.8	Bottom	3	2	25.96	8.10	30.10	122.60	8.1	3.5	2.7
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	SR10A(N)	08:52:07	1.0	Surface	1	1	26.21	8.11	29.55	123.40	8.1	3.4	4.0
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	SR10A(N)	08:52:49	1.0	Surface	1	2	26.24	8.10	29.54	123.50	8.1	3.5	3.2
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	SR10A(N)	08:51:59	5.6	Middle	2	1	26.21	8.10	30.05	123.00	8.1	3.5	3.1
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	SR10A(N)	08:52:33	5.6	Middle	2	2	26.21	8.10	29.99	123.30	8.1	3.4	2.7
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	SR10A(N)	08:51:42	10.2	Bottom	3	1	26.17	8.10	29.97	122.70	8.1	3.5	2.7
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	SR10A(N)	08:52:17	10.2	Bottom	3	2	26.17	8.10	29.96	123.70	8.1	3.4	3.5
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	SR10B(N2)	08:41:40	1.0	Surface	1	1	26.17	8.12	30.14	123.20	8.1	3.3	3.0
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	SR10B(N2)	08:42:20	1.0	Surface	1	2	26.12	8.12	30.14	123.20	8.1	3.4	2.5
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	SR10B(N2)	08:41:28	3.9	Middle	2	1	25.94	8.11	30.07	122.40	8.1	3.3	2.6
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	SR10B(N2)	08:42:06	3.9	Middle	2	2	25.92	8.11	30.05	122.80	8.1	3.3	2.4
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	SR10B(N2)	08:40:45	6.8	Bottom	3	1	25.96	8.11	29.62	122.30	8.1	3.4	3.1
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	SR10B(N2)	08:41:52	6.8	Bottom	3	2	25.95	8.11	29.60	122.70	8.1	3.3	2.7
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	CS2(A)	10:46:45	1.0	Surface	1	1	26.24	8.11	29.72	123.20	8.1	3.5	3.3
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	CS2(A)	10:47:22	1.0	Surface	1	2	26.25	8.11	29.67	123.20	8.1	3.4	3.2
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	CS2(A)	10:46:34	3.1	Middle	2	1	26.24	8.10	30.16	122.80	8.1	3.4	2.7
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	CS2(A)	10:47:11	3.1	Middle	2	2	26.25	8.10	30.16	122.90	8.1	3.4	2.7
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	CS2(A)	10:46:15	5.2	Bottom	3	1	26.18	8.10	30.07	122.80	8.1	3.4	3.3
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	CS2(A)	10:47:01	5.2	Bottom	3	2	26.18	8.10	30.05	122.60	8.1	3.5	3.4

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	CS(Mf)5	08:56:22	1.0	Surface	1	1	26.53	8.08	29.70	123.40	8.2	3.3	2.8
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	CS(Mf)5	08:57:19	1.0	Surface	1	2	26.36	8.08	29.75	123.80	8.2	3.4	2.8
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	CS(Mf)5	08:56:03	5.9	Middle	2	1	26.25	8.06	30.40	122.40	8.2	3.4	3.2
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	CS(Mf)5	08:56:51	5.9	Middle	2	2	26.49	8.07	30.36	123.70	8.2	3.4	4.0
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	CS(Mf)5	08:55:25	10.8	Bottom	3	1	26.22	8.06	30.42	121.90	8.1	3.4	3.5
HKLR	HY/2011/03	2025-04-23	Mid-Ebb	Fine	CS(Mf)5	08:56:42	10.8	Bottom	3	2	26.26	8.07	30.37	123.60	8.2	3.4	3.9
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	IS5	13:35:59	1.0	Surface	1	1	26.41	8.05	29.90	122.10	8.1	3.4	3.2
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	IS5	13:36:45	1.0	Surface	1	2	26.42	8.05	30.03	123.70	8.2	3.5	3.0
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	IS5	13:35:47	4.1	Middle	2	1	26.39	8.07	30.50	121.90	8.1	3.4	2.8
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	IS5	13:36:24	4.1	Middle	2	2	26.35	8.04	30.51	123.20	8.1	3.4	2.5
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	IS5	13:35:31	7.2	Bottom	3	1	26.44	8.06	30.44	121.10	8.0	3.4	2.6
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	IS5	13:36:11	7.2	Bottom	3	2	26.12	8.05	30.49	121.90	8.1	3.5	2.8
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	IS(Mf)6	13:46:23	1.0	Surface	1	1	26.40	8.05	30.02	122.10	8.1	3.3	3.0
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	IS(Mf)6	13:46:52	1.0	Surface	1	2	26.47	8.05	29.98	121.90	8.1	3.3	3.6
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	IS(Mf)6	13:46:03	2.0	Bottom	3	1	26.26	8.04	30.26	121.90	8.1	3.3	3.4
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	IS(Mf)6	13:46:35	2.0	Bottom	3	2	26.30	8.04	30.25	121.80	8.1	3.3	3.8
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	IS7	13:56:23	1.0	Surface	1	1	26.43	8.02	30.05	121.30	8.0	3.5	3.6
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	IS7	13:56:39	1.0	Surface	1	2	26.42	8.02	30.06	121.10	8.0	3.4	2.6
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	IS7	13:56:04	2.0	Bottom	3	1	26.37	8.02	30.26	121.10	8.0	3.5	3.3
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	IS7	13:56:30	2.0	Bottom	3	2	26.37	8.02	30.32	121.00	8.0	3.5	2.9
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	IS8(N)	14:27:37	1.0	Surface	1	1	26.36	8.10	29.94	122.00	8.1	3.5	3.0
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	IS8(N)	14:28:08	1.0	Surface	1	2	26.36	8.10	29.94	121.80	8.1	3.5	2.7
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	IS8(N)	14:27:26	3.0	Bottom	3	1	26.25	8.09	30.09	121.90	8.1	3.5	3.0
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	IS8(N)	14:27:49	3.0	Bottom	3	2	26.26	8.10	30.13	122.00	8.1	3.5	3.7
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	IS(Mf)9	14:06:46	1.0	Surface	1	1	26.46	8.06	29.90	120.70	8.0	3.5	3.2
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	IS(Mf)9	14:07:22	1.0	Surface	1	2	26.44	8.07	29.89	121.00	8.0	3.5	4.1
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	IS(Mf)9	14:06:36	2.7	Bottom	3	1	26.38	8.05	30.13	120.60	8.0	3.5	2.9
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	IS(Mf)9	14:07:01	2.7	Bottom	3	2	26.42	8.06	30.10	120.30	8.0	3.5	3.6
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	IS10(N)	14:25:19	1.0	Surface	1	1	26.27	8.11	30.16	122.70	8.1	3.4	3.0
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	IS10(N)	14:26:03	1.0	Surface	1	2	26.28	8.11	30.16	122.30	8.0	3.5	3.0
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	IS10(N)	14:25:10	4.2	Middle	2	1	26.01	8.10	30.11	122.60	8.1	3.4	3.4
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	IS10(N)	14:25:48	4.2	Middle	2	2	26.02	8.10	30.10	122.20	8.0	3.4	3.7
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	IS10(N)	14:24:53	7.4	Bottom	3	1	26.09	8.11	29.59	121.90	8.0	3.4	2.8
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	IS10(N)	14:25:36	7.4	Bottom	3	2	26.10	8.11	29.47	121.80	8.0	3.4	3.2
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	SR3(N)	13:26:00	1.0	Surface	1	1	26.17	8.06	29.85	121.60	8.1	3.5	3.7
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	SR3(N)	13:26:25	1.0	Surface	1	2	26.17	8.06	29.81	121.90	8.1	3.5	4.1
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	SR3(N)	13:25:47	2.0	Bottom	3	1	26.16	8.06	30.13	121.50	8.1	3.6	3.5
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	SR3(N)	13:26:11	2.0	Bottom	3	2	26.36	8.07	29.96	121.20	8.1	3.5	3.2
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	SR4(N3)	14:16:50	1.0	Surface	1	1	26.45	8.07	29.90	121.70	8.1	3.4	3.4
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	SR4(N3)	14:17:22	1.0	Surface	1	2	26.44	8.07	29.95	121.90	8.1	3.4	3.9
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	SR4(N3)	14:16:35	2.7	Bottom	3	1	26.43	8.07	30.43	121.90	8.1	3.4	3.0
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	SR4(N3)	14:17:07	2.7	Bottom	3	2	26.39	8.07	30.11	121.80	8.1	3.4	3.2
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	SR5(N)	14:14:38	1	Surface	1	1	26.11	8.12	29.57	122.80	8.1	3.4	2.6
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	SR5(N)	14:15:07	1	Surface	1	2	26.14	8.12	29.61	122.50	8.1	3.4	3.6
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	SR5(N)	14:14:27	4.3	Middle	2	1	25.88	8.11	30.06	122.70	8.1	3.5	3.2
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	SR5(N)	14:14:57	4.3	Middle	2	2	25.88	8.12	30.08	122.20	8.0	3.5	4.0
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	SR5(N)	14:14:10	7.6	Bottom	3	1	25.90	8.11	30.06	123.50	8.1	3.5	3.3
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	SR5(N)	14:14:49	7.6	Bottom	3	2	25.92	8.12	30.12	122.00	8.0	3.4	3.2
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	SR10A(N)	15:14:46	1	Surface	1	1	26.24	8.13	30.11	123.50	8.1	3.5	2.9
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	SR10A(N)	15:15:18	1	Surface	1	2	26.24	8.13	30.12	123.30	8.1	3.5	3.3
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	SR10A(N)	15:14:34	5.5	Middle	2	1	26.24	8.12	30.15	123.50	8.1	3.5	3.4
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	SR10A(N)	15:15:07	5.5	Middle	2	2	26.24	8.12	30.14	123.10	8.1	3.5	3.1
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	SR10A(N)	15:14:18	10.0	Bottom	3	1	26.23	8.13	29.67	122.90	8.1	3.4	3.1
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	SR10A(N)	15:14:58	10.0	Bottom	3	2	26.23	8.13	29.70	122.70	8.1	3.5	3.8
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	SR10B(N2)	15:22:54	1.0	Surface	1	1	26.24	8.12	30.00	122.80	8.1	3.4	3.1
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	SR10B(N2)	15:23:51	1.0	Surface	1	2	26.21	8.12	29.98	122.30	8.1	3.4	3.2
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	SR10B(N2)	15:22:46	3.9	Middle	2	1	25.95	8.11	29.62	122.50	8.1	3.4	2.8
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	SR10B(N2)	15:23:16	3.9	Middle	2	2	25.93	8.11	29.61	122.00	8.0	3.4	3.1
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	SR10B(N2)	15:22:36	6.8	Bottom	3	1	26.01	8.11	30.10	121.80	8.0	3.4	3.6
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	SR10B(N2)	15:23:07	6.8	Bottom	3	2	25.94	8.11	29.98	121.70	8.0	3.4	3.3
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	CS2(A)	13:28:11	1	Surface	1	1	26.13	8.10	30.01	123.60	8.2	3.4	3.7
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	CS2(A)	13:28:39	1	Surface	1	2	26.14	8.10	30.04	123.10	8.1	3.3	2.8
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	CS2(A)	13:28:02	3.1	Middle	2	1	25.87	8.10	29.62	123.20	8.1	3.3	2.8
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	CS2(A)	13:28:28	3.1	Middle	2	2	25.88	8.10	29.58	121.90	8.1	3.4	2.9
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	CS2(A)	13:27:44	5.2	Bottom	3	1	25.92	8.10	30.10	122.80	8.1	3.3	3.3
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	CS2(A)	13:28:20	5.2	Bottom	3	2	25.94	8.09	30.09	121.90	8.1	3.3	3.3
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	CS(Mf)5	15:13:15	1.0	Surface	1	1	26.47	8.06	29.95	120.70	8.0	3.5	3.3
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	CS(Mf)5	15:14:07	1.0	Surface	1	2	26.40	8.07	30.02	121.30	8.1	3.4	2.9
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	CS(Mf)5	15:13:04	5.9	Middle	2	1	26.22	8.06	30.46	120.00	8.0	3.5	3.3
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	CS(Mf)5	15:13:45	5.9	Middle	2	2	26.21	8.06	29.91	121.00	8.0	3.5	4.0
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	CS(Mf)5	15:12:43	10.8	Bottom	3	1	26.19	8.06	30.45	119.90	8.0	3.5	4.7
HKLR	HY/2011/03	2025-04-23	Mid-Flood	Fine	CS(Mf)5	15:13:27	10.8	Bottom	3	2	26.18	8.06	30.41	121.00	8.0	3.4	4.0
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	IS5	10:07:11	1.0	Surface	1	1	26.28	8.02	29.65	116.00	7.7	3.2	2.0
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	IS5	10:07:58	1.0	Surface	1	2	26.27	8.02	29.52	114.40	7.6	3.2	3.0
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	IS5	10:07:00	4.1	Middle	2	1	26.21	8.01	30.13	115.50	7.7	3.4	2.0
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	IS5	10:07:37	4.1	Middle	2	2	26.25	8.04	30.12	114.20	7.6	3.2	2.8
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	IS5	10:06:44	7.2	Bottom	3	1	25.98	8.02	30.11	114.20	7.6	3.3	3.4
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	IS5	10:07:24	7.2	Bottom	3	2	26.30	8.03	30.06	113.40	7.5	3.2	3.2
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	IS(Mf)6	10:17:36	1.0	Surface	1	1	26.31	7.99	29.67	113.60	7.6	3.4	1.6
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	IS(Mf)6	10:18:05	1.0	Surface	1	2	26.30	7.99	29.68	113.40	7.6	3.3	2.9
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	IS(Mf)6	10:17:15	2.0	Bottom	3	1	26.25	7.99	29.88	113.40	7.6	3.4	2.3
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	IS(Mf)6	10:17:48	2.0	Bottom	3	2	26.25	7.99	29.94	113.30	7.6	3.4	3.0
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	IS7	10:28:12	1.0	Surface	1	1	26.34	8.04	29.52	113.00	7.5	3.4	2.2
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	IS7	10:28:30	1.0	Surface	1	2	26.32	8.05	29.51	113.30	7.6	3.4	1.7
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	IS7	10:27:55	2.0	Bottom	3	1	26.26	8.03	29.75	112.90	7.5	3.4	2.1
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	IS7	10:28:21	2.0	Bottom	3	2	26.30	8.04	29.72	112.60	7.5	3.4	2.5
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	IS8(N)	10:59:28	1.0	Surface	1	1	26.26	8.02	29.64	114.40	7.7	3.2	2.6
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	IS8(N)	10:59:59	1.0	Surface	1	2	26.33	8.02	29.60	114.20	7.7	3.2	2.0
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	IS8(N)	10:59:17	2.8	Bottom	3	1	26.12	8.01	29.88	114.20	7.7	3.2	2.3
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	IS8(N)	10:59:41	2.8	Bottom	3	2	26.16	8.01	29.87	114.10	7.6	3.2	2.2
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	IS(Mf)9	10:38:36	1.0	Surface	1	1	26.33	8.05	29.52	114.00	7.6	3.2	1.8
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	IS(Mf)9	10:39:13	1.0	Surface	1	2	26.32	8.05	29.57	114.20	7.7	3.2	1.7
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	IS(Mf)9	10:38:27	2.6	Bottom	3	1	26.31	8.05	30.05	114.20	7.7	3.2	1.7
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	IS(Mf)9	10:38:52	2.6	Bottom	3	2	26.27	8.05	29.73	114.10	7.7	3.2	1.5
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	IS10(N)	10:46:52	1.0	Surface	1	1	26.43	8.04	29.93	117.60	7.6	3.3	2.1
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	IS10(N)	10:47:36	1.0	Surface	1	2	26.43	8.04	29.94	117.40	7.5	3.2	2.8
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	IS10(N)	10:46:43	4.2	Middle	2	1	26.43	8.03	29.97	117.60	7.6	3.2	2.1
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	IS10(N)	10:47:21	4.2	Middle	2	2	26.43	8.03	29.96	117.20	7.5	3.2	2.6
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	IS10(N)	10:46:26	7.4	Bottom	3	1	26.42	8.03	29.49	117.00	7.5	3.2	2.5
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	IS10(N)	10:47:07	7.4	Bottom	3	2	26.42	8.03	29.52	116.80	7.5	3.3	2.4
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	SR3(N)	09:56:13	1.0	Surface	1	1	26.23	8.04	29.50	112.00	7.5	3.3	2.4
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	SR3(N)	09:56:39	1.0	Surface	1	2	26.22	8.04	29.50	112.00	7.5	3.4	2.6
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	SR3(N)	09:56:02	2.0	Bottom	3	1	26.15	8.03	29.67	111.60	7.5	3.3	3.2
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	SR3(N)	09:56:24	2.0	Bottom	3	2	26.19	8.04	29.76	112.60	7.5	3.3	1.9

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	SR4(N3)	10:48:42	1.0	Surface	1	1	26.24	8.03	29.56	114.30	7.6	3.3	3.7
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	SR4(N3)	10:49:13	1.0	Surface	1	2	26.24	8.03	29.56	114.10	7.6	3.3	2.6
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	SR4(N3)	10:48:26	2.6	Bottom	3	1	26.13	8.03	29.71	114.20	7.6	3.3	2.9
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	SR4(N3)	10:48:58	2.6	Bottom	3	2	26.14	8.03	29.75	114.30	7.6	3.3	2.8
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	SR5(N)	10:39:11	1.0	Surface	1	1	26.43	8.04	29.54	116.80	7.5	3.1	1.7
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	SR5(N)	10:39:40	1.0	Surface	1	2	26.44	8.04	29.49	116.40	7.5	3.2	2.4
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	SR5(N)	10:39:00	4.4	Middle	2	1	26.43	8.03	29.98	116.70	7.5	3.1	2.3
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	SR5(N)	10:39:32	4.4	Middle	2	2	26.44	8.03	29.98	116.30	7.5	3.1	2.0
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	SR5(N)	10:38:44	7.8	Bottom	3	1	26.37	8.04	29.89	116.00	7.5	3.1	2.0
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	SR5(N)	10:39:22	7.8	Bottom	3	2	26.37	8.04	29.87	115.90	7.5	3.1	2.1
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	SR10A(N)	11:36:19	1.0	Surface	1	1	26.43	8.05	29.82	116.90	7.5	3.1	2.4
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	SR10A(N)	11:36:51	1.0	Surface	1	2	26.40	8.05	29.80	116.40	7.5	3.1	2.0
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	SR10A(N)	11:36:06	5.6	Middle	2	1	26.14	8.04	29.44	116.60	7.5	3.1	2.0
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	SR10A(N)	11:36:40	5.6	Middle	2	2	26.12	8.04	29.43	116.10	7.5	3.1	2.6
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	SR10A(N)	11:35:42	10.2	Bottom	3	1	26.20	8.04	29.92	115.90	7.5	3.1	2.0
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	SR10A(N)	11:36:31	10.2	Bottom	3	2	26.13	8.04	29.80	115.80	7.5	3.1	2.2
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	SR10B(N2)	11:46:27	1.0	Surface	1	1	26.46	8.06	29.98	117.70	7.6	3.2	2.0
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	SR10B(N2)	11:47:24	1.0	Surface	1	2	26.47	8.06	29.98	117.20	7.6	3.2	2.2
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	SR10B(N2)	11:46:19	3.7	Middle	2	1	26.20	8.05	29.93	117.30	7.6	3.2	2.0
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	SR10B(N2)	11:46:48	3.7	Middle	2	2	26.21	8.05	29.92	116.00	7.5	3.2	2.5
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	SR10B(N2)	11:46:06	6.4	Bottom	3	1	26.28	8.06	29.41	116.90	7.5	3.1	2.0
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	SR10B(N2)	11:46:40	6.4	Bottom	3	2	26.29	8.06	29.29	116.00	7.5	3.2	2.1
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	CS2(A)	09:49:45	1.0	Surface	1	1	26.30	8.05	29.39	116.90	7.5	3.2	2.0
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	CS2(A)	09:50:12	1.0	Surface	1	2	26.33	8.05	29.43	116.60	7.5	3.2	2.4
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	CS2(A)	09:49:35	3.2	Middle	2	1	26.07	8.04	29.88	116.80	7.5	3.3	3.1
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	CS2(A)	09:50:01	3.2	Middle	2	2	26.07	8.05	29.90	116.30	7.5	3.3	2.8
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	CS2(A)	09:49:17	5.4	Bottom	3	1	26.09	8.04	29.88	117.60	7.6	3.3	2.5
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	CS2(A)	09:49:53	5.4	Bottom	3	2	26.11	8.05	29.94	116.10	7.5	3.2	2.3
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	CS(Mf)5	11:43:13	1.0	Surface	1	1	26.28	8.05	29.64	113.60	7.6	3.2	2.4
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	CS(Mf)5	11:44:18	1.0	Surface	1	2	26.35	8.04	29.57	113.00	7.6	3.3	2.6
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	CS(Mf)5	11:43:05	5.9	Middle	2	1	26.09	8.04	29.53	113.30	7.6	3.3	2.2
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	CS(Mf)5	11:43:46	5.9	Middle	2	2	26.10	8.04	30.08	112.30	7.5	3.3	2.0
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	CS(Mf)5	11:42:44	10.8	Bottom	3	1	26.06	8.04	30.03	113.30	7.6	3.2	2.7
HKLR	HY/2011/03	2025-04-25	Mid-Ebb	Fine	CS(Mf)5	11:43:28	10.8	Bottom	3	2	26.07	8.04	30.07	112.20	7.5	3.3	2.2
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	IS5	06:03:55	1.0	Surface	1	1	26.35	8.05	29.37	111.50	7.4	3.2	2.8
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	IS5	06:04:37	1.0	Surface	1	2	26.22	8.04	29.51	111.70	7.4	3.2	2.7
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	IS5	06:03:34	4.3	Middle	2	1	26.34	8.04	29.96	111.40	7.4	3.3	3.1
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	IS5	06:04:18	4.3	Middle	2	2	26.36	8.04	29.97	111.10	7.4	3.3	3.1
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	IS5	06:03:14	7.6	Bottom	3	1	26.26	8.04	30.01	111.10	7.4	3.3	2.0
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	IS5	06:04:03	7.6	Bottom	3	2	26.08	8.04	30.01	110.70	7.4	3.3	1.5
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	IS(Mf)6	05:51:51	1.0	Surface	1	1	26.47	8.05	29.69	113.00	7.6	3.2	1.9
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	IS(Mf)6	05:52:24	1.0	Surface	1	2	26.47	8.05	29.64	113.00	7.6	3.3	2.4
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	IS(Mf)6	05:51:43	2.0	Bottom	3	1	26.36	8.06	29.72	112.20	7.5	3.3	1.6
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	IS(Mf)6	05:51:59	2.0	Bottom	3	2	26.36	8.06	29.37	113.20	7.6	3.2	2.1
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	IS7	05:42:38	1.0	Surface	1	1	26.33	8.06	29.45	113.60	7.6	3.3	2.1
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	IS7	05:42:59	1.0	Surface	1	2	26.38	8.06	29.42	113.60	7.6	3.3	2.2
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	IS7	05:42:09	2.0	Bottom	3	1	26.11	8.05	29.73	113.20	7.6	3.3	1.4
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	IS7	05:42:47	2.0	Bottom	3	2	26.31	8.05	29.68	113.50	7.6	3.3	1.8
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	IS8(N)	05:10:03	1.0	Surface	1	1	26.46	8.03	29.51	114.20	7.7	3.2	2.0
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	IS8(N)	05:10:33	1.0	Surface	1	2	26.45	8.03	29.43	114.00	7.6	3.1	1.8
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	IS8(N)	05:09:51	3.2	Bottom	3	1	26.39	8.02	29.76	114.10	7.6	3.2	1.7
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	IS8(N)	05:10:14	3.2	Bottom	3	2	26.39	8.02	29.72	113.80	7.6	3.2	2.4
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	IS(Mf)9	05:31:06	1.0	Surface	1	1	26.39	8.04	29.35	113.10	7.6	3.2	2.0
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	IS(Mf)9	05:31:29	1.0	Surface	1	2	26.28	8.03	29.36	113.00	7.6	3.2	1.9
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	IS(Mf)9	05:30:47	2.6	Bottom	3	1	26.21	8.04	29.55	113.00	7.6	3.2	1.9
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	IS(Mf)9	05:31:17	2.6	Bottom	3	2	26.22	8.04	29.61	112.80	7.5	3.2	2.3
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	IS10(N)	05:33:27	1.0	Surface	1	1	26.37	8.03	29.84	118.40	7.6	3.2	1.8
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	IS10(N)	05:34:02	1.0	Surface	1	2	26.37	8.04	29.92	117.20	7.5	3.2	2.4
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	IS10(N)	05:33:14	4.3	Middle	2	1	26.12	8.03	29.39	117.30	7.5	3.2	1.7
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	IS10(N)	05:33:54	4.3	Middle	2	2	26.08	8.03	29.40	117.10	7.5	3.2	3.2
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	IS10(N)	05:33:05	7.6	Bottom	3	1	26.16	8.03	29.78	116.90	7.5	3.2	2.1
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	IS10(N)	05:33:40	7.6	Bottom	3	2	26.15	8.03	29.92	116.70	7.5	3.3	2.1
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	SR3(N)	06:15:31	1.0	Surface	1	1	26.03	8.03	29.47	113.90	7.6	3.4	4.3
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	SR3(N)	06:16:10	1.0	Surface	1	2	26.03	8.03	29.43	114.20	7.6	3.4	2.6
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	SR3(N)	06:15:07	2.0	Bottom	3	1	26.02	8.03	29.75	113.80	7.6	3.5	2.6
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	SR3(N)	06:15:49	2.0	Bottom	3	2	26.22	8.04	29.58	113.50	7.6	3.4	2.6
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	SR4(N3)	05:20:01	1.0	Surface	1	1	26.47	8.04	29.40	113.20	7.6	3.1	2.3
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	SR4(N3)	05:20:33	1.0	Surface	1	2	26.49	8.04	29.38	113.00	7.6	3.1	2.7
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	SR4(N3)	05:19:52	3.0	Bottom	3	1	26.38	8.04	29.36	113.20	7.6	3.1	2.4
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	SR4(N3)	05:20:15	3.0	Bottom	3	2	26.41	8.04	29.73	112.90	7.5	3.2	2.6
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	SR5(N)	05:41:34	1	Surface	1	1	26.40	8.05	29.96	117.30	7.6	3.0	2.6
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	SR5(N)	05:42:05	1	Surface	1	2	26.43	8.05	29.96	117.30	7.6	3.1	3.1
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	SR5(N)	05:41:20	4.4	Middle	2	1	26.40	8.04	29.89	116.90	7.6	3.0	2.3
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	SR5(N)	05:41:56	4.4	Middle	2	2	26.40	8.04	29.87	117.00	7.6	3.0	2.9
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	SR5(N)	05:41:11	7.8	Bottom	3	1	26.36	8.04	29.44	116.90	7.6	3.1	2.8
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	SR5(N)	05:41:44	7.8	Bottom	3	2	26.36	8.04	29.42	116.70	7.5	3.0	2.4
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	SR10A(N)	04:42:40	1	Surface	1	1	26.66	8.05	29.97	117.60	7.6	3.1	3.6
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	SR10A(N)	04:43:22	1	Surface	1	2	26.42	8.05	29.98	117.50	7.6	3.1	2.1
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	SR10A(N)	04:42:32	5.7	Middle	2	1	26.41	8.04	29.92	117.40	7.5	3.1	3.3
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	SR10A(N)	04:43:06	5.7	Middle	2	2	26.45	8.04	29.95	117.10	7.5	3.1	2.4
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	SR10A(N)	04:42:16	10.4	Bottom	3	1	26.41	8.05	29.55	117.80	7.6	3.1	2.5
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	SR10A(N)	04:42:52	10.4	Bottom	3	2	26.42	8.05	29.50	116.80	7.5	3.2	2.6
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	SR10B(N2)	04:32:13	1.0	Surface	1	1	26.31	8.04	29.37	117.30	7.6	3.1	2.8
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	SR10B(N2)	04:32:53	1.0	Surface	1	2	26.36	8.03	29.36	117.30	7.6	3.2	2.6
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	SR10B(N2)	04:32:01	3.8	Middle	2	1	26.11	8.03	29.87	116.90	7.6	3.2	2.2
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	SR10B(N2)	04:32:39	3.8	Middle	2	2	26.13	8.03	29.81	116.50	7.5	3.1	3.4
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	SR10B(N2)	04:31:15	6.6	Bottom	3	1	26.14	8.03	29.79	116.80	7.5	3.2	3.0
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	SR10B(N2)	04:32:26	6.6	Bottom	3	2	26.15	8.03	29.78	116.40	7.5	3.1	2.3
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	CS2(A)	06:35:18	1	Surface	1	1	26.32	8.03	29.83	117.60	7.6	3.2	3.2
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	CS2(A)	06:35:55	1	Surface	1	2	26.33	8.03	29.86	117.50	7.6	3.1	5.2
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	CS2(A)	06:35:07	3.2	Middle	2	1	26.06	8.03	29.44	116.80	7.5	3.1	3.3
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	CS2(A)	06:35:43	3.2	Middle	2	2	26.07	8.03	29.40	117.20	7.6	3.2	3.0
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	CS2(A)	06:34:46	5.4	Bottom	3	1	26.11	8.03	29.92	116.20	7.5	3.1	2.0
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	CS2(A)	06:35:34	5.4	Bottom	3	2	26.13	8.02	29.91	116.80	7.5	3.1	2.2
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	CS(Mf)5	04:21:32	1.0	Surface	1	1	26.28	8.05	29.37	116.10	7.7	3.2	3.2
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	CS(Mf)5	04:22:31	1.0	Surface	1	2	26.45	8.05	29.32	115.70	7.7	3.1	3.2
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	CS(Mf)5	04:21:15	6.0	Middle	2	1	26.41	8.04	29.98	116.00	7.7	3.2	2.4
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	CS(Mf)5	04:22:03	6.0	Middle	2	2	26.17	8.03	30.02	114.70	7.7	3.2	4.0
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	CS(Mf)5	04:20:44	11.0	Bottom	3	1	26.18	8.04	29.99	115.90	7.7	3.2	1.5
HKLR	HY/2011/03	2025-04-25	Mid-Flood	Fine	CS(Mf)5	04:21:54	11.0	Bottom	3	2	26.14	8.03	30.04	114.20	7.7	3.2	2.2
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	IS5	11:56:39	1.0	Surface	1	1	26.74	7.89	28.64	76.40	5.6	3.9	3.0
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	IS5	11:57:26	1.0	Surface	1	2	26.75	7.89	28.77	78.00	5.8	3.9	2.7
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	IS5	11:56:28	4.1	Middle	2	1	26.72	7.91	29.24	76.20	5.6	3.9	4.4
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	IS5	11:57:05	4.1	Middle	2	2	26.68	7.88	29.25	77.50	5.7	4.0	2.6

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	IS5	11:56:12	7.2	Bottom	3	1	26.77	7.90	29.18	75.40	5.6	3.9	2.5
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	IS5	11:56:51	7.2	Bottom	3	2	26.45	7.89	29.23	76.20	5.6	4.0	2.9
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	IS(Mf)6	12:06:04	1.0	Surface	1	1	26.81	7.91	28.64	75.00	5.6	4.1	4.4
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	IS(Mf)6	12:06:33	1.0	Surface	1	2	26.79	7.92	28.63	75.30	5.6	4.1	3.5
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	IS(Mf)6	12:05:45	2.0	Bottom	3	1	26.73	7.90	28.87	74.90	5.6	4.1	3.3
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	IS(Mf)6	12:06:16	2.0	Bottom	3	2	26.77	7.91	28.84	74.60	5.5	4.1	3.1
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	IS7	12:16:40	1.0	Surface	1	1	26.80	7.92	28.64	76.00	5.7	3.9	3.3
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	IS7	12:16:58	1.0	Surface	1	2	26.79	7.92	28.69	76.20	5.7	3.9	2.3
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	IS7	12:16:26	2.0	Bottom	3	1	26.78	7.92	29.17	76.20	5.7	3.9	2.6
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	IS7	12:16:49	2.0	Bottom	3	2	26.74	7.92	28.85	76.10	5.7	3.9	3.1
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	IS8(N)	12:47:56	1.0	Surface	1	1	26.78	7.86	28.79	75.60	5.6	4.1	2.4
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	IS8(N)	12:48:27	1.0	Surface	1	2	26.77	7.86	28.80	75.40	5.6	4.0	2.6
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	IS8(N)	12:47:45	2.8	Bottom	3	1	26.72	7.86	29.00	75.40	5.6	4.1	3.0
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	IS8(N)	12:48:06	2.8	Bottom	3	2	26.72	7.86	29.06	75.30	5.6	4.1	2.8
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	IS(Mf)9	12:28:04	1.0	Surface	1	1	26.71	7.90	28.68	76.30	5.7	4.0	2.8
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	IS(Mf)9	12:28:41	1.0	Surface	1	2	26.71	7.90	28.68	76.10	5.7	4.0	2.8
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	IS(Mf)9	12:27:52	2.6	Bottom	3	1	26.60	7.90	28.83	76.20	5.7	4.0	2.9
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	IS(Mf)9	12:28:20	2.6	Bottom	3	2	26.61	7.90	28.87	76.30	5.7	4.0	3.6
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	IS10(N)	12:46:20	1.0	Surface	1	1	26.05	7.98	28.95	80.20	5.8	3.9	3.8
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	IS10(N)	12:47:04	1.0	Surface	1	2	26.02	7.98	28.98	79.70	5.8	3.9	3.7
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	IS10(N)	12:46:11	4.2	Middle	2	1	25.76	7.97	28.56	79.80	5.8	3.9	3.3
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	IS10(N)	12:46:49	4.2	Middle	2	2	25.74	7.97	28.52	78.50	5.7	3.9	3.6
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	IS10(N)	12:45:54	7.4	Bottom	3	1	25.82	7.97	29.04	79.40	5.8	3.9	3.5
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	IS10(N)	12:46:37	7.4	Bottom	3	2	25.75	7.97	29.03	78.50	5.7	3.9	3.3
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	SR3(N)	11:45:47	1.0	Surface	1	1	26.50	7.90	28.59	75.90	5.6	4.1	2.5
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	SR3(N)	11:46:09	1.0	Surface	1	2	26.50	7.90	28.55	76.20	5.7	4.1	4.1
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	SR3(N)	11:45:35	2.0	Bottom	3	1	26.49	7.90	28.87	75.80	5.6	4.2	2.2
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	SR3(N)	11:45:59	2.0	Bottom	3	2	26.69	7.91	28.70	75.50	5.6	4.1	2.1
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	SR4(N3)	12:38:10	1.0	Surface	1	1	26.73	7.89	28.76	76.40	5.7	3.9	2.6
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	SR4(N3)	12:38:44	1.0	Surface	1	2	26.80	7.89	28.72	76.20	5.7	3.9	3.0
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	SR4(N3)	12:37:57	2.7	Bottom	3	1	26.59	7.88	29.00	76.20	5.7	3.9	2.5
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	SR4(N3)	12:38:26	2.7	Bottom	3	2	26.63	7.88	28.99	76.10	5.7	3.9	2.1
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	SR5(N)	12:35:59	1.0	Surface	1	1	25.94	7.97	29.05	79.80	5.8	4.1	3.5
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	SR5(N)	12:36:29	1.0	Surface	1	2	25.95	7.97	29.06	79.80	5.8	4.0	3.7
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	SR5(N)	12:35:49	4.3	Middle	2	1	25.68	7.96	29.09	79.40	5.8	4.0	3.6
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	SR5(N)	12:36:20	4.3	Middle	2	2	25.69	7.96	29.08	79.50	5.8	4.0	4.1
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	SR5(N)	12:35:32	7.6	Bottom	3	1	25.73	7.96	28.61	79.40	5.8	4.0	3.7
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	SR5(N)	12:36:10	7.6	Bottom	3	2	25.75	7.96	28.64	79.20	5.8	4.1	3.6
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	SR10A(N)	13:43:17	1.0	Surface	1	1	26.08	7.99	29.10	80.10	5.8	4.0	3.8
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	SR10A(N)	13:43:48	1.0	Surface	1	2	26.09	7.99	29.10	79.90	5.8	4.0	4.6
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	SR10A(N)	13:43:02	5.6	Middle	2	1	25.82	7.98	29.05	80.10	5.8	4.0	3.3
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	SR10A(N)	13:43:38	5.6	Middle	2	2	25.83	7.98	29.04	79.70	5.8	4.0	3.6
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	SR10A(N)	13:42:40	10.2	Bottom	3	1	25.90	7.99	28.53	79.50	5.8	3.9	3.9
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	SR10A(N)	13:43:29	10.2	Bottom	3	2	25.91	7.99	28.41	79.30	5.7	4.0	2.9
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	SR10B(N2)	13:52:25	1.0	Surface	1	1	26.05	7.98	28.94	79.40	5.7	3.9	4.3
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	SR10B(N2)	13:53:28	1.0	Surface	1	2	26.05	7.98	28.92	78.90	5.7	4.0	3.6
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	SR10B(N2)	13:52:17	3.7	Middle	2	1	26.05	7.97	28.56	79.10	5.7	3.9	3.0
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	SR10B(N2)	13:52:46	3.7	Middle	2	2	26.05	7.98	28.55	78.60	5.7	3.9	3.8
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	SR10B(N2)	13:52:04	6.4	Bottom	3	1	26.04	7.97	29.04	78.40	5.7	3.9	3.4
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	SR10B(N2)	13:52:39	6.4	Bottom	3	2	26.04	7.98	28.92	78.30	5.7	3.9	3.9
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	CS2(A)	11:41:33	1.0	Surface	1	1	26.05	7.97	28.66	79.30	5.7	3.9	3.0
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	CS2(A)	11:42:00	1.0	Surface	1	2	26.06	7.97	28.61	78.90	5.7	3.9	3.3
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	CS2(A)	11:41:23	3.1	Middle	2	1	26.05	7.96	29.10	79.20	5.7	3.9	4.3
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	CS2(A)	11:41:49	3.1	Middle	2	2	26.06	7.96	29.10	78.80	5.7	3.9	3.8
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	CS2(A)	11:41:02	5.2	Bottom	3	1	25.99	7.97	29.01	78.50	5.7	3.9	4.2
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	CS2(A)	11:41:40	5.2	Bottom	3	2	25.99	7.97	28.99	78.40	5.7	4.0	4.0
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	CS(Mf)5	13:41:14	1.0	Surface	1	1	26.82	7.91	28.69	75.00	5.6	4.0	2.2
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	CS(Mf)5	13:42:15	1.0	Surface	1	2	26.75	7.92	28.76	75.60	5.6	3.9	2.4
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	CS(Mf)5	13:41:02	5.9	Middle	2	1	26.57	7.91	29.20	74.30	5.5	4.0	2.2
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	CS(Mf)5	13:41:43	5.9	Middle	2	2	26.56	7.91	28.65	75.30	5.6	4.0	3.7
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	CS(Mf)5	13:40:41	10.8	Bottom	3	1	26.54	7.91	29.19	74.20	5.5	4.0	2.9
HKLR	HY/2011/03	2025-04-28	Mid-Ebb	Fine	CS(Mf)5	13:41:25	10.8	Bottom	3	2	26.53	7.91	29.15	75.30	5.6	3.9	4.0
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	IS5	06:53:22	1.0	Surface	1	1	26.69	7.91	28.63	73.70	5.5	3.9	2.8
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	IS5	06:54:05	1.0	Surface	1	2	26.82	7.92	28.49	73.50	5.5	3.9	2.7
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	IS5	06:53:02	4.2	Middle	2	1	26.83	7.91	29.09	73.10	5.4	4.0	3.7
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	IS5	06:53:46	4.2	Middle	2	2	26.81	7.91	29.08	73.40	5.5	4.0	3.8
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	IS5	06:52:42	7.4	Bottom	3	1	26.55	7.91	29.13	72.70	5.4	4.0	3.3
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	IS5	06:53:31	7.4	Bottom	3	2	26.73	7.91	29.13	73.10	5.4	4.0	3.3
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	IS(Mf)6	06:41:19	1.0	Surface	1	1	26.93	7.90	28.63	76.20	5.7	3.9	4.2
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	IS(Mf)6	06:41:52	1.0	Surface	1	2	26.92	7.90	28.55	76.00	5.7	3.8	3.5
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	IS(Mf)6	06:41:11	2.0	Bottom	3	1	26.86	7.89	28.88	76.10	5.7	3.9	2.9
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	IS(Mf)6	06:41:29	2.0	Bottom	3	2	26.86	7.89	28.84	75.80	5.6	3.9	2.6
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	IS7	06:32:06	1.0	Surface	1	1	26.94	7.92	28.81	75.00	5.6	3.9	2.4
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	IS7	06:32:27	1.0	Surface	1	2	26.94	7.92	28.76	75.00	5.6	4.0	3.0
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	IS7	06:31:37	2.0	Bottom	3	1	26.83	7.93	28.84	74.20	5.6	4.0	2.5
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	IS7	06:32:13	2.0	Bottom	3	2	26.83	7.93	28.49	75.20	5.6	3.9	3.8
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	IS8(N)	06:02:11	1.0	Surface	1	1	26.94	7.91	28.52	75.20	5.6	3.8	2.0
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	IS8(N)	06:02:41	1.0	Surface	1	2	26.96	7.91	28.50	75.00	5.6	3.8	2.8
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	IS8(N)	06:01:59	3.1	Bottom	3	1	26.85	7.91	28.48	75.20	5.6	3.8	1.7
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	IS8(N)	06:02:26	3.1	Bottom	3	2	26.88	7.91	28.85	74.90	5.6	3.9	2.6
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	IS(Mf)9	06:22:14	1.0	Surface	1	1	26.80	7.93	28.57	75.60	5.7	4.0	3.7
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	IS(Mf)9	06:22:37	1.0	Surface	1	2	26.85	7.93	28.54	75.60	5.7	4.0	2.7
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	IS(Mf)9	06:21:55	2.7	Bottom	3	1	26.58	7.92	28.85	75.20	5.6	4.0	2.8
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	IS(Mf)9	06:22:26	2.7	Bottom	3	2	26.78	7.92	28.80	75.50	5.6	4.0	2.8
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	IS10(N)	06:02:15	1.0	Surface	1	1	26.02	7.98	29.08	80.10	5.8	3.8	3.6
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	IS10(N)	06:02:50	1.0	Surface	1	2	26.05	7.98	29.08	80.00	5.8	3.9	4.0
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	IS10(N)	06:02:02	4.4	Middle	2	1	26.02	7.97	29.01	79.90	5.8	3.8	3.2
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	IS10(N)	06:02:42	4.4	Middle	2	2	26.02	7.97	28.99	79.60	5.8	3.8	3.0
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	IS10(N)	06:01:53	7.8	Bottom	3	1	25.98	7.97	28.56	80.30	5.8	3.9	3.7
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	IS10(N)	06:02:29	7.8	Bottom	3	2	25.98	7.97	28.54	79.30	5.7	3.8	3.7
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	SR3(N)	07:02:59	1.0	Surface	1	1	26.70	7.91	28.62	74.00	5.5	4.0	2.9
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	SR3(N)	07:03:38	1.0	Surface	1	2	26.69	7.91	28.62	74.00	5.5	4.1	3.3
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	SR3(N)	07:02:32	2.0	Bottom	3	1	26.62	7.90	28.79	73.60	5.5	4.0	2.5
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	SR3(N)	07:03:17	2.0	Bottom	3	2	26.66	7.91	28.88	74.60	5.5	4.0	4.0
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	SR4(N3)	06:12:09	1.0	Surface	1	1	26.86	7.91	28.47	75.10	5.6	3.9	2.2
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	SR4(N3)	06:12:41	1.0	Surface	1	2	26.75	7.90	28.48	75.00	5.6	3.9	2.7
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	SR4(N3)	06:12:00	3.0	Bottom	3	1	26.68	7.91	28.67	75.00	5.6	3.9	2.5
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	SR4(N3)	06:12:27	3.0	Bottom	3	2	26.69	7.91	28.73	74.80	5.6	3.9	2.5
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	SR5(N)	06:12:22	1	Surface	1	1	25.93	7.96	28.49	80.10	5.8	4.0	3.9
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	SR5(N)	06:12:54	1	Surface	1	2	25.98	7.96	28.48	80.00	5.8	3.9	3.4
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	SR5(N)	06:12:09	4.4	Middle	2	1	25.73	7.96	28.99	79.30	5.8	3.9	3.6
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	SR5(N)	06:12:44	4.4	Middle	2	2	25.75	7.96	28.93	79.70	5.8	4.0	3.5
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	SR5(N)	06:11:59	7.8	Bottom	3	1	25.76	7.96	28.91	78.70	5.7	3.9	3.8
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	SR5(N)	06:12:32	7.8	Bottom	3	2	25.77	7.95	28.90	79.30	5.8	3.9	4.2

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	SR10A(N)	05:15:58	1	Surface	1	1	25.99	7.96	28.96	80.90	5.8	4.0	4.3
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	SR10A(N)	05:16:42	1	Surface	1	2	25.99	7.97	29.04	79.70	5.8	4.0	5.0
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	SR10A(N)	05:15:48	5.9	Middle	2	1	25.74	7.96	28.51	79.80	5.8	4.0	4.9
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	SR10A(N)	05:16:24	5.9	Middle	2	2	25.70	7.96	28.52	79.60	5.8	4.0	4.5
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	SR10A(N)	05:15:34	10.8	Bottom	3	1	25.78	7.96	28.90	79.40	5.7	4.0	4.1
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	SR10A(N)	05:16:10	10.8	Bottom	3	2	25.77	7.96	29.04	79.20	5.7	4.1	5.3
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	SR10B(N2)	05:07:31	1.0	Surface	1	1	26.28	7.98	29.09	79.80	5.8	4.0	2.9
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	SR10B(N2)	05:08:11	1.0	Surface	1	2	26.04	7.98	29.10	79.80	5.8	3.9	3.6
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	SR10B(N2)	05:07:19	3.9	Middle	2	1	26.03	7.97	29.04	79.00	5.8	3.9	3.6
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	SR10B(N2)	05:07:55	3.9	Middle	2	2	26.07	7.97	29.07	79.40	5.8	4.0	3.4
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	SR10B(N2)	05:06:31	6.8	Bottom	3	1	26.03	7.98	28.67	78.90	5.7	3.9	5.8
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	SR10B(N2)	05:07:44	6.8	Bottom	3	2	26.04	7.98	28.62	79.30	5.8	4.0	4.2
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	CS2(A)	07:04:06	1	Surface	1	1	25.92	7.97	28.51	79.40	5.7	4.0	2.0
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	CS2(A)	07:04:43	1	Surface	1	2	25.95	7.96	28.55	79.10	5.7	4.0	1.6
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	CS2(A)	07:03:55	3.1	Middle	2	1	25.69	7.96	29.00	79.30	5.7	4.1	2.5
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	CS2(A)	07:04:31	3.1	Middle	2	2	25.69	7.96	29.02	78.80	5.7	4.1	3.5
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	CS2(A)	07:03:34	5.2	Bottom	3	1	25.71	7.96	29.00	80.10	5.8	4.1	3.6
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	CS2(A)	07:04:22	5.2	Bottom	3	2	25.73	7.96	29.06	78.60	5.7	4.0	5.2
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	CS(Mf)5	05:16:44	1.0	Surface	1	1	26.92	7.92	28.44	77.70	5.7	3.8	2.2
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	CS(Mf)5	05:17:39	1.0	Surface	1	2	26.75	7.92	28.49	78.10	5.8	3.9	2.5
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	CS(Mf)5	05:16:23	5.9	Middle	2	1	26.64	7.90	29.14	76.70	5.7	3.9	2.6
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	CS(Mf)5	05:17:15	5.9	Middle	2	2	26.88	7.91	29.10	78.00	5.7	3.9	2.5
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	CS(Mf)5	05:15:50	10.8	Bottom	3	1	26.61	7.90	29.16	76.20	5.7	3.9	1.9
HKLR	HY/2011/03	2025-04-28	Mid-Flood	Cloudy	CS(Mf)5	05:17:02	10.8	Bottom	3	2	26.65	7.91	29.11	77.90	5.7	3.9	2.1
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	IS5	13:18:38	1.0	Surface	1	1	26.38	7.92	28.52	79.60	5.9	5.6	10.2
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	IS5	13:19:25	1.0	Surface	1	2	26.37	7.92	28.39	78.00	5.8	5.6	8.4
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	IS5	13:18:27	4.1	Middle	2	1	26.31	7.91	29.00	79.10	5.9	5.7	9.4
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	IS5	13:19:04	4.1	Middle	2	2	26.35	7.94	28.99	77.80	5.8	5.6	8.1
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	IS5	13:18:11	7.2	Bottom	3	1	26.08	7.92	28.98	77.80	5.8	5.7	7.9
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	IS5	13:18:50	7.2	Bottom	3	2	26.40	7.93	28.93	77.00	5.7	5.6	11.5
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	IS(Mf)6	13:28:03	1.0	Surface	1	1	26.43	7.95	28.39	77.60	5.8	5.6	9.7
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	IS(Mf)6	13:28:32	1.0	Surface	1	2	26.42	7.95	28.44	77.80	5.8	5.6	8.0
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	IS(Mf)6	13:27:44	2.0	Bottom	3	1	26.41	7.95	28.92	77.80	5.8	5.6	9.3
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	IS(Mf)6	13:28:15	2.0	Bottom	3	2	26.37	7.95	28.60	77.70	5.8	5.6	7.9
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	IS7	13:39:17	1.0	Surface	1	1	26.34	7.94	28.43	77.90	5.8	5.7	10.2
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	IS7	13:39:35	1.0	Surface	1	2	26.34	7.94	28.43	77.70	5.8	5.7	8.6
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	IS7	13:39:03	2.0	Bottom	3	1	26.23	7.94	28.58	77.80	5.8	5.7	9.1
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	IS7	13:39:26	2.0	Bottom	3	2	26.24	7.94	28.62	77.90	5.8	5.7	10.0
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	IS8(N)	14:10:33	1.0	Surface	1	1	26.44	7.94	28.39	76.60	5.7	5.8	10.0
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	IS8(N)	14:11:04	1.0	Surface	1	2	26.42	7.95	28.38	76.90	5.7	5.8	9.8
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	IS8(N)	14:10:22	2.8	Bottom	3	1	26.36	7.93	28.62	76.50	5.7	5.8	9.0
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	IS8(N)	14:10:43	2.8	Bottom	3	2	26.40	7.94	28.59	76.20	5.7	5.8	10.9
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	IS(Mf)9	13:50:41	1.0	Surface	1	1	26.36	7.93	28.51	78.00	5.9	5.6	9.4
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	IS(Mf)9	13:51:18	1.0	Surface	1	2	26.43	7.93	28.47	77.80	5.8	5.6	9.2
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	IS(Mf)9	13:50:29	2.5	Bottom	3	1	26.22	7.92	28.75	77.80	5.8	5.6	8.6
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	IS(Mf)9	13:50:57	2.5	Bottom	3	2	26.26	7.92	28.74	77.70	5.8	5.6	7.7
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	IS10(N)	14:13:29	1.0	Surface	1	1	26.05	7.94	29.19	80.80	5.9	5.8	8.2
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	IS10(N)	14:14:13	1.0	Surface	1	2	26.02	7.94	29.19	80.60	5.9	5.8	7.4
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	IS10(N)	14:13:20	4.2	Middle	2	1	25.76	7.93	29.14	80.80	5.9	5.9	8.3
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	IS10(N)	14:13:57	4.2	Middle	2	2	25.74	7.93	29.13	80.40	5.9	5.9	7.6
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	IS10(N)	14:13:02	7.4	Bottom	3	1	25.82	7.94	28.62	80.20	5.9	5.9	8.4
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	IS10(N)	14:13:46	7.4	Bottom	3	2	25.75	7.94	28.50	80.00	5.9	5.8	7.9
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	SR3(N)	13:07:46	1.0	Surface	1	1	26.33	7.93	28.37	75.60	5.7	5.7	8.3
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	SR3(N)	13:08:08	1.0	Surface	1	2	26.32	7.93	28.37	75.60	5.7	5.8	8.2
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	SR3(N)	13:07:34	2.0	Bottom	3	1	26.25	7.92	28.54	75.20	5.7	5.7	10.3
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	SR3(N)	13:07:58	2.0	Bottom	3	2	26.29	7.93	28.63	76.20	5.7	5.7	8.5
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	SR4(N3)	14:00:47	1.0	Surface	1	1	26.41	7.90	28.54	77.20	5.8	5.8	9.9
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	SR4(N3)	14:01:21	1.0	Surface	1	2	26.40	7.90	28.55	77.00	5.8	5.7	9.4
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	SR4(N3)	14:00:34	2.6	Bottom	3	1	26.35	7.90	28.75	77.00	5.8	5.8	9.2
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	SR4(N3)	14:01:03	2.6	Bottom	3	2	26.35	7.90	28.81	76.90	5.7	5.8	8.6
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	SR5(N)	14:03:07	1.0	Surface	1	1	25.94	7.93	28.60	80.90	5.9	5.7	7.1
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	SR5(N)	14:03:38	1.0	Surface	1	2	25.95	7.93	28.64	80.40	5.9	5.7	6.8
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	SR5(N)	14:02:58	4.2	Middle	2	1	25.68	7.92	29.09	80.50	5.9	5.7	7.3
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	SR5(N)	14:03:29	4.2	Middle	2	2	25.69	7.92	29.11	79.20	5.8	5.7	7.4
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	SR5(N)	14:02:41	7.4	Bottom	3	1	25.73	7.92	29.09	80.10	5.9	5.7	9.1
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	SR5(N)	14:03:19	7.4	Bottom	3	2	25.75	7.92	29.15	79.20	5.8	5.7	10.4
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	SR10A(N)	15:09:25	1.0	Surface	1	1	26.08	7.93	29.03	80.10	5.9	5.7	8.5
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	SR10A(N)	15:09:57	1.0	Surface	1	2	26.09	7.93	29.01	79.60	5.8	5.8	7.5
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	SR10A(N)	15:09:11	5.6	Middle	2	1	25.82	7.92	28.65	79.80	5.8	5.7	8.9
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	SR10A(N)	15:09:47	5.6	Middle	2	2	25.83	7.93	28.64	79.30	5.8	5.7	8.3
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	SR10A(N)	15:08:49	10.2	Bottom	3	1	25.90	7.92	29.13	79.10	5.8	5.7	9.4
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	SR10A(N)	15:09:38	10.2	Bottom	3	2	25.91	7.93	29.01	79.00	5.8	5.7	10.4
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	SR10B(N2)	15:19:14	1.0	Surface	1	1	26.05	7.92	29.04	80.10	5.9	5.8	8.9
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	SR10B(N2)	15:20:27	1.0	Surface	1	2	26.05	7.91	29.07	79.80	5.8	5.8	8.9
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	SR10B(N2)	15:19:08	3.8	Middle	2	1	26.05	7.91	28.65	80.00	5.9	5.8	10.6
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	SR10B(N2)	15:19:35	3.8	Middle	2	2	26.05	7.91	28.61	79.50	5.8	5.8	9.2
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	SR10B(N2)	15:18:59	6.6	Bottom	3	1	26.04	7.91	29.13	80.80	5.9	5.7	9.9
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	SR10B(N2)	15:19:28	6.6	Bottom	3	2	26.04	7.91	29.12	79.30	5.8	5.8	8.1
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	CS2(A)	13:11:42	1.0	Surface	1	1	26.05	7.92	29.14	80.50	5.9	5.9	9.3
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	CS2(A)	13:12:09	1.0	Surface	1	2	26.06	7.92	29.15	80.50	5.9	5.8	8.3
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	CS2(A)	13:11:32	3.1	Middle	2	1	26.05	7.91	29.18	80.10	5.9	5.8	7.5
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	CS2(A)	13:11:59	3.1	Middle	2	2	26.06	7.91	29.17	80.20	5.9	5.8	7.9
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	CS2(A)	13:11:13	5.2	Bottom	3	1	25.99	7.91	28.70	80.10	5.9	5.8	7.8
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	CS2(A)	13:11:49	5.2	Bottom	3	2	25.99	7.91	28.73	79.90	5.9	5.9	8.1
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	CS(Mf)5	15:01:51	1.0	Surface	1	1	26.38	7.96	28.51	77.20	5.8	5.6	11.2
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	CS(Mf)5	15:02:52	1.0	Surface	1	2	26.45	7.95	28.44	76.60	5.7	5.7	9.7
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	CS(Mf)5	15:01:39	5.9	Middle	2	1	26.19	7.95	28.40	76.90	5.8	5.7	9.7
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	CS(Mf)5	15:02:20	5.9	Middle	2	2	26.20	7.95	28.95	75.90	5.7	5.7	10.4
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	CS(Mf)5	15:01:18	10.8	Bottom	3	1	26.16	7.95	28.90	76.90	5.8	5.6	9.9
HKLR	HY/2011/03	2025-04-30	Mid-Ebb	Sunny	CS(Mf)5	15:02:02	10.8	Bottom	3	2	26.17	7.95	28.94	75.80	5.7	5.7	8.9
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	IS5	08:43:51	1.0	Surface	1	1	26.45	7.94	28.24	79.30	5.9	5.6	9.9
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	IS5	08:44:34	1.0	Surface	1	2	26.32	7.93	28.38	79.70	5.9	5.6	11.3
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	IS5	08:43:31	4.3	Middle	2	1	26.44	7.93	28.83	78.30	5.9	5.7	8.8
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	IS5	08:44:15	4.3	Middle	2	2	26.46	7.93	28.84	79.60	5.9	5.7	10.2
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	IS5	08:43:11	7.6	Bottom	3	1	26.36	7.93	28.88	77.80	5.8	5.7	9.6
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	IS5	08:44:00	7.6	Bottom	3	2	26.18	7.93	28.88	79.50	5.9	5.7	9.6
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	IS(Mf)6	08:32:48	1.0	Surface	1	1	26.57	7.94	28.27	76.80	5.8	5.5	9.5
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	IS(Mf)6	08:33:21	1.0	Surface	1	2	26.59	7.94	28.25	76.60	5.7	5.5	10.2
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	IS(Mf)6	08:32:40	2.1	Bottom	3	1	26.48	7.94	28.23	76.80	5.8	5.5	9.5
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	IS(Mf)6	08:32:58	2.1	Bottom	3	2	26.51	7.94	28.60	76.50	5.7	5.6	9.1
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	IS7	08:23:35	1.0	Surface	1	1	26.56	7.92	28.38	77.80	5.8	5.6	8.7
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	IS7	08:23:56	1.0	Surface	1	2	26.55	7.92	28.30	77.60	5.8	5.5	10.3
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	IS7	08:23:06	2.0	Bottom	3	1	26.49	7.91	28.63	77.70	5.8	5.6	9.4
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	IS7	08:23:42	2.0	Bottom	3	2	26.49	7.91	28.59	77.40	5.8	5.6	8.0

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	IS8(N)	07:52:20	1.0	Surface	1	1	26.49	7.94	28.22	76.70	5.8	5.6	9.8
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	IS8(N)	07:52:50	1.0	Surface	1	2	26.38	7.93	28.23	76.60	5.7	5.6	10.0
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	IS8(N)	07:52:08	3.0	Bottom	3	1	26.31	7.94	28.42	76.60	5.7	5.6	9.6
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	IS8(N)	07:52:35	3.0	Bottom	3	2	26.32	7.94	28.48	76.40	5.7	5.6	8.0
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	IS(Mf)9	08:13:03	1.0	Surface	1	1	26.57	7.94	28.56	76.60	5.8	5.6	8.0
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	IS(Mf)9	08:13:26	1.0	Surface	1	2	26.57	7.94	28.51	76.60	5.8	5.7	9.7
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	IS(Mf)9	08:12:44	2.6	Bottom	3	1	26.46	7.95	28.59	75.80	5.7	5.7	7.4
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	IS(Mf)9	08:13:15	2.6	Bottom	3	2	26.46	7.95	28.24	76.80	5.8	5.6	7.9
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	IS10(N)	08:04:14	1.0	Surface	1	1	26.02	7.89	28.58	80.80	5.9	5.8	7.3
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	IS10(N)	08:04:52	1.0	Surface	1	2	26.05	7.89	28.57	80.70	5.9	5.7	8.8
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	IS10(N)	08:04:02	4.3	Middle	2	1	26.02	7.89	29.08	80.00	5.9	5.7	7.8
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	IS10(N)	08:04:41	4.3	Middle	2	2	26.02	7.89	29.02	80.40	5.9	5.8	7.5
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	IS10(N)	08:03:52	7.6	Bottom	3	1	25.98	7.89	29.00	79.40	5.8	5.7	7.6
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	IS10(N)	08:04:28	7.6	Bottom	3	2	25.98	7.88	28.99	80.00	5.9	5.7	8.5
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	SR3(N)	08:54:28	1.0	Surface	1	1	26.13	7.93	28.34	77.50	5.8	5.8	9.3
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	SR3(N)	08:55:07	1.0	Surface	1	2	26.13	7.93	28.30	77.80	5.8	5.8	9.0
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	SR3(N)	08:54:01	2.0	Bottom	3	1	26.12	7.93	28.62	77.40	5.8	5.9	8.8
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	SR3(N)	08:54:46	2.0	Bottom	3	2	26.32	7.94	28.45	77.10	5.8	5.8	9.6
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	SR4(N3)	08:01:58	1.0	Surface	1	1	26.43	7.95	28.32	77.20	5.8	5.7	9.3
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	SR4(N3)	08:02:30	1.0	Surface	1	2	26.48	7.95	28.29	77.20	5.8	5.7	9.0
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	SR4(N3)	08:01:49	2.9	Bottom	3	1	26.21	7.94	28.60	76.80	5.8	5.7	8.8
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	SR4(N3)	08:02:16	2.9	Bottom	3	2	26.41	7.94	28.55	77.10	5.8	5.7	9.3
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	SR5(N)	08:14:21	1	Surface	1	1	25.93	7.91	29.18	80.50	5.9	5.8	8.0
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	SR5(N)	08:14:53	1	Surface	1	2	25.98	7.91	29.19	80.50	5.9	5.7	7.8
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	SR5(N)	08:14:08	4.4	Middle	2	1	25.73	7.90	29.13	79.70	5.9	5.7	7.9
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	SR5(N)	08:14:41	4.4	Middle	2	2	25.75	7.90	29.16	80.10	5.9	5.8	7.6
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	SR5(N)	08:13:54	7.8	Bottom	3	1	25.76	7.91	28.76	79.60	5.9	5.7	6.3
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	SR5(N)	08:14:31	7.8	Bottom	3	2	25.77	7.91	28.71	80.00	5.9	5.8	7.4
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	SR10A(N)	07:12:59	1	Surface	1	1	25.99	7.91	29.17	80.80	5.9	5.6	7.6
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	SR10A(N)	07:13:41	1	Surface	1	2	25.99	7.91	29.17	80.70	5.9	5.7	8.1
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	SR10A(N)	07:12:47	5.9	Middle	2	1	25.74	7.90	29.10	80.60	5.9	5.6	8.6
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	SR10A(N)	07:13:23	5.9	Middle	2	2	25.70	7.90	29.08	80.30	5.9	5.6	8.3
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	SR10A(N)	07:12:33	10.8	Bottom	3	1	25.78	7.90	28.65	81.00	5.9	5.7	7.8
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	SR10A(N)	07:13:09	10.8	Bottom	3	2	25.77	7.90	28.63	80.00	5.8	5.6	7.7
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	SR10B(N2)	07:03:40	1.0	Surface	1	1	26.28	7.89	29.05	81.60	5.9	5.8	7.3
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	SR10B(N2)	07:04:20	1.0	Surface	1	2	26.04	7.90	29.13	80.40	5.9	5.8	8.7
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	SR10B(N2)	07:03:28	3.8	Middle	2	1	26.03	7.89	28.60	80.50	5.9	5.8	7.9
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	SR10B(N2)	07:04:05	3.8	Middle	2	2	26.07	7.89	28.61	80.30	5.9	5.8	7.8
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	SR10B(N2)	07:02:37	6.6	Bottom	3	1	26.03	7.89	28.99	80.10	5.9	5.8	8.7
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	SR10B(N2)	07:03:53	6.6	Bottom	3	2	26.04	7.89	29.13	79.90	5.8	5.9	7.4
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	CS2(A)	09:05:15	1	Surface	1	1	25.92	7.92	28.75	80.00	5.9	5.7	7.1
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	CS2(A)	09:05:52	1	Surface	1	2	25.95	7.92	28.70	79.60	5.8	5.7	7.5
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	CS2(A)	09:05:04	3.1	Middle	2	1	25.69	7.91	29.19	79.90	5.8	5.7	8.4
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	CS2(A)	09:05:40	3.1	Middle	2	2	25.69	7.91	29.19	79.50	5.8	5.7	8.5
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	CS2(A)	09:04:43	5.2	Bottom	3	1	25.71	7.92	29.10	79.20	5.8	5.7	8.2
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	CS2(A)	09:05:30	5.2	Bottom	3	2	25.73	7.92	29.08	79.10	5.8	5.8	8.3
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	CS(Mf)5	07:06:53	1.0	Surface	1	1	26.38	7.95	28.24	75.30	5.6	5.6	9.8
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	CS(Mf)5	07:07:48	1.0	Surface	1	2	26.55	7.95	28.19	75.10	5.6	5.5	9.9
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	CS(Mf)5	07:06:32	6.0	Middle	2	1	26.51	7.94	28.85	74.70	5.6	5.6	9.5
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	CS(Mf)5	07:07:24	6.0	Middle	2	2	26.27	7.93	28.89	75.00	5.6	5.6	10.1
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	CS(Mf)5	07:05:59	11.0	Bottom	3	1	26.28	7.94	28.86	74.30	5.6	5.6	10.0
HKLR	HY/2011/03	2025-04-30	Mid-Flood	Sunny	CS(Mf)5	07:07:11	11.0	Bottom	3	2	26.24	7.93	28.91	74.70	5.6	5.6	8.6

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	IS5	15:02:27	1.0	Surface	1	1	26.65	7.95	28.68	78.80	6.1	3.8	3.8
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	IS5	15:03:14	1.0	Surface	1	2	26.66	7.95	28.81	80.40	6.2	3.8	3.8
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	IS5	15:02:16	4.1	Middle	2	1	26.63	7.97	29.28	78.60	6.1	3.8	3.4
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	IS5	15:02:53	4.1	Middle	2	2	26.59	7.94	29.29	79.90	6.1	3.9	3.4
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	IS5	15:02:00	7.2	Bottom	3	1	26.68	7.96	29.22	77.80	6.0	3.8	5.0
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	IS5	15:02:35	7.2	Bottom	3	2	26.36	7.95	29.27	78.60	6.1	3.9	5.0
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	IS(Mf)6	15:11:51	1.0	Surface	1	1	26.62	7.97	28.72	78.70	6.1	3.9	5.4
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	IS(Mf)6	15:12:21	1.0	Surface	1	2	26.62	7.97	28.72	78.50	6.1	3.9	5.4
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	IS(Mf)6	15:11:33	2.0	Bottom	3	1	26.51	7.97	28.87	78.60	6.1	3.9	2.6
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	IS(Mf)6	15:12:04	2.0	Bottom	3	2	26.52	7.97	28.91	78.70	6.1	3.9	2.6
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	IS7	15:23:03	1.0	Surface	1	1	26.64	7.96	28.80	78.80	6.1	3.8	3.4
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	IS7	15:23:24	1.0	Surface	1	2	26.71	7.96	28.76	78.60	6.1	3.8	3.4
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	IS7	15:22:52	2.0	Bottom	3	1	26.50	7.95	29.04	78.60	6.1	3.8	4.5
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	IS7	15:23:15	2.0	Bottom	3	2	26.54	7.95	29.03	78.50	6.1	3.8	4.5
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	IS8(N)	15:52:22	1.0	Surface	1	1	26.71	7.98	28.68	78.40	6.1	3.8	3.1
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	IS8(N)	15:52:53	1.0	Surface	1	2	26.70	7.98	28.73	78.60	6.1	3.8	3.1
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	IS8(N)	15:52:13	2.8	Bottom	3	1	26.69	7.98	29.21	78.60	6.1	3.8	4.4
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	IS8(N)	15:52:32	2.8	Bottom	3	2	26.65	7.98	28.89	78.50	6.1	3.8	4.4
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	IS(Mf)9	15:34:30	1.0	Surface	1	1	26.69	7.93	28.83	78.00	6.0	4.0	3.2
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	IS(Mf)9	15:35:07	1.0	Surface	1	2	26.68	7.93	28.84	77.80	6.0	3.9	3.2
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	IS(Mf)9	15:34:16	2.5	Bottom	3	1	26.63	7.93	29.04	77.80	6.0	4.0	3.2
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	IS(Mf)9	15:34:46	2.5	Bottom	3	2	26.63	7.93	29.10	77.70	6.0	4.0	3.2
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	IS10(N)	15:55:34	1.0	Surface	1	1	26.35	7.99	29.30	80.60	5.9	4.2	3.2
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	IS10(N)	15:56:22	1.0	Surface	1	2	26.36	7.99	29.28	80.10	5.9	4.2	3.2
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	IS10(N)	15:55:27	4.2	Middle	2	1	26.09	7.98	28.92	80.30	5.9	4.2	4.7
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	IS10(N)	15:56:04	4.2	Middle	2	2	26.10	7.99	28.91	79.80	5.9	4.2	4.7
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	IS10(N)	15:55:09	7.4	Bottom	3	1	26.17	7.98	29.40	79.60	5.9	4.2	2.7
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	IS10(N)	15:55:53	7.4	Bottom	3	2	26.18	7.99	29.28	79.50	5.9	4.3	2.7
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	SR3(N)	14:52:35	1.0	Surface	1	1	26.41	7.96	28.63	78.30	6.1	4.0	4.8
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	SR3(N)	14:52:56	1.0	Surface	1	2	26.41	7.96	28.59	78.60	6.1	4.0	4.8
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	SR3(N)	14:52:23	2.0	Bottom	3	1	26.40	7.96	28.91	78.20	6.1	4.1	4.8
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	SR3(N)	14:52:47	2.0	Bottom	3	2	26.60	7.97	28.74	77.90	6.1	4.0	4.8
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	SR4(N3)	15:44:36	1.0	Surface	1	1	26.72	7.97	28.68	77.40	6.0	4.0	4.6
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	SR4(N3)	15:45:10	1.0	Surface	1	2	26.70	7.98	28.67	77.70	6.0	4.0	4.6
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	SR4(N3)	15:44:22	2.8	Bottom	3	1	26.64	7.96	28.91	77.30	6.0	4.0	4.0
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	SR4(N3)	15:44:52	2.8	Bottom	3	2	26.68	7.97	28.88	77.00	6.0	4.0	4.0
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	SR5(N)	15:45:14	1.0	Surface	1	1	26.19	7.97	29.46	81.00	6.0	4.3	3.9
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	SR5(N)	15:45:47	1.0	Surface	1	2	26.22	7.97	29.46	81.00	6.0	4.3	3.9
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	SR5(N)	15:45:06	4.3	Middle	2	1	25.96	7.96	29.41	80.20	5.9	4.4	3.8
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	SR5(N)	15:45:36	4.3	Middle	2	2	25.96	7.96	29.40	80.60	6.0	4.4	3.8
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	SR5(N)	15:44:48	7.6	Bottom	3	1	25.98	7.97	28.89	80.10	5.9	4.4	3.1
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	SR5(N)	15:45:26	7.6	Bottom	3	2	26.00	7.97	28.77	80.50	6.0	4.3	3.1
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	SR10A(N)	16:42:32	1.0	Surface	1	1	26.32	7.98	29.31	80.60	5.9	4.3	2.2
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	SR10A(N)	16:43:04	1.0	Surface	1	2	26.32	7.97	29.34	80.30	5.9	4.3	2.2
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	SR10A(N)	16:42:18	5.6	Middle	2	1	26.32	7.97	28.92	80.50	5.9	4.3	2.7
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	SR10A(N)	16:42:58	5.6	Middle	2	2	26.32	7.97	28.88	80.00	5.9	4.3	2.7
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	SR10A(N)	16:41:56	10.2	Bottom	3	1	26.31	7.97	29.40	81.30	6.0	4.2	2.9
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	SR10A(N)	16:42:47	10.2	Bottom	3	2	26.31	7.97	29.39	79.80	5.9	4.3	2.9
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	SR10B(N2)	16:52:21	1.0	Surface	1	1	26.32	8.00	28.87	81.30	6.0	4.2	3.0
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	SR10B(N2)	16:53:38	1.0	Surface	1	2	26.29	8.00	28.91	81.10	6.0	4.3	3.0
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	SR10B(N2)	16:52:16	3.7	Middle	2	1	26.03	7.99	29.36	81.30	6.0	4.2	4.4
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	SR10B(N2)	16:52:42	3.7	Middle	2	2	26.01	7.99	29.38	80.90	6.0	4.2	4.4
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	SR10B(N2)	16:52:06	6.4	Bottom	3	1	26.09	8.00	29.36	80.70	6.0	4.2	4.0
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	SR10B(N2)	16:52:33	6.4	Bottom	3	2	26.02	8.00	29.42	80.50	5.9	4.2	4.0
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	CS2(A)	14:51:48	1.0	Surface	1	1	26.21	7.99	29.45	81.40	6.0	4.2	3.3
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	CS2(A)	14:52:16	1.0	Surface	1	2	26.22	7.99	29.46	80.90	6.0	4.2	3.3
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	CS2(A)	14:51:39	3.2	Middle	2	1	25.95	7.98	29.40	81.00	6.0	4.2	2.2
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	CS2(A)	14:52:06	3.2	Middle	2	2	25.96	7.98	29.43	79.70	5.9	4.2	2.2
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	CS2(A)	14:51:20	5.4	Bottom	3	1	26.00	7.98	29.03	80.60	6.0	4.2	3.6
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	CS2(A)	14:51:56	5.4	Bottom	3	2	26.02	7.98	28.98	79.70	5.9	4.2	3.6
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	CS(Mf)5	16:44:40	1.0	Surface	1	1	26.73	7.98	28.73	77.40	6.0	3.9	3.3
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	CS(Mf)5	16:45:41	1.0	Surface	1	2	26.66	7.99	28.80	78.00	6.1	3.8	3.3
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	CS(Mf)5	16:44:28	5.8	Middle	2	1	26.48	7.98	29.24	76.70	6.0	3.9	4.2
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	CS(Mf)5	16:45:07	5.8	Middle	2	2	26.47	7.98	28.69	77.70	6.0	3.9	4.2
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	CS(Mf)5	16:44:08	10.6	Bottom	3	1	26.45	7.98	29.23	76.60	6.0	3.9	4.7
HKLR	HY/2011/03	2025-05-02	Mid-Ebb	Sunny	CS(Mf)5	16:44:51	10.6	Bottom	3	2	26.44	7.98	29.19	77.70	6.0	3.8	4.7
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	IS5	09:11:40	1.0	Surface	1	1	26.60	7.96	28.67	80.50	6.2	3.8	3.0
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	IS5	09:12:25	1.0	Surface	1	2	26.73	7.97	28.53	80.10	6.2	3.8	3.0
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	IS5	09:11:22	4.2	Middle	2	1	26.74	7.96	29.13	80.40	6.2	3.9	4.6
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	IS5	09:12:04	4.2	Middle	2	2	26.72	7.96	29.12	79.10	6.2	3.9	4.6
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	IS5	09:11:00	7.4	Bottom	3	1	26.46	7.96	29.17	80.30	6.2	3.9	5.2
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	IS5	09:11:49	7.4	Bottom	3	2	26.64	7.96	29.17	78.60	6.1	3.9	5.2
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	IS(Mf)6	09:00:36	1.0	Surface	1	1	26.77	7.97	28.51	77.50	6.0	3.8	3.0
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	IS(Mf)6	09:01:10	1.0	Surface	1	2	26.66	7.96	28.52	77.40	6.0	3.8	3.0
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	IS(Mf)6	09:00:29	2.1	Bottom	3	1	26.59	7.97	28.71	77.40	6.0	3.8	2.3
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	IS(Mf)6	09:00:47	2.1	Bottom	3	2	26.60	7.97	28.77	77.20	6.0	3.8	2.3
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	IS7	08:50:14	1.0	Surface	1	1	26.85	7.97	28.56	77.60	6.0	3.7	2.1
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	IS7	08:50:34	1.0	Surface	1	2	26.87	7.97	28.54	77.40	6.0	3.7	2.1
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	IS7	08:49:44	2.0	Bottom	3	1	26.76	7.97	28.52	77.60	6.0	3.7	2.8
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	IS7	08:50:20	2.0	Bottom	3	2	26.79	7.97	28.89	77.30	6.0	3.8	2.8
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	IS8(N)	08:19:55	1.0	Surface	1	1	26.71	7.98	28.61	78.00	6.1	3.9	3.1
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	IS8(N)	08:20:28	1.0	Surface	1	2	26.76	7.98	28.58	78.00	6.1	3.9	3.1
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	IS8(N)	08:19:46	3.0	Bottom	3	1	26.49	7.97	28.89	77.60	6.1	3.9	2.9
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	IS8(N)	08:20:13	3.0	Bottom	3	2	26.69	7.97	28.84	77.90	6.1	3.9	2.9
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	IS(Mf)9	08:40:43	1.0	Surface	1	1	26.84	7.95	28.67	78.60	6.1	3.8	3.4
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	IS(Mf)9	08:41:04	1.0	Surface	1	2	26.83	7.95	28.59	78.40	6.1	3.7	3.4
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	IS(Mf)9	08:40:22	2.7	Bottom	3	1	26.77	7.94	28.92	78.50	6.1	3.8	3.4
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	IS(Mf)9	08:40:53	2.7	Bottom	3	2	26.77	7.94	28.88	78.20	6.1	3.8	3.4
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	IS10(N)	08:20:51	1.0	Surface	1	1	26.20	7.95	29.32	82.10	6.0	4.3	3.0
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	IS10(N)	08:21:27	1.0	Surface	1	2	26.25	7.96	29.40	80.90	5.9	4.2	3.0
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	IS10(N)	08:20:39	4.3	Middle	2	1	26.00	7.95	28.87	81.00	6.0	4.2	5.2
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	IS10(N)	08:21:18	4.3	Middle	2	2	26.02	7.95	28.88	80.80	5.9	4.3	5.2
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	IS10(N)	08:20:26	7.6	Bottom	3	1	26.03	7.95	29.26	80.60	5.9	4.2	3.6
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	IS10(N)	08:21:05	7.6	Bottom	3	2	26.04	7.95	29.40	80.40	5.9	4.3	3.6
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	SR3(N)	09:23:17	1.0	Surface	1	1	26.61	7.96	28.66	76.40	6.0	3.9	3.9
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	SR3(N)	09:23:54	1.0	Surface	1	2	26.60	7.96	28.66	76.40	6.0	4.0	3.9
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	SR3(N)	09:22:50	2.0	Bottom	3	1	26.53	7.95	28.83	76.00	5.9	3.9	4.3
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	SR3(N)	09:23:35	2.0	Bottom	3	2	26.57	7.96	28.92	77.00	6.0	3.9	4.3
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	SR4(N3)	08:29:37	1.0	Surface	1	1	26.85	7.97	28.85	77.40	6.1	3.8	3.6
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	SR4(N3)	08:30:08	1.0	Surface	1	2	26.85	7.97	28.80	77.40	6.1	3.9	3.6
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	SR4(N3)	08:29:27	2.8	Bottom	3	1	26.74	7.98	28.88	76.60	6.0	3.9	3.5
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	SR4(N3)	08:29:54	2.8	Bottom	3	2	26.74	7.98	28.53	77.60	6.1	3.8	3.5
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	SR5(N)	08:31:56	1	Surface	1	1	26.55	7.98	29.02	80.50	5.9	4.3	2.7
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	SR5(N)	08:32:30	1	Surface	1	2	26.31	7.98	28.97	80.10	5.9	4.3	2.7
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	SR5(N)	08:31:45	4.3	Middle	2	1	26.30	7.97	29.46	80.40	5.9	4.3	3.2
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	SR5(N)	08:32:18	4.3	Middle	2	2	26.34	7.97	29.46	80.00	5.9	4.3	3.2
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	SR5(N)	08:31:31	7.6	Bottom	3	1	26.30	7.98	29.37	79.70	5.9	4.2	3.5
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	SR5(N)	08:32:08	7.6	Bottom	3	2	26.31	7.98	29.35	79.60	5.9	4.4	3.5
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	SR10A(N)	07:36:35	1	Surface	1	1	26.29	7.95	28.85	81.30	6.0	4.3	3.2
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	SR10A(N)	07:37:18	1	Surface	1	2	26.32	7.95	28.84	81.20	6.0	4.2	3.2
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	SR10A(N)	07:36:24	5.8	Middle	2	1	26.29	7.95	29.35	80.50	6.0	4.2	3.0
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	SR10A(N)	07:37:00	5.8	Middle	2	2	26.29	7.95	29.29	80.90	6.0	4.3	3.0
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	SR10A(N)	07:36:10	10.6	Bottom	3	1	26.25	7.95	29.27	79.90	5.9	4.2	4.2
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	SR10A(N)	07:36:46	10.6	Bottom	3	2	26.25	7.94	29.26	80.50	6.0	4.2	4.2

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	SR10B(N2)	07:27:17	1.0	Surface	1	1	26.26	7.97	29.44	81.30	6.0	4.1	2.3
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	SR10B(N2)	07:27:57	1.0	Surface	1	2	26.26	7.97	29.44	81.20	6.0	4.2	2.3
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	SR10B(N2)	07:27:05	3.9	Middle	2	1	26.01	7.96	29.37	81.10	6.0	4.1	3.0
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	SR10B(N2)	07:27:44	3.9	Middle	2	2	25.97	7.96	29.35	80.80	5.9	4.1	3.0
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	SR10B(N2)	07:26:12	6.8	Bottom	3	1	26.05	7.96	28.92	81.50	6.0	4.2	2.7
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	SR10B(N2)	07:27:30	6.8	Bottom	3	2	26.04	7.96	28.90	80.50	5.9	4.1	2.7
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	CS2(A)	09:25:52	1	Surface	1	1	26.32	7.98	29.41	81.00	6.0	4.4	3.8
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	CS2(A)	09:26:29	1	Surface	1	2	26.33	7.98	29.42	81.00	6.0	4.3	3.8
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	CS2(A)	09:25:41	3.1	Middle	2	1	26.32	7.97	29.45	80.60	6.0	4.3	3.4
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	CS2(A)	09:26:16	3.1	Middle	2	2	26.33	7.97	29.44	80.70	6.0	4.3	3.4
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	CS2(A)	09:25:21	5.2	Bottom	3	1	26.26	7.97	28.97	80.60	6.0	4.3	3.7
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	CS2(A)	09:26:07	5.2	Bottom	3	2	26.26	7.97	29.00	80.40	6.0	4.4	3.7
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	CS(Mf)5	07:31:31	1.0	Surface	1	1	26.83	7.98	28.48	75.90	5.9	3.7	3.1
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	CS(Mf)5	07:32:26	1.0	Surface	1	2	26.66	7.98	28.53	76.10	5.9	3.8	3.1
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	CS(Mf)5	07:31:10	5.9	Middle	2	1	26.55	7.96	29.18	75.80	5.9	3.8	2.4
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	CS(Mf)5	07:32:02	5.9	Middle	2	2	26.79	7.97	29.14	75.50	5.9	3.8	2.4
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	CS(Mf)5	07:30:32	10.8	Bottom	3	1	26.52	7.96	29.20	75.50	5.9	3.8	4.0
HKLR	HY/2011/03	2025-05-02	Mid-Flood	Sunny	CS(Mf)5	07:31:45	10.8	Bottom	3	2	26.56	7.97	29.15	75.10	5.8	3.8	4.0
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Cloudy	IS5	18:46:15	1.0	Surface	1	1	25.79	8.03	28.63	97.80	6.7	3.0	3.0
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Cloudy	IS5	18:47:01	1.0	Surface	1	2	25.78	8.03	28.50	96.20	6.6	3.0	3.0
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Cloudy	IS5	18:46:03	4.1	Middle	2	1	25.72	8.02	29.11	97.30	6.6	3.1	4.4
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Cloudy	IS5	18:46:40	4.1	Middle	2	2	25.76	8.05	29.10	96.00	6.6	3.0	4.4
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Cloudy	IS5	18:45:47	7.2	Bottom	3	1	25.49	8.03	29.09	96.00	6.6	3.1	3.4
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Cloudy	IS5	18:46:22	7.2	Bottom	3	2	25.81	8.04	29.04	95.20	6.5	3.0	3.4
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Cloudy	IS(Mf)6	18:56:38	1.0	Surface	1	1	25.77	8.04	28.62	96.20	6.6	3.0	3.0
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Cloudy	IS(Mf)6	18:57:08	1.0	Surface	1	2	25.84	8.04	28.58	96.00	6.6	3.0	3.0
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Cloudy	IS(Mf)6	18:56:22	2.0	Bottom	3	1	25.63	8.03	28.86	96.00	6.6	3.0	3.2
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Cloudy	IS(Mf)6	18:56:51	2.0	Bottom	3	2	25.67	8.03	28.85	95.90	6.6	3.0	3.2
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Cloudy	IS7	19:06:50	1.0	Surface	1	1	25.82	8.01	28.65	95.40	6.5	3.2	3.8
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Cloudy	IS7	19:07:11	1.0	Surface	1	2	25.81	8.01	28.66	95.20	6.5	3.1	3.8
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Cloudy	IS7	19:06:37	2.0	Bottom	3	1	25.76	8.01	28.86	95.20	6.5	3.2	3.4
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Cloudy	IS7	19:07:02	2.0	Bottom	3	2	25.76	8.01	28.92	95.10	6.5	3.2	3.4
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Cloudy	IS8(N)	19:41:04	1.0	Surface	1	1	25.75	8.05	28.54	96.10	6.6	3.1	3.2
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Cloudy	IS8(N)	19:41:35	1.0	Surface	1	2	25.75	8.05	28.54	95.90	6.6	3.1	3.2
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Cloudy	IS8(N)	19:40:52	2.8	Bottom	3	1	25.64	8.05	28.69	96.00	6.6	3.1	5.4
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Cloudy	IS8(N)	19:41:14	2.8	Bottom	3	2	25.65	8.05	28.73	96.10	6.6	3.1	5.4
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Cloudy	IS(Mf)9	19:18:17	1.0	Surface	1	1	25.85	8.05	28.50	94.80	6.5	3.2	4.3
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Cloudy	IS(Mf)9	19:18:54	1.0	Surface	1	2	25.83	8.06	28.49	95.10	6.5	3.2	4.3
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Cloudy	IS(Mf)9	19:18:02	2.6	Bottom	3	1	25.77	8.04	28.73	94.70	6.5	3.2	3.6
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Cloudy	IS(Mf)9	19:18:33	2.6	Bottom	3	2	25.81	8.05	28.70	94.40	6.5	3.2	3.6
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Fine	IS10(N)	20:02:28	1.0	Surface	1	1	25.61	8.10	28.32	91.50	6.4	2.8	3.4
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Fine	IS10(N)	20:03:11	1.0	Surface	1	2	25.64	8.10	28.30	92.20	6.4	2.8	3.4
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Fine	IS10(N)	20:02:56	5.3	Middle	2	1	25.42	8.08	29.01	90.80	6.3	2.9	3.7
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Fine	IS10(N)	20:02:16	5.3	Middle	2	2	25.40	8.07	29.03	90.60	6.3	2.9	3.7
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Fine	IS10(N)	20:02:26	9.6	Bottom	3	1	25.40	8.07	29.07	90.50	6.3	3.0	3.2
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Fine	IS10(N)	20:02:42	9.6	Bottom	3	2	25.45	8.07	29.05	90.70	6.3	3.0	3.2
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Cloudy	SR3(N)	18:35:52	1.0	Surface	1	1	25.74	8.04	28.48	93.80	6.5	3.1	3.0
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Cloudy	SR3(N)	18:36:13	1.0	Surface	1	2	25.73	8.04	28.48	93.80	6.5	3.2	3.0
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Cloudy	SR3(N)	18:35:40	2.0	Bottom	3	1	25.66	8.03	28.65	93.40	6.4	3.1	4.2
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Cloudy	SR3(N)	18:36:02	2.0	Bottom	3	2	25.70	8.04	28.74	94.40	6.5	3.1	4.2
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Cloudy	SR4(N3)	19:29:23	1.0	Surface	1	1	25.84	8.06	28.50	95.80	6.6	3.0	3.7
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Cloudy	SR4(N3)	19:29:57	1.0	Surface	1	2	25.83	8.06	28.55	96.00	6.6	3.0	3.7
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Cloudy	SR4(N3)	19:29:06	2.8	Bottom	3	1	25.82	8.06	29.03	96.00	6.6	3.0	3.4
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Cloudy	SR4(N3)	19:29:39	2.8	Bottom	3	2	25.78	8.06	28.71	95.90	6.6	3.0	3.4
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Fine	SR5(N)	19:54:28	1.0	Surface	1	1	25.65	8.10	28.30	92.60	6.4	2.6	5.8
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Fine	SR5(N)	19:53:41	1.0	Surface	1	2	25.60	8.10	28.30	92.00	6.4	2.6	5.8
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Fine	SR5(N)	19:54:16	4.8	Middle	2	1	25.44	8.07	28.93	91.00	6.3	2.8	5.0
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Fine	SR5(N)	19:53:28	4.8	Middle	2	2	25.43	8.08	28.92	90.80	6.3	2.8	5.0
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Fine	SR5(N)	19:53:16	8.5	Bottom	3	1	25.41	8.07	29.14	90.90	6.3	3.0	4.3
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Fine	SR5(N)	19:53:56	8.5	Bottom	3	2	25.43	8.07	29.14	91.20	6.3	3.1	4.3
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Fine	SR10A(N)	20:57:13	1.0	Surface	1	1	25.62	8.10	29.14	93.50	6.5	2.4	3.3
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Fine	SR10A(N)	20:56:28	1.0	Surface	1	2	25.62	8.11	29.12	92.70	6.4	2.4	3.3
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Fine	SR10A(N)	20:56:56	6.6	Middle	2	1	25.41	8.08	29.64	90.20	6.2	2.6	3.6
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Fine	SR10A(N)	20:56:03	6.6	Middle	2	2	25.40	8.09	29.64	90.90	6.3	2.6	3.6
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Fine	SR10A(N)	20:55:52	12.2	Bottom	3	1	25.42	8.10	29.66	90.70	6.3	2.7	5.0
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Fine	SR10A(N)	20:56:44	12.2	Bottom	3	2	25.43	8.09	29.64	90.50	6.3	2.7	5.0
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Fine	SR10B(N2)	21:07:06	1.0	Surface	1	1	25.62	8.11	29.18	91.90	6.4	2.5	3.5
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Fine	SR10B(N2)	21:06:18	1.0	Surface	1	2	25.62	8.11	29.16	91.80	6.3	2.4	3.5
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Fine	SR10B(N2)	21:06:06	3.7	Middle	2	1	25.49	8.09	29.46	90.90	6.3	2.5	4.4
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Fine	SR10B(N2)	21:06:55	3.7	Middle	2	2	25.43	8.09	29.47	90.80	6.3	2.6	4.4
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Fine	SR10B(N2)	21:06:31	6.4	Bottom	3	1	25.47	8.08	29.57	90.80	6.3	2.6	3.0
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Fine	SR10B(N2)	21:05:57	6.4	Bottom	3	2	25.47	8.09	29.57	90.90	6.3	2.6	3.0
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Fine	CS2(A)	18:59:32	1.0	Surface	1	1	25.55	8.10	28.38	94.60	6.6	2.6	3.8
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Fine	CS2(A)	18:58:53	1.0	Surface	1	2	25.53	8.11	28.45	95.20	6.6	2.7	3.8
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Fine	CS2(A)	18:58:40	3.4	Middle	2	1	25.37	8.09	29.03	92.70	6.5	3.0	3.2
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Fine	CS2(A)	18:59:21	3.4	Middle	2	2	25.38	8.09	29.04	92.50	6.4	2.9	3.2
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Fine	CS2(A)	18:59:09	5.7	Bottom	3	1	25.39	8.08	29.18	92.60	6.4	3.1	3.3
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Fine	CS2(A)	18:58:30	5.7	Bottom	3	2	25.35	8.09	29.22	92.40	6.4	3.0	3.3
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Cloudy	CS(Mf)5	20:28:22	1.0	Surface	1	1	25.79	8.07	28.62	95.40	6.6	3.0	3.9
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Cloudy	CS(Mf)5	20:29:23	1.0	Surface	1	2	25.86	8.06	28.55	94.80	6.5	3.1	3.9
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Cloudy	CS(Mf)5	20:28:10	5.8	Middle	2	1	25.60	8.06	28.51	95.10	6.5	3.1	3.3
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Cloudy	CS(Mf)5	20:28:45	5.8	Middle	2	2	25.61	8.06	29.06	94.10	6.5	3.1	3.3
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Cloudy	CS(Mf)5	20:27:54	10.6	Bottom	3	1	25.57	8.06	29.01	95.10	6.5	3.0	2.3
HKLR	HY/2011/03	2025-05-05	Mid-Ebb	Cloudy	CS(Mf)5	20:28:33	10.6	Bottom	3	2	25.58	8.06	29.05	94.00	6.5	3.1	2.3
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Cloudy	IS5	08:19:33	1.0	Surface	1	1	25.86	8.05	28.35	97.50	6.7	3.0	5.5
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Cloudy	IS5	08:20:18	1.0	Surface	1	2	25.73	8.04	28.49	97.90	6.7	3.0	5.5
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Cloudy	IS5	08:19:15	4.2	Middle	2	1	25.85	8.04	28.94	96.50	6.7	3.1	4.0
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Cloudy	IS5	08:19:57	4.2	Middle	2	2	25.87	8.04	28.95	97.80	6.7	3.1	4.0
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Cloudy	IS5	08:18:53	7.4	Bottom	3	1	25.77	8.04	28.99	96.00	6.6	3.1	4.6
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Cloudy	IS5	0:00	7.4	Bottom	3	2	25.59	8.04	28.99	97.70	6.7	3.1	4.6
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Cloudy	IS(Mf)6	08:10:29	1.0	Surface	1	1	25.84	8.06	28.43	95.40	6.6	3.1	4.0
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Cloudy	IS(Mf)6	08:11:02	1.0	Surface	1	2	25.89	8.06	28.40	95.40	6.6	3.1	4.0
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Cloudy	IS(Mf)6	08:10:22	2.2	Bottom	3	1	25.62	8.05	28.71	95.00	6.6	3.1	2.4
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Cloudy	IS(Mf)6	08:10:40	2.2	Bottom	3	2	25.82	8.05	28.66	95.30	6.6	3.1	2.4
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Cloudy	IS7	08:00:07	1.0	Surface	1	1	25.90	8.05	28.33	94.90	6.5	3.0	3.2
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Cloudy	IS7	08:00:27	1.0	Surface	1	2	25.79	8.04	28.34	94.80	6.5	3.0	3.2
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Cloudy	IS7	07:59:37	2.0	Bottom	3	1	25.72	8.05	28.53	94.80	6.5	3.0	3.3
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Cloudy	IS7	08:00:14	2.0	Bottom	3	2	25.73	8.05	28.59	94.60	6.5	3.0	3.3
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Cloudy	IS8(N)	07:25:08	1.0	Surface	1	1	25.98	8.05	28.67	94.80	6.6	3.0	3.4
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Cloudy	IS8(N)	07:25:41	1.0	Surface	1	2	25.98	8.05	28.62	94.80	6.6	3.1	3.4
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Cloudy	IS8(N)	07:24:55	3.2	Bottom	3	1	25.87	8.06	28.70	94.00	6.5	3.1	5.0
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Cloudy	IS8(N)	07:25:26	3.2	Bottom	3	2	25.87	8.06	28.35	95.00	6.6	3.0	5.0
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Cloudy	IS(Mf)9	07:50:36	1.0	Surface	1	1	25.98	8.05	28.38	95.00	6.5	2.9	4.1
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Cloudy	IS(Mf)9	07:50:55	1.0	Surface	1	2	26.00	8.05	28.36	94.80	6.5	2.9	4.1
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Cloudy	IS(Mf)9	07:50:15	2.6	Bottom	3	1	25.89	8.05	28.34	95.00	6.5	2.9	4.9
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Cloudy	IS(Mf)9	07:50:46	2.6	Bottom	3	2	25.92	8.05	28.71	94.70	6.5	3.0	4.9
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Fine	IS10(N)	07:50:19	1.0	Surface	1	1	25.48	8.10	28.61	92.50	6.4	2.6	2.4
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Fine	IS10(N)	07:49:39	1.0	Surface	1	2	25.44	8.10	28.61	92.40	6.4	2.6	2.4
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Fine	IS10(N)	07:50:04	5.4	Middle	2	1	25.29	8.07	29.13	90.30	6.3	2.8	2.9
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Fine	IS10(N)	07:49:25	5.4	Middle	2	2	25.28	8.07	29.13	90.60	6.3	2.8	2.9
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Fine	IS10(N)	07:49:54	9.7	Bottom	3	1	25.31	8.07	29.16	90.40	6.3	3.1	2.7
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Fine	IS10(N)	07:49:13	9.7	Bottom	3	2	25.29	8.07	29.17	90.60	6.3	3.0	2.7
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Cloudy	SR3(N)	08:35:10	1.0	Surface	1	1	25.54	8.04	28.45	95.70	6.6	3.2	2.8
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Cloudy	SR3(N)	08:35:43	1.0	Surface	1	2	25.54	8.04	28.41	96.00	6.6	3.2	2.8
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Cloudy	SR3(N)	08:34:45	2.0	Bottom	3	1	25.53	8.04	28.73	95.60	6.6	3.3	3.6

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Cloudy	SR3(N)	08:35:28	2.0	Bottom	3	2	25.73	8.05	28.56	95.30	6.6	3.2	3.6
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Cloudy	SR4(N3)	07:34:50	1.0	Surface	1	1	25.97	8.03	28.49	96.00	6.6	3.0	3.4
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Cloudy	SR4(N3)	07:35:23	1.0	Surface	1	2	25.96	8.03	28.41	95.80	6.6	2.9	3.4
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Cloudy	SR4(N3)	07:34:42	3.0	Bottom	3	1	25.90	8.02	28.74	95.90	6.6	3.0	3.2
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Cloudy	SR4(N3)	07:35:07	3.0	Bottom	3	2	25.90	8.02	28.70	95.60	6.6	3.0	3.2
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Fine	SR5(N)	07:59:25	1	Surface	1	1	25.46	8.11	28.61	91.30	6.3	2.6	2.9
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Fine	SR5(N)	07:58:42	1	Surface	1	2	25.47	8.10	28.61	91.20	6.3	2.6	2.9
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Fine	SR5(N)	07:59:10	4.8	Middle	2	1	25.32	8.08	29.06	90.00	6.3	2.8	4.1
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Fine	SR5(N)	07:58:29	4.8	Middle	2	2	25.32	8.07	29.07	90.10	6.3	2.8	4.1
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Fine	SR5(N)	07:59:00	8.5	Bottom	3	1	25.30	8.08	29.16	89.90	6.3	3.1	4.1
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Fine	SR5(N)	07:58:18	8.5	Bottom	3	2	25.29	8.07	29.17	90.00	6.3	3.0	4.1
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Fine	SR10A(N)	06:58:44	1	Surface	1	1	25.60	8.11	28.82	90.80	6.3	2.3	3.3
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Fine	SR10A(N)	06:58:00	1	Surface	1	2	25.60	8.09	28.79	90.50	6.3	2.4	3.3
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Fine	SR10A(N)	06:57:44	6.7	Middle	2	1	25.37	8.06	29.40	89.30	6.2	2.6	3.7
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Fine	SR10A(N)	06:58:27	6.7	Middle	2	2	25.36	8.08	29.40	89.10	6.2	2.6	3.7
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Fine	SR10A(N)	06:58:17	12.4	Bottom	3	1	25.39	8.08	29.42	89.00	6.2	2.8	5.4
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Fine	SR10A(N)	06:57:34	12.4	Bottom	3	2	25.38	8.07	29.43	89.10	6.2	2.8	5.4
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Fine	SR10B(N2)	06:48:38	1.0	Surface	1	1	25.61	8.10	28.79	95.40	6.6	2.3	3.7
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Fine	SR10B(N2)	06:47:58	1.0	Surface	1	2	25.62	8.08	28.75	95.10	6.6	2.4	3.7
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Fine	SR10B(N2)	06:47:40	3.8	Middle	2	1	25.43	8.05	29.20	92.40	6.4	2.5	3.8
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Fine	SR10B(N2)	06:48:23	3.8	Middle	2	2	25.45	8.07	29.17	91.20	6.3	2.5	3.8
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Fine	SR10B(N2)	06:48:11	6.6	Bottom	3	1	25.43	8.05	29.33	90.40	6.3	2.7	6.4
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Fine	SR10B(N2)	06:47:28	6.6	Bottom	3	2	25.39	8.05	29.36	90.60	6.3	2.7	6.4
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Fine	CS2(A)	08:51:41	1	Surface	1	1	25.42	8.10	28.59	91.90	6.4	2.8	4.0
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Fine	CS2(A)	08:50:59	1	Surface	1	2	25.42	8.10	28.59	91.90	6.4	2.8	4.0
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Fine	CS2(A)	08:51:27	3.4	Middle	2	1	25.31	8.09	28.97	91.00	6.3	2.9	5.0
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Fine	CS2(A)	08:50:47	3.4	Middle	2	2	25.33	8.09	28.95	90.90	6.3	3.0	5.0
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Fine	CS2(A)	08:50:35	5.7	Bottom	3	1	25.27	8.09	29.11	90.80	6.3	3.0	3.2
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Fine	CS2(A)	08:51:14	5.7	Bottom	3	2	25.29	8.09	29.11	90.90	6.3	3.2	3.2
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Cloudy	CS(Mf)5	06:42:29	1.0	Surface	1	1	25.79	8.06	28.35	93.50	6.4	3.0	2.6
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Cloudy	CS(Mf)5	06:43:24	1.0	Surface	1	2	25.96	8.06	28.30	93.30	6.4	2.9	2.6
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Cloudy	CS(Mf)5	06:42:08	6.0	Middle	2	1	25.92	8.05	28.96	92.90	6.4	3.0	4.1
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Cloudy	CS(Mf)5	06:43:00	6.0	Middle	2	2	25.68	8.04	29.00	93.20	6.4	3.0	4.1
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Cloudy	CS(Mf)5	06:41:11	11.0	Bottom	3	1	25.69	8.05	28.97	92.50	6.3	3.0	4.2
HKLR	HY/2011/03	2025-05-05	Mid-Flood	Cloudy	CS(Mf)5	06:42:44	11.0	Bottom	3	2	25.65	8.04	29.02	92.90	6.4	3.0	4.2
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	IS5	09:27:39	1.0	Surface	1	1	25.03	8.08	25.87	97.30	7.1	2.8	0.5
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	IS5	09:28:17	1.0	Surface	1	2	25.06	8.08	25.87	97.80	7.1	2.9	0.5
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	IS5	09:28:04	4.3	Middle	2	1	24.89	8.06	27.69	90.60	6.6	3.2	1.2
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	IS5	09:27:27	4.3	Middle	2	2	24.87	8.05	27.70	90.40	6.5	3.2	1.2
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	IS5	09:27:18	7.5	Bottom	3	1	24.86	8.05	27.75	90.20	6.5	3.3	1.5
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	IS5	09:27:53	7.5	Bottom	3	2	24.87	8.05	27.74	90.50	6.6	3.4	1.5
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	IS(Mf)6	09:36:44	1.0	Surface	1	1	25.07	8.09	25.87	100.20	7.3	2.9	1.1
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	IS(Mf)6	09:36:25	1.0	Surface	1	2	25.06	8.09	25.83	99.30	7.2	2.9	1.1
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	IS(Mf)6	09:36:33	2.2	Bottom	3	1	25.03	8.08	25.94	98.50	7.1	3.5	0.9
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	IS(Mf)6	09:36:15	2.2	Bottom	3	2	25.00	8.10	25.93	97.00	7.0	3.5	0.9
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	IS7	09:48:47	1.0	Surface	1	1	25.07	8.11	25.88	99.70	7.2	2.3	0.8
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	IS7	09:48:29	1.0	Surface	1	2	25.06	8.10	25.89	99.20	7.2	2.6	0.8
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	IS7	09:48:36	2.3	Bottom	3	1	25.03	8.10	25.96	98.70	7.2	2.8	1.3
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	IS7	09:48:20	2.3	Bottom	3	2	25.00	8.10	25.98	98.30	7.1	2.9	1.3
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	IS8(N)	10:22:02	1.0	Surface	1	1	25.07	8.05	25.84	97.10	7.0	2.7	1.1
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	IS8(N)	10:22:21	1.0	Surface	1	2	25.09	8.07	25.82	97.80	7.1	2.6	1.1
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	IS8(N)	10:22:11	2.9	Bottom	3	1	25.04	8.05	25.92	97.10	7.0	3.0	0.9
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	IS8(N)	10:21:52	2.9	Bottom	3	2	25.00	8.05	25.97	96.50	7.0	3.1	0.9
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	IS(Mf)9	09:58:52	1.0	Surface	1	1	25.07	8.09	25.89	98.90	7.2	2.7	0.9
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	IS(Mf)9	09:58:32	1.0	Surface	1	2	25.06	8.09	25.89	98.40	7.1	2.7	0.9
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	IS(Mf)9	09:58:41	2.6	Bottom	3	1	25.02	8.09	26.00	98.40	7.1	3.0	0.6
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	IS(Mf)9	09:58:25	2.6	Bottom	3	2	24.99	8.08	25.99	98.10	7.1	3.0	0.6
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	IS10(N)	10:32:32	1.0	Surface	1	1	25.42	8.08	26.11	93.60	6.6	2.9	0.9
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	IS10(N)	10:31:48	1.0	Surface	1	2	25.39	8.08	26.13	93.00	6.6	2.9	0.9
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	IS10(N)	10:32:17	5.3	Middle	2	1	25.14	8.05	28.10	85.60	6.0	3.2	0.6
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	IS10(N)	10:31:36	5.3	Middle	2	2	25.13	8.05	28.07	85.40	6.0	3.2	0.6
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	IS10(N)	10:32:04	9.6	Bottom	3	1	25.17	8.05	28.19	85.40	6.0	3.4	0.7
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	IS10(N)	10:31:36	9.6	Bottom	3	2	25.15	8.05	28.19	85.40	6.0	3.4	0.7
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	SR3(N)	09:12:35	1.0	Surface	1	1	25.05	8.07	27.42	98.40	7.1	3.0	0.7
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	SR3(N)	09:12:53	1.0	Surface	1	2	25.05	8.08	27.43	99.40	7.2	3.0	0.7
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	SR3(N)	09:12:26	2.4	Bottom	3	1	25.00	8.07	27.48	96.50	6.9	3.2	<0.5
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	SR3(N)	09:12:43	2.4	Bottom	3	2	25.03	8.08	27.45	97.80	7.1	3.1	<0.5
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	SR4(N3)	10:12:52	1.0	Surface	1	1	25.06	8.07	25.85	97.30	7.1	2.3	1.2
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	SR4(N3)	10:12:35	1.0	Surface	1	2	25.07	8.07	25.85	97.10	7.0	2.5	1.2
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	SR4(N3)	10:12:42	2.9	Bottom	3	1	25.03	8.05	25.95	96.60	7.0	2.7	0.8
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	SR4(N3)	10:12:25	2.9	Bottom	3	2	24.56	8.05	25.96	95.90	6.9	2.7	0.8
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	SR5(N)	10:21:19	1.0	Surface	1	1	25.40	8.09	25.66	93.90	6.6	3.1	1.3
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	SR5(N)	10:20:34	1.0	Surface	1	2	25.33	8.10	25.77	93.10	6.6	3.1	1.3
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	SR5(N)	10:21:07	4.7	Middle	2	1	25.17	8.06	27.98	85.50	6.0	3.3	1.1
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	SR5(N)	10:20:22	4.7	Middle	2	2	25.16	8.07	27.99	85.10	6.0	3.3	1.1
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	SR5(N)	10:20:50	8.4	Bottom	3	1	25.17	8.05	28.26	85.60	6.0	3.4	<0.5
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	SR5(N)	10:20:10	8.4	Bottom	3	2	25.15	8.06	28.26	85.00	6.0	3.4	<0.5
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	SR10A(N)	11:23:47	1.0	Surface	1	1	25.29	8.08	26.40	93.20	6.5	2.1	0.6
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	SR10A(N)	11:23:02	1.0	Surface	1	2	25.31	8.10	26.51	92.80	6.5	2.1	0.6
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	SR10A(N)	11:22:39	6.6	Middle	2	1	25.11	8.08	28.90	84.60	5.9	2.7	0.8
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	SR10A(N)	11:23:30	6.6	Middle	2	2	25.12	8.06	28.89	84.10	5.9	2.7	0.8
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	SR10A(N)	11:22:28	12.2	Bottom	3	1	25.12	8.09	28.93	84.50	5.9	2.9	0.9
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	SR10A(N)	11:23:18	12.2	Bottom	3	2	25.13	8.07	28.90	84.40	5.9	2.9	0.9
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	SR10B(N2)	11:34:42	1.0	Surface	1	1	25.31	8.09	26.48	92.00	6.5	2.2	1.6
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	SR10B(N2)	11:33:58	1.0	Surface	1	2	25.30	8.09	26.28	91.80	6.4	2.1	1.6
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	SR10B(N2)	11:34:29	3.7	Middle	2	1	25.17	8.06	28.66	84.60	5.9	2.6	1.4
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	SR10B(N2)	11:33:46	3.7	Middle	2	2	25.20	8.07	28.66	84.60	5.9	2.6	1.4
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	SR10B(N2)	11:33:36	6.3	Bottom	3	1	25.17	8.07	28.82	84.50	5.9	2.8	1.2
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	SR10B(N2)	11:34:11	6.3	Bottom	3	2	25.19	8.06	28.78	84.50	5.9	2.9	1.2
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	CS2(A)	09:31:43	1.0	Surface	1	1	25.30	8.08	25.92	95.90	6.8	3.0	0.9
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	CS2(A)	09:31:05	1.0	Surface	1	2	25.26	8.09	25.95	95.90	6.8	3.2	0.9
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	CS2(A)	09:30:52	3.4	Middle	2	1	25.11	8.08	28.16	86.90	6.1	3.6	0.9
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	CS2(A)	09:31:32	3.4	Middle	2	2	25.12	8.08	28.16	87.20	6.2	3.4	0.9
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	CS2(A)	09:31:21	5.7	Bottom	3	1	25.12	8.07	28.40	86.60	6.1	3.6	1.2
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	CS2(A)	09:30:42	5.7	Bottom	3	2	25.11	8.08	28.42	85.90	6.1	3.6	1.2
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	CS(Mf)5	11:04:36	1.0	Surface	1	1	25.08	8.10	26.01	93.60	6.8	2.2	1.2
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	CS(Mf)5	11:03:57	1.0	Surface	1	2	25.09	8.09	26.00	92.90	6.7	2.2	1.2
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	CS(Mf)5	11:03:41	6.4	Middle	2	1	24.68	8.05	28.13	85.50	6.2	2.5	1.2
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	CS(Mf)5	11:04:22	6.4	Middle	2	2	24.68	8.06	28.13	85.70	6.2	2.6	1.2
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	CS(Mf)5	11:04:12	11.7	Bottom	3	1	24.68	8.06	28.15	85.10	6.1	2.7	1.1
HKLR	HY/2011/03	2025-05-07	Mid-Ebb	Rainy	CS(Mf)5	11:03:32	11.7	Bottom	3	2	24.68	8.05	28.13	85.10	6.1	2.7	1.1
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	IS5	04:39:23	1.0	Surface	1	1	24.78	8.08	26.20	94.40	6.7	2.5	1.4
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	IS5	04:38:38	1.0	Surface	1	2	24.80	8.08	26.19	95.60	6.8	2.5	1.4
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	IS5	04:38:25	4.3	Middle	2	1	24.57	8.05	28.07	86.20	6.1	2.8	1.6
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	IS5	04:39:11	4.3	Middle	2	2	24.56	8.05	28.06	86.80	6.2	2.8	1.6
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	IS5	04:38:53	7.5	Bottom	3	1	24.49	8.04	28.14	85.80	6.1	3.0	1.2
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	IS5	04:38:15	7.5	Bottom	3	2	24.56	8.05	28.13	85.50	6.1	3.0	1.2
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	IS(Mf)6	04:27:40	1.0	Surface	1	1	24.84	8.10	26.20	97.10	6.9	2.5	1.3
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	IS(Mf)6	04:27:22	1.0	Surface	1	2	24.82	8.10	26.20	96.70	6.8	2.5	1.3
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	IS(Mf)6	04:27:30	2.3	Bottom	3	1	24.80	8.11	26.26	96.50	6.8	2.7	1.3
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	IS(Mf)6	04:27:10	2.3	Bottom	3	2	24.78	8.10	26.29	96.50	6.8	2.7	1.3
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	IS7	04:18:59	1.0	Surface	1	1	24.84	8.11	26.19	96.60	6.8	2.2	1.2
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	IS7	04:18:44	1.0	Surface	1	2	24.82	8.11	26.21	96.20	6.8	2.2	1.2
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	IS7	04:18:51	2.3	Bottom	3	1	24.80	8.09	26.25	96.20	6.8	2.7	1.2
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	IS7	04:18:36	2.3	Bottom	3	2	24.79	8.09	26.27	95.90	6.8	2.7	1.2

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	IS8(N)	03:45:53	1.0	Surface	1	1	24.80	8.09	26.18	97.30	6.9	2.5	1.2
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	IS8(N)	03:45:16	1.0	Surface	1	2	24.82	8.09	26.17	96.40	6.8	2.5	1.2
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	IS8(N)	03:45:24	3.1	Bottom	3	1	24.75	8.07	26.34	95.90	6.8	2.7	1.8
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	IS8(N)	03:45:05	3.1	Bottom	3	2	24.75	8.08	26.36	95.30	6.8	2.9	1.8
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	IS(Mf)9	04:09:06	1.0	Surface	1	1	24.85	8.10	26.18	96.20	6.8	2.3	1.4
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	IS(Mf)9	04:09:22	1.0	Surface	1	2	24.86	8.11	26.17	96.60	6.8	2.3	1.4
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	IS(Mf)9	04:09:13	2.5	Bottom	3	1	24.82	8.08	26.28	95.70	6.8	2.9	1.7
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	IS(Mf)9	04:08:56	2.5	Bottom	3	2	24.76	8.09	26.28	95.20	6.7	2.8	1.7
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	IS10(N)	04:00:47	1.0	Surface	1	1	25.19	8.09	25.95	92.90	6.6	2.9	1.4
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	IS10(N)	04:01:28	1.0	Surface	1	2	25.21	8.08	25.99	92.90	6.6	2.9	1.4
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	IS10(N)	04:01:13	5.5	Middle	2	1	25.07	8.04	28.28	84.60	6.0	3.3	1.1
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	IS10(N)	04:00:32	5.5	Middle	2	2	25.07	8.04	28.28	85.00	6.0	3.2	1.1
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	IS10(N)	04:01:02	9.9	Bottom	3	1	25.10	8.05	28.31	84.90	6.0	3.4	1.4
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	IS10(N)	04:00:20	9.9	Bottom	3	2	25.08	8.05	28.34	85.00	6.0	3.3	1.4
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	SR3(N)	04:51:49	1.0	Surface	1	1	24.81	8.11	27.75	95.60	6.8	2.5	1.1
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	SR3(N)	04:51:33	1.0	Surface	1	2	24.81	8.11	27.76	94.60	6.7	2.6	1.1
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	SR3(N)	04:51:40	2.4	Bottom	3	1	24.80	8.11	27.83	94.50	6.7	3.0	1.0
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	SR3(N)	04:51:25	2.4	Bottom	3	2	24.75	8.10	27.85	93.40	6.6	3.2	1.0
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	SR4(N3)	03:54:01	1.0	Surface	1	1	24.79	8.09	26.17	95.90	6.8	2.1	0.7
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	SR4(N3)	03:54:21	1.0	Surface	1	2	24.83	8.10	26.17	95.60	6.8	2.1	0.7
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	SR4(N3)	03:54:12	2.9	Bottom	3	1	24.75	8.06	26.34	95.40	6.8	2.5	0.6
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	SR4(N3)	03:53:51	2.9	Bottom	3	2	24.73	8.08	26.36	95.70	6.8	2.3	0.6
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	SR5(N)	04:10:45	1	Surface	1	1	25.19	8.08	25.99	91.70	6.5	2.9	1.0
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	SR5(N)	04:10:03	1	Surface	1	2	25.19	8.08	25.94	91.80	6.5	2.9	1.0
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	SR5(N)	04:10:31	4.7	Middle	2	1	25.10	8.04	28.23	84.20	5.9	3.1	1.1
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	SR5(N)	04:09:50	4.7	Middle	2	2	25.10	8.04	28.23	84.40	6.0	3.2	1.1
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	SR5(N)	04:10:22	8.4	Bottom	3	1	25.09	8.04	28.33	84.30	5.9	3.3	0.8
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	SR5(N)	04:09:38	8.4	Bottom	3	2	25.08	8.04	28.34	84.50	6.0	3.4	0.8
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	SR10A(N)	03:09:24	1	Surface	1	1	25.28	8.07	26.19	91.00	6.4	2.0	0.7
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	SR10A(N)	03:08:39	1	Surface	1	2	25.29	8.05	25.96	91.00	6.4	2.1	0.7
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	SR10A(N)	03:08:22	6.7	Middle	2	1	25.10	8.04	28.58	83.50	5.9	2.4	<0.5
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	SR10A(N)	03:09:07	6.7	Middle	2	2	25.09	8.02	28.57	83.10	5.8	2.4	<0.5
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	SR10A(N)	03:08:11	12.3	Bottom	3	1	25.12	8.02	28.66	83.40	5.9	2.8	0.9
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	SR10A(N)	03:08:56	12.3	Bottom	3	2	25.13	8.02	28.68	83.20	5.8	2.8	0.9
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	SR10B(N2)	02:59:15	1.0	Surface	1	1	25.29	8.05	26.25	95.60	6.7	2.1	1.1
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	SR10B(N2)	02:58:36	1.0	Surface	1	2	25.30	8.04	26.24	95.70	6.7	2.1	1.1
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	SR10B(N2)	02:58:18	3.8	Middle	2	1	25.16	8.02	28.44	86.30	6.1	2.4	1.2
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	SR10B(N2)	02:59:02	3.8	Middle	2	2	25.17	8.02	28.39	85.10	6.0	2.4	1.2
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	SR10B(N2)	02:58:51	6.5	Bottom	3	1	25.16	8.03	28.62	84.60	5.9	2.7	0.9
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	SR10B(N2)	02:58:06	6.5	Bottom	3	2	24.93	8.02	28.65	84.80	6.0	2.7	0.9
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	CS2(A)	05:01:30	1	Surface	1	1	25.15	8.09	25.72	93.00	6.6	3.2	1.4
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	CS2(A)	05:00:52	1	Surface	1	2	25.15	8.09	25.88	92.70	6.6	3.2	1.4
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	CS2(A)	05:01:18	3.4	Middle	2	1	25.07	8.08	28.14	85.50	6.0	3.4	1.1
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	CS2(A)	05:00:40	3.4	Middle	2	2	25.09	8.09	28.12	84.90	6.0	3.4	1.1
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	CS2(A)	05:01:06	5.7	Bottom	3	1	25.07	8.08	28.31	84.60	6.0	3.5	1.2
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	CS2(A)	05:00:28	5.7	Bottom	3	2	25.05	8.08	28.31	84.50	6.0	3.5	1.2
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	CS(Mf)5	03:03:09	1.0	Surface	1	1	24.81	8.08	26.26	95.70	6.8	2.7	1.1
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	CS(Mf)5	03:03:53	1.0	Surface	1	2	24.81	8.08	26.25	96.20	6.8	2.5	1.1
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	CS(Mf)5	03:03:37	6.3	Middle	2	1	24.59	8.07	28.18	87.90	6.2	2.8	1.0
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	CS(Mf)5	03:02:54	6.3	Middle	2	2	24.61	8.07	28.18	88.10	6.2	2.9	1.0
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	CS(Mf)5	03:02:44	11.6	Bottom	3	1	24.60	8.06	28.18	87.10	6.2	3.1	1.1
HKLR	HY/2011/03	2025-05-07	Mid-Flood	Rainy	CS(Mf)5	03:03:26	11.6	Bottom	3	2	24.59	8.07	28.21	86.70	6.1	3.0	1.1
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	IS5	10:37:37	1.0	Surface	1	1	24.94	8.05	26.83	96.60	6.9	2.7	2.4
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	IS5	10:38:14	1.0	Surface	1	2	24.97	8.04	26.83	97.10	6.9	2.9	2.4
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	IS5	10:37:25	4.2	Middle	2	1	24.82	8.03	27.81	92.80	6.6	3.3	3.3
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	IS5	10:38:01	4.2	Middle	2	2	24.84	8.03	27.80	93.00	6.7	3.2	3.3
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	IS5	10:37:16	7.4	Bottom	3	1	24.82	8.03	27.84	92.70	6.6	3.4	4.3
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	IS5	10:37:50	7.4	Bottom	3	2	24.83	8.02	27.83	93.00	6.7	3.3	4.3
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	IS(Mf)6	10:47:13	1.0	Surface	1	1	24.97	8.05	26.82	99.20	7.1	2.9	3.6
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	IS(Mf)6	10:46:55	1.0	Surface	1	2	24.96	8.05	26.80	98.30	7.0	2.9	3.6
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	IS(Mf)6	10:47:04	2.2	Bottom	3	1	24.93	8.05	26.89	97.50	7.0	3.0	3.8
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	IS(Mf)6	10:46:46	2.2	Bottom	3	2	24.90	8.06	26.89	96.20	6.9	3.0	3.8
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	IS7	10:56:08	1.0	Surface	1	1	24.97	8.07	26.83	98.70	7.1	2.2	5.2
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	IS7	10:55:50	1.0	Surface	1	2	24.96	8.06	26.83	98.40	7.0	2.3	5.2
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	IS7	10:55:42	2.3	Bottom	3	1	24.90	8.06	26.93	97.70	7.0	3.0	3.2
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	IS7	10:55:58	2.3	Bottom	3	2	24.93	8.06	26.90	97.90	7.0	2.9	3.2
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	IS8(N)	11:29:51	1.0	Surface	1	1	24.96	8.02	26.80	96.40	6.9	2.6	4.4
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	IS8(N)	11:30:10	1.0	Surface	1	2	24.98	8.04	26.78	97.00	6.9	2.5	4.4
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	IS8(N)	11:30:01	3.0	Bottom	3	1	24.94	8.02	26.88	96.30	6.9	2.7	3.9
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	IS8(N)	11:29:42	3.0	Bottom	3	2	24.90	8.02	26.92	95.80	6.9	2.7	3.9
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	IS(Mf)9	11:07:10	1.0	Surface	1	1	24.96	8.05	26.83	98.00	7.0	2.5	2.6
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	IS(Mf)9	11:06:49	1.0	Surface	1	2	24.96	8.05	26.83	97.60	7.0	2.6	2.6
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	IS(Mf)9	11:07:00	2.6	Bottom	3	1	24.92	8.05	26.94	97.60	7.0	3.1	2.5
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	IS(Mf)9	11:06:43	2.6	Bottom	3	2	24.89	8.04	26.94	97.30	7.0	3.1	2.5
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	IS10(N)	11:31:58	1.0	Surface	1	1	25.09	8.06	26.94	93.30	6.6	2.0	4.0
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	IS10(N)	11:31:17	1.0	Surface	1	2	25.07	8.06	26.96	92.80	6.6	2.0	4.0
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	IS10(N)	11:31:05	5.3	Middle	2	1	24.91	8.04	28.08	88.70	6.3	2.6	4.0
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	IS10(N)	11:31:44	5.3	Middle	2	2	24.91	8.04	28.11	88.90	6.3	2.6	4.0
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	IS10(N)	11:31:32	9.5	Bottom	3	1	24.93	8.04	28.17	88.60	6.3	3.0	4.2
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	IS10(N)	11:31:00	9.5	Bottom	3	2	24.92	8.04	28.17	88.80	6.3	2.8	4.2
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	SR3(N)	10:21:44	1.0	Surface	1	1	24.96	8.05	27.56	98.80	7.1	3.1	4.2
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	SR3(N)	10:21:26	1.0	Surface	1	2	24.97	8.04	27.55	97.80	7.0	3.1	4.2
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	SR3(N)	10:21:16	2.3	Bottom	3	1	24.94	8.04	27.60	96.20	6.8	3.4	5.0
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	SR3(N)	10:21:33	2.3	Bottom	3	2	24.94	8.05	27.59	97.20	7.0	3.3	5.0
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	SR4(N3)	11:21:12	1.0	Surface	1	1	24.96	8.04	26.81	96.60	6.9	2.0	3.5
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	SR4(N3)	11:20:54	1.0	Surface	1	2	24.97	8.04	26.80	96.40	6.9	2.2	3.5
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	SR4(N3)	11:21:03	2.8	Bottom	3	1	24.94	8.02	26.90	95.90	6.9	2.6	2.4
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	SR4(N3)	11:20:45	2.8	Bottom	3	2	24.69	8.02	26.90	95.40	6.8	2.6	2.4
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	SR5(N)	11:21:48	1.0	Surface	1	1	25.09	8.07	26.74	93.90	6.7	2.2	4.1
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	SR5(N)	11:21:07	1.0	Surface	1	2	25.05	8.08	26.80	93.20	6.6	2.2	4.1
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	SR5(N)	11:21:36	4.7	Middle	2	1	24.94	8.05	28.01	88.80	6.3	2.6	3.8
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	SR5(N)	11:20:54	4.7	Middle	2	2	24.94	8.06	28.02	88.50	6.3	2.7	3.8
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	SR5(N)	11:21:23	8.3	Bottom	3	1	24.92	8.04	28.22	89.00	6.3	3.2	4.6
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	SR5(N)	11:20:42	8.3	Bottom	3	2	24.91	8.05	28.21	88.60	6.3	3.2	4.6
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	SR10A(N)	12:33:02	1.0	Surface	1	1	25.02	8.07	27.33	93.30	6.6	2.4	2.6
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	SR10A(N)	12:32:16	1.0	Surface	1	2	25.04	8.08	27.37	93.10	6.6	2.6	2.6
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	SR10A(N)	12:31:58	6.5	Middle	2	1	24.91	8.06	28.67	88.30	6.2	2.9	3.2
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	SR10A(N)	12:32:44	6.5	Middle	2	2	24.92	8.05	28.67	87.80	6.2	2.9	3.2
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	SR10A(N)	12:31:46	11.9	Bottom	3	1	24.92	8.07	28.69	88.40	6.2	3.2	2.6
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	SR10A(N)	12:32:33	11.9	Bottom	3	2	24.93	8.06	28.67	88.20	6.2	3.3	2.6
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	SR10B(N2)	12:44:24	1.0	Surface	1	1	25.04	8.07	27.38	92.30	6.5	2.3	3.7
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	SR10B(N2)	12:43:44	1.0	Surface	1	2	25.04	8.07	27.28	92.20	6.5	2.4	3.7
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	SR10B(N2)	12:43:32	3.8	Middle	2	1	24.98	8.06	28.51	88.20	6.2	2.7	4.4
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	SR10B(N2)	12:44:12	3.8	Middle	2	2	24.96	8.05	28.50	88.20	6.2	2.7	4.4
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	SR10B(N2)	12:43:22	6.5	Bottom	3	1	24.95	8.06	28.62	88.10	6.2	3.2	4.1
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	SR10B(N2)	12:43:57	6.5	Bottom	3	2	24.97	8.05	28.58	88.10	6.2	3.3	4.1
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	CS2(A)	10:25:22	1.0	Surface	1	1	24.99	8.07	26.90	95.90	6.8	2.2	4.0
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	CS2(A)	10:24:46	1.0	Surface	1	2	24.96	8.07	26.93	96.00	6.8	2.1	4.0
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	CS2(A)	10:24:35	3.3	Middle	2	1	24.87	8.06	28.12	90.50	6.4	3.0	4.6
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	CS2(A)	10:25:11	3.3	Middle	2	2	24.89	8.06	28.12	90.70	6.4	2.9	4.6
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	CS2(A)	10:24:24	5.6	Bottom	3	1	24.87	8.06	28.33	90.00	6.4	3.2	3.0
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	CS2(A)	10:25:01	5.6	Bottom	3	2	24.87	8.05	28.31	90.50	6.4	3.1	3.0
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	CS(Mf)5	12:13:50	1.0	Surface	1	1	24.96	8.05	26.96	93.00	6.6	2.3	3.2
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	CS(Mf)5	12:13:11	1.0	Surface	1	2	24.98	8.05	26.96	92.40	6.6	2.3	3.2
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	CS(Mf)5	12:12:55	6.3	Middle	2	1	24.65	8.01	28.21	87.90	6.3	2.5	3.7

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	CS(Mf)5	12:13:36	6.3	Middle	2	2	24.66	8.01	28.20	88.10	6.3	2.5	3.7
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	CS(Mf)5	12:13:27	11.6	Bottom	3	1	24.65	8.01	27.92	87.60	6.2	2.9	4.1
HKLR	HY/2011/03	2025-05-09	Mid-Ebb	Cloudy	CS(Mf)5	12:12:46	11.6	Bottom	3	2	24.65	8.01	28.20	87.60	6.2	2.9	4.1
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Rainy	IS5	05:39:54	1.0	Surface	1	1	24.72	8.05	27.07	93.80	6.6	2.5	3.7
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Rainy	IS5	05:39:09	1.0	Surface	1	2	24.74	8.05	27.07	95.00	6.7	2.5	3.7
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Rainy	IS5	05:38:58	4.2	Middle	2	1	24.58	8.02	28.08	88.80	6.3	3.0	3.6
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Rainy	IS5	05:39:42	4.2	Middle	2	2	24.57	8.02	28.08	89.40	6.3	3.0	3.6
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Rainy	IS5	05:39:25	7.4	Bottom	3	1	24.52	8.01	28.14	88.60	6.3	3.1	4.2
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Rainy	IS5	05:38:47	7.4	Bottom	3	2	24.57	8.02	28.13	88.20	6.2	3.0	4.2
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Rainy	IS(Mf)6	05:29:03	1.0	Surface	1	1	24.77	8.07	27.07	96.20	6.8	2.5	4.8
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Rainy	IS(Mf)6	05:28:46	1.0	Surface	1	2	24.76	8.07	27.07	95.90	6.8	2.5	4.8
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Rainy	IS(Mf)6	05:28:53	2.3	Bottom	3	1	24.75	8.07	27.13	95.70	6.7	2.5	4.7
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Rainy	IS(Mf)6	05:28:34	2.3	Bottom	3	2	24.73	8.06	27.15	95.60	6.7	2.6	4.7
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Rainy	IS7	05:19:17	1.0	Surface	1	1	24.78	8.07	27.06	95.90	6.8	2.1	4.8
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Rainy	IS7	05:19:02	1.0	Surface	1	2	24.76	8.07	27.08	95.50	6.7	2.1	4.8
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Rainy	IS7	05:19:09	2.3	Bottom	3	1	24.75	8.06	27.12	95.50	6.7	2.4	4.1
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Rainy	IS7	05:18:54	2.3	Bottom	3	2	24.74	8.06	27.13	95.20	6.7	2.5	4.1
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Rainy	IS8(N)	04:44:53	1.0	Surface	1	1	24.75	8.06	27.03	95.80	6.8	2.5	3.6
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Rainy	IS8(N)	04:45:33	1.0	Surface	1	2	24.74	8.06	27.04	96.70	6.8	2.5	3.6
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Rainy	IS8(N)	04:45:01	3.0	Bottom	3	1	24.71	8.04	27.19	95.40	6.7	2.9	4.2
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Rainy	IS8(N)	04:44:43	3.0	Bottom	3	2	24.70	8.05	27.21	94.60	6.7	3.2	4.2
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Rainy	IS(Mf)9	05:09:32	1.0	Surface	1	1	24.78	8.07	27.04	95.90	6.8	2.2	3.7
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Rainy	IS(Mf)9	05:09:17	1.0	Surface	1	2	24.78	8.07	27.05	95.50	6.7	2.2	3.7
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Rainy	IS(Mf)9	05:09:24	2.5	Bottom	3	1	24.76	8.05	27.14	95.10	6.7	3.3	4.5
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Rainy	IS(Mf)9	05:09:07	2.5	Bottom	3	2	24.72	8.06	27.14	94.50	6.7	3.2	4.5
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Cloudy	IS10(N)	05:10:09	1.0	Surface	1	1	24.93	8.07	26.91	93.40	6.6	3.0	4.2
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Cloudy	IS10(N)	05:10:48	1.0	Surface	1	2	24.94	8.06	26.93	93.40	6.6	3.0	4.2
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Cloudy	IS10(N)	05:10:34	5.4	Middle	2	1	24.86	8.03	28.20	88.40	6.3	3.5	5.2
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Cloudy	IS10(N)	05:09:54	5.4	Middle	2	2	24.86	8.03	28.19	88.80	6.3	3.8	5.2
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Cloudy	IS10(N)	05:10:23	9.8	Bottom	3	1	24.88	8.04	28.22	88.80	6.3	3.6	3.8
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Cloudy	IS10(N)	05:09:43	9.8	Bottom	3	2	24.87	8.04	28.24	88.90	6.3	3.8	3.8
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Rainy	SR3(N)	05:51:23	1.0	Surface	1	1	24.76	8.07	27.81	94.00	6.6	2.9	3.2
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Rainy	SR3(N)	05:51:38	1.0	Surface	1	2	24.76	8.07	27.80	94.80	6.7	2.7	3.2
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Rainy	SR3(N)	05:51:30	2.4	Bottom	3	1	24.75	8.06	27.87	93.80	6.6	3.0	2.9
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Rainy	SR3(N)	05:51:14	2.4	Bottom	3	2	24.71	8.06	27.89	92.70	6.5	3.0	2.9
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Rainy	SR4(N3)	04:54:12	1.0	Surface	1	1	24.77	8.06	27.03	95.00	6.7	2.0	3.1
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Rainy	SR4(N3)	04:53:53	1.0	Surface	1	2	24.74	8.05	27.03	95.20	6.7	2.0	3.1
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Rainy	SR4(N3)	04:54:04	2.9	Bottom	3	1	24.71	8.03	27.19	94.80	6.7	2.3	4.3
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Rainy	SR4(N3)	04:53:43	2.9	Bottom	3	2	24.69	8.05	27.22	95.10	6.7	2.2	4.3
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Cloudy	SR5(N)	05:19:40	1	Surface	1	1	24.94	8.06	26.95	92.00	6.5	3.2	3.0
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Cloudy	SR5(N)	05:18:58	1	Surface	1	2	24.94	8.06	26.92	92.10	6.5	3.2	3.0
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Cloudy	SR5(N)	05:19:26	4.7	Middle	2	1	24.88	8.04	28.14	87.80	6.2	3.4	4.6
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Cloudy	SR5(N)	05:18:45	4.7	Middle	2	2	24.89	8.04	28.14	88.10	6.2	3.3	4.6
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Cloudy	SR5(N)	05:18:33	8.4	Bottom	3	1	24.86	8.03	28.25	88.40	6.3	3.4	5.2
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Cloudy	SR5(N)	05:19:17	8.4	Bottom	3	2	24.87	8.03	28.24	88.10	6.2	3.5	5.2
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Cloudy	SR10A(N)	04:19:10	1	Surface	1	1	25.01	8.05	27.16	91.70	6.5	2.1	3.6
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Cloudy	SR10A(N)	04:18:25	1	Surface	1	2	25.02	8.04	27.04	91.50	6.5	2.0	3.6
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Cloudy	SR10A(N)	04:18:08	6.5	Middle	2	1	24.90	8.03	28.45	87.30	6.2	2.3	3.5
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Cloudy	SR10A(N)	04:18:52	6.5	Middle	2	2	24.89	8.02	28.44	86.80	6.1	2.3	3.5
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Cloudy	SR10A(N)	04:18:41	12.0	Bottom	3	1	24.93	8.02	28.53	87.10	6.1	3.2	3.1
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Cloudy	SR10A(N)	04:17:57	12.0	Bottom	3	2	24.91	8.02	28.51	87.50	6.2	3.2	3.1
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Cloudy	SR10B(N2)	04:08:50	1.0	Surface	1	1	25.03	8.04	27.18	95.80	6.8	2.2	2.3
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Cloudy	SR10B(N2)	04:08:10	1.0	Surface	1	2	25.03	8.03	27.17	95.70	6.8	2.3	2.3
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Cloudy	SR10B(N2)	04:07:52	3.8	Middle	2	1	24.94	8.01	28.34	90.20	6.4	2.3	2.4
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Cloudy	SR10B(N2)	04:08:36	3.8	Middle	2	2	24.95	8.02	28.28	88.80	6.3	2.3	2.4
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Cloudy	SR10B(N2)	04:08:25	6.6	Bottom	3	1	24.93	8.02	28.48	88.30	6.2	2.9	2.2
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Cloudy	SR10B(N2)	04:07:40	6.6	Bottom	3	2	24.81	8.01	28.51	88.40	6.2	2.9	2.2
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Cloudy	CS2(A)	06:09:31	1	Surface	1	1	24.89	8.07	26.81	93.30	6.6	2.5	3.9
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Cloudy	CS2(A)	06:08:54	1	Surface	1	2	24.89	8.07	26.89	93.10	6.6	2.4	3.9
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Cloudy	CS2(A)	06:09:19	3.4	Middle	2	1	24.84	8.06	28.06	89.20	6.3	2.9	3.1
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Cloudy	CS2(A)	06:08:42	3.4	Middle	2	2	24.86	8.07	28.05	88.70	6.3	2.9	3.1
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Cloudy	CS2(A)	06:09:08	5.7	Bottom	3	1	24.83	8.06	28.21	88.60	6.3	3.3	3.7
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Cloudy	CS2(A)	06:08:30	5.7	Bottom	3	2	24.82	8.06	28.21	88.50	6.3	3.2	3.7
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Rainy	CS(Mf)5	04:03:44	1.0	Surface	1	1	24.76	8.04	27.15	95.40	6.7	2.2	3.1
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Rainy	CS(Mf)5	04:04:26	1.0	Surface	1	2	24.76	8.04	27.12	95.60	6.7	2.0	3.1
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Rainy	CS(Mf)5	04:04:11	6.3	Middle	2	1	24.59	8.03	28.19	90.40	6.4	2.6	2.5
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Rainy	CS(Mf)5	04:03:28	6.3	Middle	2	2	24.61	8.02	28.19	90.90	6.4	2.9	2.5
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Rainy	CS(Mf)5	04:03:18	11.5	Bottom	3	1	24.61	8.02	28.22	89.80	6.3	3.3	4.7
HKLR	HY/2011/03	2025-05-09	Mid-Flood	Rainy	CS(Mf)5	04:04:00	11.5	Bottom	3	2	24.58	8.03	28.22	89.50	6.3	3.1	4.7
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	IS5	11:54:43	1.0	Surface	1	1	26.41	8.04	28.25	95.70	6.6	2.9	3.2
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	IS5	11:55:21	1.0	Surface	1	2	26.47	8.04	28.26	96.90	6.6	3.1	3.2
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	IS5	11:55:06	4.2	Middle	2	1	26.31	8.02	28.91	93.70	6.4	3.3	4.6
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	IS5	11:54:32	4.2	Middle	2	2	26.26	8.02	28.94	93.50	6.4	3.4	4.6
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	IS5	11:54:24	7.4	Bottom	3	1	26.27	8.02	28.95	93.90	6.4	3.5	4.8
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	IS5	11:54:56	7.4	Bottom	3	2	26.29	8.02	28.93	93.90	6.4	3.5	4.8
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	IS(Mf)6	12:05:46	1.0	Surface	1	1	26.34	8.04	28.22	96.50	6.6	2.8	4.0
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	IS(Mf)6	12:05:30	1.0	Surface	1	2	26.31	8.04	28.22	95.50	6.6	2.8	4.0
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	IS(Mf)6	12:05:39	2.2	Bottom	3	1	26.31	8.04	28.34	94.20	6.5	2.9	4.6
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	IS(Mf)6	12:05:22	2.2	Bottom	3	2	26.25	8.05	28.35	92.80	6.4	2.8	4.6
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	IS7	12:15:15	1.0	Surface	1	1	26.36	8.05	28.22	97.00	6.7	2.6	3.0
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	IS7	12:14:59	1.0	Surface	1	2	26.32	8.04	28.23	96.70	6.6	2.8	3.0
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	IS7	12:14:51	2.3	Bottom	3	1	26.26	8.04	28.40	96.30	6.6	3.2	3.8
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	IS7	12:15:05	2.3	Bottom	3	2	26.31	8.03	28.36	96.40	6.6	3.3	3.8
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	IS8(N)	12:50:53	1.0	Surface	1	1	26.30	8.00	28.18	94.40	6.5	2.7	3.3
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	IS8(N)	12:51:10	1.0	Surface	1	2	26.32	8.02	28.13	95.30	6.6	2.5	3.3
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	IS8(N)	12:51:01	3.0	Bottom	3	1	26.29	8.00	28.32	94.70	6.5	3.0	7.0
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	IS8(N)	12:50:45	3.0	Bottom	3	2	26.23	7.99	28.40	94.10	6.5	2.8	7.0
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	IS(Mf)9	12:25:50	1.0	Surface	1	1	26.35	8.03	28.22	96.60	6.6	2.4	3.6
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	IS(Mf)9	12:25:32	1.0	Surface	1	2	26.34	8.03	28.23	96.00	6.6	2.5	3.6
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	IS(Mf)9	12:25:41	2.5	Bottom	3	1	26.31	8.03	28.40	96.10	6.6	2.9	5.8
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	IS(Mf)9	12:25:25	2.5	Bottom	3	2	26.24	8.01	28.41	95.80	6.6	2.8	5.8
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	IS10(N)	12:30:44	1.0	Surface	1	1	26.03	8.07	28.47	88.70	6.2	2.6	5.7
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	IS10(N)	12:31:22	1.0	Surface	1	2	26.09	8.07	28.43	89.60	6.3	2.7	5.7
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	IS10(N)	12:31:09	5.3	Middle	2	1	25.63	8.03	29.42	86.90	6.1	2.9	3.5
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	IS10(N)	12:30:31	5.3	Middle	2	2	25.62	8.03	29.45	86.20	6.0	2.9	3.5
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	IS10(N)	12:30:58	9.5	Bottom	3	1	25.62	8.03	29.51	85.50	6.0	3.2	4.1
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	IS10(N)	12:30:26	9.5	Bottom	3	2	25.60	8.03	29.53	86.10	6.0	3.2	4.1
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	SR3(N)	11:38:40	1.0	Surface	1	1	26.43	8.04	28.57	97.20	6.7	3.0	4.2
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	SR3(N)	11:38:57	1.0	Surface	1	2	26.44	8.05	28.58	98.00	6.7	3.2	4.2
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	SR3(N)	11:38:46	2.2	Bottom	3	1	26.42	8.05	28.62	96.40	6.6	3.2	4.6
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	SR3(N)	11:38:30	2.2	Bottom	3	2	26.39	8.04	28.65	95.10	6.5	3.3	4.6
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	SR4(N3)	12:40:07	1.0	Surface	1	1	26.32	8.02	28.20	94.50	6.5	2.1	3.5
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	SR4(N3)	12:39:51	1.0	Surface	1	2	26.32	8.01	28.18	94.10	6.5	2.3	3.5
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	SR4(N3)	12:39:59	2.8	Bottom	3	1	26.29	8.00	28.36	93.40	6.4	2.6	4.3
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	SR4(N3)	12:39:43	2.8	Bottom	3	2	26.14	7.99	28.35	92.30	6.3	2.6	4.3
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	SR5(N)	12:20:14	1.0	Surface	1	1	26.04	8.09	28.38	91.50	6.4	2.5	4.0
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	SR5(N)	12:19:36	1.0	Surface	1	2	26.01	8.09	28.40	90.40	6.4	2.6	4.0
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	SR5(N)	12:20:04	4.6	Middle	2	1	25.69	8.04	29.31	85.90	6.0	3.1	4.0
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	SR5(N)	12:19:22	4.6	Middle	2	2	25.72	8.06	29.30	85.70	6.0	3.1	4.0
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	SR5(N)	12:19:10	8.2	Bottom	3	1	25.58	8.04	29.57	85.80	6.0	3.5	4.0
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	SR5(N)	12:19:53	8.2	Bottom	3	2	25.59	8.03	29.57	86.50	6.0	3.5	4.0
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	SR10A(N)	13:18:39	1.0	Surface	1	1	25.95	8.08	28.84	90.40	6.3	2.7	4.1
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	SR10A(N)	13:19:25	1.0	Surface	1	2	25.84	8.08	28.86	90.50	6.3	2.6	4.1
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	SR10A(N)	13:18:24	6.4	Middle	2	1	25.66	8.07	29.75	87.60	6.1	3.0	4.7
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	SR10A(N)	13:19:09	6.4	Middle	2	2	25.66	8.06	29.74	87.00	6.1	3.1	4.7

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	SR10A(N)	13:18:12	11.7	Bottom	3	1	25.65	8.07	29.78	88.20	6.1	3.2	4.5
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	SR10A(N)	13:18:55	11.7	Bottom	3	2	25.70	8.07	29.75	88.30	6.1	3.4	4.5
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	SR10B(N2)	13:29:13	1.0	Surface	1	1	25.93	8.08	28.88	90.70	6.3	2.6	3.6
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	SR10B(N2)	13:28:36	1.0	Surface	1	2	25.92	8.08	28.86	90.40	6.3	2.6	3.6
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	SR10B(N2)	13:29:01	4.1	Middle	2	1	25.76	8.05	29.59	87.90	6.1	2.8	3.7
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	SR10B(N2)	13:28:25	4.1	Middle	2	2	25.76	8.06	29.60	87.70	6.1	2.8	3.7
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	SR10B(N2)	13:28:14	7.1	Bottom	3	1	25.66	8.06	29.73	86.90	6.1	3.3	4.9
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	SR10B(N2)	13:28:48	7.1	Bottom	3	2	25.75	8.05	29.65	86.70	6.0	3.3	4.9
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	CS2(A)	11:31:32	1.0	Surface	1	1	26.00	8.07	28.45	95.00	6.7	2.7	3.2
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	CS2(A)	11:30:56	1.0	Surface	1	2	26.01	8.07	28.46	95.30	6.7	2.6	3.2
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	CS2(A)	11:30:44	3.3	Middle	2	1	25.73	8.07	29.25	90.20	6.3	3.4	5.6
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	CS2(A)	11:31:21	3.3	Middle	2	2	25.84	8.06	29.26	91.20	6.4	3.3	5.6
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	CS2(A)	11:31:09	5.5	Bottom	3	1	25.71	8.05	29.48	91.60	6.4	3.5	4.7
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	CS2(A)	11:30:34	5.5	Bottom	3	2	25.72	8.06	29.47	90.30	6.3	3.5	4.7
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	CS(Mf)5	13:33:23	1.0	Surface	1	1	26.16	8.00	28.22	89.60	6.1	2.8	5.2
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	CS(Mf)5	13:32:45	1.0	Surface	1	2	26.17	8.00	28.23	88.60	6.1	2.9	5.2
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	CS(Mf)5	13:32:30	6.3	Middle	2	1	25.18	7.92	29.87	84.10	5.8	3.1	5.4
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	CS(Mf)5	13:33:09	6.3	Middle	2	2	25.19	7.91	29.86	84.80	5.8	2.5	5.4
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	CS(Mf)5	13:33:00	11.6	Bottom	3	1	25.16	7.92	29.14	82.90	5.7	3.3	4.7
HKLR	HY/2011/03	2025-05-12	Mid-Ebb	Fine	CS(Mf)5	13:32:21	11.6	Bottom	3	2	25.14	7.92	29.90	82.90	5.7	3.3	4.7
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	IS5	06:21:18	1.0	Surface	1	1	26.00	7.99	28.31	88.10	6.0	2.8	5.8
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	IS5	06:20:34	1.0	Surface	1	2	26.06	8.00	28.29	89.70	6.1	2.6	5.8
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	IS5	06:20:23	4.2	Middle	2	1	25.57	7.93	29.29	85.10	5.8	3.4	3.4
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	IS5	06:21:07	4.2	Middle	2	2	25.52	7.92	29.32	85.20	5.8	3.4	3.4
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	IS5	06:20:49	7.4	Bottom	3	1	25.32	7.91	29.59	84.00	5.7	3.4	5.3
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	IS5	06:20:13	7.4	Bottom	3	2	25.59	7.91	29.53	84.10	5.7	3.4	5.3
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	IS(Mf)6	06:10:57	1.0	Surface	1	1	26.18	8.03	28.33	93.80	6.4	2.7	4.2
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	IS(Mf)6	06:10:41	1.0	Surface	1	2	26.15	8.03	28.35	93.70	6.4	2.7	4.2
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	IS(Mf)6	06:10:48	2.2	Bottom	3	1	26.14	8.03	28.43	93.60	6.4	2.9	3.8
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	IS(Mf)6	06:10:32	2.2	Bottom	3	2	26.10	8.02	28.48	93.40	6.4	2.9	3.8
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	IS7	06:01:56	1.0	Surface	1	1	26.13	8.03	28.37	92.80	6.3	2.3	4.7
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	IS7	06:02:11	1.0	Surface	1	2	26.17	8.03	28.32	93.40	6.4	2.4	4.7
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	IS7	06:02:03	2.3	Bottom	3	1	26.13	8.02	28.44	92.90	6.3	2.9	5.4
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	IS7	06:01:49	2.3	Bottom	3	2	26.09	8.02	28.45	92.80	6.3	2.8	5.4
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	IS8(N)	05:27:14	1.0	Surface	1	1	26.05	8.02	28.32	92.40	6.3	2.5	4.2
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	IS8(N)	05:26:40	1.0	Surface	1	2	26.09	8.02	28.29	91.80	6.3	2.6	4.2
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	IS8(N)	05:26:49	3.1	Bottom	3	1	26.01	8.00	28.55	91.90	6.3	2.9	3.1
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	IS8(N)	05:26:31	3.1	Bottom	3	2	26.04	8.02	28.58	90.20	6.1	2.9	3.1
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	IS(Mf)9	05:52:13	1.0	Surface	1	1	26.22	8.03	28.29	93.20	6.4	2.5	3.0
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	IS(Mf)9	05:52:00	1.0	Surface	1	2	26.22	8.04	28.31	92.60	6.3	2.4	3.0
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	IS(Mf)9	05:52:07	2.5	Bottom	3	1	26.21	8.03	28.44	91.80	6.2	3.3	3.8
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	IS(Mf)9	05:51:51	2.5	Bottom	3	2	26.10	8.04	28.43	90.60	6.2	3.3	3.8
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	IS10(N)	06:03:21	1.0	Surface	1	1	25.87	8.04	28.37	90.00	6.4	3.1	3.0
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	IS10(N)	06:03:56	1.0	Surface	1	2	25.90	8.05	28.39	89.90	6.4	3.1	3.0
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	IS10(N)	06:03:44	5.4	Middle	2	1	25.67	8.03	29.32	86.90	6.1	3.5	4.1
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	IS10(N)	06:03:07	5.4	Middle	2	2	25.70	8.04	29.28	87.30	6.1	3.6	4.1
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	IS10(N)	06:03:34	9.7	Bottom	3	1	25.74	8.04	29.43	87.70	6.1	3.6	4.8
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	IS10(N)	06:02:58	9.7	Bottom	3	2	25.69	8.03	29.40	88.10	6.2	3.7	4.8
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	SR3(N)	06:31:22	1.0	Surface	1	1	26.09	8.01	28.62	90.10	6.1	3.0	5.8
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	SR3(N)	06:31:36	1.0	Surface	1	2	26.13	8.02	28.58	91.00	6.2	2.7	5.8
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	SR3(N)	06:31:28	2.3	Bottom	3	1	26.10	8.00	28.79	89.30	6.1	2.9	3.8
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	SR3(N)	06:31:14	2.3	Bottom	3	2	25.97	7.99	28.86	87.90	6.0	3.0	3.8
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	SR4(N3)	05:36:33	1.0	Surface	1	1	26.11	8.02	28.28	91.90	6.3	2.4	2.8
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	SR4(N3)	05:36:14	1.0	Surface	1	2	26.04	8.01	28.30	92.00	6.3	2.5	2.8
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	SR4(N3)	05:36:24	2.9	Bottom	3	1	26.00	7.99	28.53	91.60	6.2	2.6	5.2
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	SR4(N3)	05:36:06	2.9	Bottom	3	2	25.99	8.01	28.58	92.00	6.3	2.7	5.2
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	SR5(N)	06:15:21	1	Surface	1	1	25.84	8.07	28.40	88.60	6.3	3.2	4.4
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	SR5(N)	06:14:43	1	Surface	1	2	25.84	8.07	28.39	88.90	6.3	3.3	4.4
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	SR5(N)	06:14:31	4.7	Middle	2	1	25.72	8.04	29.25	86.30	6.1	3.4	4.1
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	SR5(N)	06:15:08	4.7	Middle	2	2	25.70	8.04	29.25	85.70	6.0	3.5	4.1
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	SR5(N)	06:15:00	8.3	Bottom	3	1	25.65	8.03	29.47	86.20	6.0	3.6	4.3
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	SR5(N)	06:14:21	8.3	Bottom	3	2	25.61	8.02	29.49	86.70	6.1	3.5	4.3
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	SR10A(N)	04:59:30	1	Surface	1	1	25.81	8.06	28.63	90.30	6.4	2.6	3.3
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	SR10A(N)	04:58:47	1	Surface	1	2	25.92	8.07	28.46	89.10	6.3	2.6	3.3
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	SR10A(N)	04:59:10	6.4	Middle	2	1	25.66	8.02	29.51	85.70	6.0	2.8	4.6
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	SR10A(N)	04:58:31	6.4	Middle	2	2	25.66	8.03	29.53	86.20	6.0	2.9	4.6
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	SR10A(N)	04:59:01	11.8	Bottom	3	1	25.75	8.02	29.60	86.50	6.0	3.4	2.7
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	SR10A(N)	04:58:21	11.8	Bottom	3	2	25.64	8.02	29.60	86.80	6.1	3.4	2.7
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	SR10B(N2)	04:49:54	1.0	Surface	1	1	25.95	8.06	28.51	94.30	6.6	2.6	5.1
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	SR10B(N2)	04:49:13	1.0	Surface	1	2	25.95	8.05	28.53	93.60	6.6	2.6	5.1
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	SR10B(N2)	04:48:47	4.1	Middle	2	1	25.76	8.02	29.32	90.30	6.3	2.8	5.4
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	SR10B(N2)	04:49:39	4.1	Middle	2	2	25.77	8.02	29.13	88.80	6.3	2.7	5.4
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	SR10B(N2)	04:49:30	7.2	Bottom	3	1	25.67	8.03	29.53	87.70	6.2	3.2	4.3
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	SR10B(N2)	04:48:36	7.2	Bottom	3	2	25.61	8.02	29.56	87.80	6.1	3.1	4.3
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	CS2(A)	07:06:48	1	Surface	1	1	25.88	8.07	28.33	90.60	6.4	2.9	6.2
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	CS2(A)	07:06:13	1	Surface	1	2	25.85	8.08	28.36	90.20	6.4	2.8	6.2
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	CS2(A)	07:06:35	3.3	Middle	2	1	25.77	8.06	28.96	88.00	6.2	3.2	3.4
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	CS2(A)	07:06:03	3.3	Middle	2	2	25.79	8.07	28.96	87.60	6.2	3.2	3.4
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	CS2(A)	07:05:52	5.6	Bottom	3	1	25.70	8.05	29.27	87.50	6.2	3.4	3.9
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	CS2(A)	07:06:26	5.6	Bottom	3	2	25.73	8.05	29.27	87.90	6.2	3.5	3.9
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	CS(Mf)5	04:52:04	1.0	Surface	1	1	25.91	7.98	28.33	90.20	6.2	2.4	3.4
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	CS(Mf)5	04:52:45	1.0	Surface	1	2	25.92	7.98	28.30	90.90	6.1	2.4	3.4
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	CS(Mf)5	04:52:31	6.3	Middle	2	1	25.57	7.96	29.21	86.20	5.9	2.7	3.5
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	CS(Mf)5	04:51:49	6.3	Middle	2	2	25.63	7.96	29.18	87.20	5.9	3.0	3.5
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	CS(Mf)5	04:51:38	11.5	Bottom	3	1	25.67	7.95	29.34	85.50	5.8	3.3	3.8
HKLR	HY/2011/03	2025-05-12	Mid-Flood	Fine	CS(Mf)5	04:52:20	11.5	Bottom	3	2	25.49	7.95	29.41	85.90	5.8	3.1	3.8
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	IS5	12:45:38	1.0	Surface	1	1	26.56	8.05	28.83	97.40	6.5	2.7	3.6
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	IS5	12:44:58	1.0	Surface	1	2	26.44	8.05	28.83	95.70	6.4	2.5	3.6
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	IS5	12:45:22	4.2	Middle	2	1	26.30	8.04	29.44	94.60	6.4	3.2	4.1
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	IS5	12:44:48	4.2	Middle	2	2	26.25	8.03	29.46	94.20	6.3	3.2	4.1
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	IS5	12:44:40	7.4	Bottom	3	1	26.25	8.03	29.46	94.60	6.4	3.2	3.5
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	IS5	12:45:12	7.4	Bottom	3	2	26.27	8.03	29.44	94.70	6.4	3.1	3.5
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	IS(Mf)6	12:55:47	1.0	Surface	1	1	26.39	8.05	28.82	95.40	6.4	2.4	4.6
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	IS(Mf)6	12:55:32	1.0	Surface	1	2	26.34	8.05	28.81	94.10	6.3	2.3	4.6
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	IS(Mf)6	12:55:39	2.2	Bottom	3	1	26.34	8.05	29.02	92.40	6.2	2.9	5.0
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	IS(Mf)6	12:55:24	2.2	Bottom	3	2	26.27	8.06	29.00	90.10	6.1	2.8	5.0
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	IS7	13:04:25	1.0	Surface	1	1	26.39	8.05	28.82	97.00	6.5	2.6	5.4
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	IS7	13:04:08	1.0	Surface	1	2	26.35	8.04	28.85	96.40	6.5	2.9	5.4
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	IS7	13:04:01	2.2	Bottom	3	1	26.28	8.04	29.12	96.10	6.5	3.3	4.0
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	IS7	13:04:14	2.2	Bottom	3	2	26.33	8.04	29.05	96.40	6.5	3.3	4.0
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	IS8(N)	13:38:23	1.0	Surface	1	1	26.32	8.03	28.79	94.00	6.4	3.0	3.8
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	IS8(N)	13:38:37	1.0	Surface	1	2	26.32	8.04	28.74	95.00	6.4	2.8	3.8
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	IS8(N)	13:38:29	3.1	Bottom	3	1	26.31	8.03	28.99	94.40	6.4	3.2	6.0
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	IS8(N)	13:38:15	3.1	Bottom	3	2	26.21	8.02	29.11	93.90	6.3	3.2	6.0
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	IS(Mf)9	13:16:10	1.0	Surface	1	1	26.38	8.04	28.83	96.90	6.5	2.3	5.6
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	IS(Mf)9	13:15:53	1.0	Surface	1	2	26.37	8.04	28.83	96.00	6.5	2.4	5.6
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	IS(Mf)9	13:16:01	2.5	Bottom	3	1	26.33	8.03	29.12	96.20	6.5	2.8	3.8
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	IS(Mf)9	13:15:45	2.5	Bottom	3	2	26.25	8.02	29.12	95.90	6.5	2.6	3.8
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	IS10(N)	14:01:07	1.0	Surface	1	1	26.00	8.05	28.98	82.60	5.7	2.9	5.0
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	IS10(N)	14:01:42	1.0	Surface	1	2	26.08	8.05	28.93	83.70	5.8	2.9	5.0
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	IS10(N)	14:01:29	5.3	Middle	2	1	25.49	8.00	29.83	81.90	5.6	3.3	4.6
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	IS10(N)	14:00:55	5.3	Middle	2	2	25.47	8.00	29.87	81.10	5.6	3.2	4.6
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	IS10(N)	14:01:20	9.5	Bottom	3	1	25.45	8.00	29.95	80.10	5.5	3.5	5.2
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	IS10(N)	14:00:48	9.5	Bottom	3	2	25.45	8.00	29.95	80.80	5.6	3.3	5.2
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	SR3(N)	12:30:30	1.0	Surface	1	1	26.49	8.05	29.00	96.30	6.5	2.8	3.5

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	SR3(N)	12:30:48	1.0	Surface	1	2	26.51	8.06	29.02	97.60	6.6	3.0	3.5
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	SR3(N)	12:30:35	2.2	Bottom	3	1	26.48	8.06	29.08	95.40	6.4	2.9	3.8
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	SR3(N)	12:30:20	2.2	Bottom	3	2	26.42	8.05	29.11	93.00	6.2	3.1	3.8
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	SR4(N3)	13:31:14	1.0	Surface	1	1	26.32	8.04	28.84	93.90	6.3	2.6	4.0
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	SR4(N3)	13:31:00	1.0	Surface	1	2	26.32	8.03	28.79	93.40	6.3	2.8	4.0
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	SR4(N3)	13:31:07	2.7	Bottom	3	1	26.30	8.02	29.08	92.40	6.2	2.9	2.7
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	SR4(N3)	13:30:53	2.7	Bottom	3	2	26.21	8.01	29.03	90.90	6.1	2.8	2.7
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	SR5(N)	13:51:37	1.0	Surface	1	1	26.01	8.07	28.94	86.00	6.0	3.1	4.2
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	SR5(N)	13:50:57	1.0	Surface	1	2	25.98	8.07	28.93	84.80	5.9	3.1	4.2
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	SR5(N)	13:51:25	4.6	Middle	2	1	25.56	8.01	29.71	80.40	5.5	3.4	2.2
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	SR5(N)	13:50:42	4.6	Middle	2	2	25.62	8.03	29.68	80.30	5.5	3.5	2.2
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	SR5(N)	13:50:31	8.2	Bottom	3	1	25.41	8.01	29.99	80.30	5.5	3.7	5.2
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	SR5(N)	13:51:14	8.2	Bottom	3	2	25.43	8.00	29.99	81.10	5.6	3.8	5.2
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	SR10A(N)	14:52:09	1.0	Surface	1	1	25.90	8.06	29.34	84.80	5.9	2.6	5.5
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	SR10A(N)	14:52:53	1.0	Surface	1	2	25.74	8.07	29.39	84.60	5.8	2.7	5.5
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	SR10A(N)	14:51:56	6.5	Middle	2	1	25.53	8.05	30.06	83.00	5.7	3.1	5.2
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	SR10A(N)	14:52:39	6.5	Middle	2	2	25.54	8.05	30.04	82.70	5.7	3.2	5.2
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	SR10A(N)	14:51:44	12.0	Bottom	3	1	25.52	8.05	30.09	84.00	5.7	3.2	4.3
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	SR10A(N)	14:52:27	12.0	Bottom	3	2	25.59	8.06	30.06	84.30	5.8	3.5	4.3
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	SR10B(N2)	15:01:18	1.0	Surface	1	1	25.86	8.06	29.40	85.80	5.9	2.7	3.2
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	SR10B(N2)	15:00:40	1.0	Surface	1	2	25.85	8.06	29.41	85.30	5.8	2.7	3.2
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	SR10B(N2)	15:01:06	3.9	Middle	2	1	25.66	8.04	29.90	83.80	5.7	2.8	4.4
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	SR10B(N2)	15:00:28	3.9	Middle	2	2	25.65	8.04	29.91	83.70	5.8	2.8	4.4
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	SR10B(N2)	15:00:17	6.7	Bottom	3	1	25.52	8.04	30.06	82.40	5.6	3.1	3.2
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	SR10B(N2)	15:00:52	6.7	Bottom	3	2	25.64	8.04	29.96	82.20	5.6	3.1	3.2
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	CS2(A)	12:44:53	1.0	Surface	1	1	26.02	8.08	28.96	90.40	6.3	2.9	3.4
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	CS2(A)	12:45:28	1.0	Surface	1	2	25.99	8.08	28.96	90.00	6.3	2.9	3.4
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	CS2(A)	12:44:40	3.3	Middle	2	1	25.65	8.04	29.57	85.60	5.9	3.7	4.8
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	CS2(A)	12:45:17	3.3	Middle	2	2	25.80	8.04	29.59	86.90	6.0	3.5	4.8
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	CS2(A)	12:44:32	5.5	Bottom	3	1	25.64	8.04	29.80	86.00	5.9	3.7	3.7
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	CS2(A)	12:45:05	5.5	Bottom	3	2	25.63	8.03	29.81	87.70	6.0	3.6	3.7
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	CS(Mf)5	14:23:21	1.0	Surface	1	1	26.12	8.01	28.79	84.70	5.7	2.3	3.7
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	CS(Mf)5	14:22:44	1.0	Surface	1	2	26.13	8.01	28.79	83.60	5.6	2.5	3.7
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	CS(Mf)5	14:22:30	6.3	Middle	2	1	24.92	7.93	30.19	79.40	5.4	2.6	5.2
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	CS(Mf)5	14:23:07	6.3	Middle	2	2	24.92	7.92	30.18	80.40	5.4	2.4	5.2
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	CS(Mf)5	14:22:59	11.6	Bottom	3	1	24.89	7.92	28.73	78.80	5.3	3.0	5.9
HKLR	HY/2011/03	2025-05-14	Mid-Ebb	Fine	CS(Mf)5	14:22:20	11.6	Bottom	3	2	24.87	7.93	30.19	78.80	5.3	3.0	5.9
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	IS5	07:14:44	1.0	Surface	1	1	26.01	8.00	28.84	84.70	5.7	3.1	4.3
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	IS5	07:13:51	1.0	Surface	1	2	26.08	8.01	28.82	86.50	5.8	2.9	4.3
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	IS5	07:13:40	4.3	Middle	2	1	25.46	7.93	29.71	82.60	5.5	3.4	5.4
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	IS5	07:14:34	4.3	Middle	2	2	25.40	7.92	29.74	82.30	5.5	3.4	5.4
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	IS5	07:14:06	7.5	Bottom	3	1	25.16	7.91	29.96	80.50	5.4	3.6	4.8
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	IS5	07:13:31	7.5	Bottom	3	2	25.50	7.91	29.91	81.20	5.4	3.6	4.8
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	IS(Mf)6	07:03:39	1.0	Surface	1	1	26.22	8.04	28.88	93.50	6.3	2.9	4.7
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	IS(Mf)6	07:03:55	1.0	Surface	1	2	26.26	8.04	28.86	93.60	6.3	3.0	4.7
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	IS(Mf)6	07:03:30	2.3	Bottom	3	1	26.13	8.04	29.07	93.30	6.3	3.1	4.2
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	IS(Mf)6	07:03:46	2.3	Bottom	3	2	26.18	8.04	29.03	93.50	6.3	3.2	4.2
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	IS7	06:54:51	1.0	Surface	1	1	26.18	8.04	28.93	92.20	6.2	2.5	4.0
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	IS7	06:55:06	1.0	Surface	1	2	26.25	8.04	28.84	92.80	6.2	2.4	4.0
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	IS7	06:54:58	2.3	Bottom	3	1	26.18	8.03	29.04	92.30	6.2	3.5	4.1
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	IS7	06:54:44	2.3	Bottom	3	2	26.12	8.03	29.06	92.40	6.2	3.4	4.1
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	IS8(N)	06:13:01	1.0	Surface	1	1	26.17	8.03	28.82	89.50	6.0	2.6	3.4
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	IS8(N)	06:18:28	1.0	Surface	1	2	26.09	8.03	28.86	90.30	6.1	2.7	3.4
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	IS8(N)	06:13:10	3.3	Bottom	3	1	26.02	8.02	29.20	90.00	6.0	3.1	4.0
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	IS8(N)	06:12:50	3.3	Bottom	3	2	26.05	8.04	29.22	87.90	5.9	3.0	4.0
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	IS(Mf)9	06:43:58	1.0	Surface	1	1	26.28	8.06	28.83	91.80	6.1	2.6	4.9
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	IS(Mf)9	06:44:11	1.0	Surface	1	2	26.30	8.04	28.81	92.50	6.2	2.5	4.9
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	IS(Mf)9	06:43:50	2.5	Bottom	3	1	26.13	8.06	28.97	88.90	6.0	3.5	5.3
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	IS(Mf)9	06:44:05	2.5	Bottom	3	2	26.28	8.05	29.04	90.50	6.1	3.5	5.3
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	IS10(N)	06:41:08	1.0	Surface	1	1	25.83	8.04	28.83	83.60	5.8	3.0	4.2
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	IS10(N)	06:41:43	1.0	Surface	1	2	25.87	8.04	28.84	84.00	5.9	3.1	4.2
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	IS10(N)	06:41:29	5.4	Middle	2	1	25.57	8.01	29.62	81.80	5.7	3.5	4.6
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	IS10(N)	06:40:55	5.4	Middle	2	2	25.62	8.02	29.56	81.80	5.7	3.5	4.6
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	IS10(N)	06:40:46	9.7	Bottom	3	1	25.60	8.00	29.72	82.60	5.7	3.6	4.9
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	IS10(N)	06:41:20	9.7	Bottom	3	2	25.66	8.01	29.77	82.80	5.7	3.5	4.9
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	SR3(N)	07:24:31	1.0	Surface	1	1	26.12	8.02	28.99	88.10	5.9	3.4	5.9
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	SR3(N)	07:24:44	1.0	Surface	1	2	26.17	8.03	28.95	89.30	6.0	3.0	5.9
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	SR3(N)	07:24:38	2.3	Bottom	3	1	26.13	8.01	29.21	86.80	5.8	3.1	6.6
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	SR3(N)	07:24:24	2.3	Bottom	3	2	25.96	8.00	29.26	85.00	5.7	3.5	6.6
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	SR4(N3)	06:27:10	1.0	Surface	1	1	26.17	8.03	28.79	90.70	6.1	2.4	4.1
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	SR4(N3)	06:26:51	1.0	Surface	1	2	26.05	8.02	28.81	90.80	6.1	2.4	4.1
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	SR4(N3)	06:26:44	2.8	Bottom	3	1	25.97	8.03	29.23	91.00	6.1	3.0	3.4
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	SR4(N3)	06:27:00	2.8	Bottom	3	2	26.01	8.01	29.13	90.30	6.1	2.7	3.4
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	SR5(N)	06:51:49	1	Surface	1	1	25.77	8.05	28.86	82.80	5.8	3.3	3.4
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	SR5(N)	06:51:13	1	Surface	1	2	25.77	8.05	28.85	83.20	5.8	3.4	3.4
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	SR5(N)	06:51:37	4.7	Middle	2	1	25.61	8.02	29.54	80.70	5.6	3.5	3.7
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	SR5(N)	06:51:03	4.7	Middle	2	2	25.64	8.02	29.54	81.40	5.6	3.5	3.7
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	SR5(N)	06:50:52	8.3	Bottom	3	1	25.48	7.99	29.85	81.60	5.6	3.6	3.2
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	SR5(N)	06:51:29	8.3	Bottom	3	2	25.53	8.00	29.83	81.30	5.6	3.6	3.2
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	SR10A(N)	05:42:34	1	Surface	1	1	25.86	8.06	28.88	82.80	5.8	3.0	4.9
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	SR10A(N)	05:43:15	1	Surface	1	2	25.78	8.05	28.97	83.10	5.8	2.9	4.9
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	SR10A(N)	05:42:59	6.5	Middle	2	1	25.54	8.00	29.79	80.60	5.6	3.1	5.8
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	SR10A(N)	05:42:18	6.5	Middle	2	2	25.54	8.01	29.81	80.70	5.6	3.2	5.8
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	SR10A(N)	05:42:50	11.9	Bottom	3	1	25.65	8.00	29.88	81.70	5.6	3.4	6.3
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	SR10A(N)	05:42:07	11.9	Bottom	3	2	25.51	8.00	29.89	81.70	5.6	3.4	6.3
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	SR10B(N2)	05:33:55	1.0	Surface	1	1	25.90	8.06	28.90	87.50	6.0	2.9	6.2
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	SR10B(N2)	05:33:17	1.0	Surface	1	2	25.90	8.04	28.92	87.00	6.1	2.9	6.2
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	SR10B(N2)	05:32:47	3.9	Middle	2	1	25.67	8.00	29.56	84.70	5.9	3.2	3.7
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	SR10B(N2)	05:33:42	3.9	Middle	2	2	25.68	8.00	29.31	83.60	5.8	3.0	3.7
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	SR10B(N2)	05:33:34	6.7	Bottom	3	1	25.54	8.01	29.79	82.30	5.7	3.4	4.7
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	SR10B(N2)	05:32:36	6.7	Bottom	3	2	25.51	8.01	29.82	82.60	5.7	3.2	4.7
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	CS2(A)	07:42:21	1	Surface	1	1	25.86	8.05	28.83	84.80	5.9	3.1	5.2
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	CS2(A)	07:41:49	1	Surface	1	2	25.82	8.05	28.83	84.50	5.9	3.1	5.2
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	CS2(A)	07:42:10	3.3	Middle	2	1	25.74	8.03	29.18	83.10	5.8	3.3	4.5
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	CS2(A)	07:41:41	3.3	Middle	2	2	25.75	8.04	29.18	82.80	5.8	3.3	4.5
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	CS2(A)	07:41:29	5.5	Bottom	3	1	25.63	8.02	29.56	82.80	5.7	3.5	4.6
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	CS2(A)	07:42:01	5.5	Bottom	3	2	25.68	8.02	29.56	83.40	5.8	3.6	4.6
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	CS(Mf)5	05:42:59	1.0	Surface	1	1	25.90	8.00	28.85	86.40	5.8	2.4	3.8
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	CS(Mf)5	05:43:40	1.0	Surface	1	2	25.92	8.00	28.81	87.60	5.8	2.4	3.8
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	CS(Mf)5	05:43:26	6.3	Middle	2	1	25.46	7.98	29.62	83.30	5.6	2.6	5.9
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	CS(Mf)5	05:42:45	6.3	Middle	2	2	25.53	7.98	29.59	84.40	5.7	2.8	5.9
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	CS(Mf)5	05:43:15	11.6	Bottom	3	1	25.37	7.97	29.78	83.00	5.6	2.9	5.1
HKLR	HY/2011/03	2025-05-14	Mid-Flood	Fine	CS(Mf)5	05:42:34	11.6	Bottom	3	2	25.59	7.98	29.71	82.00	5.5	3.0	5.1
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	IS5	14:03:56	1.0	Surface	1	1	26.69	8.03	30.07	87.60	5.9	2.3	4.6
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	IS5	14:04:34	1.0	Surface	1	2	26.78	8.03	30.07	88.60	6.0	2.3	4.6
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	IS5	14:03:46	4.3	Middle	2	1	26.51	8.02	30.66	86.40	5.9	2.8	3.3
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	IS5	14:04:19	4.3	Middle	2	2	26.53	8.02	30.62	86.50	5.9	2.8	3.3
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	IS5	14:04:09	7.6	Bottom	3	1	26.52	8.01	30.68	86.40	5.9	2.9	4.1
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	IS5	14:03:37	7.6	Bottom	3	2	26.48	8.01	30.70	86.60	5.9	3.0	4.1
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	IS(Mf)6	14:16:10	1.0	Surface	1	1	26.70	8.03	30.12	88.70	6.0	2.2	4.6
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	IS(Mf)6	14:15:54	1.0	Surface	1	2	26.67	8.04	30.12	87.90	6.0	2.2	4.6
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	IS(Mf)6	14:16:02	2.2	Bottom	3	1	26.66	8.04	30.28	87.00	5.9	2.5	4.0
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	IS(Mf)6	14:15:46	2.2	Bottom	3	2	26.61	8.05	30.27	85.90	5.8	2.5	4.0
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	IS7	14:25:57	1.0	Surface	1	1	26.71	8.03	30.11	89.60	6.1	2.1	4.7
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	IS7	14:25:41	1.0	Surface	1	2	26.68	8.03	30.14	89.20	6.0	2.3	4.7

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	IS7	14:25:34	2.3	Bottom	3	1	26.63	8.03	30.36	88.90	6.0	2.6	6.3
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	IS7	14:25:48	2.3	Bottom	3	2	26.65	8.02	30.30	89.00	6.0	2.6	6.3
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	IS8(N)	14:58:13	1.0	Surface	1	1	26.67	8.02	30.08	87.00	5.9	2.3	5.8
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	IS8(N)	14:58:28	1.0	Surface	1	2	26.68	8.02	30.05	87.80	6.0	2.2	5.8
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	IS8(N)	14:58:20	3.1	Bottom	3	1	26.63	8.02	30.26	87.40	5.9	2.5	5.1
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	IS8(N)	14:58:04	3.1	Bottom	3	2	26.55	8.01	30.36	86.50	5.9	2.5	5.1
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	IS(Mf)9	14:34:37	1.0	Surface	1	1	26.71	8.03	30.11	89.20	6.0	2.0	4.4
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	IS(Mf)9	14:34:18	1.0	Surface	1	2	26.70	8.03	30.11	88.60	6.0	2.1	4.4
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	IS(Mf)9	14:34:27	2.6	Bottom	3	1	26.66	8.02	30.34	88.60	6.0	2.4	4.1
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	IS(Mf)9	14:34:09	2.6	Bottom	3	2	26.60	8.01	30.35	88.40	6.0	2.3	4.1
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	IS10(N)	15:08:06	1.0	Surface	1	1	26.43	8.03	29.64	81.50	5.6	2.7	4.2
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	IS10(N)	15:06:59	1.0	Surface	1	2	26.38	8.03	29.67	80.80	5.5	2.7	4.2
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	IS10(N)	15:06:46	5.2	Middle	2	1	26.06	8.00	30.43	79.50	5.4	2.9	5.0
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	IS10(N)	15:07:52	5.2	Middle	2	2	26.06	8.00	30.47	79.90	5.4	2.9	5.0
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	IS10(N)	15:07:25	9.4	Bottom	3	1	26.03	8.00	30.56	79.10	5.4	3.2	3.4
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	IS10(N)	15:06:36	9.4	Bottom	3	2	26.06	8.00	30.47	79.60	5.4	3.0	3.4
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	SR3(N)	13:50:29	1.0	Surface	1	1	26.75	8.04	30.16	89.40	6.1	2.5	3.7
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	SR3(N)	13:50:46	1.0	Surface	1	2	26.76	8.05	30.18	90.10	6.1	2.5	3.7
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	SR3(N)	13:50:34	2.2	Bottom	3	1	26.74	8.04	30.24	88.90	6.0	2.5	4.9
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	SR3(N)	13:50:18	2.2	Bottom	3	2	26.71	8.04	30.26	87.70	5.9	2.7	4.9
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	SR4(N3)	14:50:15	1.0	Surface	1	1	26.66	8.02	30.12	87.30	5.9	2.2	5.8
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	SR4(N3)	14:49:58	1.0	Surface	1	2	26.66	8.02	30.08	86.90	5.9	2.2	5.8
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	SR4(N3)	14:49:49	2.9	Bottom	3	1	26.42	8.01	30.30	85.40	5.8	2.4	3.7
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	SR4(N3)	14:50:07	2.9	Bottom	3	2	26.65	8.01	30.33	86.40	5.9	2.5	3.7
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	SR5(N)	14:56:02	1.0	Surface	1	1	26.37	8.04	29.60	81.80	5.6	2.5	5.4
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	SR5(N)	14:57:00	1.0	Surface	1	2	26.38	8.04	29.62	82.30	5.6	2.5	5.4
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	SR5(N)	14:55:46	4.8	Middle	2	1	26.14	8.02	30.29	79.30	5.4	2.7	3.8
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	SR5(N)	14:56:48	4.8	Middle	2	2	26.10	8.00	30.32	79.10	5.4	2.6	3.8
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	SR5(N)	14:56:17	8.5	Bottom	3	1	26.06	8.00	30.49	79.90	5.4	3.3	5.4
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	SR5(N)	14:55:36	8.5	Bottom	3	2	26.04	8.01	30.49	79.60	5.4	3.2	5.4
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	SR10A(N)	15:59:25	1.0	Surface	1	1	26.20	8.04	30.22	82.00	5.6	2.2	4.5
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	SR10A(N)	15:58:36	1.0	Surface	1	2	26.30	8.04	30.17	81.80	5.6	2.1	4.5
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	SR10A(N)	15:58:02	6.6	Middle	2	1	25.95	8.03	31.05	79.80	5.4	2.5	5.5
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	SR10A(N)	15:59:07	6.6	Middle	2	2	25.97	8.03	30.98	79.50	5.4	2.5	5.5
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	SR10A(N)	15:57:51	12.2	Bottom	3	1	25.95	8.03	31.11	80.50	5.5	2.6	5.2
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	SR10A(N)	15:58:55	12.2	Bottom	3	2	25.99	8.03	31.04	80.50	5.5	2.8	5.2
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	SR10B(N2)	16:10:46	1.0	Surface	1	1	26.26	8.04	30.24	82.00	5.6	2.2	5.7
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	SR10B(N2)	16:09:40	1.0	Surface	1	2	26.25	8.04	30.25	81.70	5.5	2.1	5.7
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	SR10B(N2)	16:09:27	3.7	Middle	2	1	26.08	8.02	30.75	80.40	5.5	2.4	6.2
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	SR10B(N2)	16:10:32	3.7	Middle	2	2	26.04	8.03	30.71	80.50	5.5	2.4	6.2
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	SR10B(N2)	16:09:53	6.4	Bottom	3	1	26.08	8.02	30.81	80.00	5.4	2.6	5.1
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	SR10B(N2)	16:09:16	6.4	Bottom	3	2	25.99	8.03	30.93	80.00	5.4	2.6	5.1
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	CS2(A)	14:03:34	1.0	Surface	1	1	26.37	8.05	29.62	84.80	5.8	2.4	5.2
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	CS2(A)	14:03:00	1.0	Surface	1	2	26.37	8.05	29.65	85.30	5.8	2.5	5.2
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	CS2(A)	14:02:30	3.4	Middle	2	1	26.15	8.03	30.19	82.20	5.6	3.0	4.4
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	CS2(A)	14:03:23	3.4	Middle	2	2	26.23	8.02	30.21	82.70	5.6	2.8	4.4
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	CS2(A)	14:03:12	5.7	Bottom	3	1	26.15	8.02	30.37	83.20	5.7	3.0	3.7
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	CS2(A)	14:02:20	5.7	Bottom	3	2	26.13	8.03	30.38	82.20	5.6	3.1	3.7
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	CS(Mf)5	15:40:40	1.0	Surface	1	1	26.56	8.08	29.95	80.70	5.5	2.2	4.9
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	CS(Mf)5	15:41:19	1.0	Surface	1	2	26.56	8.07	29.97	81.20	5.5	2.1	4.9
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	CS(Mf)5	15:41:05	6.3	Middle	2	1	25.75	8.01	31.06	78.00	5.3	2.2	3.0
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	CS(Mf)5	15:40:25	6.3	Middle	2	2	25.74	8.02	31.07	77.90	5.3	2.4	3.0
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	CS(Mf)5	15:40:16	11.6	Bottom	3	1	25.68	8.02	31.13	77.30	5.2	2.8	6.3
HKLR	HY/2011/03	2025-05-16	Mid-Ebb	Fine	CS(Mf)5	15:40:56	11.6	Bottom	3	2	25.73	8.01	29.99	77.10	5.2	2.9	6.3
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	IS5	08:36:35	1.0	Surface	1	1	26.43	8.02	30.14	81.20	5.5	2.6	4.9
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	IS5	08:35:48	1.0	Surface	1	2	26.49	8.02	30.13	82.40	5.5	2.4	4.9
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	IS5	08:35:35	4.3	Middle	2	1	25.98	8.01	30.80	79.60	5.3	2.8	6.2
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	IS5	08:36:23	4.3	Middle	2	2	25.96	8.00	30.81	79.20	5.3	2.8	6.2
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	IS5	08:36:03	7.5	Bottom	3	1	25.83	8.00	30.99	78.10	5.2	3.0	4.3
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	IS5	08:35:26	7.5	Bottom	3	2	25.95	8.01	30.96	78.70	5.3	3.0	4.3
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	IS(Mf)6	08:27:24	1.0	Surface	1	1	26.57	8.03	30.09	86.40	5.8	2.5	4.1
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	IS(Mf)6	08:27:08	1.0	Surface	1	2	26.55	8.03	30.09	86.30	5.8	2.5	4.1
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	IS(Mf)6	08:27:16	2.3	Bottom	3	1	26.51	8.03	30.25	86.20	5.8	2.6	4.1
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	IS(Mf)6	08:27:00	2.3	Bottom	3	2	26.47	8.03	30.28	86.20	5.8	2.6	4.1
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	IS7	08:17:56	1.0	Surface	1	1	26.54	8.03	30.15	85.70	5.8	2.4	5.7
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	IS7	08:18:11	1.0	Surface	1	2	26.58	8.03	30.08	86.10	5.8	2.3	5.7
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	IS7	08:18:03	2.3	Bottom	3	1	26.52	8.02	30.26	85.60	5.8	2.9	5.7
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	IS7	08:17:48	2.3	Bottom	3	2	26.47	8.02	30.27	85.70	5.8	2.8	5.7
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	IS8(N)	07:45:34	1.0	Surface	1	1	26.48	8.02	30.05	84.70	5.7	2.4	4.5
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	IS8(N)	07:44:43	1.0	Surface	1	2	26.53	8.02	30.02	84.60	5.7	2.4	4.5
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	IS8(N)	07:44:50	3.1	Bottom	3	1	26.43	8.01	30.33	84.60	5.7	2.7	3.6
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	IS8(N)	07:44:32	3.1	Bottom	3	2	26.38	8.02	30.36	83.30	5.6	2.6	3.6
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	IS(Mf)9	08:08:20	1.0	Surface	1	1	26.59	8.03	30.02	85.80	5.8	2.3	4.5
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	IS(Mf)9	08:08:06	1.0	Surface	1	2	26.59	8.05	30.03	85.40	5.8	2.4	4.5
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	IS(Mf)9	08:08:14	2.6	Bottom	3	1	26.56	8.03	30.26	84.70	5.7	2.8	6.4
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	IS(Mf)9	08:07:57	2.6	Bottom	3	2	26.42	8.04	30.21	83.80	5.6	2.9	6.4
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	IS10(N)	08:04:59	1.0	Surface	1	1	26.26	8.02	29.93	80.70	5.5	2.4	4.2
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	IS10(N)	08:05:40	1.0	Surface	1	2	26.28	8.02	29.94	81.00	5.5	2.5	4.2
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	IS10(N)	08:05:22	5.4	Middle	2	1	26.06	8.00	30.56	78.90	5.4	2.8	6.1
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	IS10(N)	08:04:43	5.4	Middle	2	2	26.08	8.01	30.54	79.20	5.4	2.8	6.1
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	IS10(N)	08:04:34	9.7	Bottom	3	1	26.06	8.00	30.67	79.20	5.4	3.0	4.8
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	IS10(N)	08:05:13	9.7	Bottom	3	2	26.10	8.00	30.66	79.40	5.4	2.9	4.8
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	SR3(N)	08:50:06	1.0	Surface	1	1	26.51	8.03	30.22	83.80	5.6	2.7	6.3
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	SR3(N)	08:50:20	1.0	Surface	1	2	26.53	8.03	30.19	84.40	5.7	2.5	6.3
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	SR3(N)	08:50:13	2.3	Bottom	3	1	26.49	8.02	30.38	83.10	5.6	2.6	6.4
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	SR3(N)	08:49:58	2.3	Bottom	3	2	26.40	8.01	30.42	82.10	5.5	2.8	6.4
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	SR4(N3)	07:54:00	1.0	Surface	1	1	26.52	8.02	30.00	84.50	5.7	2.3	4.2
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	SR4(N3)	07:53:43	1.0	Surface	1	2	26.45	8.02	30.01	84.70	5.7	2.3	4.2
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	SR4(N3)	07:53:52	2.9	Bottom	3	1	26.43	8.01	30.28	84.20	5.7	2.5	5.1
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	SR4(N3)	07:53:34	2.9	Bottom	3	2	26.37	8.02	30.37	84.60	5.7	2.6	5.1
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	SR5(N)	08:15:32	1	Surface	1	1	26.20	8.03	30.00	80.10	5.5	2.6	5.0
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	SR5(N)	08:14:50	1	Surface	1	2	26.21	8.03	29.97	80.30	5.5	2.7	5.0
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	SR5(N)	08:15:19	4.9	Middle	2	1	26.10	8.01	30.48	78.60	5.3	2.7	3.5
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	SR5(N)	08:14:38	4.9	Middle	2	2	26.11	8.01	30.49	79.00	5.4	2.7	3.5
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	SR5(N)	08:14:27	8.8	Bottom	3	1	26.02	7.99	30.69	79.20	5.4	2.9	5.0
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	SR5(N)	08:15:09	8.8	Bottom	3	2	26.05	8.00	30.66	79.10	5.4	3.0	5.0
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	SR10A(N)	07:13:23	1	Surface	1	1	26.28	8.03	29.95	80.00	5.5	2.2	3.9
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	SR10A(N)	07:14:09	1	Surface	1	2	26.23	8.03	30.02	79.80	5.5	2.2	3.9
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	SR10A(N)	07:13:52	6.8	Middle	2	1	26.01	7.99	30.77	77.90	5.3	2.4	4.0
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	SR10A(N)	07:13:05	6.8	Middle	2	2	26.01	8.00	30.78	78.10	5.3	2.4	4.0
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	SR10A(N)	07:12:53	12.5	Bottom	3	1	25.99	7.99	30.87	78.40	5.3	2.8	3.9
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	SR10A(N)	07:13:41	12.5	Bottom	3	2	26.06	7.99	30.85	78.40	5.3	2.8	3.9
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	SR10B(N2)	07:03:47	1.0	Surface	1	1	26.29	8.03	29.97	83.80	5.7	2.1	4.6
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	SR10B(N2)	07:03:08	1.0	Surface	1	2	26.30	8.02	29.95	83.20	5.7	2.1	4.6
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	SR10B(N2)	07:02:45	3.9	Middle	2	1	26.12	7.99	30.49	81.40	5.5	2.5	4.3
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	SR10B(N2)	07:03:33	3.9	Middle	2	2	26.13	7.99	30.36	80.50	5.5	2.4	4.3
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	SR10B(N2)	07:03:23	6.7	Bottom	3	1	26.06	8.00	30.73	79.40	5.4	2.7	3.9
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	SR10B(N2)	07:02:32	6.7	Bottom	3	2	25.99	7.99	30.79	79.40	5.4	2.6	3.9
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	CS2(A)	08:57:21	1	Surface	1	1	26.25	8.03	29.96	81.20	5.6	2.6	4.8
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	CS2(A)	08:56:47	1	Surface	1	2	26.24	8.03	29.95	81.00	5.5	2.6	4.8
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	CS2(A)	08:57:08	3.4	Middle	2	1	26.17	8.01	30.25	80.20	5.5	2.8	3.2
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	CS2(A)	08:56:36	3.4	Middle	2	2	26.18	8.02	30.24	80.00	5.5	2.8	3.2
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	CS2(A)	08:56:59	5.8	Bottom	3	1	26.15	8.01	30.47	80.30	5.5	3.1	5.8
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	CS2(A)	08:56:24	5.8	Bottom	3	2	26.11	8.01	30.48	79.90	5.5	3.0	5.8
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	CS(Mf)5	07:04:42	1.0	Surface	1	1	26.38	8.06	29.89	83.20	5.6	1.8	5.7

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	CS(Mf)5	07:04:01	1.0	Surface	1	2	26.39	8.05	29.93	82.80	5.6	1.9	5.7
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	CS(Mf)5	07:04:26	6.4	Middle	2	1	25.92	8.03	30.69	80.00	5.4	2.1	4.0
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	CS(Mf)5	07:03:46	6.4	Middle	2	2	25.98	8.02	30.69	80.70	5.4	2.1	4.0
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	CS(Mf)5	07:03:34	11.7	Bottom	3	1	26.00	8.02	30.81	79.10	5.4	2.5	3.9
HKLR	HY/2011/03	2025-05-16	Mid-Flood	Fine	CS(Mf)5	07:04:16	11.7	Bottom	3	2	25.90	8.02	30.81	79.20	5.1	2.4	3.9
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	IS5	16:18:21	1.0	Surface	1	1	27.65	8.07	30.43	92.80	6.3	2.5	5.0
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	IS5	16:18:57	1.0	Surface	1	2	27.70	8.06	30.43	93.10	6.3	2.4	5.0
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	IS5	16:18:11	4.3	Middle	2	1	27.46	8.05	30.89	91.20	6.2	2.8	5.7
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	IS5	16:18:45	4.3	Middle	2	2	27.49	8.05	30.85	91.10	6.2	2.8	5.7
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	IS5	16:18:34	7.6	Bottom	3	1	27.48	8.04	30.90	91.20	6.2	3.0	2.7
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	IS5	16:18:02	7.6	Bottom	3	2	27.42	8.05	30.92	91.30	6.2	3.0	2.7
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	IS(Mf)6	16:29:01	1.0	Surface	1	1	27.68	8.07	30.41	94.70	6.5	2.4	3.8
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	IS(Mf)6	16:28:45	1.0	Surface	1	2	27.66	8.08	30.41	94.00	6.4	2.4	3.8
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	IS(Mf)6	16:28:53	2.2	Bottom	3	1	27.63	8.07	30.53	93.30	6.4	2.7	4.9
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	IS(Mf)6	16:28:37	2.2	Bottom	3	2	27.57	8.08	30.56	92.60	6.3	2.7	4.9
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	IS7	16:38:24	1.0	Surface	1	1	27.71	8.08	30.32	95.70	6.5	2.2	4.1
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	IS7	16:38:08	1.0	Surface	1	2	27.68	8.07	30.35	95.30	6.5	2.4	4.1
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	IS7	16:38:01	2.3	Bottom	3	1	27.62	8.07	30.54	95.00	6.5	2.6	5.1
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	IS7	16:38:15	2.3	Bottom	3	2	27.64	8.07	30.49	95.00	6.5	2.6	5.1
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	IS8(N)	17:13:38	1.0	Surface	1	1	27.60	8.06	30.29	92.40	6.3	2.7	3.3
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	IS8(N)	17:13:54	1.0	Surface	1	2	27.65	8.06	30.25	93.00	6.3	2.6	3.3
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	IS8(N)	17:13:46	3.0	Bottom	3	1	27.58	8.05	30.44	92.30	6.3	2.8	4.8
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	IS8(N)	17:13:29	3.0	Bottom	3	2	27.50	8.04	30.53	91.70	6.3	2.8	4.8
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	IS(Mf)9	16:48:22	1.0	Surface	1	1	27.70	8.08	30.33	95.10	6.5	2.2	3.5
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	IS(Mf)9	16:48:02	1.0	Surface	1	2	27.69	8.07	30.34	94.60	6.4	2.3	3.5
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	IS(Mf)9	16:47:54	2.6	Bottom	3	1	27.60	8.05	30.53	94.40	6.4	2.5	5.7
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	IS(Mf)9	16:48:11	2.6	Bottom	3	2	27.65	8.07	30.53	94.60	6.4	2.5	5.7
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	IS10(N)	17:21:37	1.0	Surface	1	1	27.27	8.07	29.96	90.30	6.1	2.7	3.2
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	IS10(N)	17:20:43	1.0	Surface	1	2	27.24	8.07	29.98	89.60	6.1	2.7	3.2
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	IS10(N)	17:20:30	5.3	Middle	2	1	27.02	8.04	30.59	88.50	6.0	2.9	3.0
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	IS10(N)	17:21:22	5.3	Middle	2	2	27.02	8.04	30.62	88.50	6.0	2.9	3.0
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	IS10(N)	17:20:20	9.5	Bottom	3	1	27.03	8.04	30.62	88.30	6.0	3.1	3.2
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	IS10(N)	17:21:03	9.5	Bottom	3	2	27.01	8.04	30.68	87.70	5.9	3.3	3.2
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	SR3(N)	16:05:05	1.0	Surface	1	1	27.72	8.08	30.42	95.60	6.5	2.7	5.0
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	SR3(N)	16:05:22	1.0	Surface	1	2	27.73	8.09	30.44	96.20	6.6	2.7	5.0
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	SR3(N)	16:05:11	2.2	Bottom	3	1	27.71	8.08	30.48	95.10	6.5	2.8	3.1
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	SR3(N)	16:04:54	2.2	Bottom	3	2	27.68	8.08	30.51	94.40	6.4	2.8	3.1
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	SR4(N3)	17:03:31	1.0	Surface	1	1	27.63	8.07	30.31	93.00	6.3	2.5	3.0
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	SR4(N3)	17:03:15	1.0	Surface	1	2	27.62	8.06	30.31	92.70	6.3	2.5	3.0
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	SR4(N3)	17:03:06	2.8	Bottom	3	1	27.30	8.05	30.51	91.90	6.3	2.7	3.4
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	SR4(N3)	17:03:24	2.8	Bottom	3	2	27.61	8.05	30.52	92.40	6.3	2.8	3.4
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	SR5(N)	17:12:09	1.0	Surface	1	1	27.22	8.08	29.97	90.00	6.1	2.7	3.0
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	SR5(N)	17:12:58	1.0	Surface	1	2	27.24	8.08	29.96	90.90	6.2	2.7	3.0
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	SR5(N)	17:11:53	4.7	Middle	2	1	27.06	8.05	30.49	88.20	6.0	2.9	2.5
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	SR5(N)	17:12:45	4.7	Middle	2	2	27.04	8.04	30.51	88.20	6.0	2.9	2.5
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	SR5(N)	17:12:25	8.4	Bottom	3	1	27.02	8.04	30.63	88.80	6.0	3.3	4.0
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	SR5(N)	17:11:42	8.4	Bottom	3	2	27.01	8.04	30.64	88.60	6.0	3.2	4.0
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	SR10A(N)	18:16:04	1.0	Surface	1	1	27.17	8.08	30.56	89.80	6.1	2.3	2.8
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	SR10A(N)	18:15:15	1.0	Surface	1	2	27.22	8.08	30.53	89.60	6.1	2.2	2.8
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	SR10A(N)	18:14:52	6.6	Middle	2	1	26.98	8.06	31.14	87.60	5.9	2.5	2.8
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	SR10A(N)	18:15:45	6.6	Middle	2	2	26.99	8.06	31.10	87.00	5.9	2.5	2.8
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	SR10A(N)	18:14:40	12.2	Bottom	3	1	26.99	8.06	31.19	87.80	5.9	2.7	2.0
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	SR10A(N)	18:15:33	12.2	Bottom	3	2	27.01	8.06	31.12	87.80	5.9	2.7	2.0
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	SR10B(N2)	18:28:43	1.0	Surface	1	1	27.20	8.07	30.58	89.60	6.1	2.3	3.3
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	SR10B(N2)	18:27:49	1.0	Surface	1	2	27.20	8.07	30.58	89.20	6.0	2.2	3.3
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	SR10B(N2)	18:27:36	3.8	Middle	2	1	27.07	8.06	30.92	88.00	5.9	2.5	2.9
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	SR10B(N2)	18:28:30	3.8	Middle	2	2	27.05	8.06	30.90	88.10	5.9	2.5	2.9
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	SR10B(N2)	18:27:26	6.5	Bottom	3	1	27.02	8.06	31.04	87.60	5.9	2.7	3.0
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	SR10B(N2)	18:28:03	6.5	Bottom	3	2	27.08	8.05	30.97	87.80	5.9	2.7	3.0
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	CS2(A)	16:22:58	1.0	Surface	1	1	27.20	8.08	29.99	93.30	6.3	2.6	2.4
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	CS2(A)	16:23:37	1.0	Surface	1	2	27.21	8.08	29.97	92.70	6.3	2.5	2.4
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	CS2(A)	16:22:35	3.4	Middle	2	1	27.04	8.06	30.42	90.80	6.2	3.0	2.6
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	CS2(A)	16:23:23	3.4	Middle	2	2	27.08	8.05	30.43	90.80	6.1	2.8	2.6
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	CS2(A)	16:23:13	5.7	Bottom	3	1	27.05	8.05	30.57	91.10	6.2	3.1	2.7
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	CS2(A)	16:22:24	5.7	Bottom	3	2	27.03	8.05	30.59	90.80	6.1	3.1	2.7
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	CS(Mf)5	17:52:36	1.0	Surface	1	1	27.58	8.10	30.15	87.50	6.0	2.2	4.6
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	CS(Mf)5	17:53:15	1.0	Surface	1	2	27.58	8.09	30.18	87.60	5.9	2.1	4.6
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	CS(Mf)5	17:53:02	6.4	Middle	2	1	26.98	8.04	31.07	84.80	5.8	2.2	3.1
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	CS(Mf)5	17:52:22	6.4	Middle	2	2	26.94	8.05	31.09	84.90	5.8	2.4	3.1
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	CS(Mf)5	17:52:50	11.8	Bottom	3	1	26.96	8.04	30.29	84.20	5.7	2.7	5.0
HKLR	HY/2011/03	2025-05-19	Mid-Ebb	Fine	CS(Mf)5	17:52:11	11.8	Bottom	3	2	26.88	8.05	31.12	84.20	5.7	2.6	5.0
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	IS5	05:16:19	1.0	Surface	1	1	27.43	8.06	30.38	87.10	5.9	2.5	2.8
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	IS5	05:15:37	1.0	Surface	1	2	27.48	8.07	30.38	88.50	6.0	2.4	2.8
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	IS5	05:15:25	4.3	Middle	2	1	27.08	8.04	30.89	85.70	5.8	2.8	2.1
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	IS5	05:16:07	4.3	Middle	2	2	27.07	8.03	30.89	85.20	5.7	2.8	2.1
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	IS5	05:15:51	7.5	Bottom	3	1	26.99	8.03	31.01	84.70	5.7	2.9	7.6
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	IS5	05:15:15	7.5	Bottom	3	2	27.04	8.04	30.99	85.20	5.7	3.0	7.6
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	IS(Mf)6	05:06:17	1.0	Surface	1	1	27.52	8.07	30.30	91.70	6.2	2.4	5.5
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	IS(Mf)6	05:06:02	1.0	Surface	1	2	27.50	8.07	30.31	91.50	6.2	2.4	5.5
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	IS(Mf)6	05:06:09	2.2	Bottom	3	1	27.47	8.06	30.44	91.40	6.2	2.5	3.2
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	IS(Mf)6	05:05:52	2.2	Bottom	3	2	27.43	8.06	30.48	91.20	6.2	2.5	3.2
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	IS7	04:56:32	1.0	Surface	1	1	27.51	8.07	30.34	91.40	6.2	2.5	5.0
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	IS7	04:56:49	1.0	Surface	1	2	27.54	8.07	30.29	92.10	6.2	2.4	5.0
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	IS7	04:56:39	2.3	Bottom	3	1	27.48	8.06	30.44	91.20	6.1	2.9	3.0
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	IS7	04:56:25	2.3	Bottom	3	2	27.44	8.06	30.44	91.20	6.2	2.8	3.0
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	IS8(N)	04:21:33	1.0	Surface	1	1	27.46	8.06	30.18	90.10	6.1	2.8	5.7
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	IS8(N)	04:20:53	1.0	Surface	1	2	27.49	8.06	30.16	90.00	6.1	2.8	5.7
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	IS8(N)	04:21:00	3.1	Bottom	3	1	27.42	8.05	30.49	89.90	6.1	3.1	3.9
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	IS8(N)	04:20:42	3.1	Bottom	3	2	27.35	8.06	30.53	88.90	6.0	3.0	3.9
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	IS(Mf)9	04:44:42	1.0	Surface	1	1	27.54	8.07	30.24	91.40	6.2	2.5	4.2
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	IS(Mf)9	04:44:27	1.0	Surface	1	2	27.54	8.08	30.25	90.50	6.1	2.6	4.2
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	IS(Mf)9	04:44:35	2.5	Bottom	3	1	27.49	8.06	30.42	90.20	6.1	3.0	4.1
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	IS(Mf)9	04:44:17	2.5	Bottom	3	2	27.39	8.07	30.41	89.20	6.0	2.9	4.1
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	IS10(N)	04:55:23	1.0	Surface	1	1	27.13	8.07	30.21	89.10	6.1	2.4	5.8
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	IS10(N)	04:56:03	1.0	Surface	1	2	27.14	8.07	30.22	89.20	6.1	2.5	5.8
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	IS10(N)	04:55:47	5.4	Middle	2	1	27.00	8.04	30.71	87.30	5.9	2.8	4.0
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	IS10(N)	04:55:08	5.4	Middle	2	2	27.00	8.04	30.71	87.70	5.9	2.8	4.0
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	IS10(N)	04:55:37	9.7	Bottom	3	1	27.02	8.04	30.77	88.00	5.9	2.9	2.9
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	IS10(N)	04:54:56	9.7	Bottom	3	2	27.00	8.04	30.80	88.00	5.9	2.9	2.9
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	SR3(N)	05:29:42	1.0	Surface	1	1	27.51	8.07	30.38	90.20	6.1	2.4	5.7
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	SR3(N)	05:29:27	1.0	Surface	1	2	27.50	8.07	30.42	89.60	6.1	2.5	5.7
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	SR3(N)	05:29:34	2.3	Bottom	3	1	27.47	8.06	30.52	89.20	6.0	2.5	5.0
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	SR3(N)	05:29:18	2.3	Bottom	3	2	27.40	8.05	30.57	88.40	6.0	2.6	5.0
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	SR4(N3)	04:30:11	1.0	Surface	1	1	27.47	8.06	30.17	89.40	6.1	2.8	4.5
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	SR4(N3)	04:29:54	1.0	Surface	1	2	27.43	8.06	30.16	89.70	6.1	2.8	4.5
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	SR4(N3)	04:30:03	2.9	Bottom	3	1	27.40	8.04	30.50	89.20	6.0	3.1	4.7
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	SR4(N3)	04:29:44	2.9	Bottom	3	2	27.36	8.05	30.56	89.60	6.1	3.1	4.7
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	SR5(N)	05:06:01	1	Surface	1	1	27.11	8.08	30.25	88.90	6.0	2.6	4.5
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	SR5(N)	05:05:18	1	Surface	1	2	27.12	8.08	30.23	89.00	6.0	2.6	4.5
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	SR5(N)	05:05:47	4.8	Middle	2	1	27.02	8.05	30.64	87.20	5.9	2.7	3.4
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	SR5(N)	05:05:05	4.8	Middle	2	2	27.03	8.05	30.64	87.50	5.9	2.7	3.4
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	SR5(N)	05:04:53	8.5	Bottom	3	1	26.97	8.04	30.80	87.70	5.9	2.9	4.0
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	SR5(N)	05:05:37	8.5	Bottom	3	2	26.99	8.04	30.79	87.60	5.9	3.0	4.0
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	SR10A(N)	04:04:17	1	Surface	1	1	27.17	8.07	30.27	88.30	6.0	2.2	2.6
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	SR10A(N)	04:05:01	1	Surface	1	2	27.14	8.07	30.31	88.40	6.0	2.3	2.6

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	SR10A(N)	04:04:45	6.7	Middle	2	1	26.98	8.03	30.90	86.50	5.8	2.4	3.4
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	SR10A(N)	04:04:02	6.7	Middle	2	2	26.98	8.03	30.90	86.80	5.9	2.4	3.4
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	SR10A(N)	04:03:49	12.4	Bottom	3	1	26.98	8.03	30.95	86.70	5.9	2.8	2.8
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	SR10A(N)	04:04:33	12.4	Bottom	3	2	27.02	8.03	30.94	86.50	5.8	2.8	2.8
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	SR10B(N2)	03:54:49	1.0	Surface	1	1	27.17	8.07	30.28	91.80	6.2	2.2	2.8
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	SR10B(N2)	03:54:08	1.0	Surface	1	2	27.18	8.06	30.26	91.30	6.2	2.3	2.8
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	SR10B(N2)	03:53:49	3.8	Middle	2	1	27.04	8.03	30.66	89.50	6.1	2.5	3.8
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	SR10B(N2)	03:54:36	3.8	Middle	2	2	27.05	8.04	30.58	88.70	6.0	2.5	3.8
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	SR10B(N2)	03:54:24	6.6	Bottom	3	1	27.02	8.04	30.84	87.40	5.9	2.7	3.3
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	SR10B(N2)	03:53:36	6.6	Bottom	3	2	26.95	8.03	30.89	87.60	5.9	2.7	3.3
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	CS2(A)	05:51:24	1	Surface	1	1	27.12	8.08	30.23	89.80	6.1	2.6	3.0
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	CS2(A)	05:50:47	1	Surface	1	2	27.11	8.08	30.23	89.90	6.1	2.7	3.0
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	CS2(A)	05:51:11	3.4	Middle	2	1	27.05	8.06	30.48	88.90	6.0	2.8	3.1
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	CS2(A)	05:50:35	3.4	Middle	2	2	27.05	8.06	30.47	88.70	6.0	2.8	3.1
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	CS2(A)	05:50:23	5.7	Bottom	3	1	27.01	8.05	30.67	88.60	6.0	3.0	2.8
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	CS2(A)	05:51:01	5.7	Bottom	3	2	27.05	8.06	30.64	89.10	6.0	3.1	2.8
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	CS(Mf)5	03:42:09	1.0	Surface	1	1	27.42	8.08	30.11	88.60	6.0	2.0	3.3
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	CS(Mf)5	03:41:29	1.0	Surface	1	2	27.42	8.06	30.18	87.90	6.0	2.0	3.3
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	CS(Mf)5	03:41:54	6.4	Middle	2	1	26.96	8.04	30.89	85.10	5.7	2.3	3.6
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	CS(Mf)5	03:41:13	6.4	Middle	2	2	26.98	8.05	30.89	86.00	5.8	2.3	3.6
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	CS(Mf)5	03:41:00	11.8	Bottom	3	1	26.97	8.04	30.98	84.40	5.7	2.6	3.9
HKLR	HY/2011/03	2025-05-19	Mid-Flood	Fine	CS(Mf)5	03:41:44	11.8	Bottom	3	2	26.96	8.03	30.99	84.00	5.5	2.6	3.9
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	IS5	09:06:22	1.0	Surface	1	1	27.43	8.09	30.25	89.70	6.1	2.9	3.7
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	IS5	09:05:33	1.0	Surface	1	2	27.46	8.10	30.25	91.30	6.2	2.8	3.7
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	IS5	09:05:19	4.3	Middle	2	1	27.13	8.07	30.69	88.20	6.0	3.3	4.1
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	IS5	09:06:09	4.3	Middle	2	2	27.12	8.06	30.70	87.80	5.9	3.1	4.1
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	IS5	09:05:48	7.5	Bottom	3	1	27.05	8.06	30.80	87.20	5.9	3.2	2.4
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	IS5	09:05:09	7.5	Bottom	3	2	27.10	8.06	30.79	87.70	5.9	3.3	2.4
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	IS(Mf)6	08:57:00	1.0	Surface	1	1	27.52	8.10	30.20	93.70	6.3	2.7	3.6
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	IS(Mf)6	08:56:45	1.0	Surface	1	2	27.50	8.10	30.21	93.60	6.3	2.7	3.6
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	IS(Mf)6	08:56:51	2.3	Bottom	3	1	27.47	8.09	30.32	93.40	6.3	2.9	2.4
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	IS(Mf)6	08:56:34	2.3	Bottom	3	2	27.44	8.09	30.36	93.30	6.3	2.9	2.4
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	IS7	08:45:06	1.0	Surface	1	1	27.50	8.10	30.23	93.30	6.3	2.8	3.5
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	IS7	08:45:22	1.0	Surface	1	2	27.53	8.10	30.18	93.80	6.3	2.6	3.5
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	IS7	08:45:13	2.3	Bottom	3	1	27.48	8.09	30.30	93.20	6.3	3.3	2.8
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	IS7	08:44:58	2.3	Bottom	3	2	27.45	8.09	30.31	93.10	6.3	3.1	2.8
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	IS8(N)	08:11:07	1.0	Surface	1	1	27.47	8.09	30.12	93.20	6.3	2.9	3.0
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	IS8(N)	08:10:33	1.0	Surface	1	2	27.50	8.09	30.11	92.80	6.3	3.0	3.0
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	IS8(N)	08:10:40	3.1	Bottom	3	1	27.43	8.08	30.37	92.60	6.3	3.1	4.4
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	IS8(N)	08:10:22	3.1	Bottom	3	2	27.37	8.09	30.42	91.50	6.2	3.2	4.4
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	IS(Mf)9	08:36:16	1.0	Surface	1	1	27.53	8.10	30.15	93.40	6.3	2.8	4.4
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	IS(Mf)9	08:36:01	1.0	Surface	1	2	27.52	8.11	30.17	92.80	6.3	2.9	4.4
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	IS(Mf)9	08:36:08	2.6	Bottom	3	1	27.49	8.09	30.30	92.30	6.2	3.0	5.0
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	IS(Mf)9	08:35:51	2.6	Bottom	3	2	27.40	8.10	30.30	91.60	6.2	3.2	5.0
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	IS10(N)	08:32:57	1.0	Surface	1	1	27.39	8.10	30.01	89.60	6.1	2.8	2.4
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	IS10(N)	08:33:36	1.0	Surface	1	2	27.44	8.10	30.00	89.90	6.1	2.9	2.4
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	IS10(N)	08:33:20	5.4	Middle	2	1	27.19	8.08	30.51	87.90	6.0	3.2	3.4
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	IS10(N)	08:32:42	5.4	Middle	2	2	27.18	8.08	30.51	88.30	6.0	3.2	3.4
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	IS10(N)	08:33:11	9.8	Bottom	3	1	27.22	8.08	30.55	88.70	6.0	3.3	4.3
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	IS10(N)	08:32:30	9.8	Bottom	3	2	27.19	8.08	30.60	88.70	6.0	3.3	4.3
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	SR3(N)	09:20:39	1.0	Surface	1	1	27.50	8.10	30.24	92.10	6.2	2.9	5.1
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	SR3(N)	09:20:24	1.0	Surface	1	2	27.49	8.10	30.27	91.60	6.2	3.0	5.1
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	SR3(N)	09:20:31	2.3	Bottom	3	1	27.46	8.09	30.36	91.20	6.2	3.2	3.6
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	SR3(N)	09:20:15	2.3	Bottom	3	2	27.40	8.09	30.40	90.40	6.1	3.2	3.6
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	SR4(N3)	08:20:45	1.0	Surface	1	1	27.48	8.09	30.12	92.10	6.2	3.0	2.1
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	SR4(N3)	08:20:27	1.0	Surface	1	2	27.44	8.09	30.12	92.20	6.3	3.0	2.1
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	SR4(N3)	08:20:36	3.0	Bottom	3	1	27.41	8.08	30.38	91.80	6.2	3.4	2.6
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	SR4(N3)	08:20:17	3.0	Bottom	3	2	27.37	8.09	30.43	92.10	6.2	3.4	2.6
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	SR5(N)	08:45:01	1.0	Surface	1	1	27.38	8.11	30.03	89.50	6.1	3.0	2.4
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	SR5(N)	08:44:17	1.0	Surface	1	2	27.39	8.11	30.02	89.50	6.1	3.0	2.4
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	SR5(N)	08:44:45	4.8	Middle	2	1	27.23	8.09	30.41	87.90	6.0	3.2	2.2
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	SR5(N)	08:44:04	4.8	Middle	2	2	27.23	8.09	30.42	88.10	6.0	3.3	2.2
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	SR5(N)	08:44:35	8.5	Bottom	3	1	27.20	8.08	30.56	88.30	6.0	3.3	3.1
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	SR5(N)	08:43:53	8.5	Bottom	3	2	27.18	8.08	30.57	88.40	6.0	3.4	3.1
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	SR10A(N)	07:45:41	1.0	Surface	1	1	27.45	8.09	30.11	89.40	6.1	2.1	3.2
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	SR10A(N)	07:44:55	1.0	Surface	1	2	27.48	8.09	30.09	88.80	6.0	2.2	3.2
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	SR10A(N)	07:45:22	6.7	Middle	2	1	27.18	8.07	30.70	86.90	5.9	2.4	3.3
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	SR10A(N)	07:44:40	6.7	Middle	2	2	27.18	8.07	30.70	87.20	5.9	2.3	3.3
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	SR10A(N)	07:44:28	12.4	Bottom	3	1	27.18	8.07	30.76	87.40	5.9	2.5	3.5
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	SR10A(N)	07:45:11	12.4	Bottom	3	2	27.22	8.07	30.77	87.30	5.9	2.5	3.5
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	SR10B(N2)	07:34:59	1.0	Surface	1	1	27.49	8.10	30.09	92.80	6.3	2.1	3.5
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	SR10B(N2)	07:34:16	1.0	Surface	1	2	27.50	8.09	30.05	92.60	6.3	2.3	3.5
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	SR10B(N2)	07:33:57	3.9	Middle	2	1	27.26	8.07	30.45	90.20	6.1	2.6	3.1
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	SR10B(N2)	07:34:45	3.9	Middle	2	2	27.29	8.08	30.38	89.60	6.1	2.5	3.1
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	SR10B(N2)	07:34:32	6.7	Bottom	3	1	27.24	8.08	30.64	88.20	6.0	2.9	3.8
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	SR10B(N2)	07:33:44	6.7	Bottom	3	2	27.17	8.06	30.73	88.30	6.0	2.8	3.8
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	CS2(A)	09:38:20	1.0	Surface	1	1	27.39	8.11	30.06	90.30	6.2	2.9	3.0
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	CS2(A)	09:37:42	1.0	Surface	1	2	27.38	8.11	30.06	90.30	6.1	3.0	3.0
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	CS2(A)	09:38:07	3.4	Middle	2	1	27.27	8.10	30.33	89.20	6.1	3.4	2.8
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	CS2(A)	09:37:29	3.4	Middle	2	2	27.27	8.10	30.32	89.10	6.1	3.4	2.8
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	CS2(A)	09:37:17	5.7	Bottom	3	1	27.20	8.09	30.52	89.00	6.1	3.5	3.3
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	CS2(A)	09:37:56	5.7	Bottom	3	2	27.23	8.10	30.50	89.30	6.1	3.5	3.3
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	CS(Mf)5	07:29:28	1.0	Surface	1	1	27.47	8.10	30.14	91.50	6.1	2.1	3.2
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	CS(Mf)5	07:28:44	1.0	Surface	1	2	27.45	8.08	30.20	91.10	6.2	2.2	3.2
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	CS(Mf)5	07:29:11	6.4	Middle	2	1	27.08	8.06	30.76	88.40	6.0	2.6	4.1
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	CS(Mf)5	07:28:28	6.4	Middle	2	2	27.10	8.07	30.77	89.10	6.0	2.6	4.1
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	CS(Mf)5	07:28:16	11.8	Bottom	3	1	27.10	8.06	30.85	87.80	6.0	2.7	4.3
HKLR	HY/2011/03	2025-05-21	Mid-Ebb	Fine	CS(Mf)5	07:28:59	11.8	Bottom	3	2	27.08	8.06	30.85	87.50	5.8	2.6	4.3
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	IS5	12:31:56	1.0	Surface	1	1	27.59	8.10	30.28	94.20	6.4	2.8	3.4
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	IS5	12:32:34	1.0	Surface	1	2	27.64	8.09	30.27	94.80	6.4	2.7	3.4
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	IS5	12:31:45	4.3	Middle	2	1	27.42	8.08	30.66	93.10	6.3	3.2	1.4
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	IS5	12:32:21	4.3	Middle	2	2	27.44	8.08	30.64	92.90	6.3	3.3	1.4
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	IS5	12:32:10	7.6	Bottom	3	1	27.43	8.08	30.68	92.90	6.3	3.4	3.1
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	IS5	12:31:36	7.6	Bottom	3	2	27.39	8.08	30.70	93.10	6.3	3.3	3.1
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	IS(Mf)6	12:40:50	1.0	Surface	1	1	27.63	8.10	30.26	96.60	6.6	2.6	1.5
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	IS(Mf)6	12:40:34	1.0	Surface	1	2	27.60	8.11	30.26	95.80	6.5	2.6	1.5
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	IS(Mf)6	12:40:42	2.2	Bottom	3	1	27.59	8.10	30.36	95.00	6.5	3.1	3.1
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	IS(Mf)6	12:40:26	2.2	Bottom	3	2	27.53	8.11	30.39	94.30	6.4	3.1	3.1
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	IS7	12:50:48	1.0	Surface	1	1	27.64	8.11	30.22	96.80	6.6	2.5	3.6
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	IS7	12:50:32	1.0	Surface	1	2	27.62	8.10	30.24	96.60	6.6	2.8	3.6
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	IS7	12:50:25	2.3	Bottom	3	1	27.57	8.10	30.39	96.30	6.5	3.0	3.2
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	IS7	12:50:39	2.3	Bottom	3	2	27.59	8.10	30.35	96.30	6.6	3.0	3.2
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	IS8(N)	13:22:30	1.0	Surface	1	1	27.57	8.09	30.20	94.30	6.4	3.1	1.2
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	IS8(N)	13:22:47	1.0	Surface	1	2	27.60	8.10	30.17	94.80	6.4	3.0	1.2
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	IS8(N)	13:22:38	3.1	Bottom	3	1	27.56	8.09	30.33	94.30	6.4	3.3	2.6
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	IS8(N)	13:22:21	3.1	Bottom	3	2	27.49	8.08	30.40	93.60	6.4	3.4	2.6
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	IS(Mf)9	13:00:32	1.0	Surface	1	1	27.63	8.11	30.23	96.30	6.5	2.4	3.4
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	IS(Mf)9	13:00:12	1.0	Surface	1	2	27.62	8.10	30.23	95.90	6.5	2.6	3.4
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	IS(Mf)9	13:00:21	2.6	Bottom	3	1	27.59	8.10	30.38	95.90	6.5	2.9	2.5
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	IS(Mf)9	13:00:05	2.6	Bottom	3	2	27.55	8.09	30.39	95.70	6.5	2.9	2.5
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	IS10(N)	13:40:20	1.0	Surface	1	1	27.53	8.10	29.72	90.60	6.2	3.0	3.7
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	IS10(N)	13:39:34	1.0	Surface	1	2	27.49	8.10	29.74	89.80	6.1	3.0	3.7
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	IS10(N)	13:39:21	5.3	Middle	2	1	27.24	8.08	30.42	88.80	6.0	3.4	3.6
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	IS10(N)	13:40:05	5.3	Middle	2	2	27.25	8.08	30.42	89.00	6.0	3.4	3.6
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	IS10(N)	13:39:51	9.5	Bottom	3	1	27.27	8.08	30.46	88.50	6.0	3.3	2.8

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	IS10(N)	13:39:10	9.5	Bottom	3	2	27.24	8.08	30.48	88.60	6.0	3.4	2.8
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	SR3(N)	12:12:38	1.0	Surface	1	1	27.65	8.11	30.26	97.00	6.6	3.1	3.4
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	SR3(N)	12:12:55	1.0	Surface	1	2	27.66	8.12	30.27	97.80	6.6	3.1	3.4
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	SR3(N)	12:12:44	2.3	Bottom	3	1	27.64	8.11	30.31	96.50	6.6	3.3	3.4
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	SR3(N)	12:12:28	2.3	Bottom	3	2	27.61	8.11	30.34	95.70	6.5	3.4	3.4
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	SR4(N3)	13:13:30	1.0	Surface	1	1	27.59	8.10	30.22	94.60	6.4	3.0	4.2
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	SR4(N3)	13:13:15	1.0	Surface	1	2	27.58	8.09	30.21	94.40	6.4	3.1	4.2
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	SR4(N3)	13:13:07	2.9	Bottom	3	1	27.41	8.08	30.36	93.60	6.4	3.2	3.6
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	SR4(N3)	13:13:24	2.9	Bottom	3	2	27.58	8.09	30.37	94.10	6.4	3.3	3.6
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	SR5(N)	13:28:02	1	Surface	1	1	27.48	8.11	29.74	90.40	6.2	2.9	2.1
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	SR5(N)	13:28:45	1	Surface	1	2	27.51	8.11	29.73	91.10	6.2	2.9	2.1
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	SR5(N)	13:27:47	4.7	Middle	2	1	27.29	8.09	30.29	89.00	6.0	3.2	2.7
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	SR5(N)	13:28:31	4.7	Middle	2	2	27.29	8.08	30.30	89.00	6.1	3.2	2.7
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	SR5(N)	13:28:17	8.4	Bottom	3	1	27.27	8.08	30.45	89.50	6.1	3.5	2.7
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	SR5(N)	13:27:36	8.4	Bottom	3	2	27.25	8.09	30.46	89.30	6.1	3.4	2.7
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	SR10A(N)	14:41:59	1	Surface	1	1	27.43	8.11	30.40	90.20	6.1	2.4	2.4
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	SR10A(N)	14:41:12	1	Surface	1	2	27.45	8.11	30.36	89.80	6.1	2.3	2.4
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	SR10A(N)	14:40:51	6.7	Middle	2	1	27.20	8.10	30.95	87.90	6.0	2.8	3.1
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	SR10A(N)	14:41:40	6.7	Middle	2	2	27.19	8.10	30.94	87.40	5.9	2.8	3.1
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	SR10A(N)	14:40:39	12.4	Bottom	3	1	27.21	8.11	31.00	88.20	6.0	3.0	1.8
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	SR10A(N)	14:41:28	12.4	Bottom	3	2	27.21	8.10	30.96	88.00	6.0	3.0	1.8
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	SR10B(N2)	14:51:53	1.0	Surface	1	1	27.45	8.10	30.42	89.50	6.1	2.3	4.8
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	SR10B(N2)	14:51:10	1.0	Surface	1	2	27.44	8.10	30.42	89.30	6.0	2.2	4.8
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	SR10B(N2)	14:50:57	3.8	Middle	2	1	27.28	8.10	30.73	88.30	6.0	2.6	1.9
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	SR10B(N2)	14:51:41	3.8	Middle	2	2	27.27	8.10	30.69	88.20	6.0	2.6	1.9
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	SR10B(N2)	14:50:47	6.6	Bottom	3	1	27.26	8.10	30.84	88.40	6.0	2.9	1.7
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	SR10B(N2)	14:51:22	6.6	Bottom	3	2	27.28	8.09	30.81	88.20	6.0	2.9	1.7
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	CS2(A)	12:34:19	1	Surface	1	1	27.47	8.11	29.83	92.50	6.3	2.7	2.8
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	CS2(A)	12:33:45	1	Surface	1	2	27.46	8.11	29.84	92.90	6.3	2.8	2.8
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	CS2(A)	12:34:07	3.4	Middle	2	1	27.31	8.10	30.32	90.90	6.2	3.1	3.8
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	CS2(A)	12:33:28	3.4	Middle	2	2	27.27	8.10	30.32	90.80	6.2	3.0	3.8
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	CS2(A)	12:33:58	5.7	Bottom	3	1	27.31	8.10	30.47	91.2	6.2	3.2	3.0
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	CS2(A)	12:33:18	5.7	Bottom	3	2	27.25	8.10	30.53	90.9	6.2	3.3	3.0
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	CS(Mf)5	14:04:50	1	Surface	1	1	27.57	8.11	30.21	90.1	6.1	2.5	2.4
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	CS(Mf)5	14:05:30	1	Surface	1	2	27.57	8.11	30.23	90.5	6.1	2.3	2.4
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	CS(Mf)5	14:05:16	6.4	Middle	2	1	27.07	8.09	30.95	87.6	5.9	2.7	1.2
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	CS(Mf)5	14:04:36	6.4	Middle	2	2	27.05	8.10	30.96	87.7	5.9	2.9	1.2
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	CS(Mf)5	14:05:05	11.8	Bottom	3	1	27.07	8.09	30.28	86.7	5.9	3.2	2.8
HKLR	HY/2011/03	2025-05-21	Mid-Flood	Fine	CS(Mf)5	14:04:25	11.8	Bottom	3	2	27.01	8.10	30.98	86.8	5.9	3.2	2.8
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	IS5	10:34:35	1	Surface	1	1	27.42	8.10	30.26	91.3	6.3	2.9	3.4
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	IS5	10:33:46	1	Surface	1	2	27.45	8.11	30.25	93.1	6.4	2.8	3.4
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	IS5	10:33:33	4.3	Middle	2	1	27.18	8.08	30.68	89.7	6.2	3.2	2.6
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	IS5	10:34:22	4.3	Middle	2	2	27.16	8.07	30.70	89.6	6.2	3.1	2.6
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	IS5	10:34:01	7.5	Bottom	3	1	27.10	8.06	30.79	88.9	6.1	3.2	2.6
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	IS5	10:33:23	7.5	Bottom	3	2	27.16	8.08	30.77	89.1	6.1	3.3	2.6
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	IS(Mf)6	10:23:55	1	Surface	1	1	27.51	8.11	30.23	94.5	6.5	2.7	2.2
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	IS(Mf)6	10:23:39	1	Surface	1	2	27.49	8.11	30.24	94.3	6.5	2.7	2.2
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	IS(Mf)6	10:23:28	2.3	Bottom	3	1	27.44	8.10	30.37	94.1	6.5	3.0	2.4
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	IS(Mf)6	10:23:46	2.3	Bottom	3	2	27.46	8.10	30.34	94.1	6.5	3.0	2.4
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	IS7	10:12:37	1	Surface	1	1	27.48	8.11	30.26	94.1	6.5	2.7	3.9
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	IS7	10:12:51	1	Surface	1	2	27.51	8.11	30.22	94.5	6.5	2.6	3.9
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	IS7	10:12:43	2.3	Bottom	3	1	27.47	8.10	30.32	94.0	6.5	2.8	2.3
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	IS7	10:12:28	2.3	Bottom	3	2	27.44	8.10	30.33	94.1	6.5	2.8	2.3
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	IS8(N)	09:41:27	1	Surface	1	1	27.46	8.09	30.20	94.8	6.6	2.8	2.8
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	IS8(N)	09:40:46	1	Surface	1	2	27.49	8.10	30.18	94.1	6.5	2.8	2.8
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	IS8(N)	09:40:54	3.1	Bottom	3	1	27.42	8.09	30.46	93.7	6.5	3.0	2.4
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	IS8(N)	09:40:36	3.1	Bottom	3	2	27.38	8.10	30.49	92.8	6.4	3.1	2.4
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	IS(Mf)9	10:03:03	1	Surface	1	1	27.52	8.11	30.20	94.2	6.5	2.7	2.5
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	IS(Mf)9	10:02:47	1	Surface	1	2	27.51	8.11	30.22	93.8	6.5	2.8	2.5
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	IS(Mf)9	10:02:38	2.6	Bottom	3	1	27.41	8.10	30.33	92.7	6.4	3.1	3.0
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	IS(Mf)9	10:02:54	2.6	Bottom	3	2	27.49	8.10	30.34	93.3	6.4	3.0	3.0
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	IS10(N)	10:06:40	1	Surface	1	1	27.39	8.10	30.07	92.3	6.4	2.8	2.9
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	IS10(N)	10:06:01	1	Surface	1	2	27.35	8.10	30.07	92.3	6.4	2.8	2.9
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	IS10(N)	10:06:24	5.5	Middle	2	1	27.20	8.09	30.56	90.4	6.2	3.0	3.8
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	IS10(N)	10:05:45	5.5	Middle	2	2	27.19	8.09	30.57	90.8	6.3	3.1	3.8
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	IS10(N)	10:06:14	9.9	Bottom	3	1	27.22	8.09	30.58	91.1	6.3	3.1	3.0
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	IS10(N)	10:05:34	9.9	Bottom	3	2	27.20	8.09	30.63	91.0	6.3	3.0	3.0
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	SR3(N)	10:47:45	1	Surface	1	1	27.48	8.11	30.24	92.9	6.4	2.9	3.4
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	SR3(N)	10:47:30	1	Surface	1	2	27.47	8.10	30.26	92.3	6.4	3.0	3.4
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	SR3(N)	10:47:37	2.4	Bottom	3	1	27.45	8.10	30.36	91.9	6.3	3.2	4.0
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	SR3(N)	10:47:21	2.4	Bottom	3	2	27.40	8.09	30.39	91.2	6.3	3.3	4.0
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	SR4(N3)	09:48:47	1	Surface	1	1	27.48	8.09	30.21	93.3	6.4	2.7	3.9
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	SR4(N3)	09:48:29	1	Surface	1	2	27.44	8.09	30.20	93.5	6.5	2.7	3.9
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	SR4(N3)	09:48:18	3	Bottom	3	1	27.38	8.09	30.49	93.4	6.4	3.0	3.2
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	SR4(N3)	09:48:38	3	Bottom	3	2	27.41	8.08	30.44	93.0	6.4	3.1	3.2
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	SR5(N)	10:20:19	1	Surface	1	1	27.34	8.11	30.09	91.6	6.3	2.9	3.4
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	SR5(N)	10:19:35	1	Surface	1	2	27.35	8.11	30.09	91.7	6.3	2.9	3.4
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	SR5(N)	10:20:03	4.8	Middle	2	1	27.24	8.09	30.47	90.3	6.2	3.1	3.8
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	SR5(N)	10:19:23	4.8	Middle	2	2	27.23	8.09	30.48	90.5	6.2	3.2	3.8
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	SR5(N)	10:19:54	8.5	Bottom	3	1	27.22	8.09	30.60	90.8	6.3	3.4	3.3
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	SR5(N)	10:19:11	8.5	Bottom	3	2	27.20	8.09	30.60	91.0	6.3	3.4	3.3
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	SR10A(N)	09:17:54	1	Surface	1	1	27.43	8.09	30.27	91.1	6.3	2.2	3.2
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	SR10A(N)	09:17:09	1	Surface	1	2	27.45	8.09	30.29	90.7	6.2	2.3	3.2
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	SR10A(N)	09:16:54	6.6	Middle	2	1	27.22	8.07	30.83	89.3	6.1	2.5	3.9
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	SR10A(N)	09:17:37	6.6	Middle	2	2	27.22	8.07	30.83	88.9	6.1	2.5	3.9
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	SR10A(N)	09:17:26	12.2	Bottom	3	1	27.25	8.07	30.89	89.6	6.1	2.7	3.2
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	SR10A(N)	09:16:42	12.2	Bottom	3	2	27.23	8.07	30.88	89.8	6.2	2.7	3.2
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	SR10B(N2)	09:02:26	1	Surface	1	1	27.46	8.09	30.28	95.0	6.5	2.3	3.7
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	SR10B(N2)	09:01:44	1	Surface	1	2	27.47	8.08	30.25	95.3	6.6	2.4	3.7
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	SR10B(N2)	09:01:25	3.8	Middle	2	1	27.28	8.07	30.62	92.5	6.4	2.7	3.7
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	SR10B(N2)	09:02:12	3.8	Middle	2	2	27.31	8.08	30.56	91.5	6.3	2.6	3.7
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	SR10B(N2)	09:01:59	6.6	Bottom	3	1	27.27	8.07	30.80	90.3	6.2	2.9	3.7
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	SR10B(N2)	09:01:12	6.6	Bottom	3	2	27.23	8.06	30.87	90.4	6.2	2.8	3.7
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	CS2(A)	11:11:45	1	Surface	1	1	27.33	8.12	30.11	92.4	6.4	3.1	3.0
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	CS2(A)	11:11:05	1	Surface	1	2	27.33	8.12	30.11	92.3	6.4	3.1	3.0
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	CS2(A)	11:11:33	3.4	Middle	2	1	27.24	8.11	30.41	91.4	6.3	3.2	3.2
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	CS2(A)	11:10:52	3.4	Middle	2	2	27.24	8.11	30.40	91.0	6.3	3.2	3.2
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	CS2(A)	11:10:40	5.7	Bottom	3	1	27.19	8.11	30.60	90.8	6.3	3.2	3.1
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	CS2(A)	11:11:20	5.7	Bottom	3	2	27.21	8.11	30.58	91.1	6.3	3.3	3.1
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	CS(Mf)5	08:56:53	1	Surface	1	1	27.47	8.09	30.28	93.1	6.4	2.3	3.2
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	CS(Mf)5	08:56:09	1	Surface	1	2	27.45	8.08	30.32	92.9	6.4	2.4	3.2
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	CS(Mf)5	08:55:53	6.2	Middle	2	1	27.18	8.06	30.81	91.3	6.3	2.8	3.2
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	CS(Mf)5	08:56:35	6.2	Middle	2	2	27.16	8.06	30.82	90.5	6.2	2.7	3.2
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	CS(Mf)5	08:56:24	11.4	Bottom	3	1	27.15	8.06	30.89	89.9	6.1	2.9	3.8
HKLR	HY/2011/03	2025-05-23	Mid-Ebb	Fine	CS(Mf)5	08:55:42	11.4	Bottom	3	2	27.19	8.06	30.88	90.1	6.2	3.0	3.8
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	IS5	14:55:40	1	Surface	1	1	27.56	8.10	30.28	95.2	6.6	2.9	3.0
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	IS5	14:56:17	1	Surface	1	2	27.60	8.09	30.27	95.7	6.6	2.8	3.0
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	IS5	14:55:29	4.3	Middle	2	1	27.42	8.08	30.62	94.3	6.5	3.2	4.5
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	IS5	14:56:04	4.3	Middle	2	2	27.43	8.08	30.61	94.3	6.5	3.3	4.5
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	IS5	14:55:20	7.6	Bottom	3	1	27.40	8.08	30.67	94.4	6.6	3.3	4.9
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	IS5	14:55:54	7.6	Bottom	3	2	27.42	8.08	30.65	94.3	6.5	3.4	4.9
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	IS(Mf)6	15:04:27	1	Surface	1	1	27.60	8.10	30.25	97.8	6.8	2.8	3.0
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	IS(Mf)6	15:04:12	1	Surface	1	2	27.57	8.11	30.25	96.9	6.7	2.7	3.0
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	IS(Mf)6	15:04:19	2.2	Bottom	3	1	27.56	8.10	30.35	96.1	6.7	3.3	2.8
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	IS(Mf)6	15:04:02	2.2	Bottom	3	2	27.52	8.11	30.37	95.2	6.6	3.3	2.8

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	IS7	15:15:27	1	Surface	1	1	27.60	8.11	30.25	97.4	6.7	2.6	3.7
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	IS7	15:15:10	1	Surface	1	2	27.59	8.10	30.26	97.3	6.7	2.8	3.7
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	IS7	15:15:02	2.3	Bottom	3	1	27.54	8.10	30.39	97.0	6.7	3.0	3.0
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	IS7	15:15:17	2.3	Bottom	3	2	27.56	8.10	30.36	97.0	6.7	3.0	3.0
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	IS8(N)	15:49:28	1	Surface	1	1	27.57	8.08	30.23	95.1	6.6	2.8	3.6
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	IS8(N)	15:49:45	1	Surface	1	2	27.58	8.09	30.20	95.5	6.6	2.7	3.6
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	IS8(N)	15:49:37	3	Bottom	3	1	27.55	8.08	30.34	95.1	6.6	3.0	3.3
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	IS8(N)	15:49:19	3	Bottom	3	2	27.50	8.07	30.40	94.5	6.6	3.0	3.3
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	IS(Mf)9	15:27:11	1	Surface	1	1	27.60	8.10	30.26	96.9	6.7	2.6	2.0
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	IS(Mf)9	15:26:51	1	Surface	1	2	27.59	8.10	30.25	96.6	6.7	2.8	2.0
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	IS(Mf)9	15:27:00	2.6	Bottom	3	1	27.56	8.10	30.40	96.6	6.7	3.0	2.2
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	IS(Mf)9	15:26:45	2.6	Bottom	3	2	27.53	8.09	30.40	96.5	6.7	3.0	2.2
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	IS10(N)	15:47:46	1	Surface	1	1	27.52	8.11	29.76	92.9	6.4	3.0	2.9
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	IS10(N)	15:47:03	1	Surface	1	2	27.48	8.11	29.79	92.1	6.4	3.0	2.9
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	IS10(N)	15:46:51	5.3	Middle	2	1	27.26	8.09	30.42	91.3	6.3	3.3	3.2
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	IS10(N)	15:47:30	5.3	Middle	2	2	27.27	8.09	30.43	91.5	6.3	3.3	3.2
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	IS10(N)	15:47:19	9.6	Bottom	3	1	27.29	8.09	30.49	91.1	6.3	3.3	3.0
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	IS10(N)	15:46:33	9.6	Bottom	3	2	27.26	8.09	30.51	91.3	6.3	3.3	3.0
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	SR3(N)	14:39:48	1	Surface	1	1	27.60	8.10	30.26	97.2	6.7	3.1	2.6
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	SR3(N)	14:40:05	1	Surface	1	2	27.61	8.11	30.27	98.3	6.8	3.1	2.6
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	SR3(N)	14:39:55	2.3	Bottom	3	1	27.59	8.10	30.32	96.7	6.7	3.3	3.6
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	SR3(N)	14:39:38	2.3	Bottom	3	2	27.57	8.10	30.35	95.8	6.6	3.3	3.6
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	SR4(N3)	15:40:22	1	Surface	1	1	27.57	8.09	30.25	95.0	6.6	2.9	1.8
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	SR4(N3)	15:40:06	1	Surface	1	2	27.57	8.09	30.23	94.8	6.6	3.0	1.8
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	SR4(N3)	15:40:15	2.8	Bottom	3	1	27.56	8.08	30.37	94.4	6.5	3.2	2.7
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	SR4(N3)	15:39:57	2.8	Bottom	3	2	27.47	8.07	30.36	94.0	6.5	3.1	2.7
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	SR5(N)	15:35:45	1	Surface	1	1	27.50	8.11	29.78	93.2	6.4	2.3	3.4
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	SR5(N)	15:35:03	1	Surface	1	2	27.45	8.11	29.80	92.5	6.4	2.4	3.4
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	SR5(N)	15:35:31	4.7	Middle	2	1	27.31	8.10	30.31	91.5	6.3	2.8	2.7
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	SR5(N)	15:34:50	4.7	Middle	2	2	27.30	8.10	30.31	91.3	6.3	2.7	2.7
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	SR5(N)	15:35:19	8.4	Bottom	3	1	27.29	8.09	30.52	91.9	6.3	3.1	3.2
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	SR5(N)	15:34:39	8.4	Bottom	3	2	27.28	8.10	30.53	91.5	6.3	3.0	3.2
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	SR10A(N)	16:40:47	1	Surface	1	1	27.42	8.12	30.58	92.5	6.4	2.4	3.8
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	SR10A(N)	16:40:01	1	Surface	1	2	27.43	8.12	30.55	92.1	6.3	2.3	3.8
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	SR10A(N)	16:39:42	6.6	Middle	2	1	27.24	8.11	31.06	90.2	6.2	2.8	4.8
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	SR10A(N)	16:40:28	6.6	Middle	2	2	27.24	8.11	31.06	89.8	6.2	2.8	4.8
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	SR10A(N)	16:40:17	12.2	Bottom	3	1	27.25	8.11	31.07	90.4	6.2	2.9	3.3
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	SR10A(N)	16:39:30	12.2	Bottom	3	2	27.25	8.12	31.11	90.6	6.2	2.9	3.3
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	SR10B(N2)	17:02:00	1	Surface	1	1	27.44	8.11	30.60	91.5	6.3	2.3	3.0
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	SR10B(N2)	17:01:20	1	Surface	1	2	27.43	8.11	30.60	91.4	6.3	2.2	3.0
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	SR10B(N2)	17:01:07	3.7	Middle	2	1	27.31	8.11	30.85	90.6	6.2	2.6	3.1
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	SR10B(N2)	17:01:48	3.7	Middle	2	2	27.30	8.11	30.83	90.5	6.2	2.6	3.1
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	SR10B(N2)	17:00:57	6.3	Bottom	3	1	27.30	8.11	30.96	90.7	6.2	2.9	2.9
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	SR10B(N2)	17:01:33	6.3	Bottom	3	2	27.30	8.10	30.94	90.5	6.2	2.9	2.9
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	CS2(A)	14:48:30	1	Surface	1	1	27.43	8.11	29.90	94.8	6.5	2.9	3.0
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	CS2(A)	14:47:55	1	Surface	1	2	27.41	8.11	29.94	95.0	6.6	2.9	3.0
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	CS2(A)	14:48:18	3.3	Middle	2	1	27.29	8.11	30.40	92.9	6.4	3.1	3.1
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	CS2(A)	14:47:41	3.3	Middle	2	2	27.27	8.11	30.40	92.8	6.4	3.2	3.1
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	CS2(A)	14:48:08	5.5	Bottom	3	1	27.29	8.10	30.59	92.9	6.4	3.4	3.4
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	CS2(A)	14:47:31	5.5	Bottom	3	2	27.25	8.11	30.64	92.5	6.4	3.4	3.4
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	CS(Mf)5	16:30:41	1	Surface	1	1	27.57	8.10	30.39	90.9	6.3	2.5	3.7
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	CS(Mf)5	16:31:20	1	Surface	1	2	27.58	8.10	30.40	91.4	6.3	2.4	3.7
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	CS(Mf)5	16:31:07	6.4	Middle	2	1	27.14	8.07	31.08	88.9	6.1	2.7	3.2
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	CS(Mf)5	16:30:27	6.4	Middle	2	2	27.13	8.07	31.08	88.8	6.1	2.8	3.2
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	CS(Mf)5	16:30:57	11.8	Bottom	3	1	27.15	8.07	30.44	88.1	6.1	2.8	3.6
HKLR	HY/2011/03	2025-05-23	Mid-Flood	Fine	CS(Mf)5	16:30:17	11.8	Bottom	3	2	27.10	8.07	31.10	88.3	6.1	2.9	3.6
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	IS5	11:13:56	1	Surface	1	1	26.16	8.08	30.73	87.3	6.3	2.2	2.7
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	IS5	11:14:30	1	Surface	1	2	26.18	8.07	30.72	87.3	6.3	2.1	2.7
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	IS5	11:13:44	4.3	Middle	2	1	26.09	8.07	30.90	86.9	6.2	2.4	1.3
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	IS5	11:14:18	4.3	Middle	2	2	26.10	8.07	30.90	86.6	6.2	2.3	1.3
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	IS5	11:14:08	7.6	Bottom	3	1	26.09	8.07	30.92	86.7	6.2	2.5	2.2
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	IS5	11:13:35	7.6	Bottom	3	2	26.08	8.07	30.93	87.1	6.3	2.5	2.2
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	IS(Mf)6	11:22:29	1	Surface	1	1	26.19	8.08	30.76	93.7	6.7	2.2	2.7
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	IS(Mf)6	11:22:45	1	Surface	1	2	26.22	8.07	30.77	95.7	6.9	2.2	2.7
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	IS(Mf)6	11:22:19	2.2	Bottom	3	1	26.12	8.10	30.83	90.3	6.5	2.4	3.4
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	IS(Mf)6	11:22:37	2.2	Bottom	3	2	26.20	8.07	30.84	91.9	6.6	2.3	3.4
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	IS7	11:32:56	1	Surface	1	1	26.22	8.09	30.77	89.2	6.4	2.2	3.1
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	IS7	11:32:39	1	Surface	1	2	26.22	8.09	30.77	89.6	6.4	2.4	3.1
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	IS7	11:32:47	2.3	Bottom	3	1	26.20	8.09	30.83	89.2	6.4	2.4	3.2
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	IS7	11:32:32	2.3	Bottom	3	2	26.19	8.09	30.85	89.6	6.4	2.4	3.2
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	IS8(N)	12:07:31	1	Surface	1	1	26.21	8.07	30.76	87.4	6.3	2.2	2.3
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	IS8(N)	12:07:47	1	Surface	1	2	26.22	8.08	30.75	87.6	6.3	2.3	2.3
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	IS8(N)	12:07:40	2.9	Bottom	3	1	26.20	8.07	30.82	87.3	6.2	2.5	2.4
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	IS8(N)	12:07:24	2.9	Bottom	3	2	26.17	8.07	30.85	87.1	6.2	2.4	2.4
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	IS(Mf)9	11:43:35	1	Surface	1	1	26.22	8.09	30.77	88.5	6.3	2.3	2.7
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	IS(Mf)9	11:43:54	1	Surface	1	2	26.23	8.09	30.78	88.4	6.3	2.2	2.7
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	IS(Mf)9	11:43:29	2.5	Bottom	3	1	26.19	8.08	30.86	88.5	6.3	2.4	2.8
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	IS(Mf)9	11:43:44	2.5	Bottom	3	2	26.22	8.09	30.88	88.3	6.3	2.4	2.8
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	IS10(N)	12:12:06	1	Surface	1	1	26.46	8.11	31.08	92.0	6.6	2.5	2.8
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	IS10(N)	12:11:25	1	Surface	1	2	26.44	8.10	31.09	91.4	6.6	2.5	2.8
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	IS10(N)	12:11:51	5.3	Middle	2	1	26.33	8.09	31.40	92.2	6.6	2.6	3.4
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	IS10(N)	12:11:13	5.3	Middle	2	2	26.33	8.08	31.40	90.9	6.6	2.6	3.4
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	IS10(N)	12:11:42	9.5	Bottom	3	1	26.34	8.09	31.43	91.1	6.6	2.7	2.1
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	IS10(N)	12:11:01	9.5	Bottom	3	2	26.33	8.08	31.44	90.9	6.5	2.7	2.1
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	SR3(N)	10:56:16	1	Surface	1	1	26.19	8.09	30.72	93.9	6.7	2.3	3.1
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	SR3(N)	10:55:58	1	Surface	1	2	26.18	8.09	30.72	91.1	6.5	2.3	3.1
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	SR3(N)	10:56:07	2.5	Bottom	3	1	26.18	8.09	30.75	90.0	6.4	2.5	1.5
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	SR3(N)	10:55:44	2.5	Bottom	3	2	26.16	8.10	30.76	89.0	6.4	2.4	1.5
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	SR4(N3)	11:58:53	1	Surface	1	1	26.21	8.08	30.77	87.3	6.3	2.4	3.7
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	SR4(N3)	11:58:39	1	Surface	1	2	26.22	8.08	30.76	87.3	6.2	2.4	3.7
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	SR4(N3)	11:58:30	2.8	Bottom	3	1	26.18	8.07	30.86	86.9	6.2	2.6	2.4
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	SR4(N3)	11:58:46	2.8	Bottom	3	2	26.21	8.07	30.84	87.0	6.2	2.5	2.4
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	SR5(N)	12:00:46	1	Surface	1	1	26.43	8.09	31.10	95.3	6.9	2.5	2.2
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	SR5(N)	12:01:21	1	Surface	1	2	26.45	8.08	31.09	94.5	6.8	2.4	2.2
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	SR5(N)	12:00:36	4.6	Middle	2	1	26.36	8.09	31.34	92.6	6.7	2.6	2.2
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	SR5(N)	12:01:10	4.6	Middle	2	2	26.36	8.08	31.34	92.9	6.7	2.6	2.2
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	SR5(N)	12:00:26	8.1	Bottom	3	1	26.35	8.10	31.45	92.2	6.6	2.7	3.0
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	SR5(N)	12:01:00	8.1	Bottom	3	2	26.35	8.08	31.45	92.2	6.6	2.6	3.0
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	SR10A(N)	13:03:15	1	Surface	1	1	26.53	8.06	31.66	96.8	6.9	2.5	2.8
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	SR10A(N)	13:02:39	1	Surface	1	2	26.54	8.07	31.64	95.4	6.8	2.5	2.8
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	SR10A(N)	13:03:01	6.5	Middle	2	1	26.44	8.06	31.90	91.8	6.6	2.7	2.6
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	SR10A(N)	13:02:21	6.5	Middle	2	2	26.44	8.08	31.89	92.9	6.7	2.7	2.6
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	SR10A(N)	13:02:10	12	Bottom	3	1	26.44	8.10	31.91	92.0	6.6	2.8	2.3
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	SR10A(N)	13:02:51	12	Bottom	3	2	26.44	8.08	31.90	92.3	6.6	2.7	2.3
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	SR10B(N2)	13:15:02	1	Surface	1	1	26.54	8.06	31.67	91.8	6.6	2.5	2.6
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	SR10B(N2)	13:14:24	1	Surface	1	2	26.54	8.05	31.67	91.8	6.6	2.5	2.6
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	SR10B(N2)	13:14:52	3.7	Middle	2	1	26.47	8.05	31.78	91.5	6.6	2.7	3.6
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	SR10B(N2)	13:14:12	3.7	Middle	2	2	26.48	8.05	31.79	91.5	6.6	2.6	3.6
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	SR10B(N2)	13:14:40	6.3	Bottom	3	1	26.46	8.05	31.84	92.0	6.6	2.8	2.5
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	SR10B(N2)	13:14:02	6.3	Bottom	3	2	26.47	8.06	31.85	91.5	6.6	2.8	2.5
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	CS2(A)	11:02:56	1	Surface	1	1	25.88	8.06	31.31	99.9	7.3	3.0	2.2
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	CS2(A)	11:03:34	1	Surface	1	2	25.90	8.05	31.29	98.8	7.2	2.9	2.2
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	CS2(A)	11:02:43	3.4	Middle	2	1	25.81	8.08	31.53	95.8	7.0	3.1	2.0
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	CS2(A)	11:03:24	3.4	Middle	2	2	25.83	8.06	31.53	96.2	7.0	3.0	2.0
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	CS2(A)	11:02:32	5.8	Bottom	3	1	25.80	8.08	31.64	94.5	6.9	3.2	1.3

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	CS2(A)	11:03:14	5.8	Bottom	3	2	25.83	8.06	31.62	95.2	6.9	3.2	1.3
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	CS(Mf)5	12:55:09	1	Surface	1	1	26.56	8.10	31.61	87.1	6.2	2.0	2.7
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	CS(Mf)5	12:55:49	1	Surface	1	2	26.57	8.10	31.63	88.7	6.3	2.0	2.7
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	CS(Mf)5	12:55:37	6.4	Middle	2	1	26.42	8.08	32.14	85.2	6.0	2.1	3.3
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	CS(Mf)5	12:54:56	6.4	Middle	2	2	26.42	8.09	32.14	84.8	6.0	2.0	3.3
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	CS(Mf)5	12:55:25	11.8	Bottom	3	1	26.42	8.08	31.81	85.3	6.0	2.2	2.3
HKLR	HY/2011/03	2025-05-26	Mid-Ebb	Fine	CS(Mf)5	12:54:44	11.8	Bottom	3	2	26.40	8.09	32.16	84.6	6.0	2.1	2.3
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	IS5	05:48:49	1	Surface	1	1	26.11	8.08	30.71	89.3	6.4	2.6	1.6
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	IS5	05:47:43	1	Surface	1	2	26.13	8.10	30.71	93.4	6.7	2.6	1.6
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	IS5	05:47:28	4.3	Middle	2	1	25.99	8.09	30.93	84.5	6.0	2.7	2.5
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	IS5	05:48:33	4.3	Middle	2	2	25.98	8.07	30.94	86.6	6.2	2.7	2.5
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	IS5	05:48:02	7.5	Bottom	3	1	25.95	8.07	30.99	84.8	6.1	2.7	3.1
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	IS5	05:47:15	7.5	Bottom	3	2	25.96	8.10	30.97	84.2	6.0	2.7	3.1
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	IS(Mf)6	05:39:34	1	Surface	1	1	26.14	8.09	30.69	86.5	6.2	2.2	2.0
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	IS(Mf)6	05:39:17	1	Surface	1	2	26.13	8.09	30.69	86.4	6.2	2.2	2.0
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	IS(Mf)6	05:39:06	2.3	Bottom	3	1	26.14	8.08	30.81	86.4	6.2	2.4	2.8
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	IS(Mf)6	05:39:25	2.3	Bottom	3	2	26.14	8.08	30.81	86.3	6.2	2.5	2.8
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	IS7	05:30:24	1	Surface	1	1	26.13	8.09	30.71	86.3	6.2	2.2	1.4
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	IS7	05:30:37	1	Surface	1	2	26.15	8.09	30.68	86.5	6.2	2.2	1.4
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	IS7	05:30:15	2.3	Bottom	3	1	26.12	8.08	30.81	86.3	6.2	2.2	2.4
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	IS7	05:30:30	2.3	Bottom	3	2	26.12	8.08	30.74	86.2	6.2	2.3	2.4
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	IS8(N)	04:57:30	1	Surface	1	1	26.13	8.09	30.68	94.8	6.8	2.4	2.1
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	IS8(N)	04:57:01	1	Surface	1	2	26.15	8.09	30.67	91.7	6.6	2.3	2.1
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	IS8(N)	04:57:10	3	Bottom	3	1	26.13	8.09	30.94	90.1	6.4	2.4	1.8
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	IS8(N)	04:56:50	3	Bottom	3	2	26.11	8.08	30.98	88.6	6.3	2.5	1.8
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	IS(Mf)9	05:22:50	1	Surface	1	1	26.15	8.09	30.69	86.4	6.2	2.3	1.8
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	IS(Mf)9	05:23:09	1	Surface	1	2	26.14	8.09	30.67	86.5	6.2	2.3	1.8
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	IS(Mf)9	05:22:40	2.6	Bottom	3	1	26.13	8.08	30.85	85.9	6.1	2.5	1.8
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	IS(Mf)9	05:22:56	2.6	Bottom	3	2	26.15	8.08	30.82	86.2	6.2	2.5	1.8
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	IS10(N)	05:27:15	1	Surface	1	1	26.33	8.07	31.15	90.6	6.5	2.7	2.0
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	IS10(N)	05:27:51	1	Surface	1	2	26.33	8.09	31.15	90.7	6.5	2.6	2.0
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	IS10(N)	05:27:37	5.4	Middle	2	1	26.27	8.08	31.40	89.6	6.5	2.7	2.0
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	IS10(N)	05:27:03	5.4	Middle	2	2	26.26	8.07	31.40	89.9	6.5	2.7	2.0
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	IS10(N)	05:26:54	9.7	Bottom	3	1	26.27	8.07	31.43	89.9	6.5	2.7	1.5
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	IS10(N)	05:27:29	9.7	Bottom	3	2	26.28	8.07	31.41	90.0	6.5	2.7	1.5
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	SR3(N)	06:00:08	1	Surface	1	1	26.14	8.08	30.71	85.5	6.1	2.7	2.7
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	SR3(N)	06:00:24	1	Surface	1	2	26.15	8.08	30.70	85.8	6.1	2.6	2.7
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	SR3(N)	06:00:16	2.6	Bottom	3	1	26.13	8.08	30.76	85.3	6.1	2.7	2.7
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	SR3(N)	05:59:58	2.6	Bottom	3	2	26.11	8.08	30.77	85.0	6.1	2.7	2.7
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	SR4(N3)	05:08:22	1	Surface	1	1	26.11	8.08	30.67	86.8	6.2	2.2	2.6
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	SR4(N3)	05:08:45	1	Surface	1	2	26.15	8.08	30.70	86.5	6.2	2.3	2.6
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	SR4(N3)	05:08:09	2.9	Bottom	3	1	26.13	8.09	30.97	87.1	6.2	2.4	2.3
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	SR4(N3)	05:08:37	2.9	Bottom	3	2	26.14	8.08	30.94	86.4	6.2	2.5	2.3
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	SR5(N)	05:45:23	1	Surface	1	1	26.31	8.09	31.16	90.3	6.5	2.7	1.9
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	SR5(N)	05:44:40	1	Surface	1	2	26.32	8.08	31.16	90.4	6.5	2.7	1.9
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	SR5(N)	05:45:09	4.6	Middle	2	1	26.28	8.08	31.35	89.6	6.5	2.7	2.3
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	SR5(N)	05:44:29	4.6	Middle	2	2	26.29	8.06	31.36	89.7	6.5	2.7	2.3
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	SR5(N)	05:44:18	8.1	Bottom	3	1	26.28	8.07	31.42	89.9	6.5	2.8	2.5
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	SR5(N)	05:44:59	8.1	Bottom	3	2	26.27	8.07	31.42	89.8	6.5	2.8	2.5
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	SR10A(N)	04:18:14	1	Surface	1	1	26.35	8.05	31.25	90.3	6.5	2.6	1.3
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	SR10A(N)	04:18:49	1	Surface	1	2	26.36	8.06	31.24	90.1	6.5	2.6	1.3
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	SR10A(N)	04:17:54	6.5	Middle	2	1	26.28	8.04	31.53	89.5	6.4	2.8	2.1
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	SR10A(N)	04:18:36	6.5	Middle	2	2	26.29	8.04	31.54	89.0	6.4	2.8	2.1
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	SR10A(N)	04:17:44	12	Bottom	3	1	26.29	8.05	31.55	89.8	6.5	2.8	2.3
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	SR10A(N)	04:18:27	12	Bottom	3	2	26.28	8.04	31.56	89.5	6.4	2.8	2.3
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	SR10B(N2)	04:05:49	1	Surface	1	1	26.40	8.05	31.24	95.7	6.9	2.7	1.3
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	SR10B(N2)	04:06:24	1	Surface	1	2	26.37	8.05	31.25	96.4	6.9	2.7	1.3
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	SR10B(N2)	04:05:36	3.7	Middle	2	1	26.31	8.05	31.43	93.4	6.7	2.9	1.6
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	SR10B(N2)	04:06:11	3.7	Middle	2	2	26.33	8.04	31.41	92.3	6.7	2.8	1.6
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	SR10B(N2)	04:05:24	6.3	Bottom	3	1	26.26	8.05	31.54	91.2	6.6	2.9	1.3
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	SR10B(N2)	04:06:01	6.3	Bottom	3	2	26.30	8.04	31.51	91.0	6.6	2.9	1.3
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	CS2(A)	06:37:43	1	Surface	1	1	26.29	8.08	31.16	90.8	6.6	3.0	1.8
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	CS2(A)	06:37:07	1	Surface	1	2	26.30	8.08	31.16	90.7	6.5	3.0	1.8
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	CS2(A)	06:37:32	3.5	Middle	2	1	26.26	8.09	31.31	90.2	6.5	3.0	1.6
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	CS2(A)	06:36:56	3.5	Middle	2	2	26.27	8.08	31.31	90.1	6.5	2.9	1.6
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	CS2(A)	06:36:45	6	Bottom	3	1	26.26	8.08	31.41	90.3	6.5	3.0	1.2
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	CS2(A)	06:37:22	6	Bottom	3	2	26.26	8.08	31.40	90.1	6.5	3.1	1.2
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	CS(Mf)5	04:16:28	1	Surface	1	1	26.47	8.07	31.36	86.6	6.1	2.6	2.2
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	CS(Mf)5	04:15:43	1	Surface	1	2	26.46	8.06	31.38	87.0	6.2	2.7	2.2
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	CS(Mf)5	04:16:11	6.3	Middle	2	1	26.32	8.05	31.64	85.2	6.0	2.7	1.5
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	CS(Mf)5	04:15:29	6.3	Middle	2	2	26.32	8.04	31.64	86.4	6.1	2.8	1.5
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	CS(Mf)5	04:16:02	11.5	Bottom	3	1	26.31	8.05	31.68	85.0	6.0	3.0	2.9
HKLR	HY/2011/03	2025-05-26	Mid-Flood	Fine	CS(Mf)5	04:15:20	11.5	Bottom	3	2	26.33	8.04	31.67	86.1	6.1	3.0	2.9
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	IS5	14:22:56	1	Surface	1	1	26.29	8.06	30.90	87.2	6.0	2.7	2.2
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	IS5	14:23:47	1	Surface	1	2	26.30	8.07	30.89	88.0	6.0	2.6	2.2
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	IS5	14:23:27	5.2	Middle	2	1	26.07	8.04	31.53	85.3	5.9	2.7	1.9
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	IS5	14:22:40	5.2	Middle	2	2	26.07	8.04	31.58	86.4	5.9	2.8	1.9
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	IS5	14:23:12	9.3	Bottom	3	1	26.08	8.04	31.70	83.9	5.8	2.9	2.5
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	IS5	14:22:25	9.3	Bottom	3	2	26.05	8.04	31.81	84.2	5.8	3.0	2.5
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	IS(Mf)6	14:11:16	1	Surface	1	1	26.28	8.06	30.91	88.9	6.1	2.6	3.3
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	IS(Mf)6	14:11:59	1	Surface	1	2	26.29	8.05	30.90	88.7	6.1	2.7	3.3
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	IS(Mf)6	14:11:43	4.9	Bottom	3	1	26.09	8.04	31.61	87.1	6.0	2.7	2.8
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	IS(Mf)6	14:11:02	4.9	Bottom	3	2	26.10	8.04	31.65	87.2	6.0	2.7	2.8
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	IS7	14:11:30	1	Surface	1	1	26.08	8.04	31.78	85.3	5.9	2.8	1.8
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	IS7	14:10:48	1	Surface	1	2	26.06	8.05	31.78	85.4	5.9	2.9	1.8
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	IS7	15:17:24	1.1	Bottom	3	1	26.33	8.05	31.17	90.2	6.2	2.7	3.1
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	IS7	15:16:35	1.1	Bottom	3	2	26.33	8.05	31.17	89.3	6.1	2.7	3.1
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	IS8(N)	15:16:15	1	Surface	1	1	26.11	8.04	31.99	87.9	6.0	2.9	2.9
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	IS8(N)	15:17:05	1	Surface	1	2	26.12	8.03	31.98	86.0	5.9	2.9	2.9
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	IS8(N)	15:16:51	12.3	Bottom	3	1	26.13	8.04	32.00	85.2	5.8	2.9	3.2
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	IS8(N)	15:16:01	12.3	Bottom	3	2	26.13	8.05	32.02	85.4	5.9	3.0	3.2
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	IS(Mf)9	15:27:36	1	Surface	1	1	26.33	8.04	31.19	87.2	6.0	2.7	2.9
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	IS(Mf)9	15:28:19	1	Surface	1	2	26.33	8.04	31.18	87.9	6.0	2.8	2.9
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	IS(Mf)9	15:28:07	3.7	Bottom	3	1	26.18	8.03	31.54	85.8	5.9	2.8	2.4
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	IS(Mf)9	15:27:24	3.7	Bottom	3	2	26.18	8.03	31.60	85.7	5.9	2.7	2.4
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	IS10(N)	15:27:53	1	Surface	1	1	26.15	8.03	31.91	86.9	6.0	3.0	2.5
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	IS10(N)	15:27:12	1	Surface	1	2	26.15	8.03	31.93	86.6	5.9	2.9	2.5
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	IS10(N)	13:17:49	2.2	Middle	2	1	25.99	8.04	31.03	91.5	6.3	3.0	3.1
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	IS10(N)	13:18:27	2.2	Middle	2	2	26.01	8.04	31.00	91.1	6.3	2.9	3.1
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	IS10(N)	13:18:13	3.4	Bottom	3	1	25.85	8.03	31.47	89.3	6.2	2.9	2.8
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	IS10(N)	13:17:37	3.4	Bottom	3	2	25.84	8.04	31.48	89.2	6.2	3.1	2.8
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	SR3(N)	13:18:03	1	Surface	1	1	25.86	8.03	31.68	88.2	6.1	3.1	3.0
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	SR3(N)	13:17:25	1	Surface	1	2	25.84	8.04	31.81	87.7	6.1	3.1	3.0
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	SR3(N)	06:24:50	1	Bottom	3	1	26.17	8.04	31.08	88.2	6.1	2.8	3.4
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	SR3(N)	06:25:31	1	Bottom	3	2	26.23	8.05	30.95	87.3	6.0	2.6	3.4
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	SR4(N3)	06:24:33	1	Surface	1	1	26.05	8.03	31.74	86.0	5.9	2.8	3.4
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	SR4(N3)	06:25:12	1	Surface	1	2	26.05	8.04	31.76	86.2	5.9	2.8	3.4
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	SR4(N3)	06:24:22	9.8	Bottom	3	1	26.03	8.03	31.83	85.4	5.9	2.9	2.6
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	SR4(N3)	06:25:04	9.8	Bottom	3	2	26.05	8.03	31.79	84.7	5.8	2.8	2.6
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	SR5(N)	06:39:28	1	Surface	1	1	26.23	8.05	30.93	87.7	6.0	2.8	4.2
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	SR5(N)	06:38:30	1	Surface	1	2	26.23	8.05	30.93	87.3	6.0	2.8	4.2
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	SR5(N)	06:38:12	4.9	Middle	2	1	26.07	8.03	31.65	84.5	5.8	2.8	2.7
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	SR5(N)	06:39:08	4.9	Middle	2	2	26.03	8.03	31.60	85.6	5.9	2.8	2.7
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	SR5(N)	06:38:01	8.8	Bottom	3	1	26.04	8.03	31.81	84.0	5.8	2.8	3.2
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	SR5(N)	06:38:57	8.8	Bottom	3	2	26.04	8.03	31.79	84.1	5.8	2.9	3.2

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	SR10A(N)	05:26:56	1	Surface	1	1	26.25	8.03	30.98	87.1	6.0	2.6	2.6
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	SR10A(N)	05:27:47	1	Surface	1	2	26.26	8.04	30.97	87.3	6.0	2.6	2.6
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	SR10A(N)	05:26:33	6.7	Middle	2	1	26.03	8.02	31.90	85.5	5.9	2.8	2.8
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	SR10A(N)	05:27:26	6.7	Middle	2	2	26.04	8.02	31.90	83.9	5.8	2.8	2.8
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	SR10A(N)	05:26:21	12.3	Bottom	3	1	26.02	8.02	31.95	83.9	5.8	2.8	2.6
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	SR10A(N)	05:27:10	12.3	Bottom	3	2	26.03	8.01	31.93	83.9	5.8	2.8	2.6
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	SR10B(N2)	05:15:47	1	Surface	1	1	26.25	8.03	30.99	90.2	6.2	2.5	2.7
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	SR10B(N2)	05:15:08	1	Surface	1	2	26.26	8.04	30.99	90.2	6.2	2.5	2.7
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	SR10B(N2)	05:15:33	3.7	Middle	2	1	26.09	8.02	31.53	86.3	5.9	2.7	2.7
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	SR10B(N2)	05:14:51	3.7	Middle	2	2	26.08	8.03	31.52	86.6	6.0	2.6	2.7
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	SR10B(N2)	05:15:21	6.4	Bottom	3	1	26.07	8.02	31.78	87.0	6.0	2.8	3.0
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	SR10B(N2)	05:14:34	6.4	Bottom	3	2	26.02	8.04	31.89	86.8	6.0	2.8	3.0
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	CS2(A)	07:29:49	1	Surface	1	1	26.21	8.05	30.94	87.1	6.0	2.9	3.5
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	CS2(A)	07:29:11	1	Surface	1	2	26.19	8.05	30.98	87.4	6.0	3.0	3.5
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	CS2(A)	07:29:36	3.4	Middle	2	1	26.07	8.04	31.36	86.0	5.9	3.0	2.2
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	CS2(A)	07:29:01	3.4	Middle	2	2	26.07	8.04	31.39	86.3	5.9	2.9	2.2
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	CS2(A)	07:28:51	5.7	Bottom	3	1	26.07	8.04	31.62	86.1	5.9	2.9	3.6
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	CS2(A)	07:29:26	5.7	Bottom	3	2	26.07	8.04	31.69	85.5	5.9	3.0	3.6
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	CS(Mf)5	13:24:56	1	Surface	1	1	26.46	8.05	30.18	85.6	5.9	2.4	2.6
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	CS(Mf)5	13:25:34	1	Surface	1	2	26.51	8.04	30.18	85.7	5.9	2.4	2.6
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	CS(Mf)5	13:25:20	4.3	Middle	2	1	26.26	8.04	30.48	84.7	5.8	2.4	2.5
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	CS(Mf)5	13:24:42	4.3	Middle	2	2	26.24	8.04	30.48	85.0	5.8	2.6	2.5
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	CS(Mf)5	13:25:08	7.5	Bottom	3	1	26.27	8.04	30.48	84.4	5.8	2.7	2.9
HKLR	HY/2011/03	2025-05-28	Mid-Ebb	Fine	CS(Mf)5	13:24:32	7.5	Bottom	3	2	26.23	8.04	30.50	85.1	5.8	2.7	2.9
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	IS5	13:34:54	1	Surface	1	1	26.51	8.06	30.13	89.4	6.1	2.6	3.7
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	IS5	13:35:11	1	Surface	1	2	26.53	8.05	30.14	90.2	6.2	2.5	3.7
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	IS5	13:35:01	1	Middle	2	1	26.45	8.05	30.28	88.1	6.0	2.7	3.4
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	IS5	13:34:42	1	Middle	2	2	26.40	8.08	30.27	87.7	6.0	2.7	3.4
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	IS5	13:45:33	1	Bottom	3	1	26.51	8.05	30.12	86.8	6.0	2.6	2.2
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	IS5	13:45:52	1	Bottom	3	2	26.51	8.05	30.10	86.6	5.9	2.3	2.2
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	IS(Mf)6	13:45:25	1	Surface	1	1	26.39	8.05	30.28	86.8	6.0	2.8	2.5
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	IS(Mf)6	13:45:41	1	Surface	1	2	26.42	8.05	30.24	86.4	5.9	2.8	2.5
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	IS(Mf)6	14:20:53	1	Bottom	3	1	26.56	8.05	30.09	85.7	5.9	2.4	3.1
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	IS(Mf)6	14:20:34	1	Bottom	3	2	26.55	8.04	30.10	85.4	5.9	2.2	3.1
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	IS7	14:20:43	1	Surface	1	1	26.44	8.04	30.22	85.5	5.9	2.8	4.6
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	IS7	14:20:24	1	Surface	1	2	26.37	8.03	30.27	84.8	5.8	2.8	4.6
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	IS7	13:55:05	1.1	Bottom	3	1	26.53	8.05	30.12	85.7	5.9	2.5	2.7
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	IS7	13:54:46	1.1	Bottom	3	2	26.52	8.05	30.10	85.9	5.9	2.5	2.7
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	IS8(N)	13:54:38	1	Surface	1	1	26.38	8.04	30.29	85.8	5.9	2.9	2.2
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	IS8(N)	13:54:56	1	Surface	1	2	26.42	8.05	30.30	85.7	5.9	2.8	2.2
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	IS8(N)	13:10:59	1	Bottom	3	1	26.48	8.06	30.17	90.4	6.2	2.8	3.0
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	IS8(N)	13:10:43	1	Bottom	3	2	26.48	8.07	30.16	89.4	6.1	2.7	3.0
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	IS(Mf)9	13:10:32	1	Surface	1	1	26.42	8.07	30.25	88.6	6.1	2.9	1.8
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	IS(Mf)9	13:10:51	1	Surface	1	2	26.45	8.06	30.22	88.6	6.1	2.9	1.8
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	IS(Mf)9	14:10:58	1	Bottom	3	1	26.53	8.05	30.08	85.2	5.8	2.5	2.3
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	IS(Mf)9	14:11:13	1	Bottom	3	2	26.50	8.04	30.11	85.2	5.8	2.5	2.3
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	IS10(N)	14:10:47	1	Surface	1	1	26.41	8.04	30.23	85.0	5.8	3.0	2.9
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	IS10(N)	14:11:05	1	Surface	1	2	26.45	8.04	30.25	85.0	5.8	3.0	2.9
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	IS10(N)	15:01:30	3.8	Middle	2	1	26.69	8.08	30.61	84.5	5.7	2.6	2.2
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	IS10(N)	15:02:12	3.8	Middle	2	2	26.73	8.08	30.63	85.4	5.8	2.6	2.2
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	IS10(N)	15:01:58	6.6	Bottom	3	1	26.34	8.06	31.86	82.5	5.6	2.8	2.7
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	IS10(N)	15:01:16	6.6	Bottom	3	2	26.33	8.07	31.87	82.6	5.6	2.6	2.7
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	SR3(N)	15:01:46	1	Surface	1	1	26.33	8.05	31.06	82.4	5.6	2.3	3.1
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	SR3(N)	15:01:06	1	Surface	1	2	26.28	8.06	31.92	81.9	5.6	2.7	3.1
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	SR3(N)	06:46:36	1	Bottom	3	1	26.37	8.07	30.11	85.3	5.9	2.7	3.5
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	SR3(N)	06:45:41	1	Bottom	3	2	26.43	8.07	30.12	87.9	6.0	2.7	3.5
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	SR4(N3)	06:45:23	1	Surface	1	1	26.01	8.06	30.45	82.2	5.6	2.8	2.6
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	SR4(N3)	06:46:19	1	Surface	1	2	26.03	8.04	30.46	83.0	5.6	2.9	2.6
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	SR4(N3)	06:45:12	7.6	Bottom	3	1	25.92	8.05	30.49	82.4	5.6	2.9	2.2
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	SR4(N3)	06:45:58	7.6	Bottom	3	2	26.01	8.03	30.49	82.6	5.6	2.9	2.2
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	SR5(N)	06:35:20	1	Surface	1	1	26.40	8.06	30.08	84.5	5.8	2.5	2.5
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	SR5(N)	06:35:39	1	Surface	1	2	26.41	8.05	30.07	84.6	5.8	2.4	2.5
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	SR5(N)	06:35:09	1	Middle	2	1	26.30	8.05	30.26	84.4	5.7	2.7	2.4
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	SR5(N)	06:35:29	1	Middle	2	2	26.33	8.04	30.24	84.3	5.7	2.8	2.4
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	SR5(N)	06:26:24	1	Bottom	3	1	26.39	8.06	30.11	85.3	5.8	2.7	2.8
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	SR5(N)	06:26:42	1	Bottom	3	2	26.47	8.06	30.09	85.2	5.8	2.6	2.8
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	SR10A(N)	06:26:15	1	Surface	1	1	26.28	8.05	30.27	85.5	5.8	2.7	2.3
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	SR10A(N)	06:26:30	1	Surface	1	2	26.33	8.05	30.21	84.9	5.8	2.7	2.3
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	SR10A(N)	05:53:58	2.1	Middle	2	1	26.39	8.07	30.07	88.5	6.1	2.5	2.6
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	SR10A(N)	05:53:34	2.1	Middle	2	2	26.43	8.07	30.03	87.5	6.0	2.5	2.6
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	SR10A(N)	05:53:43	3.1	Bottom	3	1	26.30	8.06	30.35	86.5	5.9	2.5	2.6
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	SR10A(N)	05:53:22	3.1	Bottom	3	2	26.17	8.06	30.39	85.4	5.8	2.7	2.6
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	SR10B(N2)	06:17:56	1	Surface	1	1	26.42	8.07	30.06	84.4	5.8	2.4	2.9
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	SR10B(N2)	06:18:17	1	Surface	1	2	26.42	8.06	30.01	84.4	5.8	2.3	2.9
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	SR10B(N2)	06:18:05	1	Middle	2	1	26.31	8.05	30.23	84.1	5.7	2.5	2.8
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	SR10B(N2)	06:17:46	1	Middle	2	2	26.20	8.05	30.20	84.0	5.7	2.4	2.8
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	SR10B(N2)	07:00:42	1	Bottom	3	1	26.42	8.05	30.14	83.7	5.7	2.8	3.0
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	SR10B(N2)	07:01:01	1	Bottom	3	2	26.41	8.05	30.11	84.0	5.7	2.7	3.0
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	CS2(A)	07:00:33	1	Surface	1	1	26.29	8.05	30.26	83.2	5.7	2.9	3.0
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	CS2(A)	07:00:52	1	Surface	1	2	26.32	8.05	30.23	83.5	5.7	2.9	3.0
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	CS2(A)	06:04:21	2	Middle	2	1	26.40	8.07	30.04	84.7	5.8	2.4	3.3
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	CS2(A)	06:04:42	2	Middle	2	2	26.42	8.06	30.01	84.4	5.8	2.4	3.3
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	CS2(A)	06:04:06	3	Bottom	3	1	26.24	8.06	30.40	84.3	5.7	2.5	2.2
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	CS2(A)	06:04:32	3	Bottom	3	2	26.32	8.05	30.32	84.2	5.7	2.6	2.2
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	CS(Mf)5	05:16:13	1	Surface	1	1	26.56	8.06	30.38	85.7	5.8	2.6	3.1
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	CS(Mf)5	05:17:02	1	Surface	1	2	26.53	8.07	30.39	85.3	5.7	2.4	3.1
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	CS(Mf)5	05:16:43	6.5	Middle	2	1	26.11	8.04	31.73	83.4	5.6	2.5	2.0
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	CS(Mf)5	05:15:59	6.5	Middle	2	2	26.14	8.05	31.73	84.5	5.7	2.6	2.0
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	CS(Mf)5	05:15:48	12	Bottom	3	1	26.13	8.04	31.75	83.8	5.7	2.9	2.4
HKLR	HY/2011/03	2025-05-28	Mid-Flood	Fine	CS(Mf)5	05:16:31	12	Bottom	3	2	26.15	8.03	31.76	83.0	5.6	3.0	2.4
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	IS5	14:12:02	1	Surface	1	1	26.06	8.01	30.39	92.4	6.4	3.2	3.0
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	IS5	14:12:48	1	Surface	1	2	26.07	8.01	30.52	94.0	6.5	3.2	3.0
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	IS5	14:11:53	4	Middle	2	1	26.04	8.03	30.99	92.2	6.4	3.2	2.4
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	IS5	14:12:27	4	Middle	2	2	26.00	8.01	31.00	93.5	6.4	3.3	2.4
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	IS5	14:11:34	7	Bottom	3	1	26.09	8.02	30.93	91.4	6.3	3.2	2.9
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	IS5	14:12:09	7	Bottom	3	2	25.77	8.01	30.98	92.2	6.4	3.3	2.9
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	IS(Mf)6	14:21:25	1	Surface	1	1	26.10	8.01	30.54	91.6	6.3	3.4	2.8
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	IS(Mf)6	14:21:55	1	Surface	1	2	26.09	8.01	30.55	91.4	6.3	3.3	2.8
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	IS(Mf)6	14:21:04	2	Bottom	3	1	26.04	8.01	30.75	91.4	6.3	3.4	5.0
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	IS(Mf)6	14:21:38	2	Bottom	3	2	26.04	8.01	30.81	91.3	6.3	3.4	5.0
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	IS7	14:31:35	1	Surface	1	1	26.13	8.02	30.39	91.0	6.3	3.3	3.2
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	IS7	14:31:59	1	Surface	1	2	26.11	8.03	30.38	91.3	6.3	3.3	3.2
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	IS7	14:31:24	2	Bottom	3	1	26.05	8.01	30.62	90.9	6.3	3.3	3.8
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	IS7	14:31:49	2	Bottom	3	2	26.09	8.02	30.59	90.6	6.3	3.3	3.8
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	IS8(N)	15:05:52	1	Surface	1	1	26.05	8.02	30.51	92.4	6.4	3.2	4.1
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	IS8(N)	15:06:22	1	Surface	1	2	26.12	8.02	30.47	92.2	6.4	3.2	4.1
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	IS8(N)	15:05:39	2.8	Bottom	3	1	25.91	8.01	30.75	92.2	6.4	3.2	3.6
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	IS8(N)	15:06:01	2.8	Bottom	3	2	25.95	8.01	30.74	92.1	6.4	3.2	3.6
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	IS(Mf)9	14:41:04	1	Surface	1	1	26.12	8.03	30.39	92.0	6.4	3.1	3.2
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	IS(Mf)9	14:41:41	1	Surface	1	2	26.11	8.03	30.44	92.2	6.4	3.1	3.2
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	IS(Mf)9	14:40:49	2.5	Bottom	3	1	26.10	8.03	30.92	92.2	6.4	3.1	3.8
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	IS(Mf)9	14:41:22	2.5	Bottom	3	2	26.06	8.03	30.60	92.1	6.4	3.1	3.8
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	IS10(N)	15:13:08	1	Surface	1	1	26.04	8.10	30.38	88.4	6.2	3.3	3.5
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	IS10(N)	15:13:55	1	Surface	1	2	26.03	8.12	30.35	89.2	6.2	3.2	3.5
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	IS10(N)	15:12:55	5.3	Middle	2	1	25.96	8.09	30.98	87.8	6.1	3.4	3.2

Project	Works	Date (yyyy-mm-dd)	Tide	Weather Condition	Station	Time	Depth, m	Level	Level_Code	Replicate	Temperature, °C	pH	Salinity, ppt	DO, %	DO, mg/L	Turbidity, NTU	SS, mg/L
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	IS10(N)	15:13:35	5.3	Middle	2	2	25.95	8.09	30.95	87.5	6.1	3.4	3.2
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	IS10(N)	15:13:23	9.6	Bottom	3	1	25.95	8.09	31.04	86.8	6.0	3.4	3.1
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	IS10(N)	15:12:43	9.6	Bottom	3	2	25.94	8.09	31.11	86.8	6.0	3.3	3.1
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	SR3(N)	13:55:39	1	Surface	1	1	25.82	8.02	30.34	91.9	6.4	3.5	3.4
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	SR3(N)	13:56:00	1	Surface	1	2	25.82	8.02	30.30	92.2	6.4	3.5	3.4
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	SR3(N)	13:55:22	2	Bottom	3	1	25.81	8.02	30.62	91.8	6.4	3.6	4.5
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	SR3(N)	13:55:49	2	Bottom	3	2	26.01	8.03	30.45	91.5	6.3	3.5	4.5
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	SR4(N3)	14:56:10	1	Surface	1	1	26.03	8.02	30.43	92.3	6.4	3.2	3.1
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	SR4(N3)	14:56:44	1	Surface	1	2	26.03	8.02	30.43	92.1	6.4	3.2	3.1
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	SR4(N3)	14:55:53	2.8	Bottom	3	1	25.92	8.02	30.58	92.2	6.4	3.2	3.1
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	SR4(N3)	14:56:24	2.8	Bottom	3	2	25.93	8.02	30.62	92.3	6.4	3.2	3.1
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	SR5(N)	15:00:54	1	Surface	1	1	26.02	8.09	30.38	89.5	6.2	3.1	2.6
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	SR5(N)	15:01:31	1	Surface	1	2	26.09	8.09	30.38	89.8	6.2	3.2	2.6
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	SR5(N)	15:01:18	4.9	Middle	2	1	25.98	8.08	30.95	88.8	6.2	3.2	3.4
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	SR5(N)	15:00:41	4.9	Middle	2	2	25.97	8.07	30.96	88.7	6.2	3.3	3.4
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	SR5(N)	15:01:07	8.8	Bottom	3	1	25.95	8.07	31.08	87.7	6.1	3.6	2.7
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	SR5(N)	15:00:29	8.8	Bottom	3	2	25.95	8.08	31.09	87.3	6.1	3.7	2.7
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	SR10A(N)	16:09:28	1	Surface	1	1	26.16	8.08	31.07	93.0	6.4	2.8	2.2
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	SR10A(N)	16:08:42	1	Surface	1	2	26.16	8.09	31.05	91.7	6.3	2.8	2.2
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	SR10A(N)	16:08:23	6.5	Middle	2	1	26.01	8.09	31.57	89.1	6.2	3.0	2.6
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	SR10A(N)	16:09:10	6.5	Middle	2	2	26.02	8.07	31.56	87.8	6.1	3.0	2.6
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	SR10A(N)	16:08:58	12	Bottom	3	1	26.03	8.08	31.56	87.6	6.1	3.1	2.6
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	SR10A(N)	16:08:10	12	Bottom	3	2	26.03	8.11	31.59	88.3	6.1	3.1	2.6
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	SR10B(N2)	16:20:03	1	Surface	1	1	26.16	8.10	31.08	88.9	6.1	2.8	3.0
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	SR10B(N2)	16:19:25	1	Surface	1	2	26.16	8.09	31.08	88.6	6.1	2.7	3.0
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	SR10B(N2)	16:19:52	3.9	Middle	2	1	26.06	8.09	31.30	87.6	6.1	2.9	2.6
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	SR10B(N2)	16:19:13	3.9	Middle	2	2	26.06	8.09	31.32	87.6	6.1	2.8	2.6
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	SR10B(N2)	16:19:39	6.7	Bottom	3	1	26.04	8.09	31.49	88.2	6.1	3.1	3.0
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	SR10B(N2)	16:19:02	6.7	Bottom	3	2	26.06	8.09	31.50	88.2	6.1	3.0	3.0
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	CS2(A)	14:11:45	1	Surface	1	1	25.88	8.07	30.48	93.9	6.6	3.4	3.0
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	CS2(A)	14:12:20	1	Surface	1	2	25.91	8.07	30.46	92.7	6.5	3.2	3.0
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	CS2(A)	14:12:09	3.4	Middle	2	1	25.83	8.06	30.94	89.6	6.3	3.3	3.5
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	CS2(A)	14:11:34	3.4	Middle	2	2	25.83	8.08	30.94	90.1	6.3	3.5	3.5
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	CS2(A)	14:11:23	5.8	Bottom	3	1	25.84	8.08	31.17	89.5	6.3	3.7	3.4
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	CS2(A)	14:11:57	5.8	Bottom	3	2	25.84	8.06	31.09	89.4	6.2	3.8	3.4
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	CS(Mf)5	15:51:09	1	Surface	1	1	26.14	8.03	30.44	91.0	6.3	3.2	2.7
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	CS(Mf)5	15:52:17	1	Surface	1	2	26.07	8.04	30.51	91.6	6.4	3.1	2.7
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	CS(Mf)5	15:50:57	5.8	Middle	2	1	25.89	8.03	30.95	90.3	6.3	3.2	2.6
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	CS(Mf)5	15:51:32	5.8	Middle	2	2	25.88	8.03	30.40	91.3	6.3	3.2	2.6
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	CS(Mf)5	15:50:44	10.6	Bottom	3	1	25.86	8.03	30.94	90.2	6.3	3.2	2.9
HKLR	HY/2011/03	2025-05-30	Mid-Ebb	Fine	CS(Mf)5	15:51:23	10.6	Bottom	3	2	25.85	8.03	30.90	91.3	6.3	3.1	2.9
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	IS5	08:31:06	1	Surface	1	1	26.01	8.01	30.38	94.1	6.5	3.3	3.0
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	IS5	08:31:51	1	Surface	1	2	26.14	8.02	30.24	93.7	6.5	3.3	3.0
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	IS5	08:30:48	4.2	Middle	2	1	26.15	8.01	30.84	94.0	6.5	3.4	2.8
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	IS5	08:31:30	4.2	Middle	2	2	26.13	8.01	30.83	92.7	6.5	3.4	2.8
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	IS5	08:30:20	7.4	Bottom	3	1	25.87	8.01	30.88	93.9	6.5	3.4	2.8
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	IS5	08:31:24	7.4	Bottom	3	2	26.05	8.01	30.88	92.2	6.4	3.4	2.8
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	IS(Mf)6	08:21:02	1	Surface	1	1	26.26	8.03	30.56	91.0	6.3	3.2	3.3
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	IS(Mf)6	08:21:35	1	Surface	1	2	26.26	8.03	30.51	91.0	6.3	3.3	3.3
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	IS(Mf)6	08:20:55	2.2	Bottom	3	1	26.15	8.04	30.59	90.2	6.3	3.3	3.1
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	IS(Mf)6	08:21:13	2.2	Bottom	3	2	26.15	8.04	30.24	91.2	6.4	3.2	3.1
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	IS7	08:12:40	1	Surface	1	1	26.12	8.03	30.32	91.6	6.4	3.4	3.4
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	IS7	08:13:00	1	Surface	1	2	26.17	8.03	30.29	91.6	6.4	3.4	3.4
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	IS7	08:12:10	2	Bottom	3	1	25.90	8.02	30.60	91.2	6.4	3.4	3.3
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	IS7	08:12:49	2	Bottom	3	2	26.10	8.02	30.55	91.5	6.4	3.4	3.3
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	IS8(N)	07:36:44	1	Surface	1	1	26.25	8.01	30.38	92.2	6.4	3.2	2.6
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	IS8(N)	07:37:14	1	Surface	1	2	26.24	8.01	30.30	92.0	6.4	3.1	2.6
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	IS8(N)	07:36:28	3.1	Bottom	3	1	26.18	8.00	30.63	92.1	6.4	3.2	3.2
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	IS8(N)	07:36:59	3.1	Bottom	3	2	26.18	8.00	30.59	91.8	6.4	3.2	3.2
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	IS(Mf)9	08:02:09	1	Surface	1	1	26.18	8.02	30.22	91.1	6.3	3.3	3.6
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	IS(Mf)9	08:02:28	1	Surface	1	2	26.07	8.01	30.23	91.0	6.3	3.3	3.6
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	IS(Mf)9	08:01:48	2.5	Bottom	3	1	26.00	8.02	30.42	91.0	6.3	3.3	2.6
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	IS(Mf)9	08:02:16	2.5	Bottom	3	2	26.01	8.02	30.48	90.8	6.3	3.3	2.6
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	IS10(N)	08:02:06	1	Surface	1	1	25.92	8.07	30.52	91.7	6.4	3.1	3.5
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	IS10(N)	08:02:46	1	Surface	1	2	25.94	8.08	30.44	90.5	6.3	3.0	3.5
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	IS10(N)	08:01:49	5.4	Middle	2	1	25.82	8.06	30.96	88.5	6.2	3.3	2.5
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	IS10(N)	08:02:29	5.4	Middle	2	2	25.82	8.07	30.97	87.9	6.1	3.4	2.5
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	IS10(N)	08:02:20	9.8	Bottom	3	1	25.82	8.06	30.98	87.1	6.1	3.7	3.9
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	IS10(N)	08:01:37	9.8	Bottom	3	2	25.82	8.07	31.01	87.6	6.1	3.7	3.9
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	SR3(N)	08:46:43	1	Surface	1	1	26.02	8.02	30.37	90.0	6.2	3.4	3.5
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	SR3(N)	08:47:16	1	Surface	1	2	26.01	8.02	30.37	90.0	6.2	3.5	3.5
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	SR3(N)	08:46:18	2	Bottom	3	1	25.94	8.01	30.54	89.6	6.2	3.4	3.0
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	SR3(N)	08:47:01	2	Bottom	3	2	25.98	8.02	30.63	90.6	6.3	3.4	3.0
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	SR4(N3)	07:48:22	1	Surface	1	1	26.26	8.02	30.27	91.2	6.3	3.1	3.6
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	SR4(N3)	07:48:56	1	Surface	1	2	26.28	8.02	30.25	91.0	6.3	3.1	3.6
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	SR4(N3)	07:48:15	3	Bottom	3	1	26.17	8.02	30.23	91.2	6.3	3.1	2.6
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	SR4(N3)	07:48:40	3	Bottom	3	2	26.20	8.02	30.60	90.9	6.3	3.2	2.6
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	SR5(N)	08:11:41	1	Surface	1	1	25.94	8.10	30.45	88.6	6.2	3.4	2.3
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	SR5(N)	08:10:53	1	Surface	1	2	25.95	8.09	30.45	88.3	6.2	3.1	2.3
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	SR5(N)	08:11:25	4.9	Middle	2	1	25.83	8.08	30.86	87.2	6.1	3.4	3.1
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	SR5(N)	08:10:39	4.9	Middle	2	2	25.83	8.08	30.89	86.6	6.0	3.4	3.1
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	SR5(N)	08:10:28	8.7	Bottom	3	1	25.82	8.07	30.99	86.5	6.0	3.6	3.6
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	SR5(N)	08:11:15	8.7	Bottom	3	2	25.82	8.08	30.99	86.4	6.0	3.7	3.6
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	SR10A(N)	07:05:18	1	Surface	1	1	26.13	8.06	30.78	87.5	6.1	2.9	2.6
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	SR10A(N)	07:06:03	1	Surface	1	2	26.14	8.08	30.78	88.0	6.1	2.9	2.6
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	SR10A(N)	07:04:59	6.6	Middle	2	1	25.98	8.05	31.36	86.4	6.0	3.1	2.8
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	SR10A(N)	07:05:45	6.6	Middle	2	2	25.97	8.06	31.37	85.5	5.9	3.1	2.8
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	SR10A(N)	07:05:32	12.2	Bottom	3	1	25.97	8.05	31.39	85.7	5.9	3.3	2.2
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	SR10A(N)	07:04:48	12.2	Bottom	3	2	25.98	8.06	31.39	85.8	5.9	3.4	2.2
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	SR10B(N2)	06:54:47	1	Surface	1	1	26.14	8.05	30.78	93.7	6.5	2.9	1.7
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	SR10B(N2)	06:54:05	1	Surface	1	2	26.16	8.04	30.77	94.8	6.6	2.9	1.7
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	SR10B(N2)	06:54:33	3.8	Middle	2	1	26.02	8.04	31.12	88.2	6.1	3.1	3.2
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	SR10B(N2)	06:53:47	3.8	Middle	2	2	26.01	8.04	31.12	89.9	6.2	3.1	3.2
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	SR10B(N2)	06:54:21	6.5	Bottom	3	1	26.01	8.04	31.29	88.1	6.1	3.4	2.6
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	SR10B(N2)	06:53:34	6.5	Bottom	3	2	25.97	8.04	31.36	88.3	6.1	3.3	2.6
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	CS2(A)	09:05:39	1	Surface	1	1	25.91	8.09	30.46	88.1	6.1	3.2	2.0
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	CS2(A)	09:04:58	1	Surface	1	2	25.92	8.09	30.49	88.2	6.1	3.2	2.0
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	CS2(A)	09:05:26	3.4	Middle	2	1	25.83	8.08	30.73	87.2	6.1	3.3	1.8
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	CS2(A)	09:04:46	3.4	Middle	2	2	25.84	8.09	30.76	87.4	6.1	3.3	1.8
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	CS2(A)	09:04:35	5.7	Bottom	3	1	25.82	8.10	30.91	87.2	6.1	3.4	3.1
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	CS2(A)	09:05:13	5.7	Bottom	3	2	25.83	8.09	30.95	86.8	6.1	3.6	3.1
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	CS(Mf)5	06:52:02	1	Surface	1	1	26.24	8.04	30.19	89.5	6.2	3.1	2.6
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	CS(Mf)5	06:52:57	1	Surface	1	2	26.07	8.04	30.24	89.7	6.2	3.2	2.6
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	CS(Mf)5	06:51:41	6	Middle	2	1	25.96	8.02	30.89	89.4	6.2	3.2	2.8
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	CS(Mf)5	06:52:33	6	Middle	2	2	26.20	8.03	30.85	89.1	6.2	3.2	2.8
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	CS(Mf)5	06:50:41	11	Bottom	3	1	25.93	8.02	30.91	89.1	6.2	3.2	3.2
HKLR	HY/2011/03	2025-05-30	Mid-Flood	Fine	CS(Mf)5	06:52:15	11	Bottom	3	2	25.97	8.03	30.86	88.7	6.1	3.2	3.2

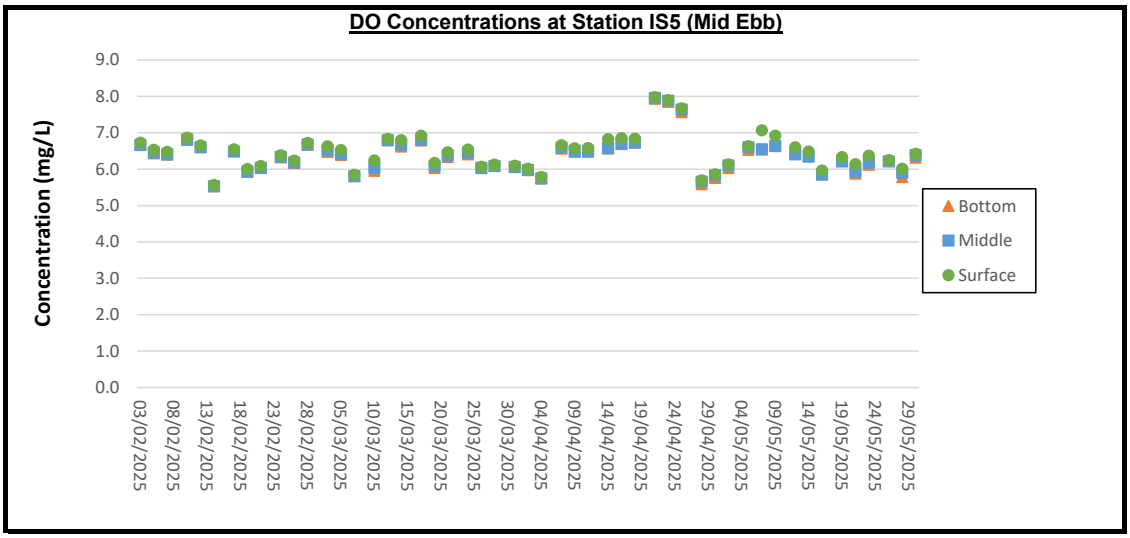
DO Concentrations at Station IS5 (Mid Ebb)
Concentration (mg/L)
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

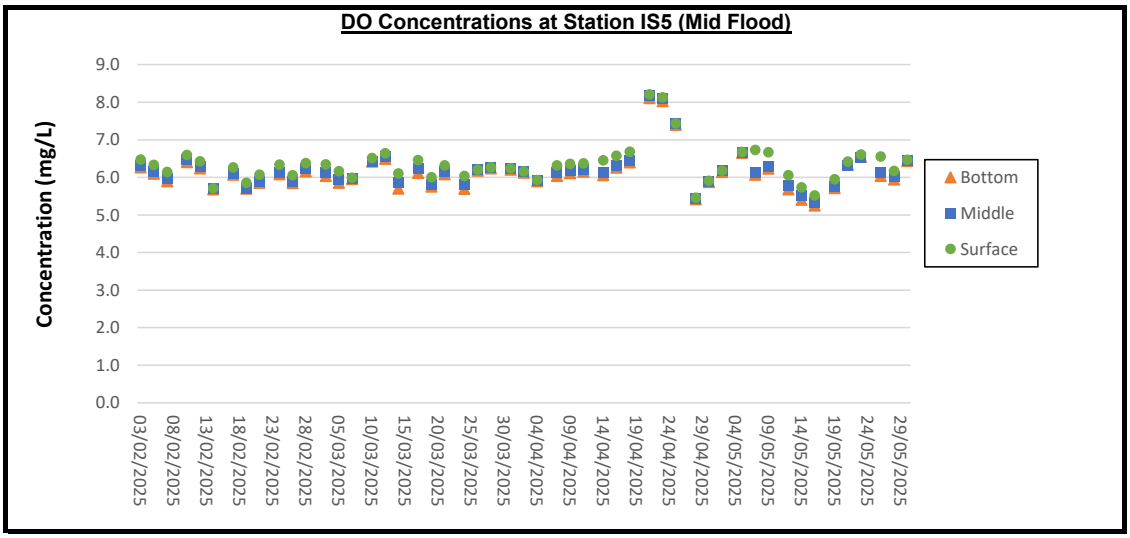
DO Concentrations at Station IS5 (Mid Flood)
Concentration (mg/L)
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

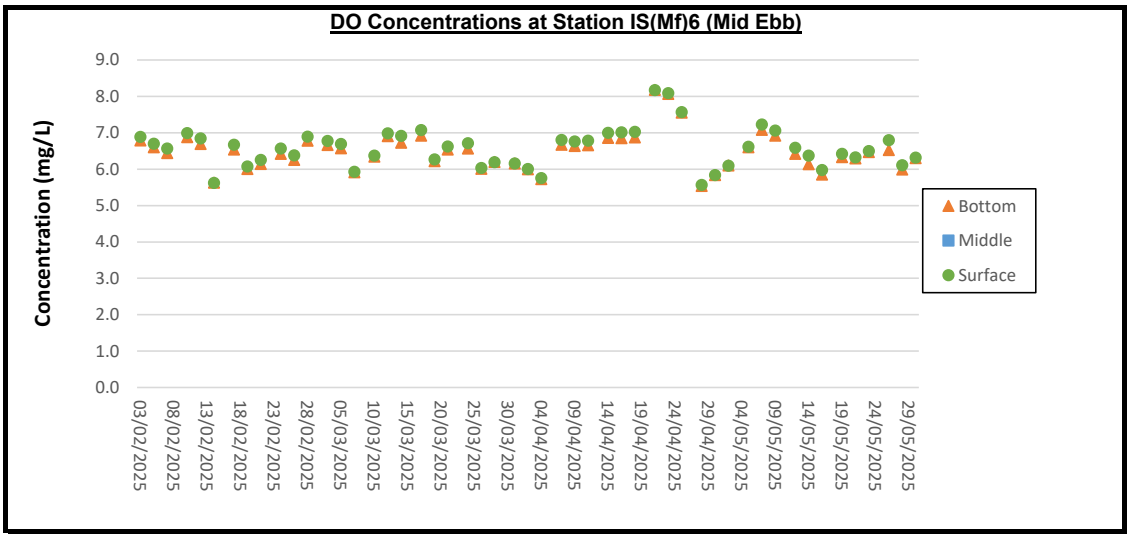
DO Concentrations at Station IS(Mf)6 (Mid Ebb)
Concentration (mg/L)
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

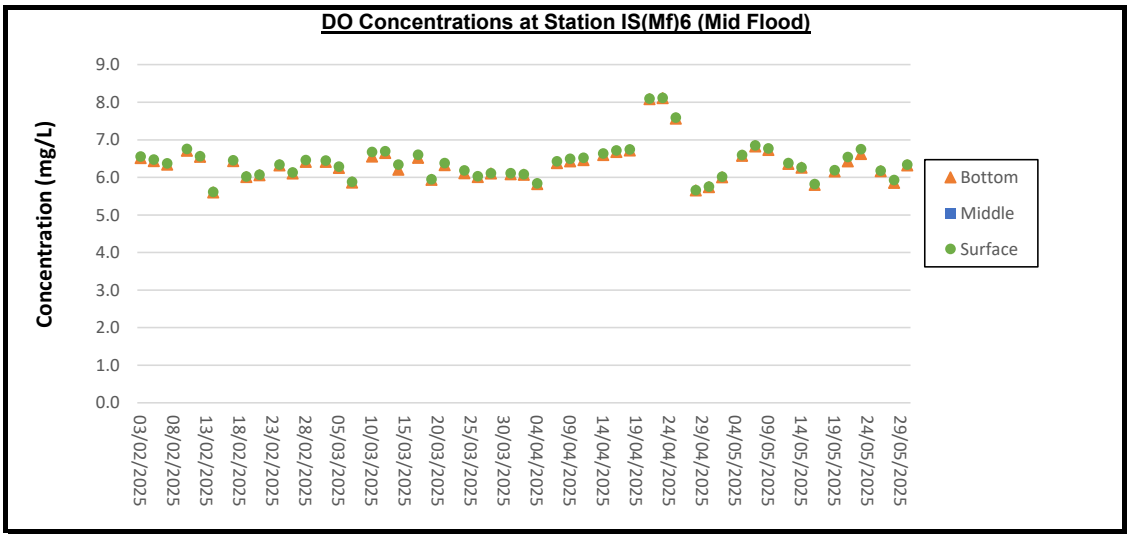
DO Concentrations at Station IS(Mf)6 (Mid Flood)
Concentration (mg/L)
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

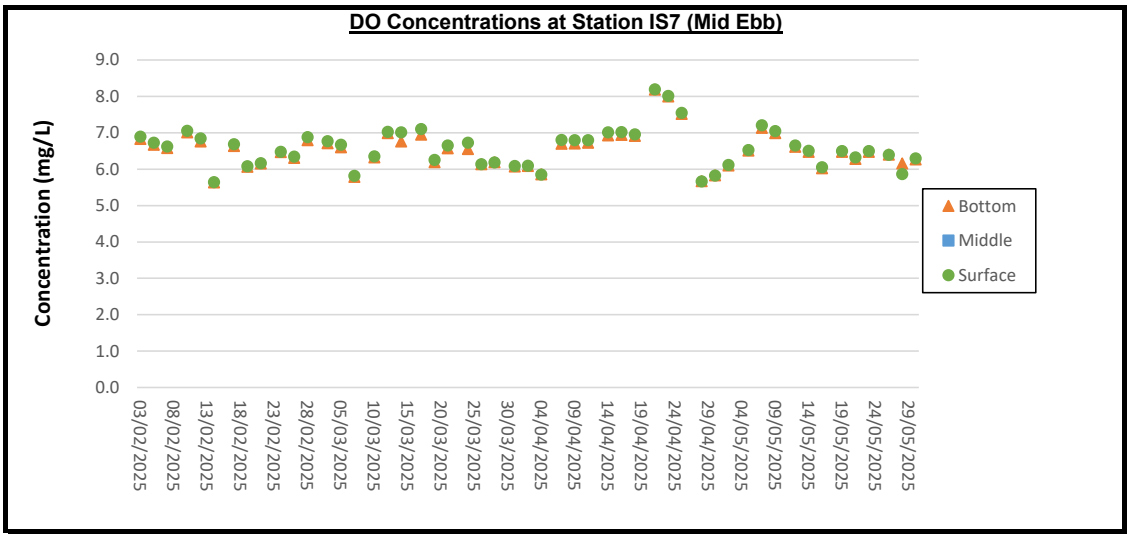
DO Concentrations at Station IS7 (Mid Ebb)
Concentration (mg/L)
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

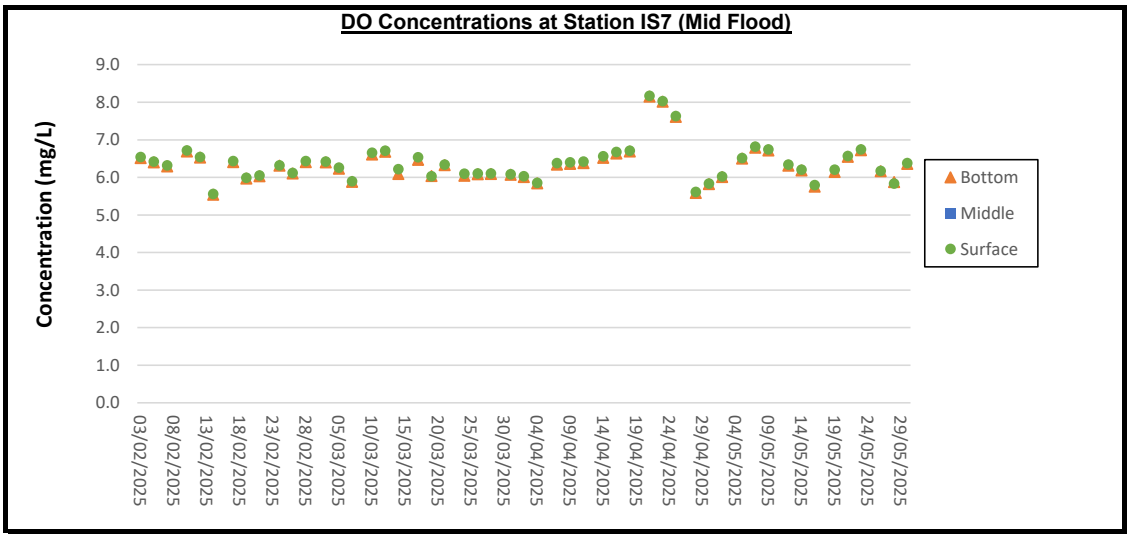
DO Concentrations at Station IS7 (Mid Flood)
Concentration (mg/L)
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

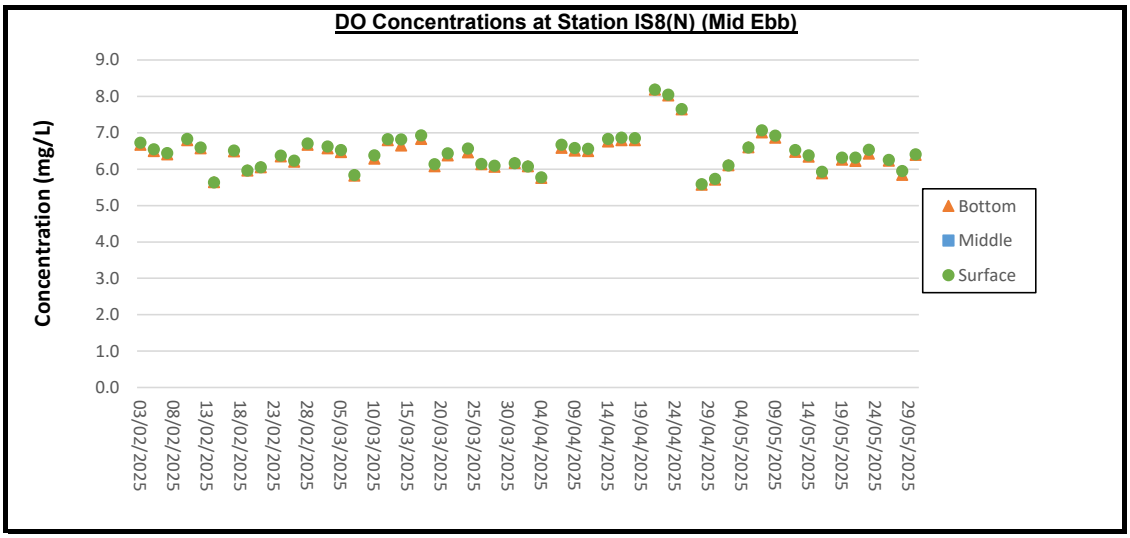
DO Concentrations at Station IS8(N) (Mid Ebb)
Concentration (mg/L)
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

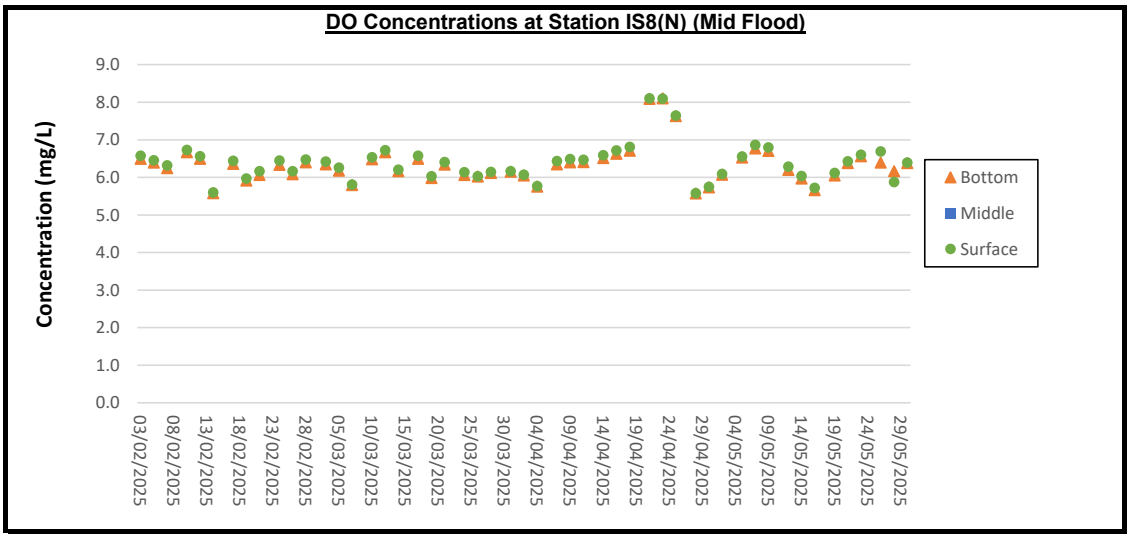
DO Concentrations at Station IS8(N) (Mid Flood)
Concentration (mg/L)
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

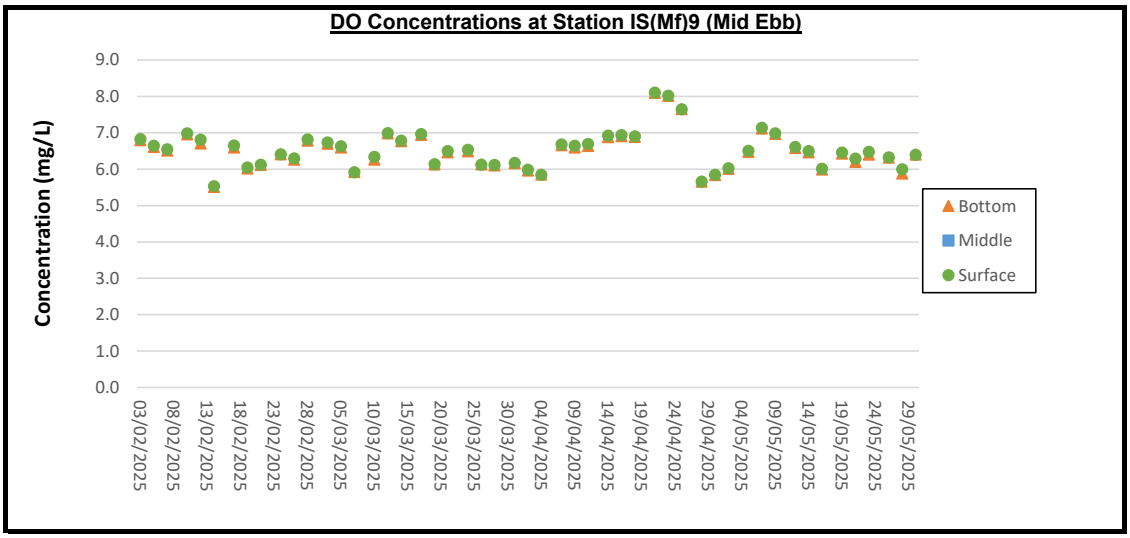
DO Concentrations at Station IS(Mf)9 (Mid Ebb)
Concentration (mg/L)
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

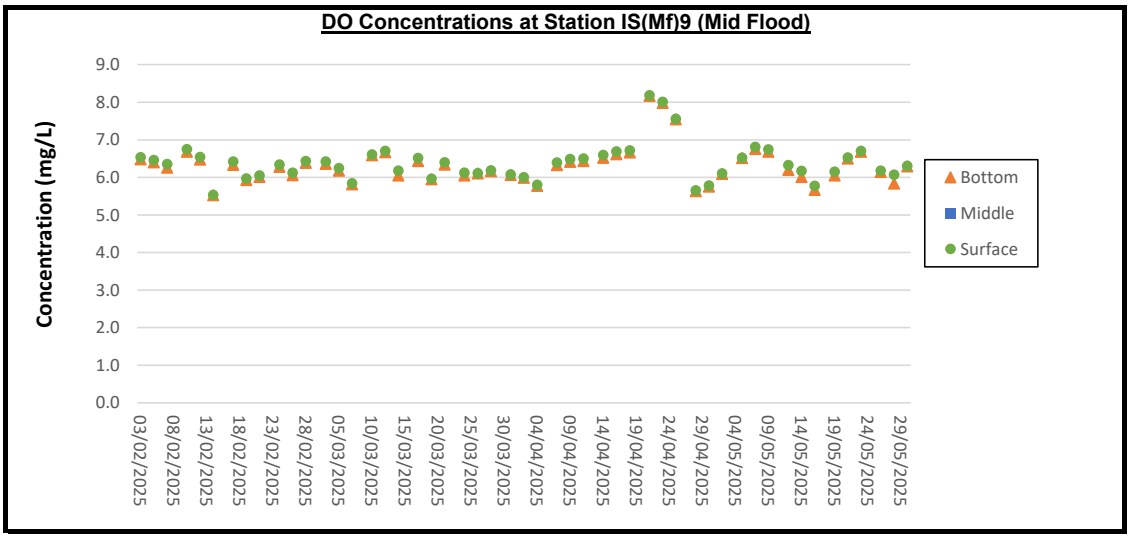
DO Concentrations at Station IS(Mf)9 (Mid Flood)
Concentration (mg/L)
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

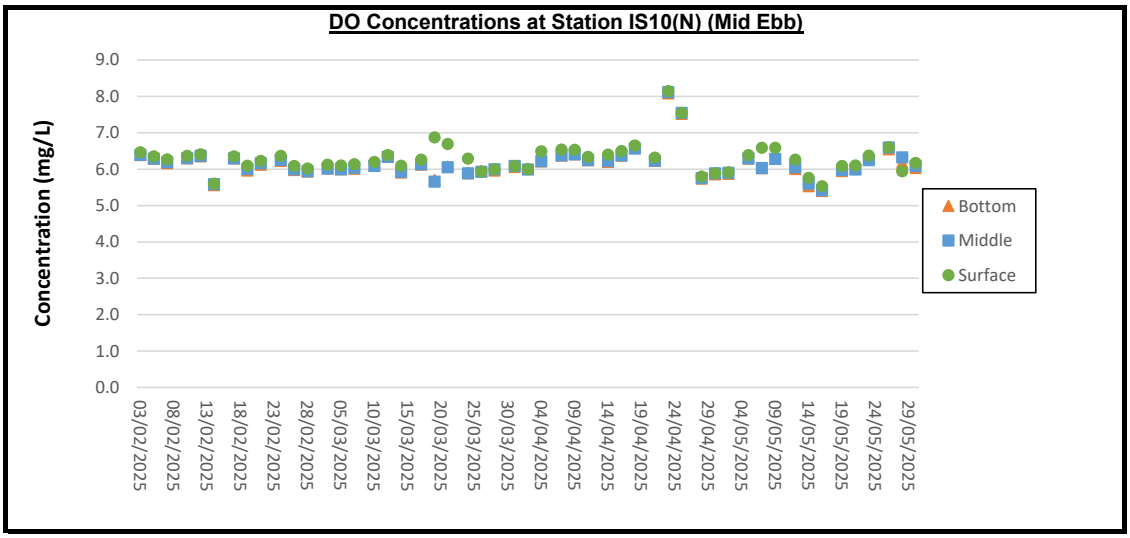
DO Concentrations at Station IS10(N) (Mid Ebb)
Concentration (mg/L)
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

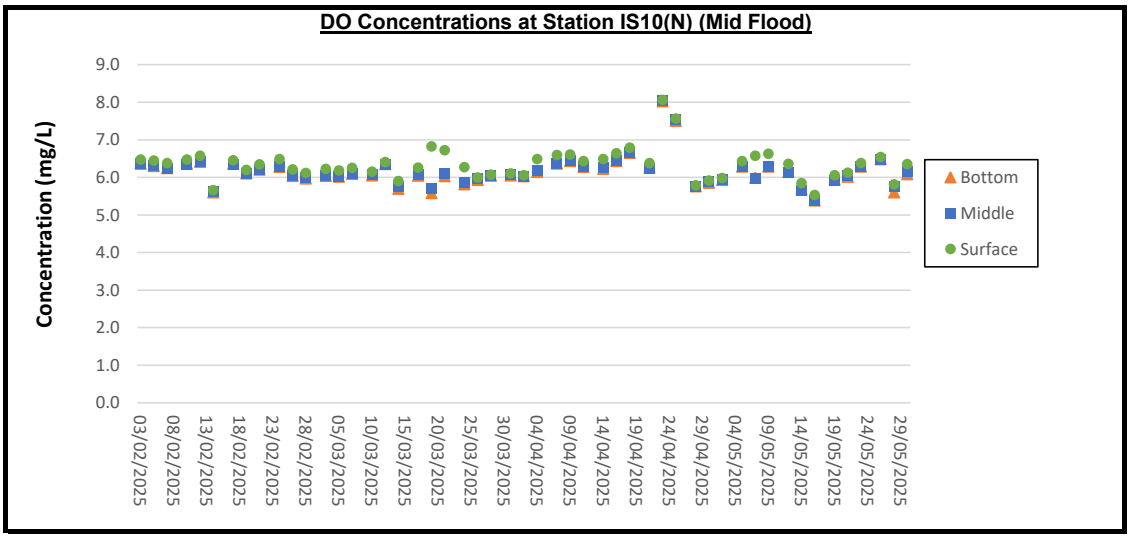
DO Concentrations at Station IS10(N) (Mid Flood)
Concentration (mg/L)
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

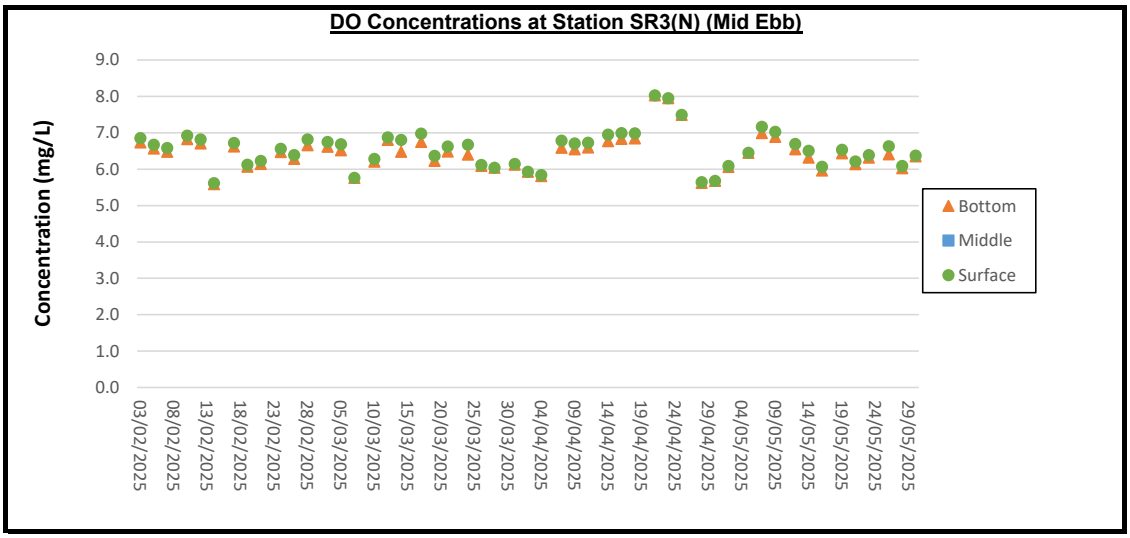
DO Concentrations at Station SR3(N) (Mid Ebb)
Concentration (mg/L)
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

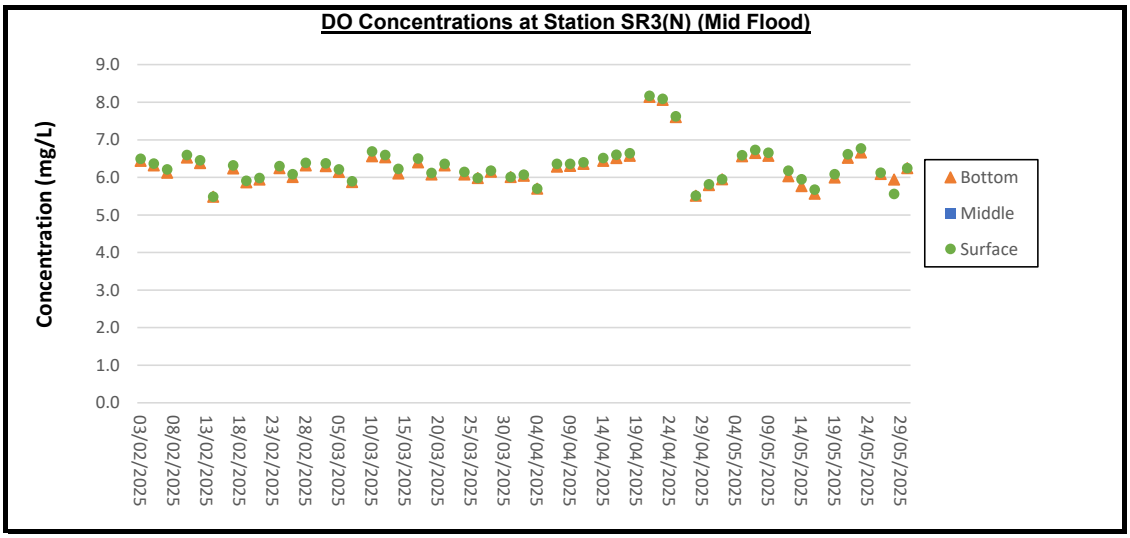
DO Concentrations at Station SR3(N) (Mid Flood)
Concentration (mg/L)
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

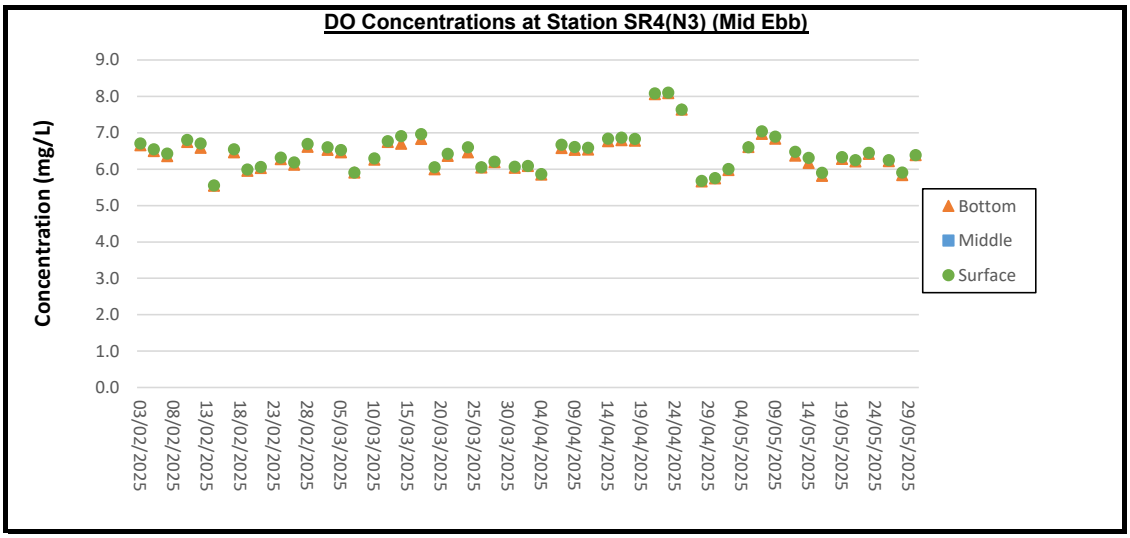
DO Concentrations at Station SR4(N3) (Mid Ebb)
Concentration (mg/L)
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

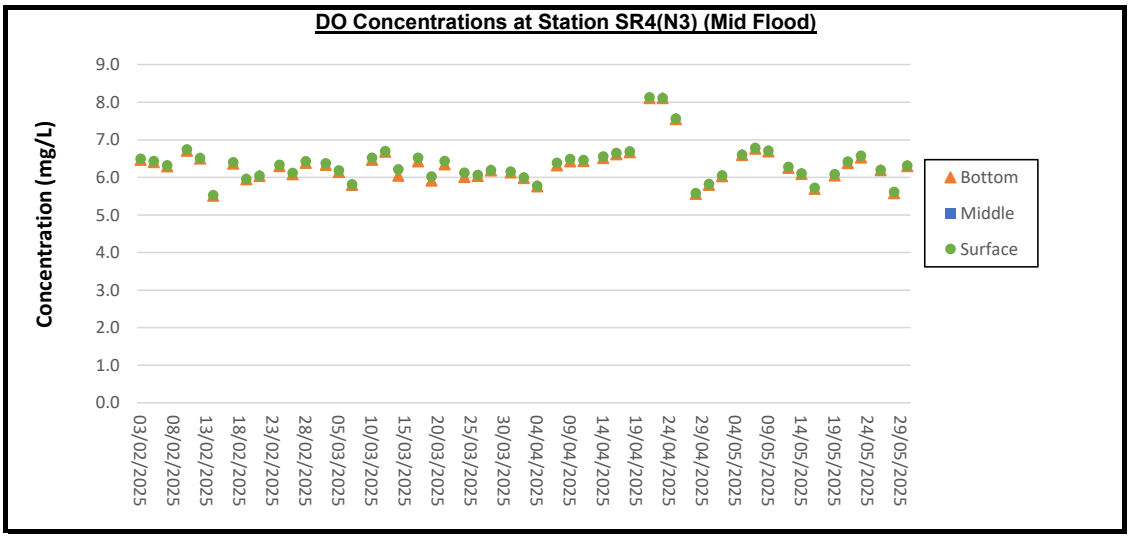
DO Concentrations at Station SR4(N3) (Mid Flood)
Concentration (mg/L)
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

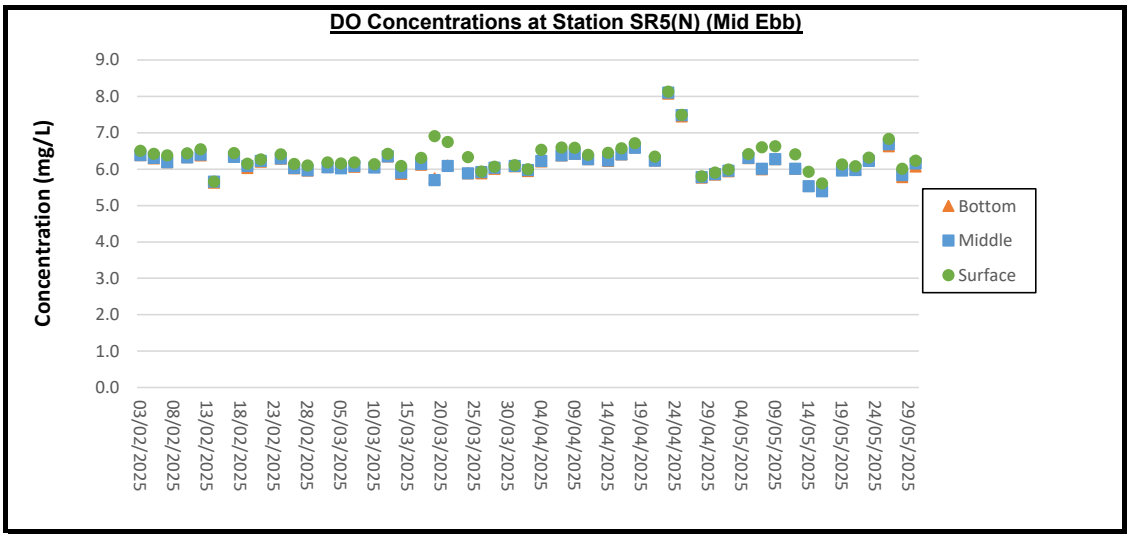
DO Concentrations at Station SR5(N) (Mid Ebb)
Concentration (mg/L)
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

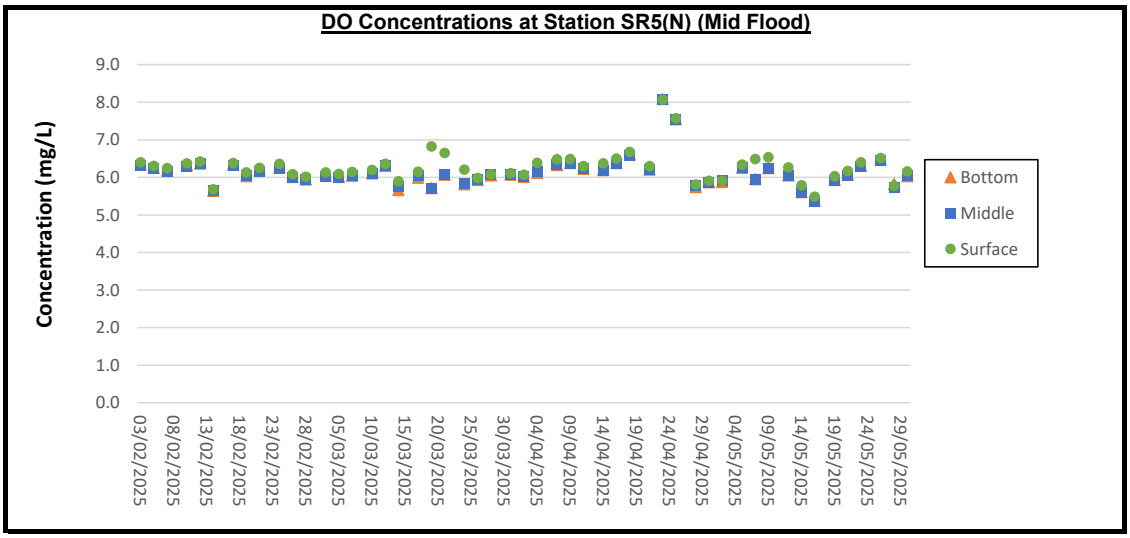
DO Concentrations at Station SR5(N) (Mid Flood)
Concentration (mg/L)
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

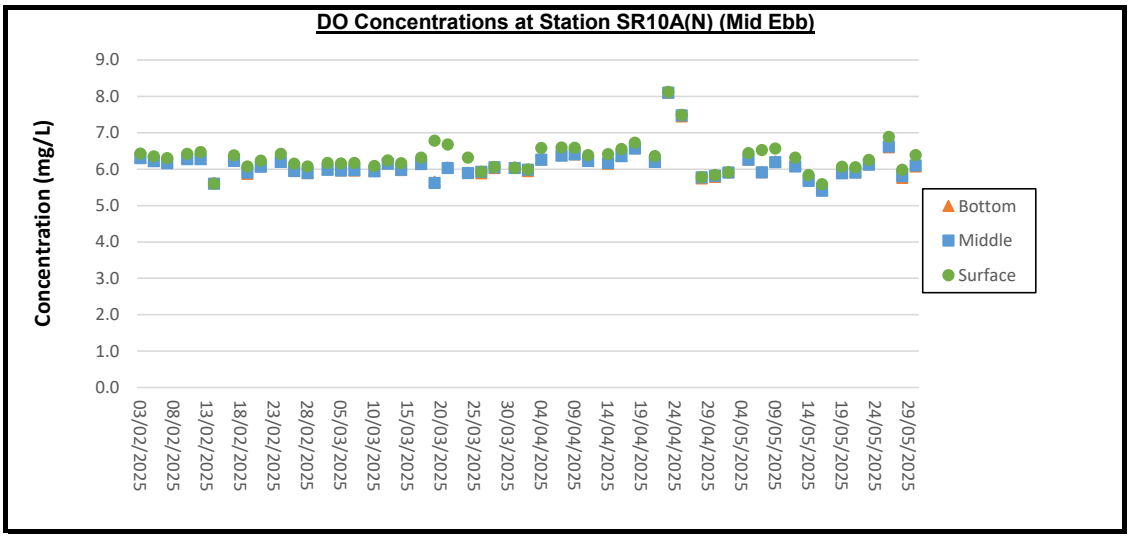
DO Concentrations at Station SR10A(N) (Mid Ebb)
Concentration (mg/L)
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

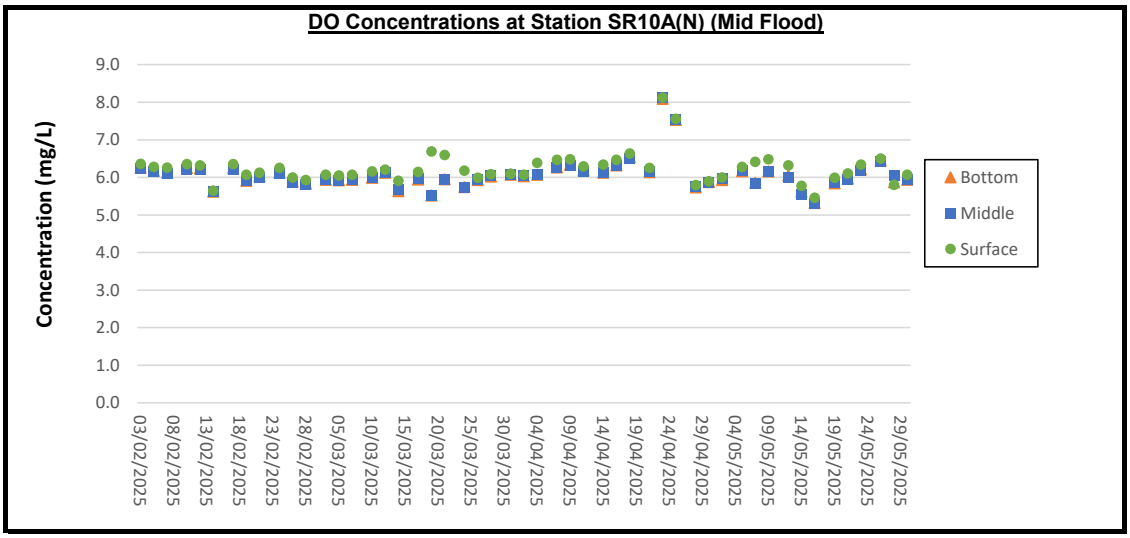
DO Concentrations at Station SR10A(N) (Mid Flood)
Concentration (mg/L)
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

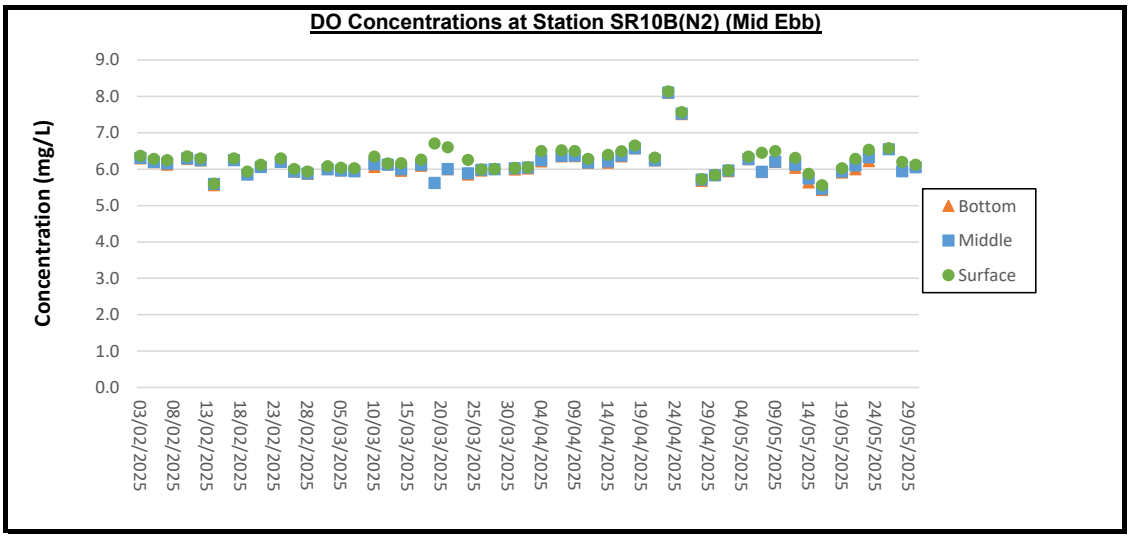
DO Concentrations at Station SR10B(N2) (Mid Ebb)
Concentration (mg/L)
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

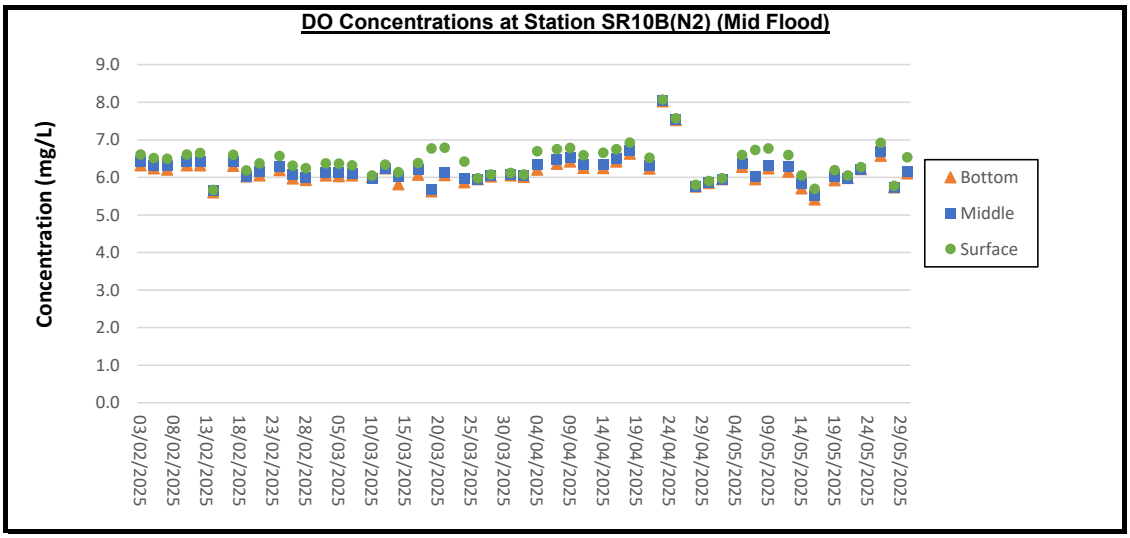
DO Concentrations at Station SR10B(N2) (Mid Flood)
Concentration (mg/L)
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

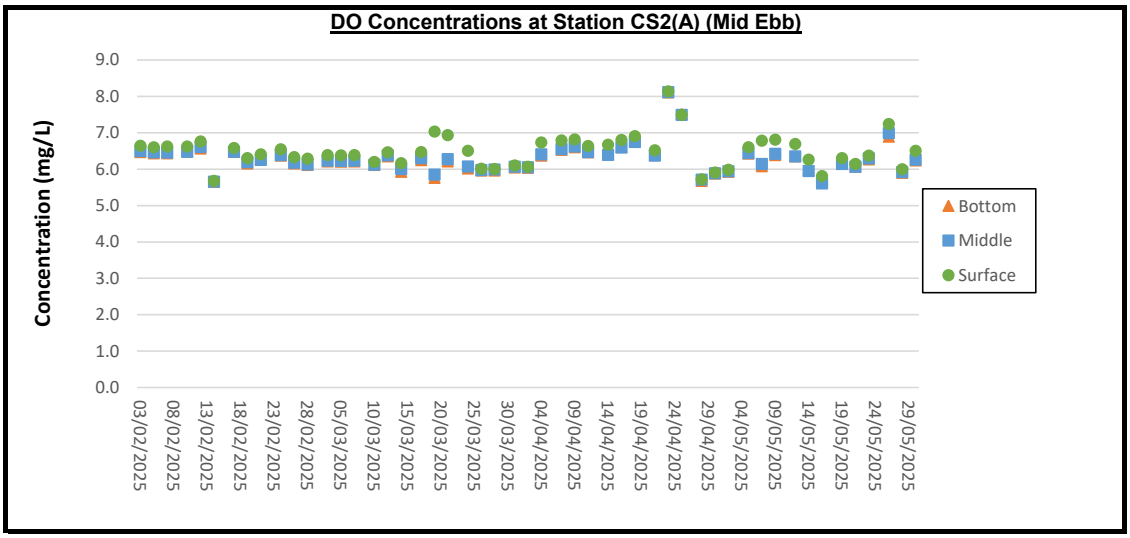
DO Concentrations at Station CS2(A) (Mid Ebb)
Concentration (mg/L)
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

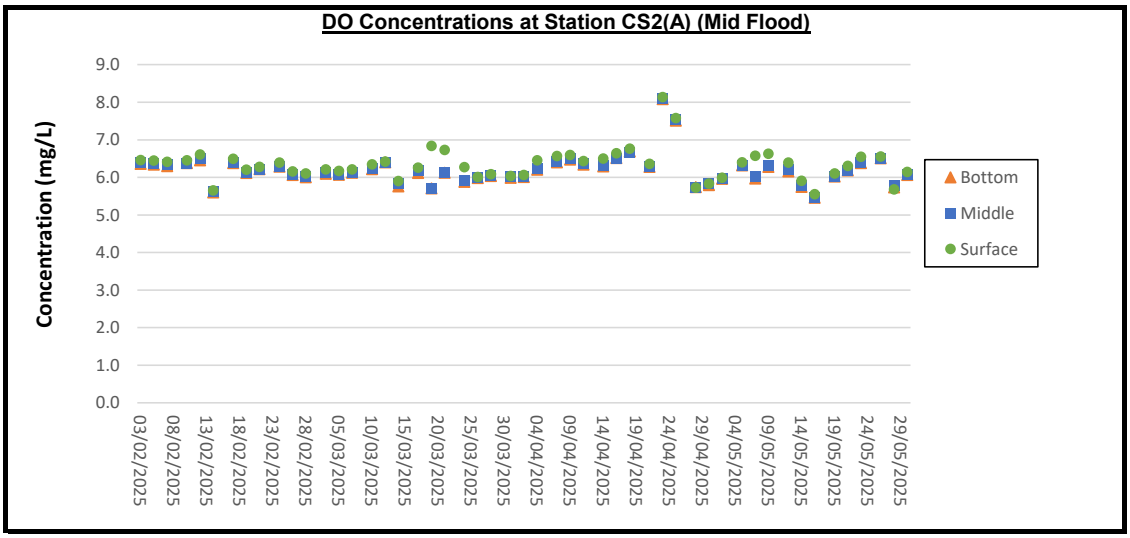
DO Concentrations at Station CS2(A) (Mid Flood)
Concentration (mg/L)
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

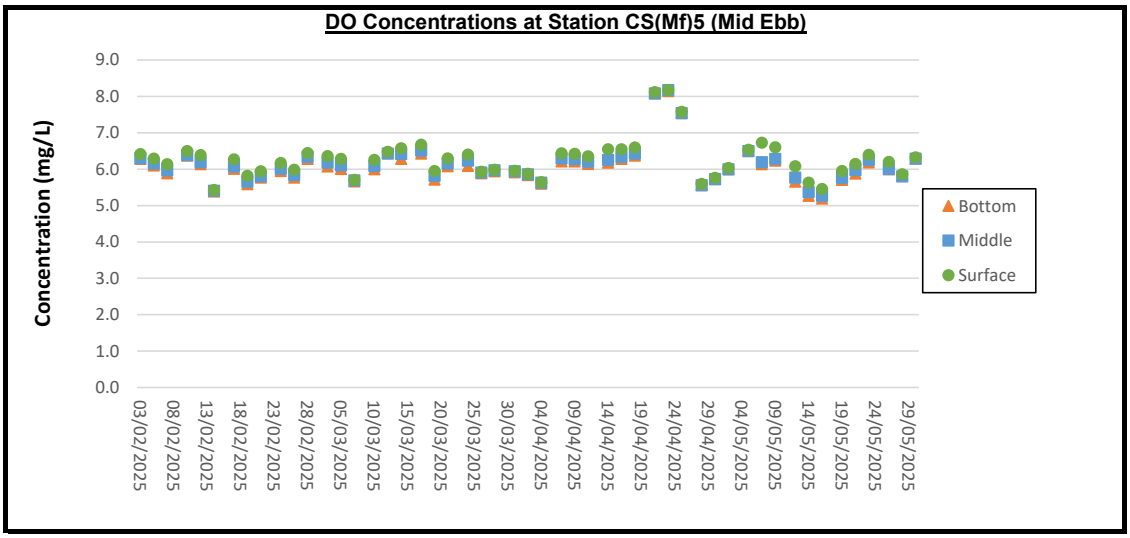
DO Concentrations at Station CS(Mf)5 (Mid Ebb)
Concentration (mg/L)
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

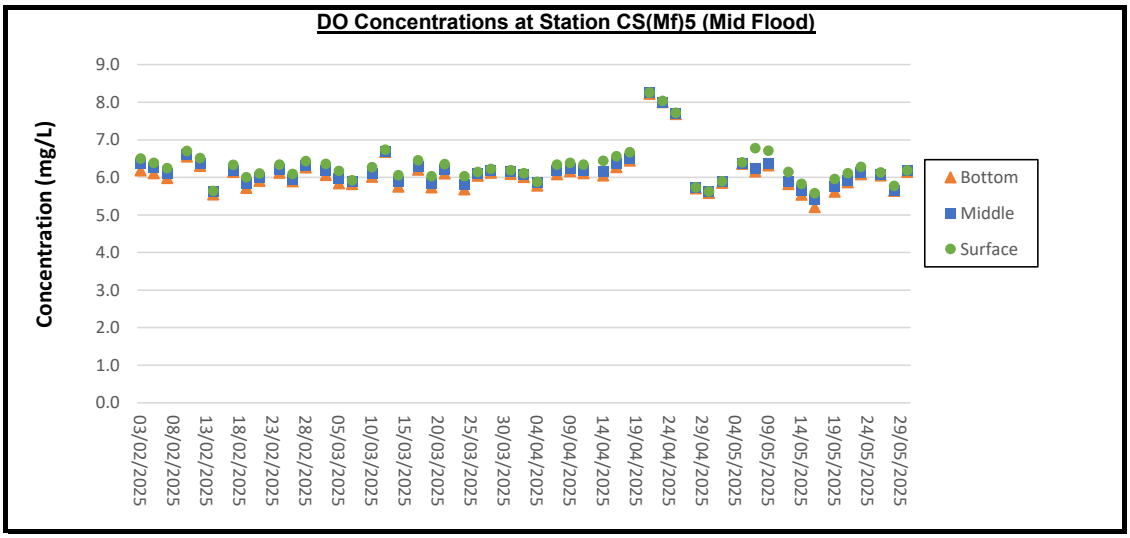
DO Concentrations at Station CS(Mf)5 (Mid Flood)
Concentration (mg/L)
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

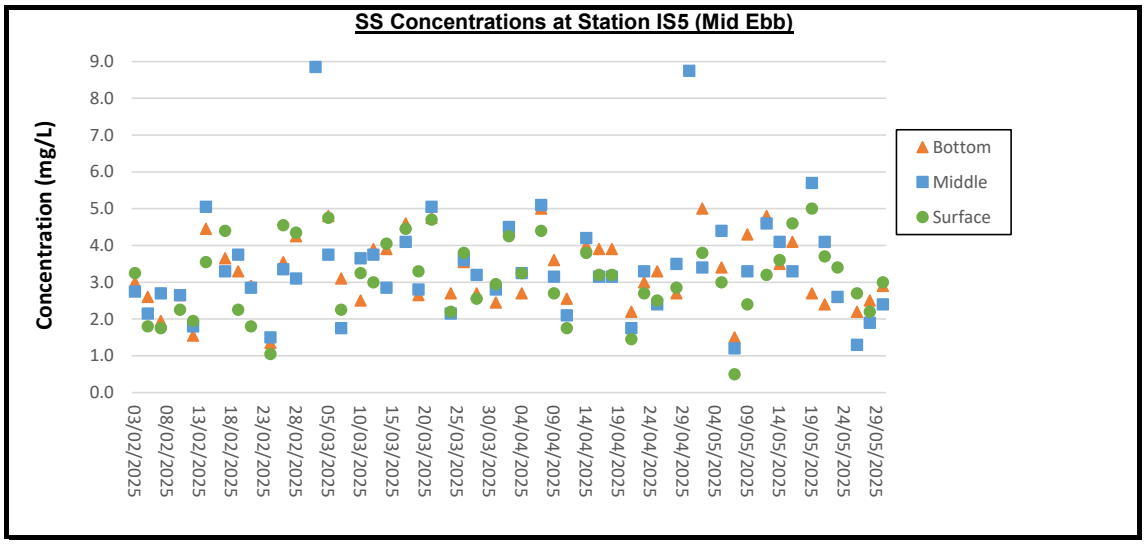
SS Concentrations at Station IS5 (Mid Ebb)
Concentration (mg/L)
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

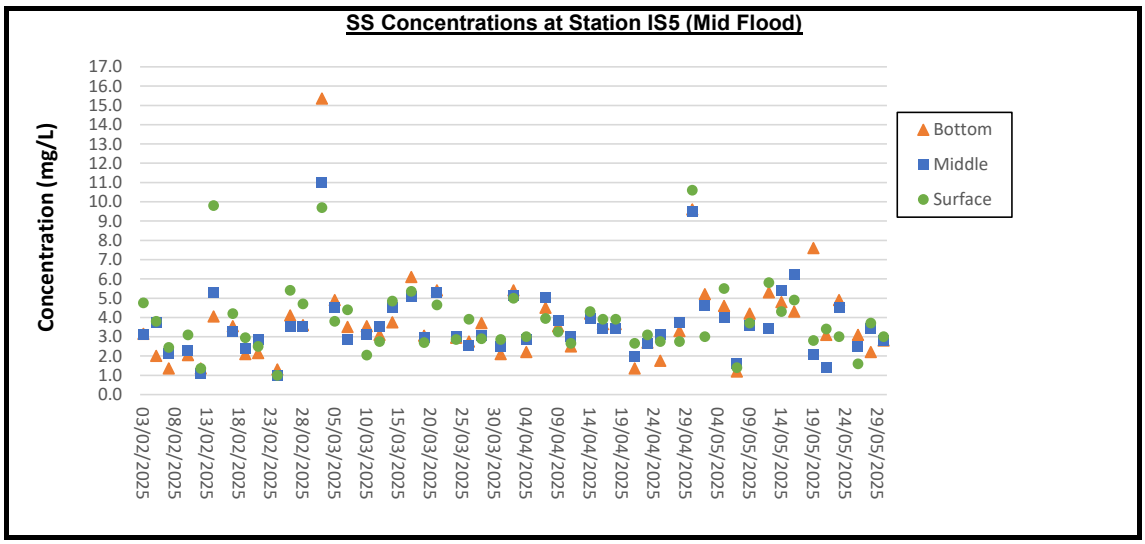
SS Concentrations at Station IS5 (Mid Flood)
Concentration (mg/L)
17.0
16.0
15.0
14.0
13.0
12.0
11.0
10.0
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

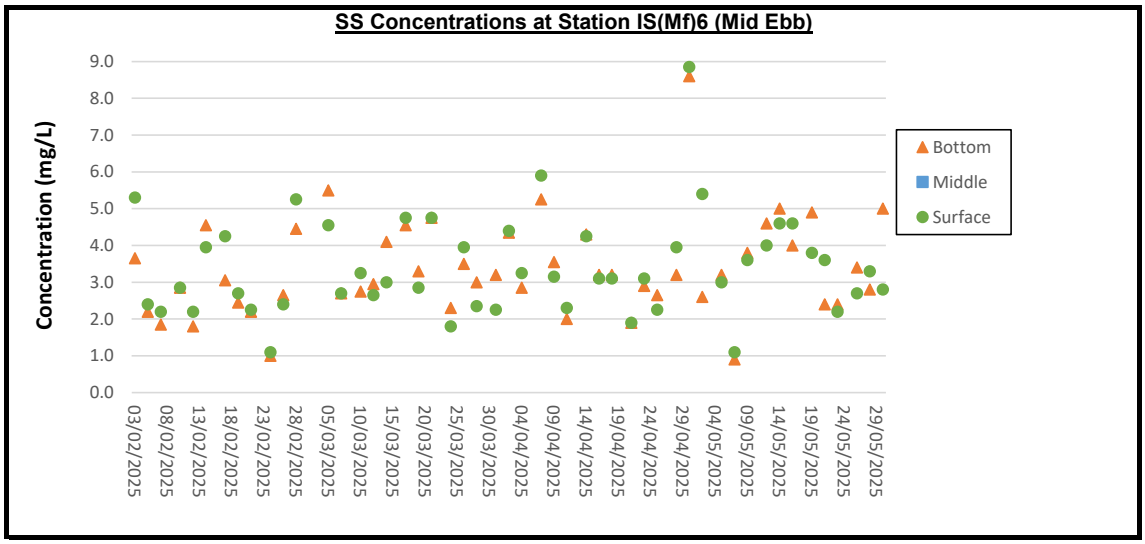
SS Concentrations at Station IS(Mf)6 (Mid Ebb)
Concentration (mg/L)
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

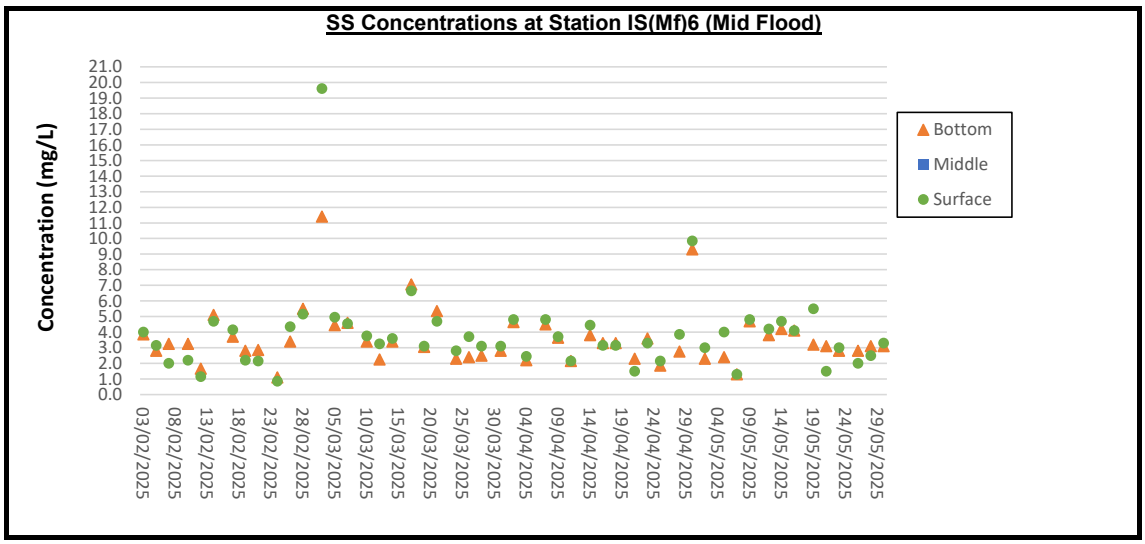
SS Concentrations at Station IS(Mf)6 (Mid Flood)
Concentration (mg/L)
21.0
20.0
19.0
18.0
17.0
16.0
15.0
14.0
13.0
12.0
11.0
10.0
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

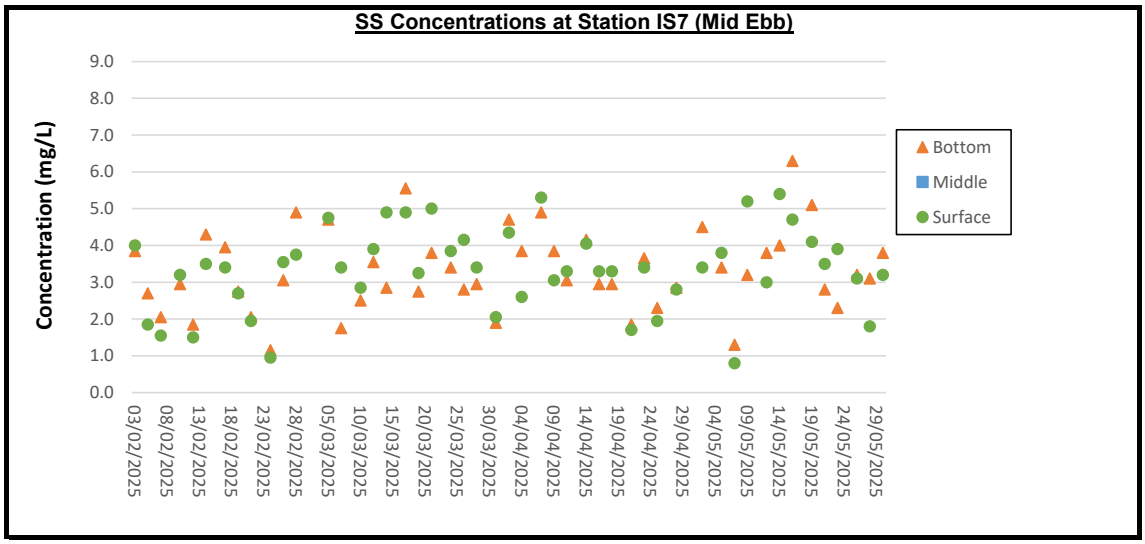
SS Concentrations at Station IS7 (Mid Ebb)
Concentration (mg/L)
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

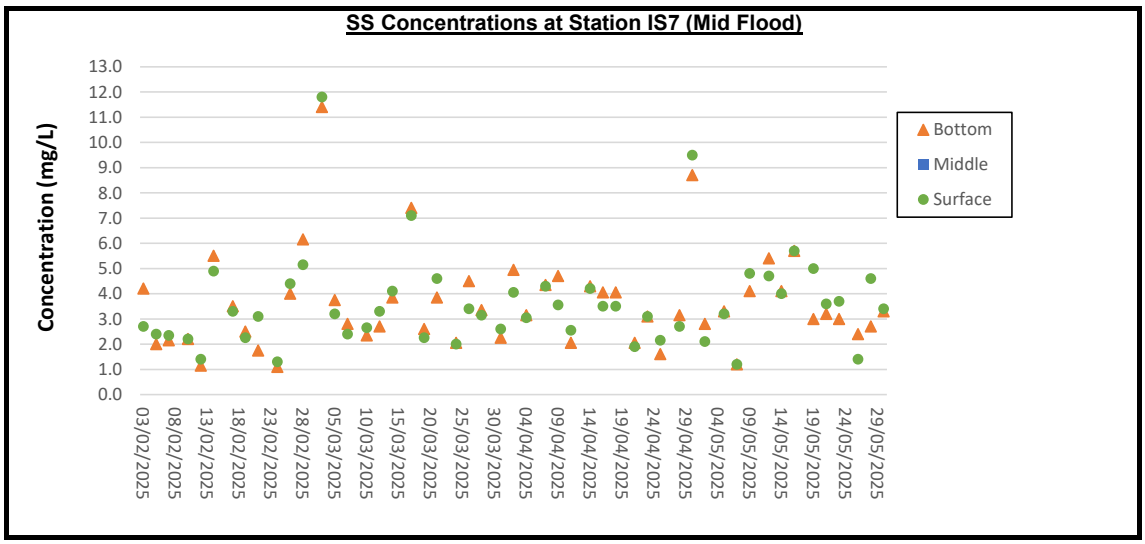
SS Concentrations at Station IS7 (Mid Flood)
Concentration (mg/L)
13.0
12.0
11.0
10.0
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

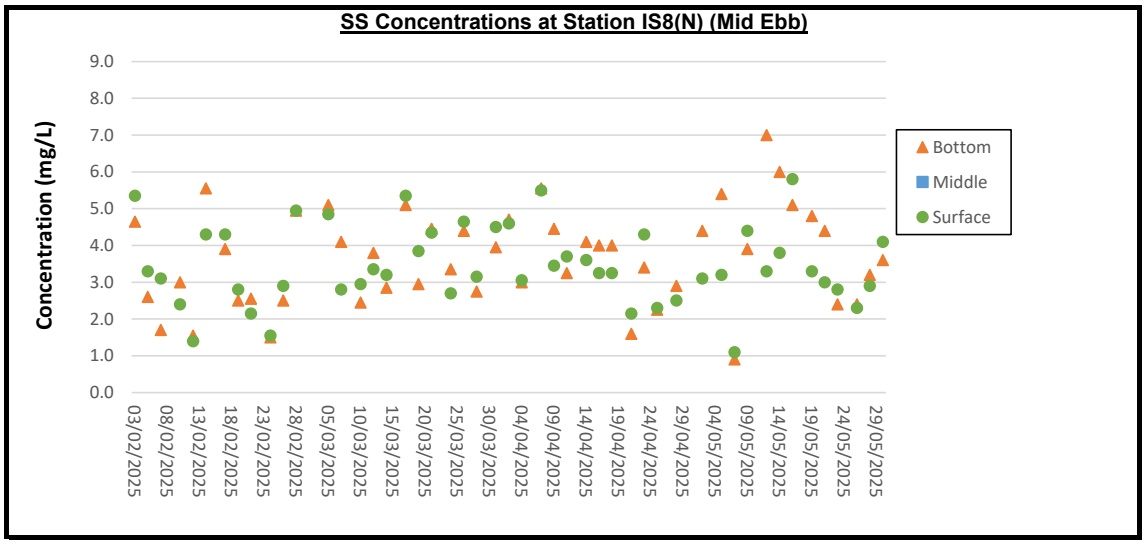
SS Concentrations at Station IS8(N) (Mid Ebb)
Concentration (mg/L)
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

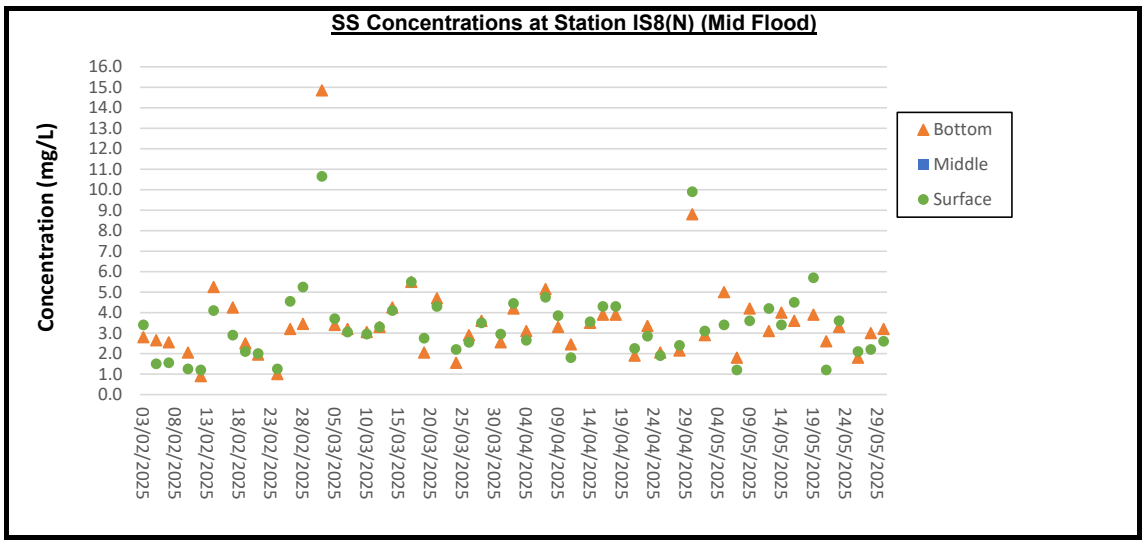
SS Concentrations at Station IS8(N) (Mid Flood)
Concentration (mg/L)
16.0
15.0
14.0
13.0
12.0
11.0
10.0
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

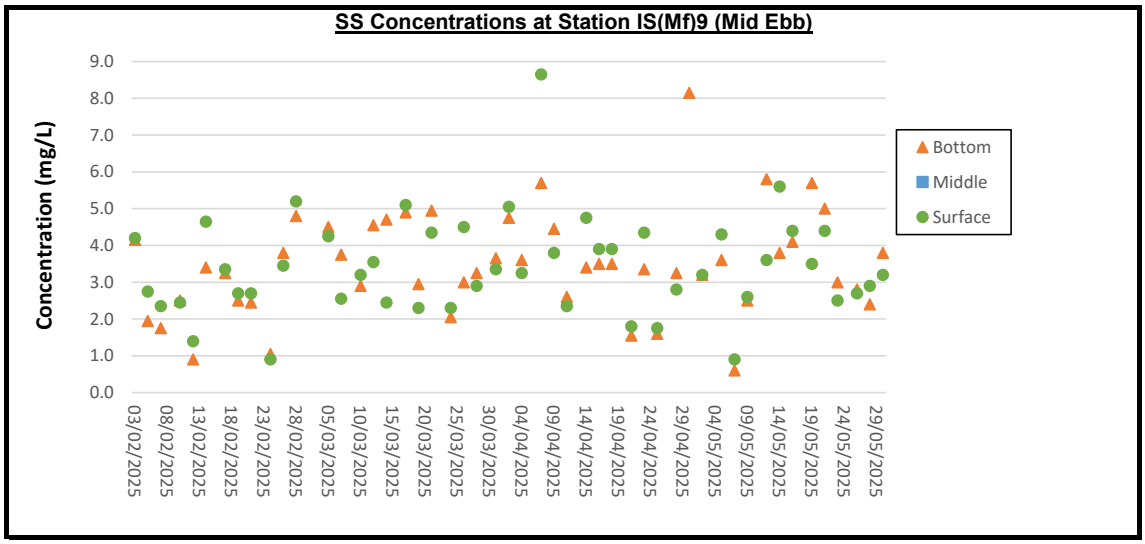
SS Concentrations at Station IS(Mf)9 (Mid Ebb)
Concentration (mg/L)
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

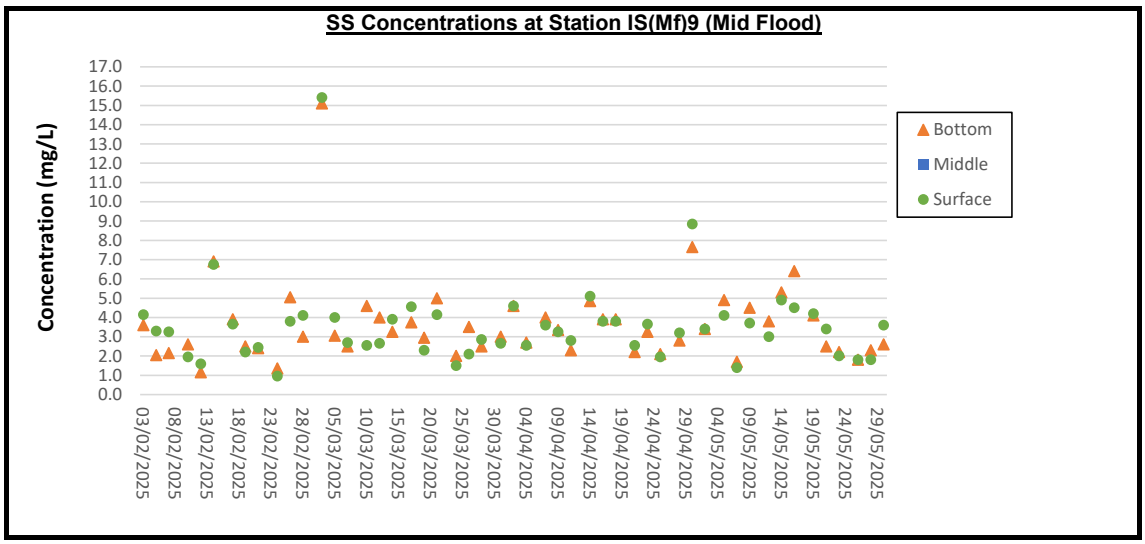
SS Concentrations at Station IS(Mf)9 (Mid Flood)
Concentration (mg/L)
17.0
16.0
15.0
14.0
13.0
12.0
11.0
10.0
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

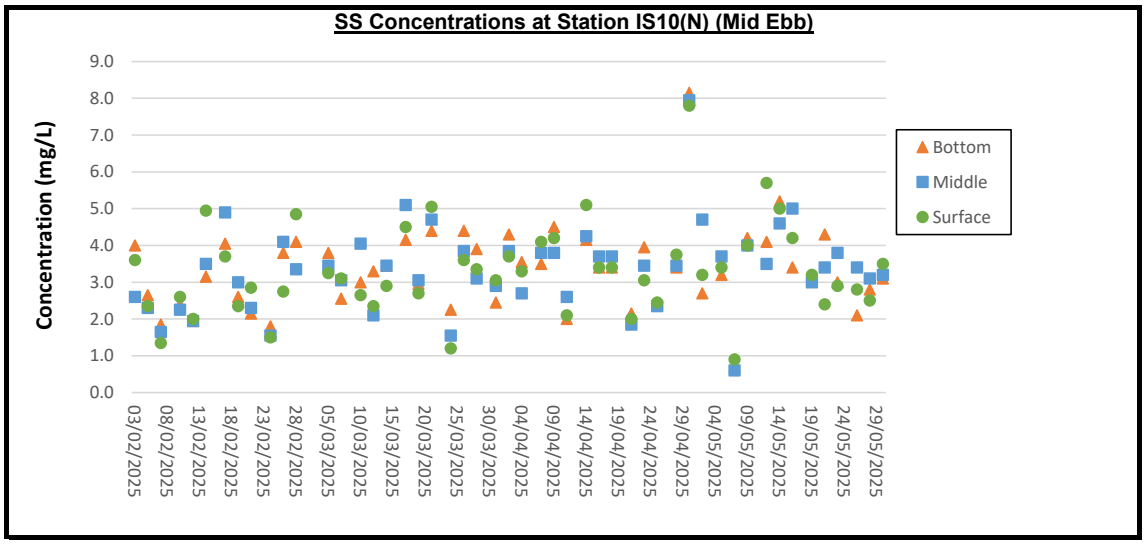
SS Concentrations at Station IS10(N) (Mid Ebb)
Concentration (mg/L)
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

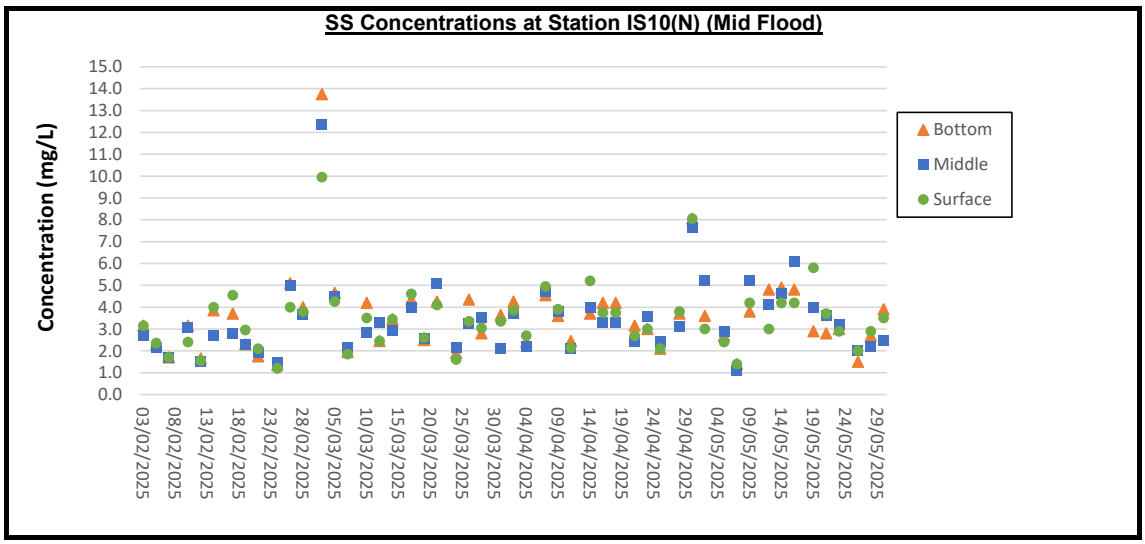
SS Concentrations at Station IS10(N) (Mid Flood)
Concentration (mg/L)
15.0
14.0
13.0
12.0
11.0
10.0
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

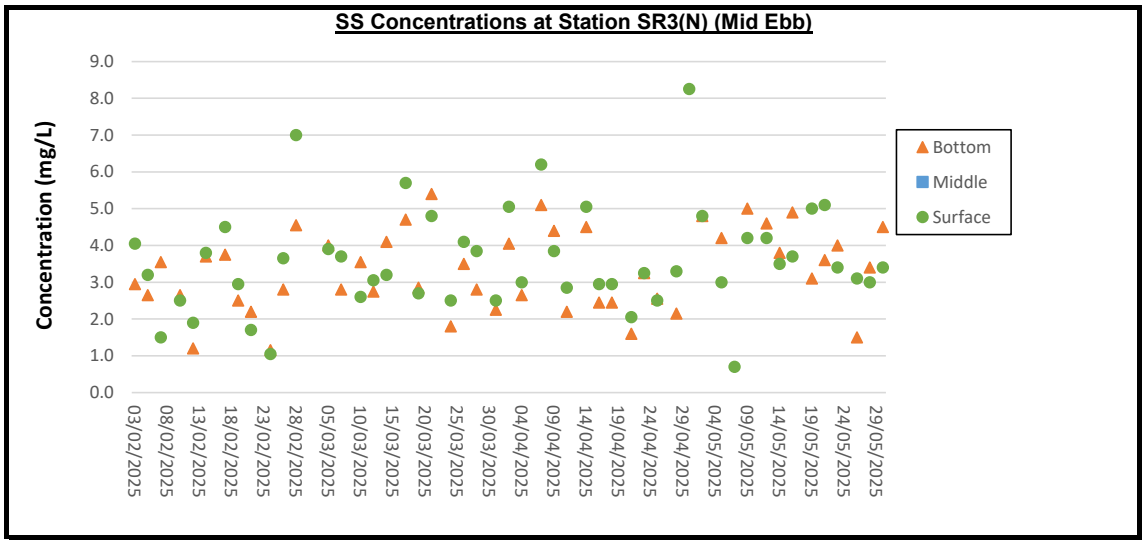
SS Concentrations at Station SR3(N) (Mid Ebb)
Concentration (mg/L)
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

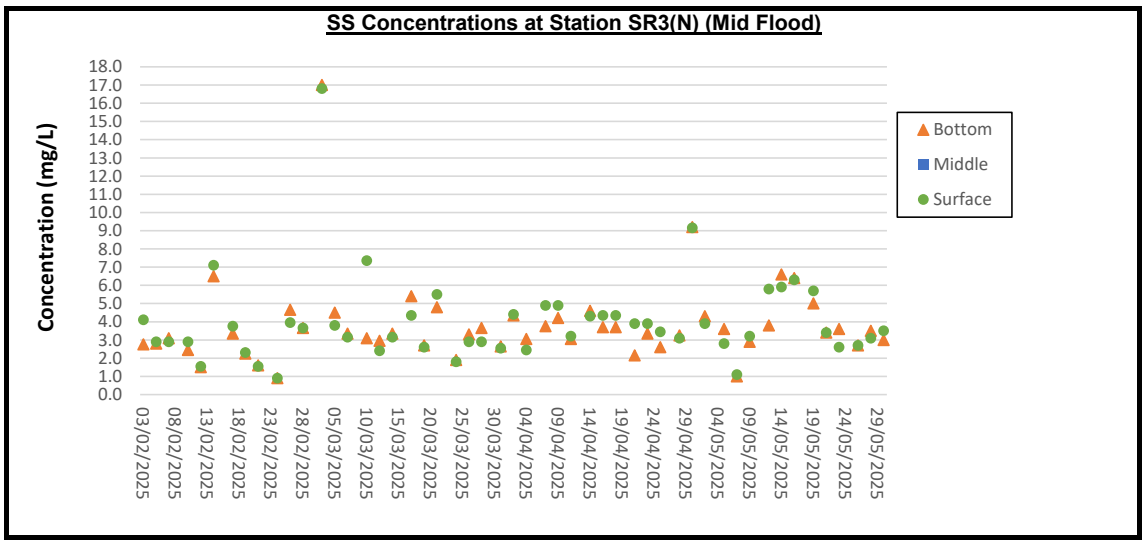
SS Concentrations at Station SR3(N) (Mid Flood)
Concentration (mg/L)
18.0
17.0
16.0
15.0
14.0
13.0
12.0
11.0
10.0
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

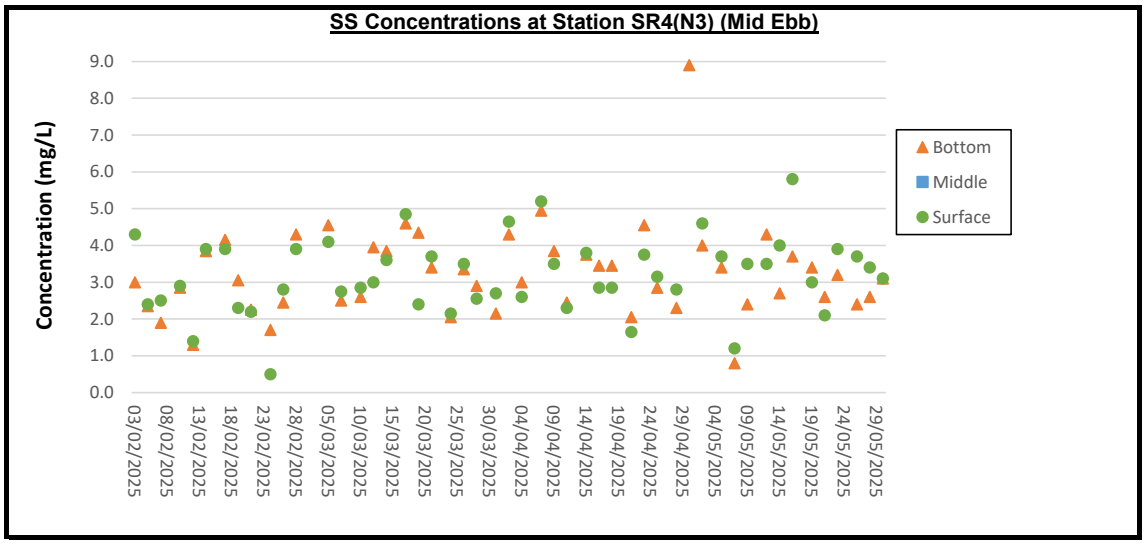
SS Concentrations at Station SR4(N3) (Mid Ebb)
Concentration (mg/L)
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

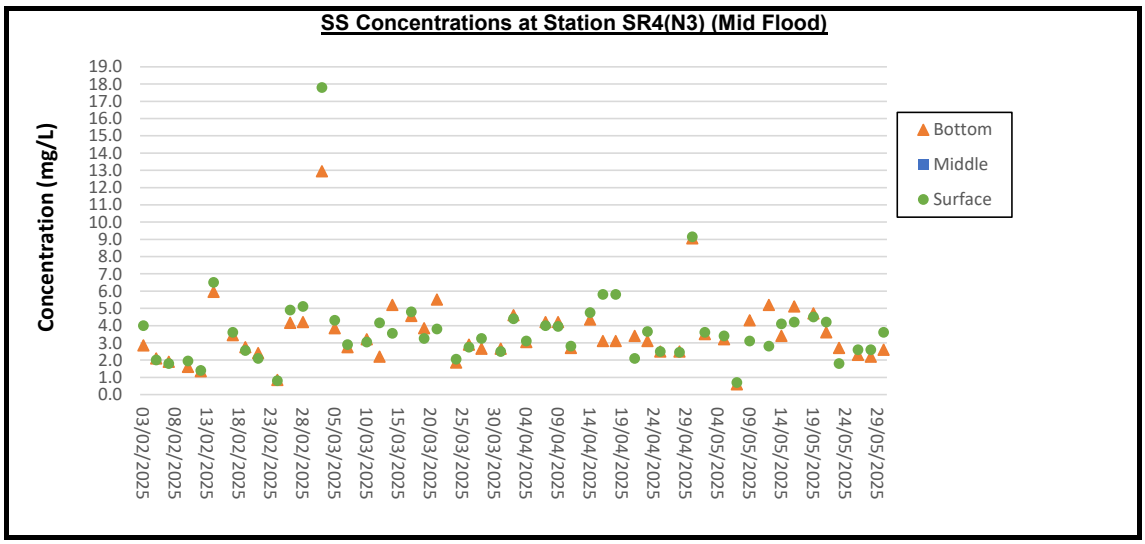
SS Concentrations at Station SR4(N3) (Mid Flood)
Concentration (mg/L)
19.0
18.0
17.0
16.0
15.0
14.0
13.0
12.0
11.0
10.0
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

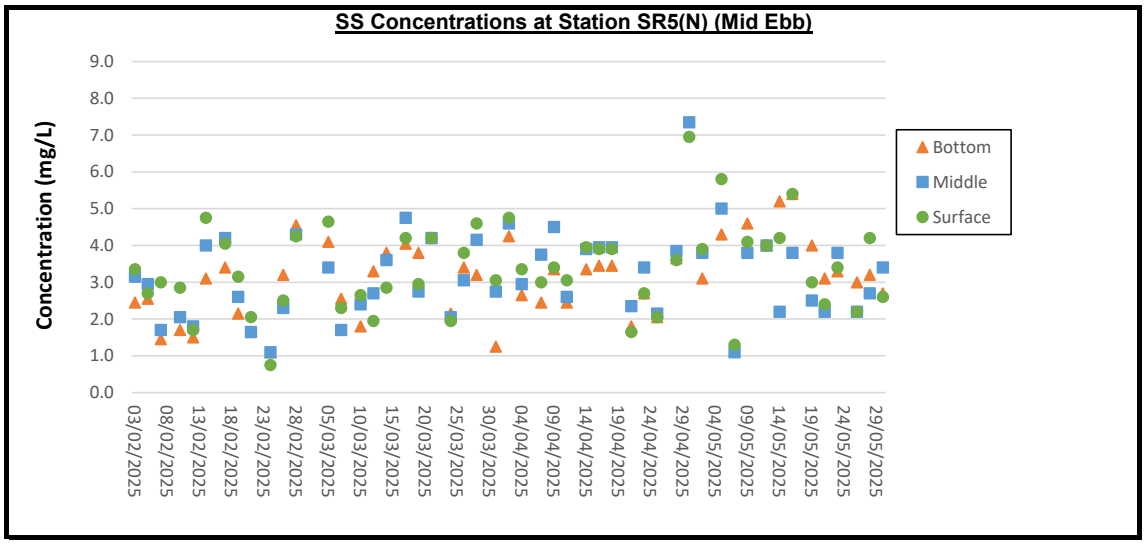
SS Concentrations at Station SR5(N) (Mid Ebb)
Concentration (mg/L)
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

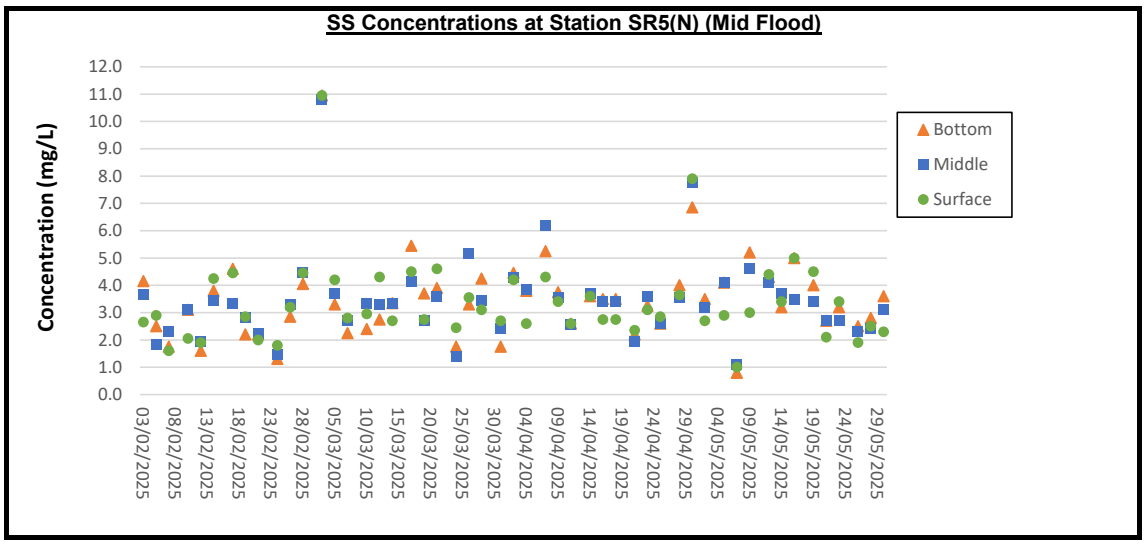
SS Concentrations at Station SR5(N) (Mid Flood)
Concentration (mg/L)
12.0
11.0
10.0
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

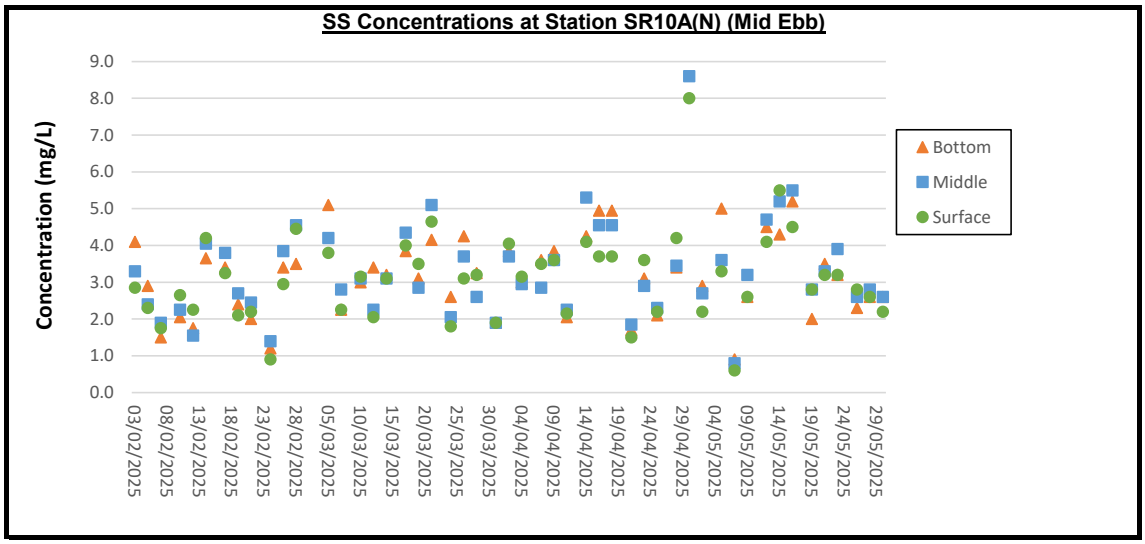
SS Concentrations at Station SR10A(N) (Mid Ebb)
Concentration (mg/L)
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

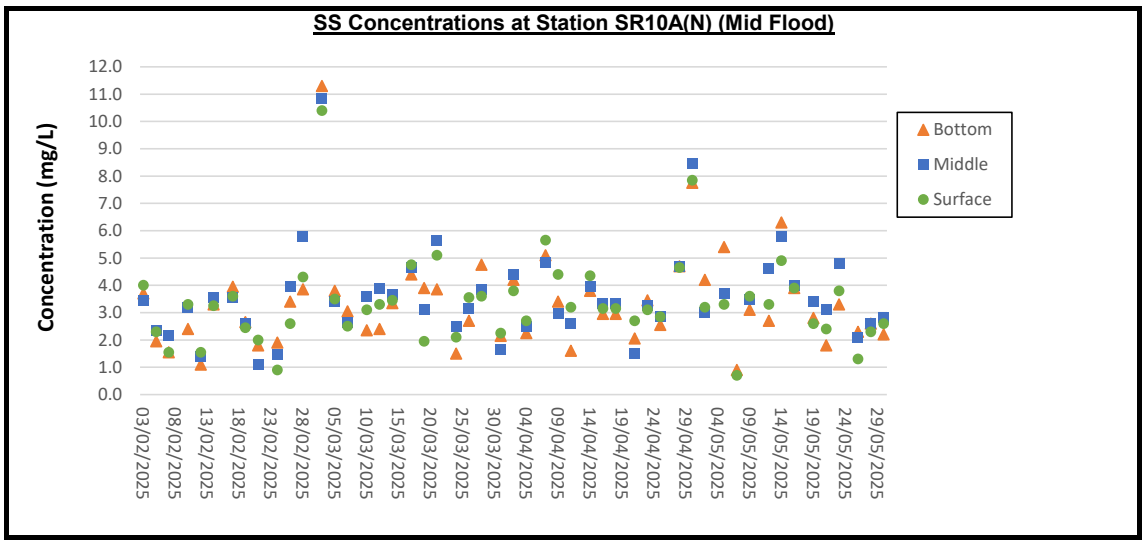
SS Concentrations at Station SR10A(N) (Mid Flood)
Concentration (mg/L)
12.0
11.0
10.0
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

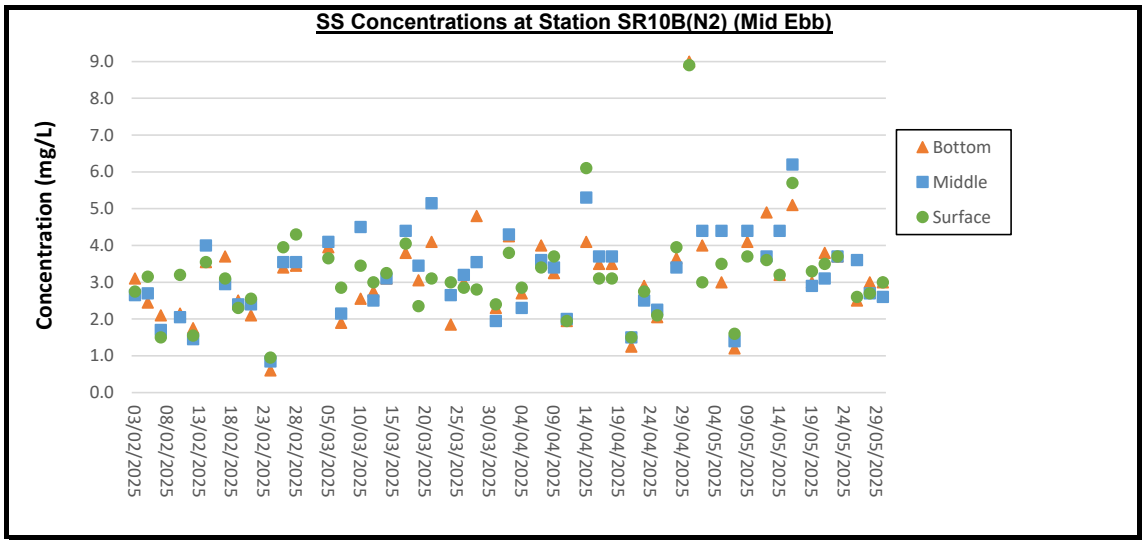
SS Concentrations at Station SR10B(N2) (Mid Ebb)
Concentration (mg/L)
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

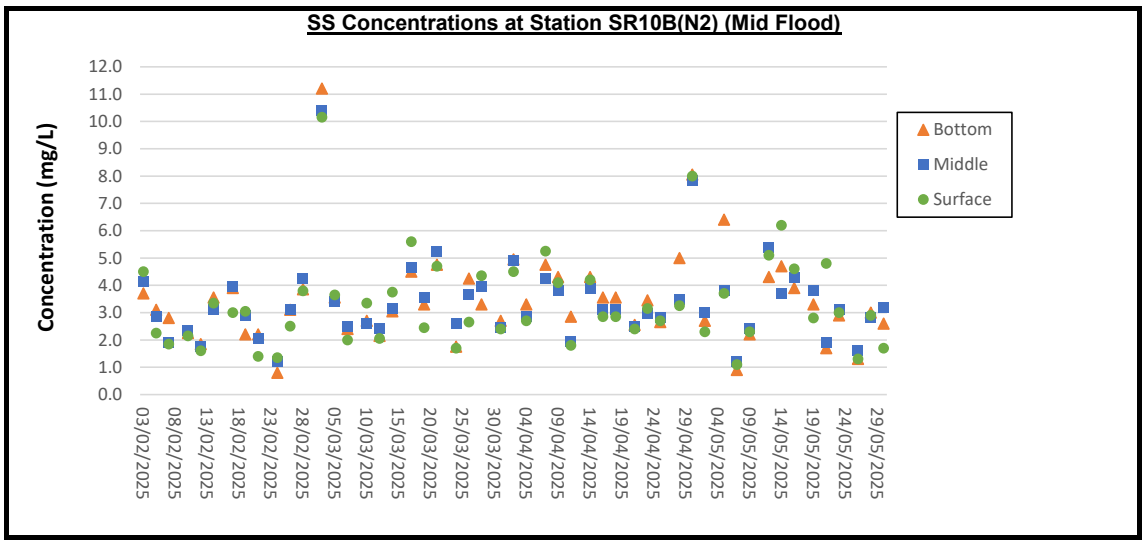
SS Concentrations at Station SR10B(N2) (Mid Flood)
Concentration (mg/L)
12.0
11.0
10.0
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

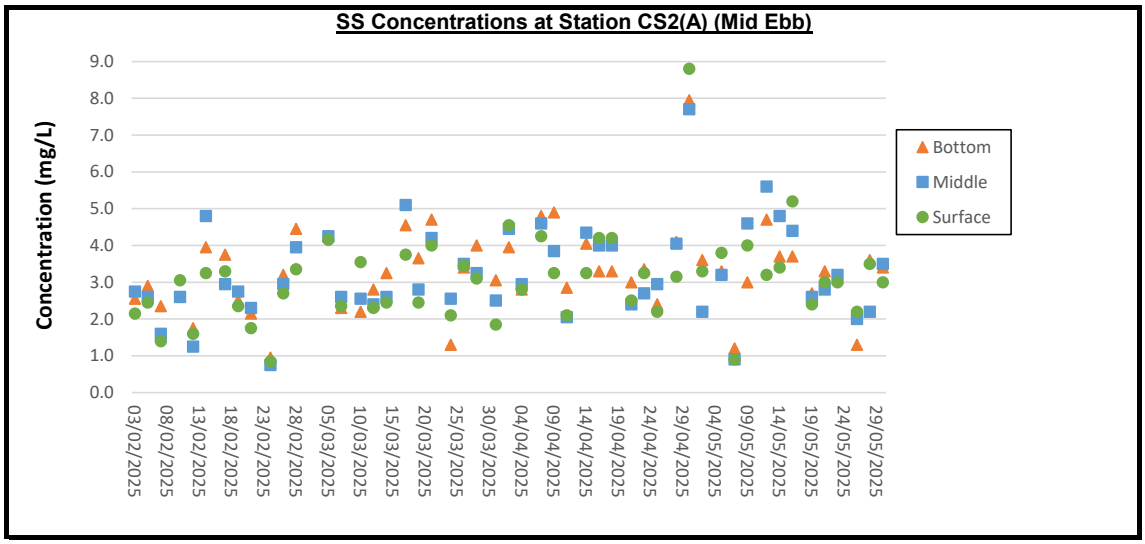
SS Concentrations at Station CS2(A) (Mid Ebb)
Concentration (mg/L)
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

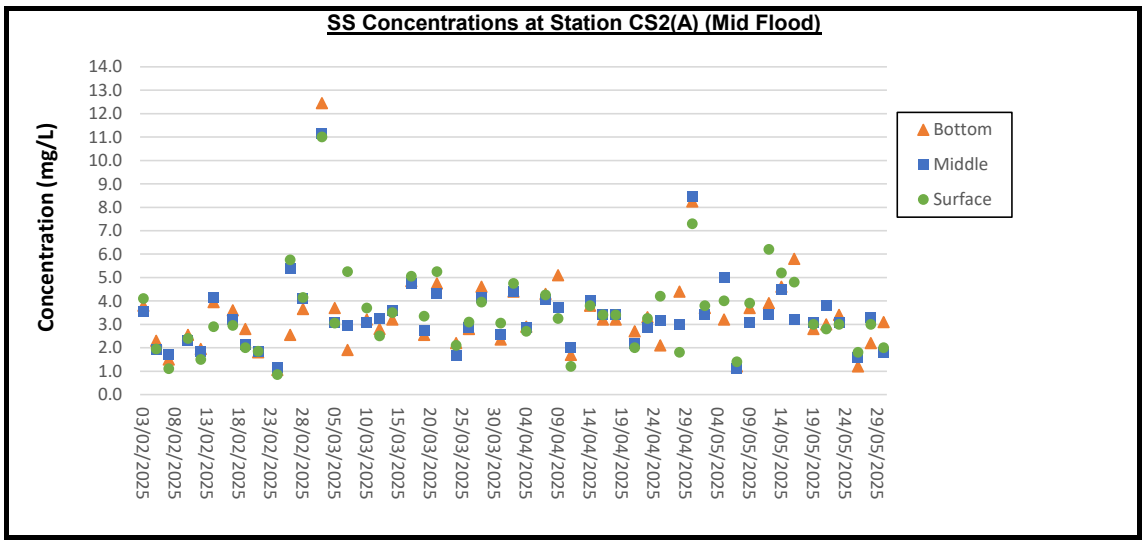
SS Concentrations at Station CS2(A) (Mid Flood)
Concentration (mg/L)
14.0
13.0
12.0
11.0
10.0
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

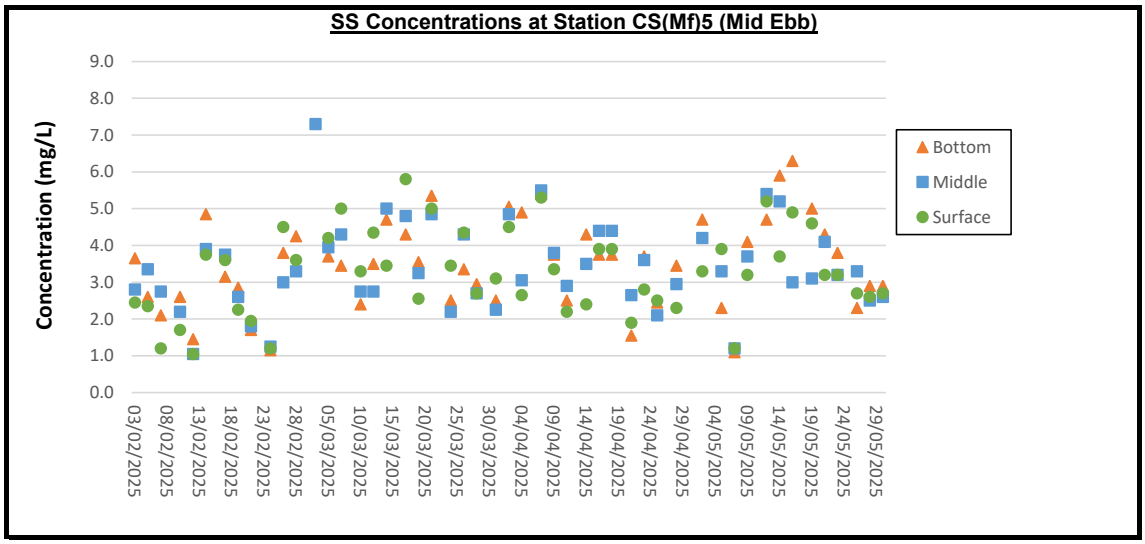
SS Concentrations at Station CS(Mf)5 (Mid Ebb)
Concentration (mg/L)
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

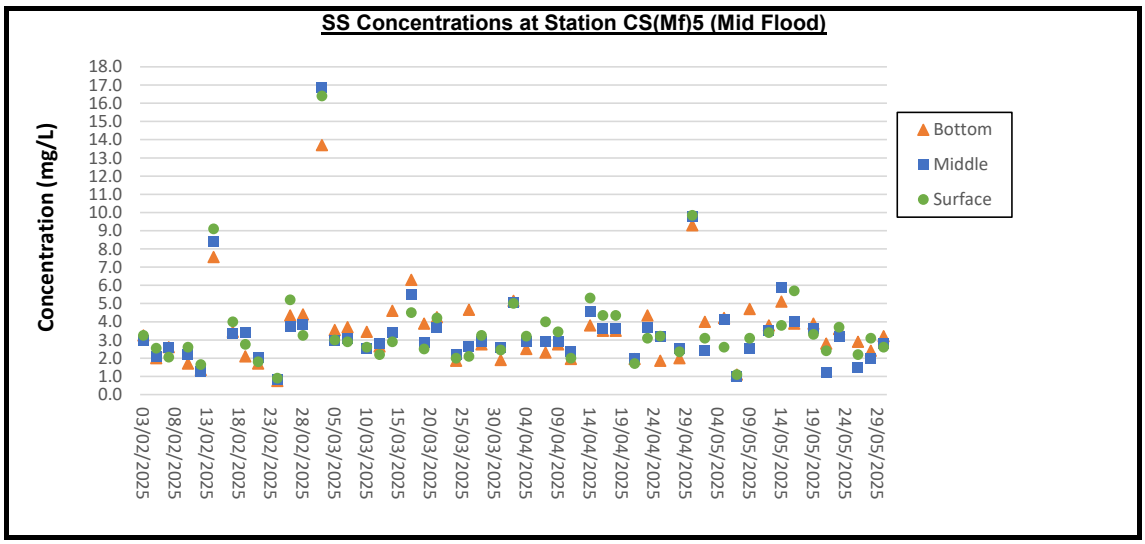
SS Concentrations at Station CS(Mf)5 (Mid Flood)
Concentration (mg/L)
18.0
17.0
16.0
15.0
14.0
13.0
12.0
11.0
10.0
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

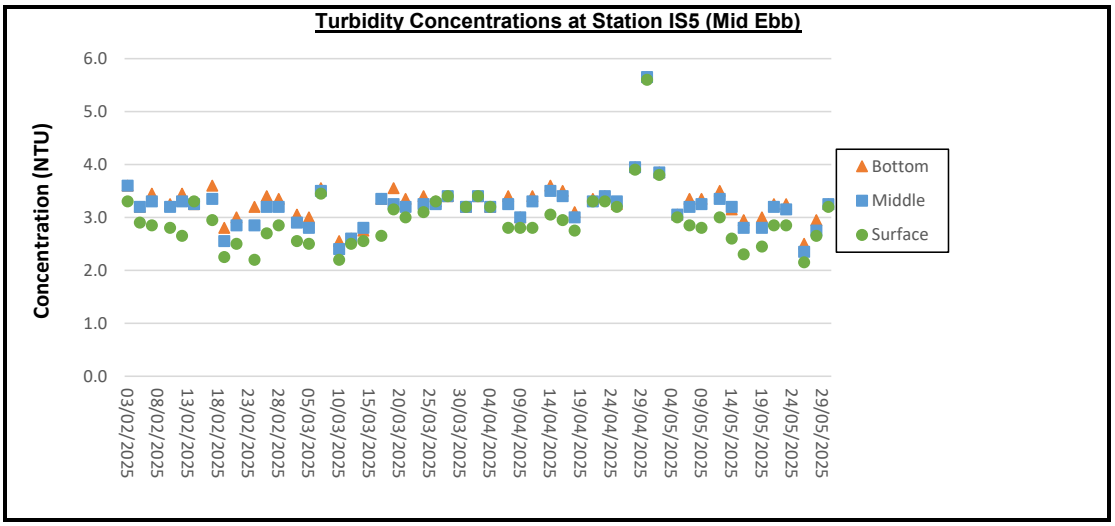
Turbidity Concentrations at Station IS5 (Mid Ebb)
Concentration (NTU)
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

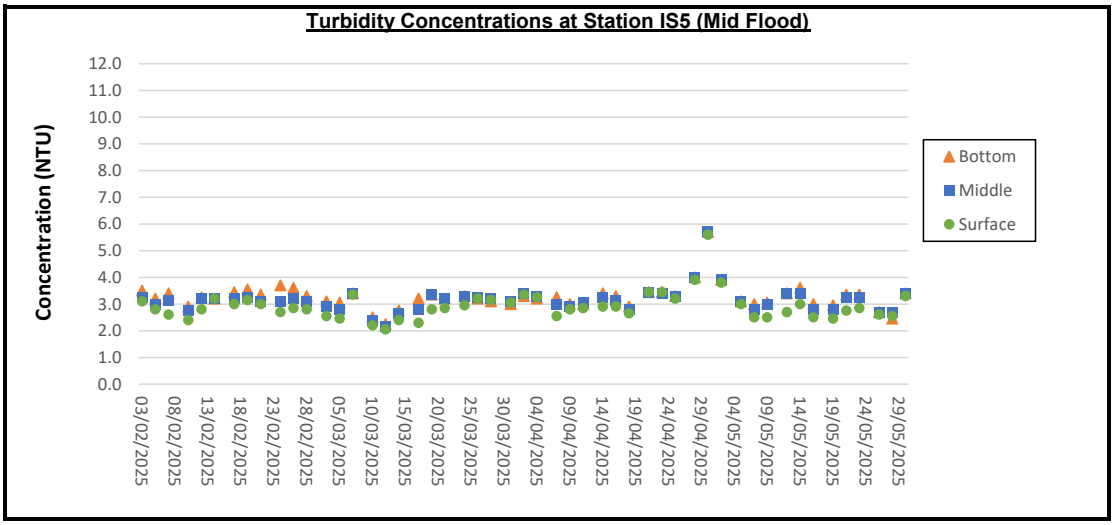
Turbidity Concentrations at Station IS5 (Mid Flood)
Concentration (NTU)
12.0
11.0
10.0
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

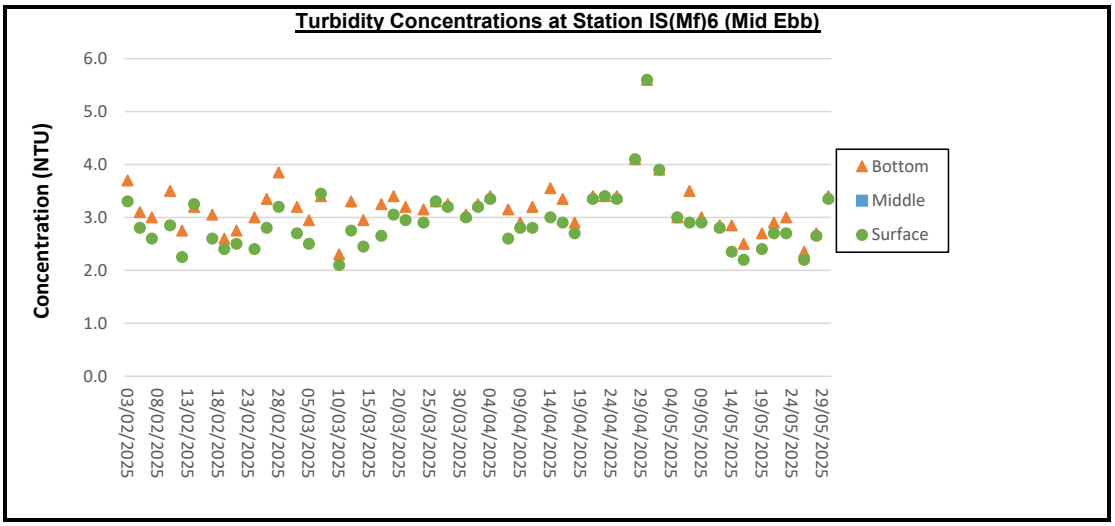
Turbidity Concentrations at Station IS(Mf)6 (Mid Ebb)
Concentration (NTU)
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

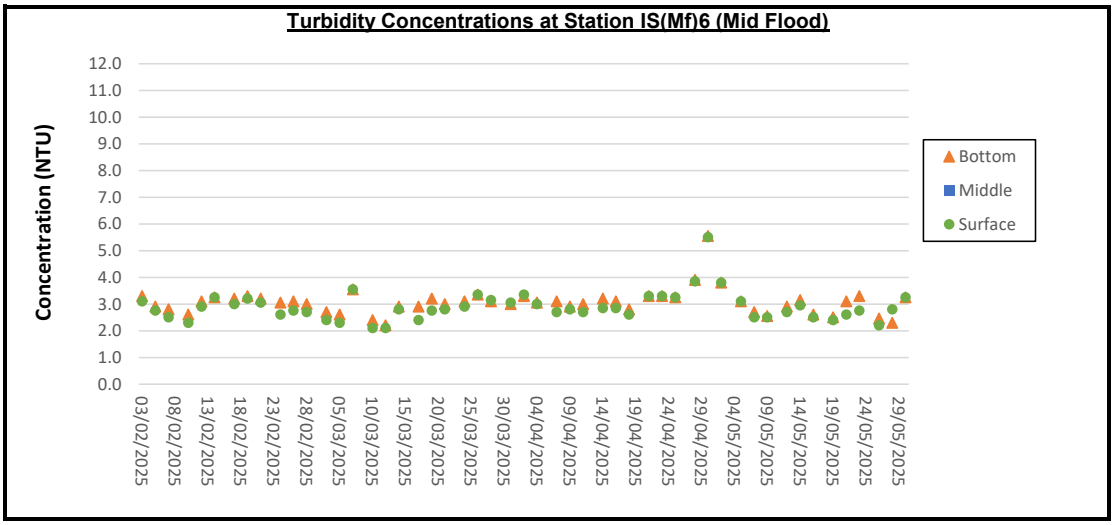
Turbidity Concentrations at Station IS(Mf)6 (Mid Flood)
Concentration (NTU)
12.0
11.0
10.0
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

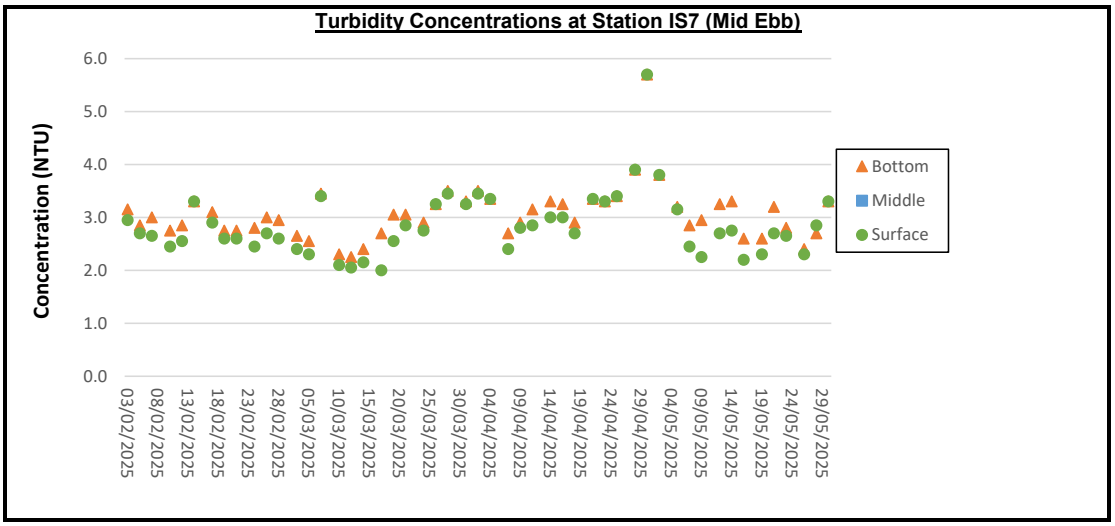
Turbidity Concentrations at Station IS7 (Mid Ebb)
Concentration (NTU)
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

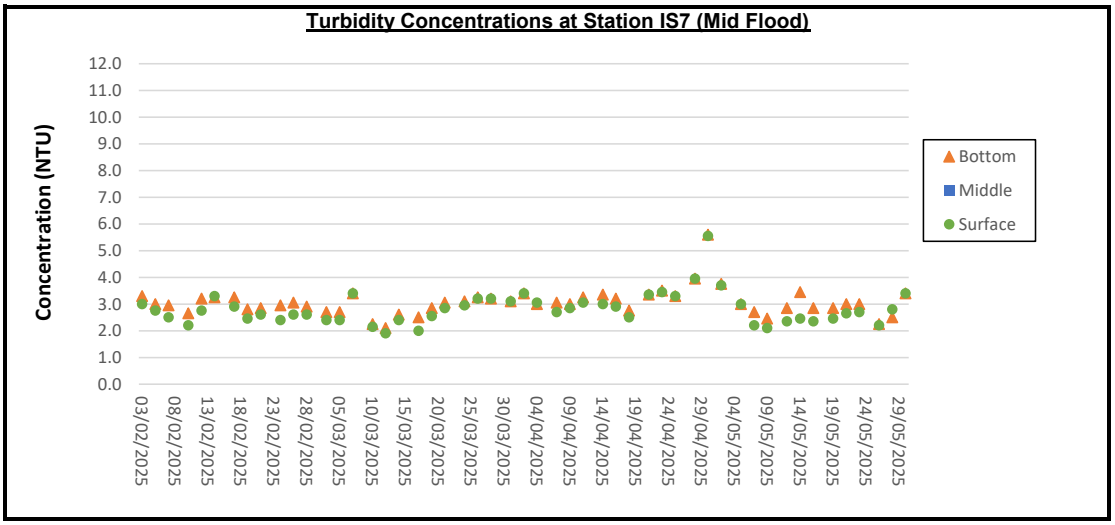
Turbidity Concentrations at Station IS7 (Mid Flood)
Concentration (NTU)
12.0
11.0
10.0
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

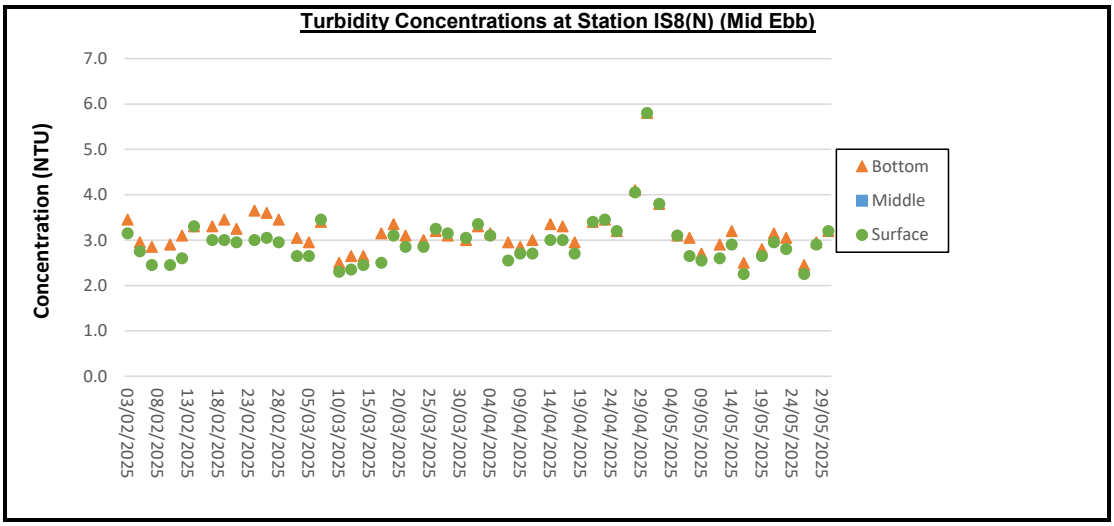
Turbidity Concentrations at Station IS8(N) (Mid Ebb)
Concentration (NTU)
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

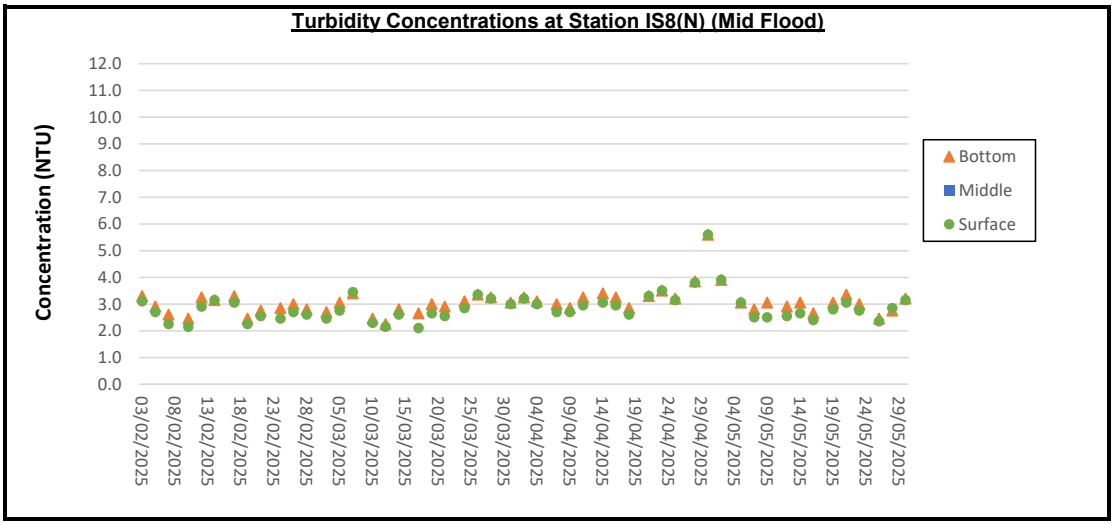
Turbidity Concentrations at Station IS8(N) (Mid Flood)
Concentration (NTU)
12.0
11.0
10.0
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

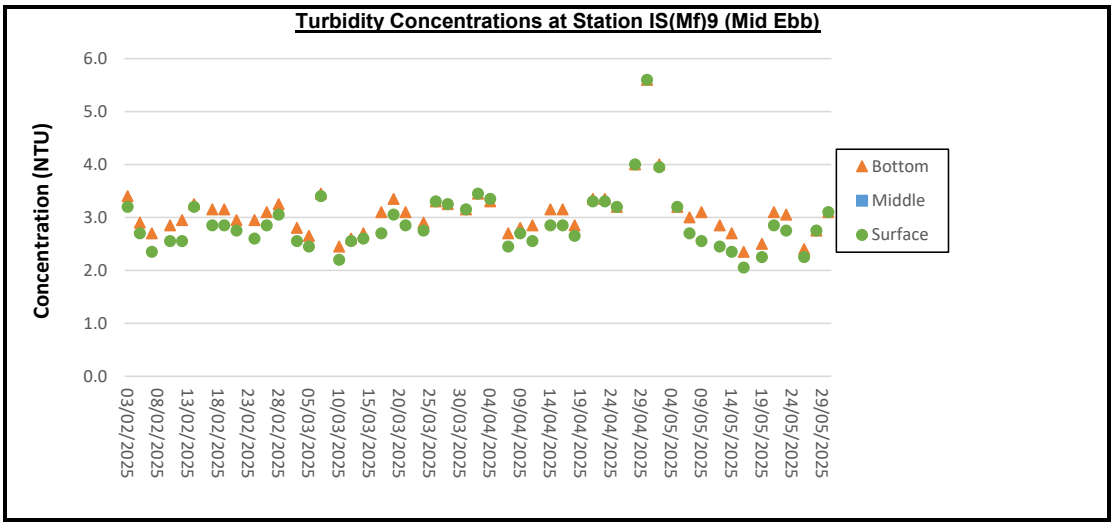
Turbidity Concentrations at Station IS(Mf)9 (Mid Ebb)
Concentration (NTU)
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

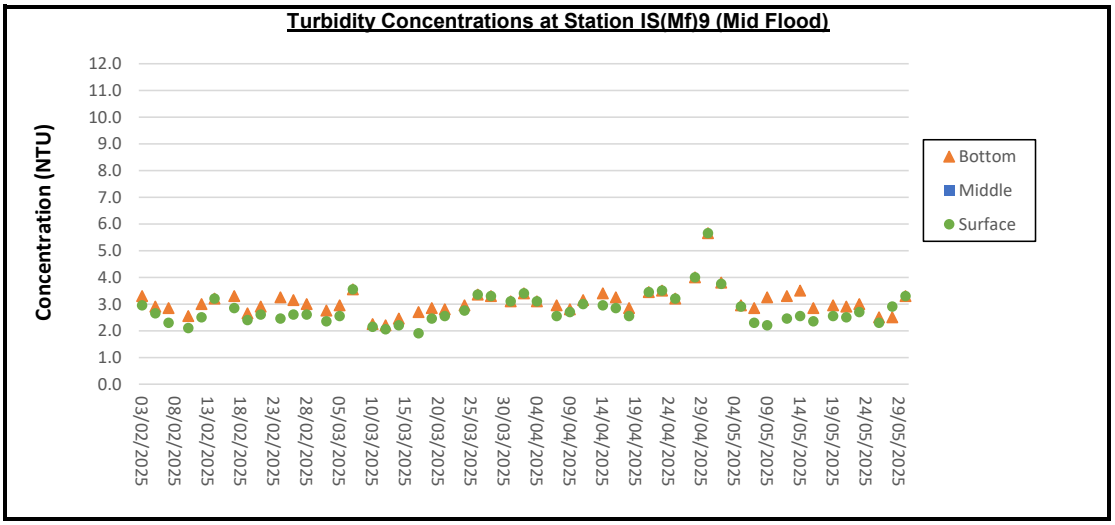
Turbidity Concentrations at Station IS(Mf)9 (Mid Flood)
Concentration (NTU)
12.0
11.0
10.0
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

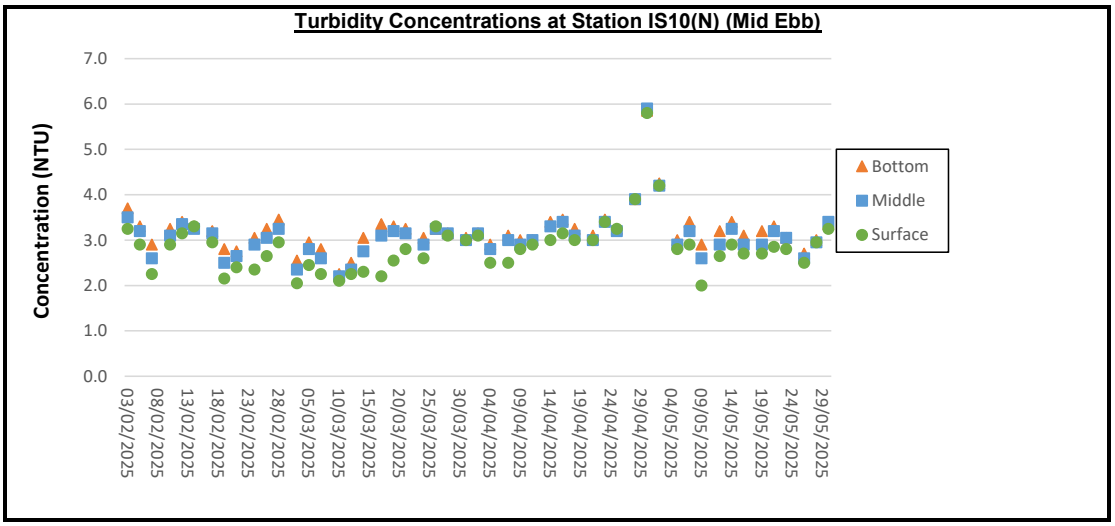
Turbidity Concentrations at Station IS10(N) (Mid Ebb)
Concentration (NTU)
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

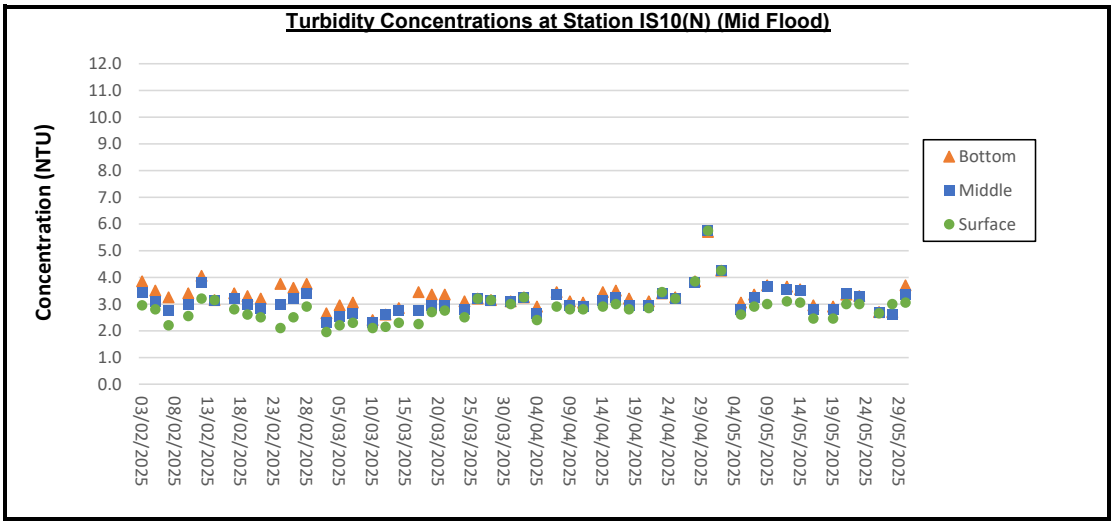
Turbidity Concentrations at Station IS10(N) (Mid Flood)
Concentration (NTU)
12.0
11.0
10.0
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

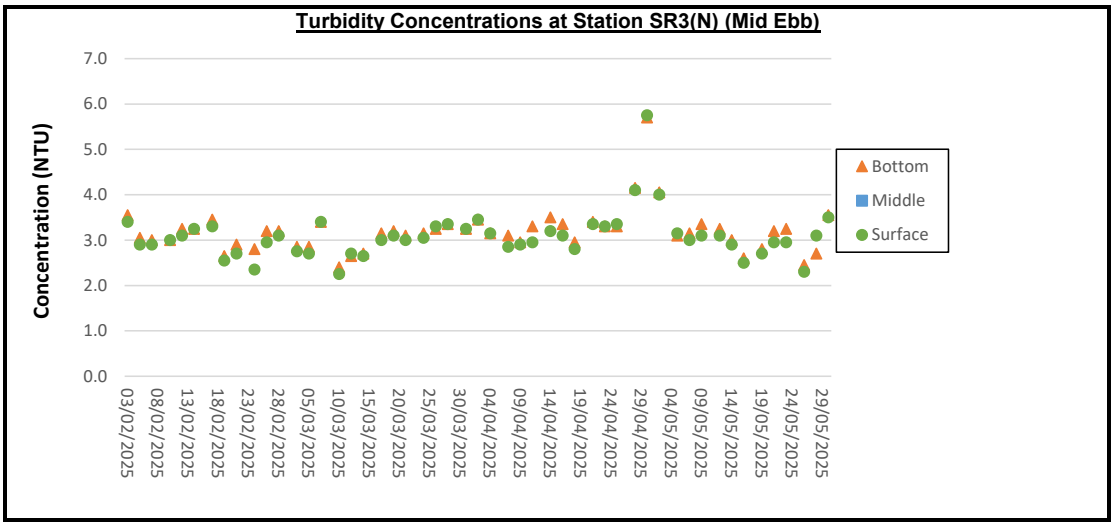
Turbidity Concentrations at Station SR3(N) (Mid Ebb)
Concentration (NTU)
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

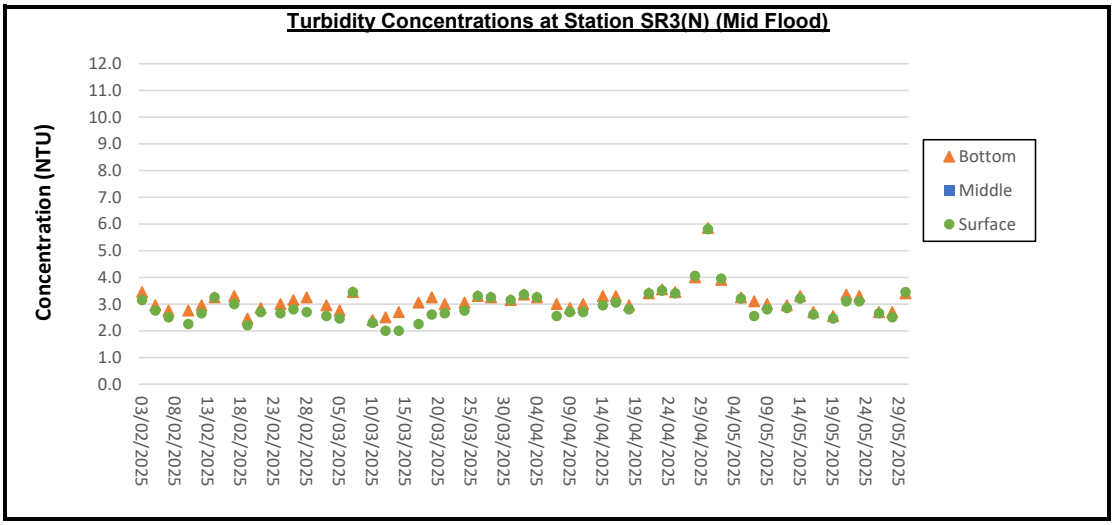
Turbidity Concentrations at Station SR3(N) (Mid Flood)
Concentration (NTU)
12.0
11.0
10.0
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

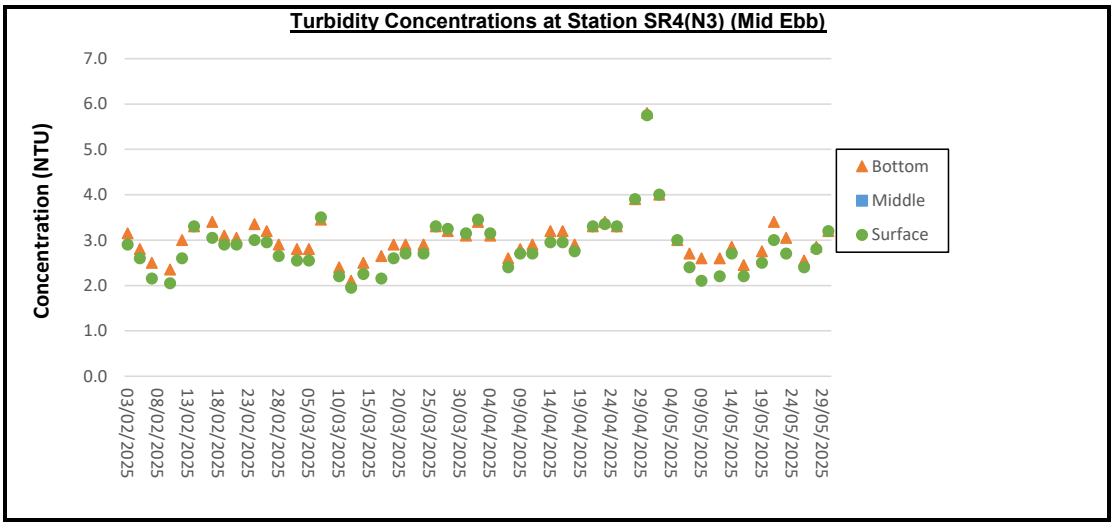
Turbidity Concentrations at Station SR4(N3) (Mid Ebb)
Concentration (NTU)
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

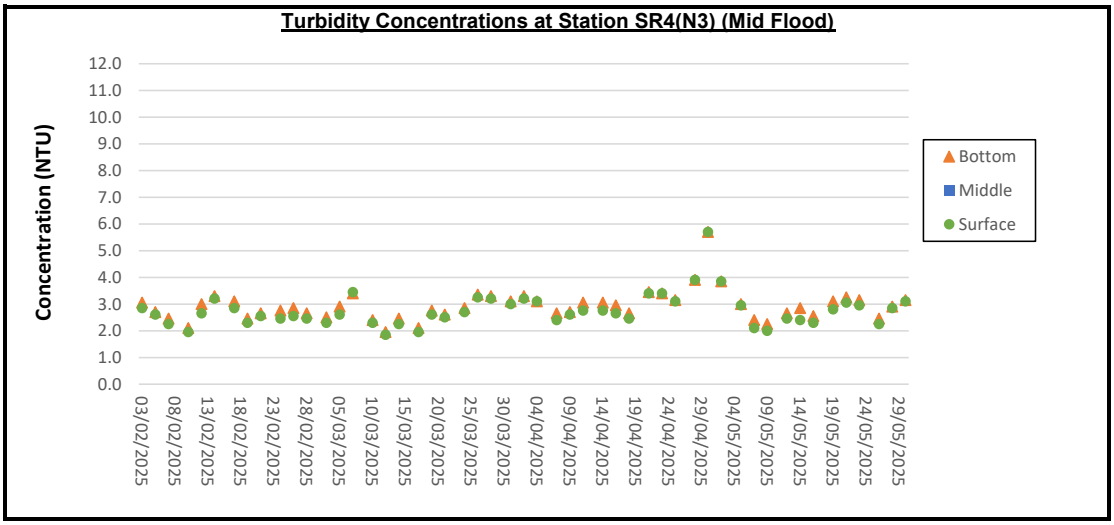
Turbidity Concentrations at Station SR4(N3) (Mid Flood)
Concentration (NTU)
12.0
11.0
10.0
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

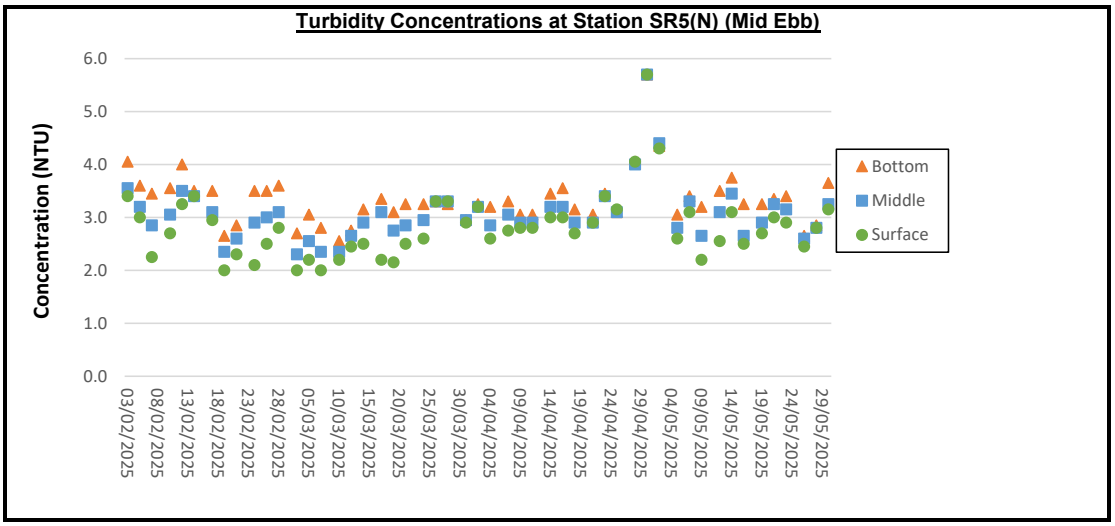
Turbidity Concentrations at Station SR5(N) (Mid Ebb)
Concentration (NTU)
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

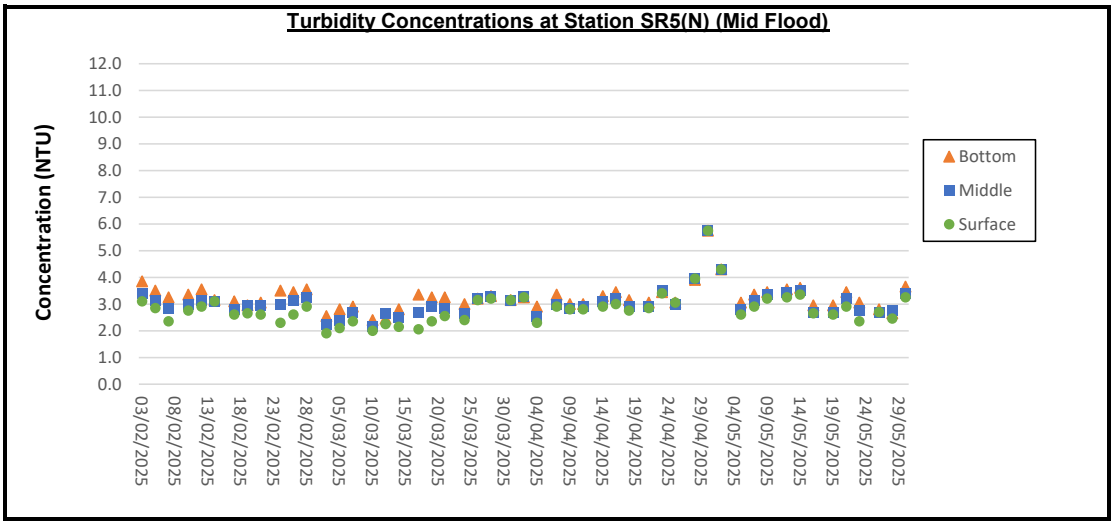
Turbidity Concentrations at Station SR5(N) (Mid Flood)
Concentration (NTU)
12.0
11.0
10.0
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

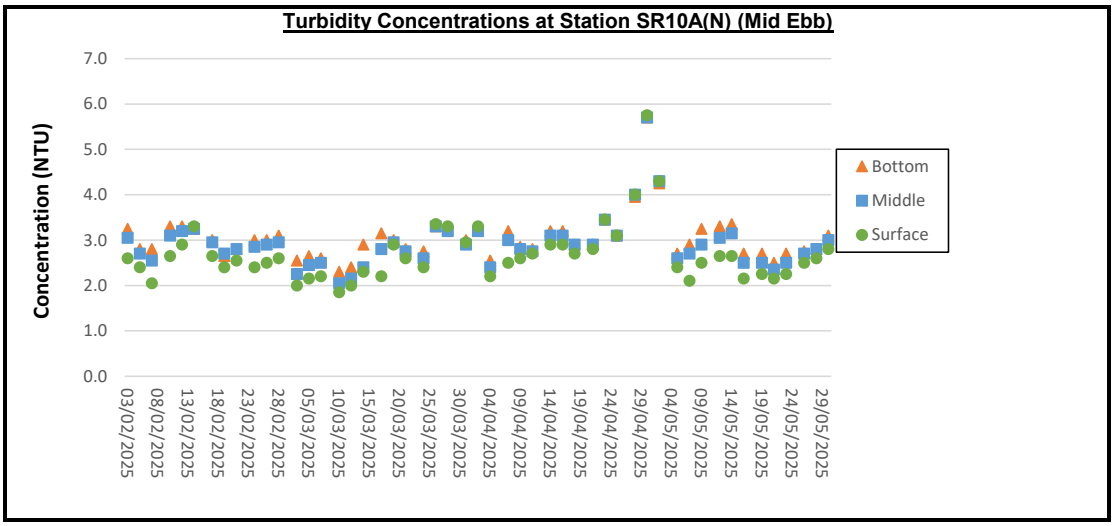
Turbidity Concentrations at Station SR10A(N) (Mid Ebb)
Concentration (NTU)
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

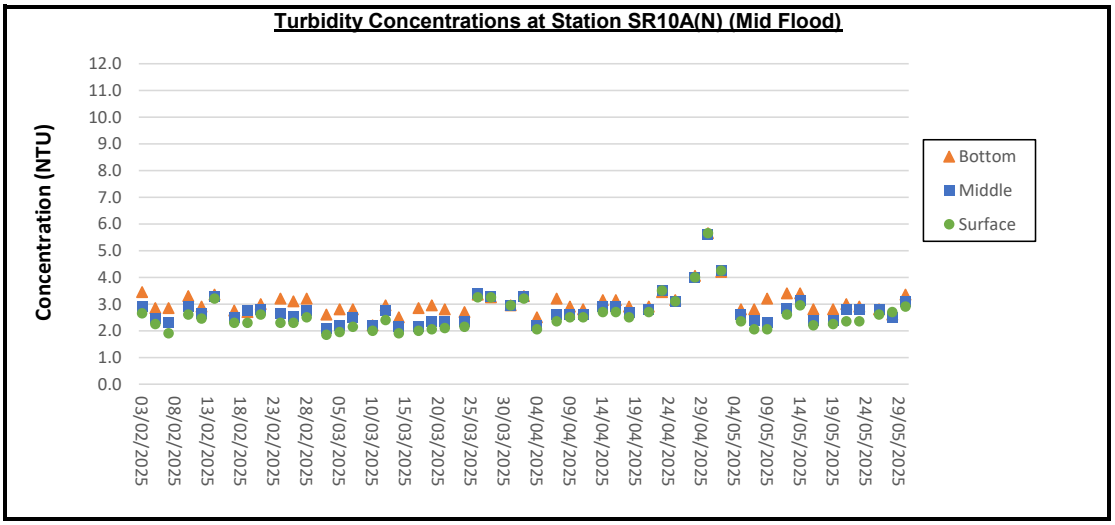
Turbidity Concentrations at Station SR10A(N) (Mid Flood)
Concentration (NTU)
12.0
11.0
10.0
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

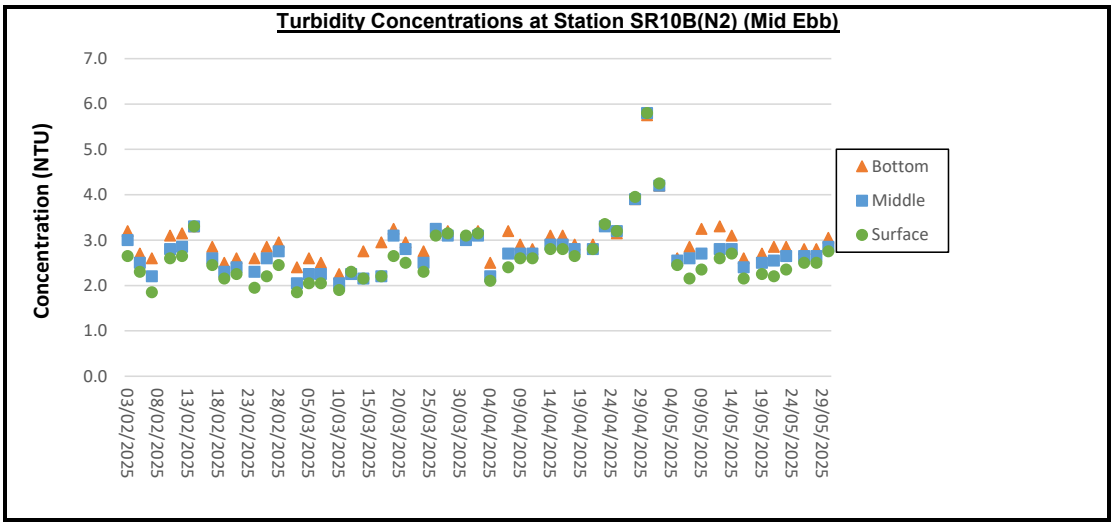
Turbidity Concentrations at Station SR10B(N2) (Mid Ebb)
Concentration (NTU)
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

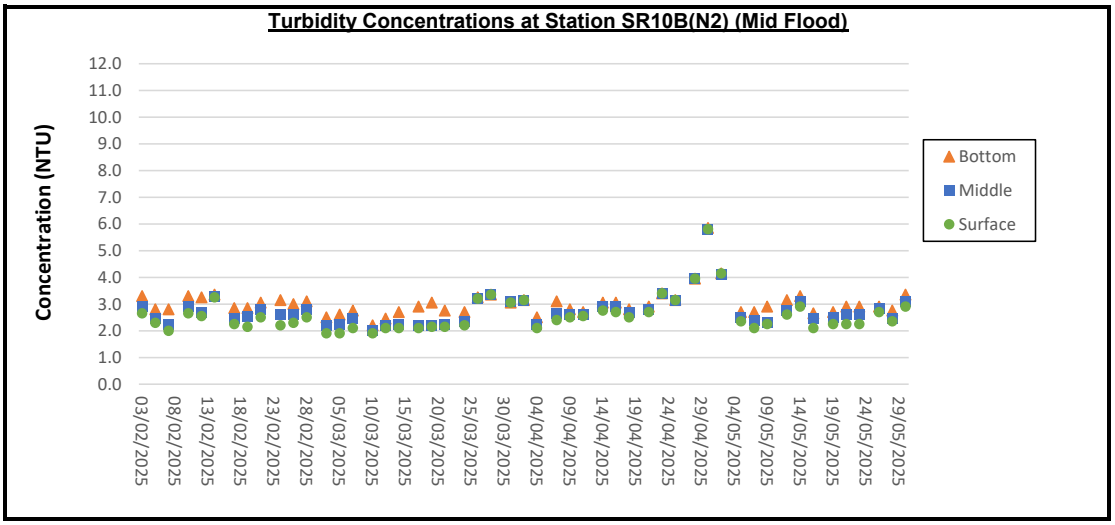
Turbidity Concentrations at Station SR10B(N2) (Mid Flood)
Concentration (NTU)
12.0
11.0
10.0
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

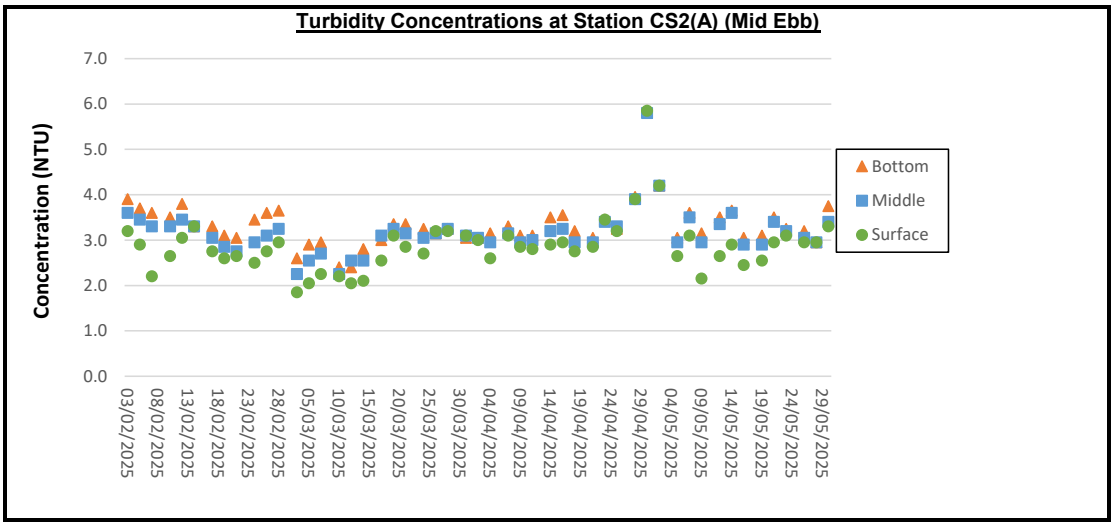
Turbidity Concentrations at Station CS2(A) (Mid Ebb)
Concentration (NTU)
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

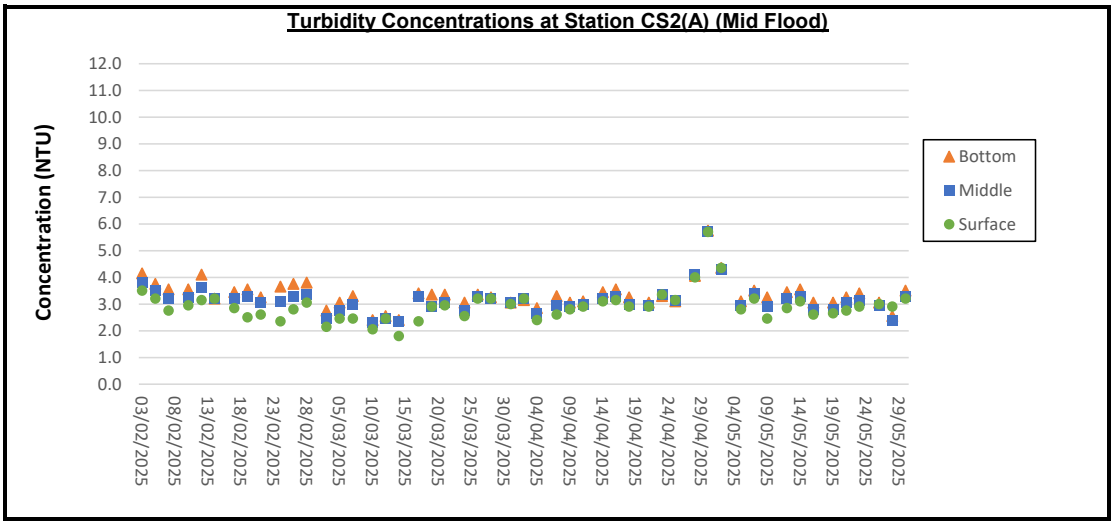
Turbidity Concentrations at Station CS2(A) (Mid Flood)
Concentration (NTU)
12.0
11.0
10.0
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

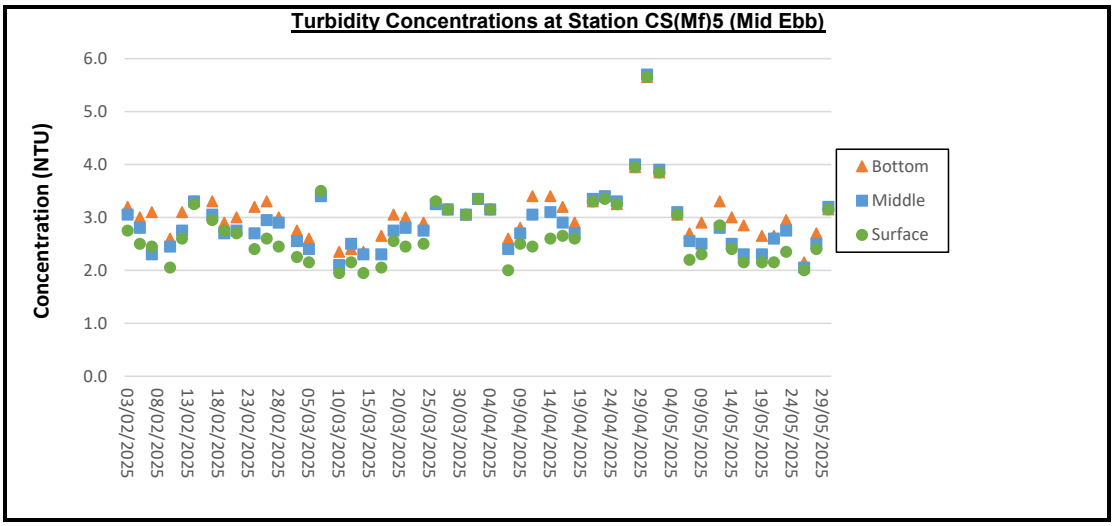
Turbidity Concentrations at Station CS(Mf)5 (Mid Ebb)
Concentration (NTU)
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

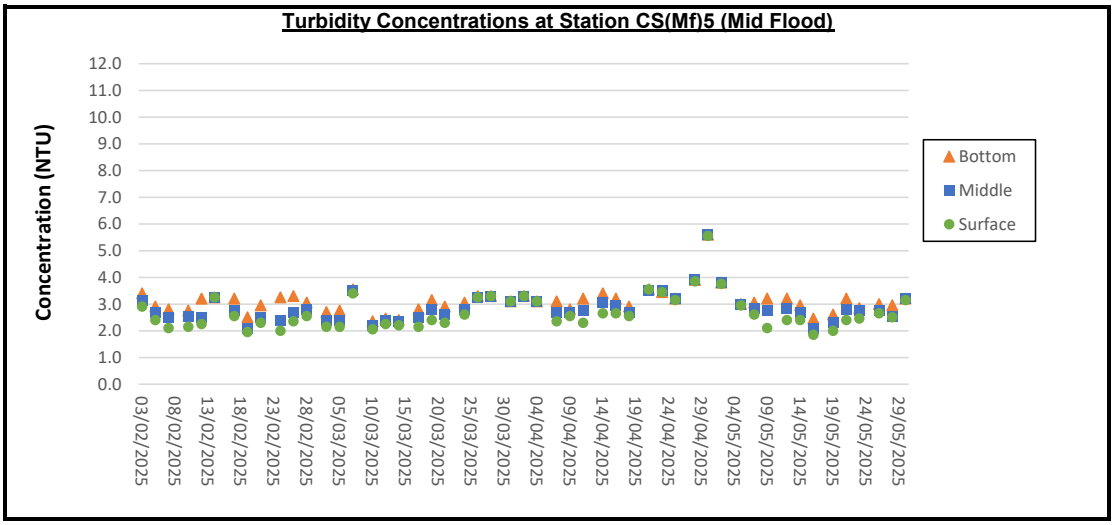
Turbidity Concentrations at Station CS(Mf)5 (Mid Flood)
Concentration (NTU)
12.0
11.0
10.0
9.0
8.0
7.0
6.0
5.0
4.0
3.0
2.0
1.0
0.0
03/02/2025
08/02/2025
13/02/2025
18/02/2025
23/02/2025
28/02/2025
05/03/2025
10/03/2025
15/03/2025
20/03/2025
25/03/2025
30/03/2025
04/04/2025
09/04/2025
14/04/2025
19/04/2025
24/04/2025
29/04/2025
04/05/2025
09/05/2025
14/05/2025
19/05/2025
24/05/2025
29/05/2025
Bottom
Middle
Surface

APPENDIX J

Dolphin Monitoring Results

Contract No. HY/2011/03

Hong Kong-Zhuhai-Macao Bridge

Hong Kong Link Road - Section between Scenic Hill and Hong Kong Boundary Crossing Facilities

Dolphin Monitoring Quarterly Progress Report

SEAMAR

Contract No. HY/2011/03 Hong Kong-Zhuhai-Macao Bridge

Hong Kong Link Road - Section between Scenic Hill and Hong Kong Boundary Crossing Facilities

Dolphin Monitoring Quarterly Progress Report March to May 2025

SEAMAR

Submitted to **China State Construction Engineering (HK) Limited** by

Dr Lindsay Porter
Southeast Asia Marine Mammal Research (SEAMAR) Limited
17/F, Lippo Centre Tower 1, 89 Queensway, Admiralty, Hong Kong
l.porter@seamar.asia

Contents

Introduction 1
Methodology 1
Vessel-Based Line Transect Survey 1
Photo-Identification 2
Data Analysis 2
Results 3
Vessel-Based Line Transect Surveys 3
Encounter Rate 4
Density 4
Distribution and Habitat Use 4
Ranging Patterns 4
Discussion 4
Conclusion 5
References 5
Tables 6
Table 1. Coordinates (HK80 Grid) of transects in the Northwest (NWL) and Northeast (NEL) Lantau survey areas. 6
Table 2. Encounter rates of Chinese white dolphins (Sousa chinensis) in Northwest (NWL) and Northeast (NEL) Lantau for surveys conducted during the current quarterly period (March to May 2025). 7
Table 3. Comparison of average encounter rates of Chinese white dolphins (Sousa chinensis) in Northwest (NWL) and Northeast (NEL) Lantau between the current quarterly period (March to May 2025) and the baseline monitoring period (September to November 2011). 7
Table 4. Comparison of average encounter rates of Chinese White dolphins (Sousa chinensis) in Northeast (NEL) from all spring quarterly periods (March to May 2013-2024) and the baseline monitoring period (September to November 2011). 8
Table 5. Comparison of average encounter rates of Indo-Pacific humpback dolphins (Sousa chinensis) in Northwest (NWL) from all spring quarterly periods (March to May 2013-2024) and the baseline monitoring period (September to November 2011). 9
Figures 10
Figure 1. Transects in the Northeast (NEL) and Northwest (NWL) Lantau survey areas. 10
Annexes 11
Annex I. Survey effort for the quarterly period March to May 2025. 11

Introduction

The Hong Kong Link Road (HKLR) serves to connect the Hong Kong-Zhuhai-Macao Bridge (HZMB) Main Bridge at the Hong Kong Special Administrative Region (HKSAR) Boundary and the HZMB Hong Kong Boundary Crossing Facilities (HKBCF) located at the northeastern waters of the Hong Kong International Airport (HKIA). The construction of HKLR is separated into two sections, with construction of the section between Scenic Hill and Hong Kong Boundary Crossing Facilities (HKBCF) commencing in October 2012.

The updated Environmental Monitoring and Audit (EM&A) Manual for the HKLR states that monthly vessel-based line transect surveys for Indo-Pacific humpback dolphins (*Sousa chinensis*), known locally, and within this and previous reports for this project, as "Chinese white dolphins", are to be conducted in the Northwest (NWL) and Northeast (NEL) Lantau survey areas, as demarcated in the Agriculture and Fisheries Conservation Department (AFCD) Long-Term Marine Mammal Monitoring Programme (AFCD 2024).

In May 2025, Southeast Asia Marine Mammal Research Limited was commissioned by China State Construction Engineering (HK) Limited to conduct vessel surveys in order to collect data on Chinese white dolphins during the final months of the construction phase (i.e., impact period) of the HKLR03 project in the NWL and NEL survey areas. Between October 2012 and May 2025, impact monitoring for HKLR03 had been conducted by another company. The data gathered during the impact monitoring period is to be used to document changes in the distribution, habitat use, encounter rates, density and ranging patterns of Chinese white dolphins; causes of said changes; and if necessary, identify appropriate mitigation measures.

This report is the 40th quarterly progress report of the HKLR03 impact phase dolphin monitoring programme, submitted to China State Construction Engineering (HK) Limited, summarising the results of surveys conducted in March (by Hong Kong Cetacean Research Project Ltd) and April-May 2025 (by Southeast Asia Marine Mammal Research Ltd).

Methodology

Vessel-Based Line Transect Survey

Vessel-based line transect surveys will be conducted on a monthly basis in NEL and NWL, such that all transect lines will be surveyed twice per month, as stated in the EM&A Manual (Figure 1, Table 1). Standard line-transect methods (Buckland et al. 2001; Buckland et al. 2012; Thomas et al. 2010; Thomas et al. 2014) will be employed to collect data comparable to the AFCD long term marine mammal monitoring programme. Surveys will be conducted using a 21.9 m twin-engine motor vessel, with a viewing platform approx. 5 m above sea level with an unobstructed 360° view, at a constant speed of 8-9 kt (tide and current dependent). Two experienced observers will search the area ahead of the vessel between 270° and 90° (in relation to the bow at 0°), with the naked eye and aided by 7x50 binoculars with an in-built compass. A data recorder will input standard effort and environmental data (i.e. prevailing weather conditions, Beaufort Sea State, swell and glare) into a bespoke marine mammal survey app (Cybertracker[1]) that also automatically records the vessel's GPS position, heading and speed. Survey effort conducted on transect lines is denoted "P", while the effort conducted while transiting between transect lines is denoted as "S". Observers and data recorders will rotate every 30 minutes to prevent fatigue. All

[1] https://cybertracker.org/

observers and data recorders are experienced in conducting marine mammal surveys and identifying local cetacean species and behaviour.

Upon sighting dolphins, search effort will be paused and sighting data (i.e. location, time, distance and bearing from the transect line) will be recorded. Distance (m) of the group from the vessel will be estimated by eye and bearing (°) of the group from the vessel will be measured using the binoculars' in-built compass. The perpendicular distance (PSD) of the group from the transect will be calculated post-hoc using the estimated distance and bearing measurement. The vessel will then leave the transect and approach the group to confirm species, group size, group composition and behaviour, as well as to collect photo-identification images. For group composition, four age classes will be used based on external appearance, colouration and body size: calf, juvenile, subadult and adult (Jefferson 2000; Hung and Jefferson 2004; Chan and Karczmarski 2017). An individual is recorded as a 'calf' if it is a solid dark grey colour, approx. 1-1.8 m in length and always in close association with an adult. An individual is classed as a 'juvenile' if it is light grey in colour and has no spots, at least 2 m in length and relatively slender. Juveniles often swim independently but are still associated with at least one adult. An individual is recorded as an 'adult' if it is mostly solid pink with dark spots, at least 2.5 m in length with a robust body and a well-developed dorsal ridge. A dolphin with an external appearance between a juvenile and an adult, with a predominantly grey cast or dense spotting, is classified as a 'subadult'. Behaviour is categorised using Parsons' (1997) ethogram for Chinese white dolphins in Hong Kong. Once all data are recorded, the vessel will return to the point it departed the transect line and search effort will resume.

Photo-Identification

Upon sighting dolphins, every effort will be made to take images (using > 20 megapixel, DSLR cameras equipped with 300 mm telephoto lenses) of both the left and right sides of the dorsal fin of each individual, regardless of perceived dorsal fin distinctiveness.

Photo-identification images of Chinese white dolphins will be catalogued using standardised methods (Würsig and Jefferson 1990). Images will first be graded based on image quality, using features such as focus, exposure, angle and visibility of the dorsal fin. Images of suitable quality will then be compared to existing Chinese white dolphin photo-identification catalogues to identify individual dolphins. Individual dolphins are identified using distinctive features such as dorsal fin shape; dorsal fin markings (nicks and notches); and body scars, deformities and injuries. Pigmentation such as spots and freckles will also be used in conjunction with other identifiers (Karczmarski and Cockcroft 1998).

Data Analysis

Encounter Rate

Encounter rates are defined as the number of sightings (STG) and the total number of dolphins (ANI) per 100 km of survey effort. Only data collected in a Beaufort Sea State 3 or better is used for encounter rate calculation.

For comparison with the baseline monitoring period of this project, monthly encounter rates are calculated using transect line effort from each survey and area (NEL and NWL) and these are then averaged to produce a rate per area for the current quarterly period.

Two-way ANOVA testing can be utilised to examine differences between survey periods (baseline and impact) and survey areas (NEL and NWL). If required, the use of two ANOVAs will be explored using the variables employed in previous quarterly reports: (1) average

encounter rates from the baseline and the relevant quarterly period; and (2) average encounter rates from the baseline and all impact quarterly periods (2013 to current). All statistical tests will be performed in R (R Core Team 2025).

Encounter rates will also be calculated using effort conducted while on the transect line plus the effort conducted while transiting between transect lines for comparison to the AFCD long term marine mammal monitoring programme data.

Density

To investigate density patterns, a quantitative grid analysis will be conducted as described in the AFCD long term marine mammal monitoring programme. The survey area is divided into 1 x 1 km grid cells; densities within each grid cell are defined as the number of sightings (SPSE) and the number of dolphins from sightings (DPSE) per 100 units of survey effort, which are calculated using the following formulae:

$$SPSE = ((S / E) \times 100 / SA\%$$
$$DPSE = ((D / E) \times 100 / SA\%$$

S = total number of on-effort sightings
D = total number of dolphins from on-effort sightings
E = total number of units of survey effort
SA% = proportion of sea area

Units of survey effort are defined as the number of times a grid cell is surveyed, such that a grid cell that has been surveyed 10 times is considered to have 10 units of survey effort. For grid cells that encompass some land area, the percentage of sea area is calculated using QGIS.

Distribution and Habitat Use

To investigate distribution patterns, all sightings will be stratified by group size, group composition and behaviour, and mapped using QGIS (QGIS Development Team 2025). These data can be used to identify important areas for different age classes (e.g. mother-calf pairs) and behaviours (e.g. foraging and resting).

Ranging Patterns

Ranging patterns of individual dolphins will be plotted, using information that is made available from previous quarterly reports (submitted by Hong Kong Cetacean Research Project) and new data collected from May 2025 onwards. Available location histories of identified dolphins will be used to calculate 95% kernel density estimates (KDE) using the *AniMove* plugin in QGIS and the *adehabitatHR* and *rgdal* packages in R (R Core Team 2025).

Results

Vessel-Based Line Transect Surveys

During the period March to May 2025, six line-transect vessel surveys were conducted in NWL and NEL, with each survey taking two days to complete. As the previous contractor did not conduct surveys in April, 'April surveys' were conducted under this contract in May. All transect lines were surveyed six times during the quarterly period. A total survey length of **808.9 km** was completed (transect lines plus transit distance; P+S), with **770.27 km** (95.22%) of effort being conducted under favourable weather conditions (i.e., Beaufort Sea State 3 or better, with visibility of more than 5km). The total surveyed distance in NEL and NWL was **312.57 km** and **496.33 km**, respectively.

Of the **808.9km** of survey effort, **602.62 km** was conducted on the transect line and **206.28 km** of effort was conducted transiting between transect lines. Observers continuously monitored the area in front of the survey vessel both while travelling the transect lines and when in transit between transects. A table of detailed survey effort is provided in Annex I.

Encounter Rate

No dolphins were recorded either on or between the transect lines in NEL and NWL between March and May 2025. As such, all STG and ANI encounter rates, in both areas, are 0 for this quarterly period (Table 2). These rates were compared to the baseline monitoring period (September-November 2011) and the previously reported March-May monitoring periods of this project (Table 3).

The encounter rates for each area were 0 therefore, and has been previously reported in quarterly reports for this project, significant differences were detected between the baseline and the present quarter, in both the STG and ANI encounter rates (Table 4; Table 5), in both NEL and NWL.

Density

No density analysis could be conducted as there were no sightings recorded.

Distribution and Habitat Use

No distribution and habitat mapping could be completed as there were no sightings recorded.

Ranging Patterns

No ranging patterns could be plotted as there were no sightings recorded.

Discussion

Since monitoring for this project began (2012), this is the second March-May quarterly period during which no sightings were recorded (the previous quarterly period was March-May 2022). In addition, two other quarterly periods also did not record any sightings (June-August 2021 and September-November 2022).

In NEL, the dolphin encounter rates (both STG and ANI) in the present three-month impact monitoring period were both 0. Encounters within NEL have been rarely recorded during this quarterly period throughout this project's duration; the only sightings recorded were in March-May 2013 and March-May 2024. Dolphins have been largely absent from the NEL area during this project's monitoring period, which is consistent with the AFCD long-term marine mammal monitoring programme which records only two sightings in NEL since 2015 (all months of the year).

In NWL, the dolphin encounter rates (both STG and ANI) in the present three-month impact monitoring period were both 0. A complete absence of dolphins in the NWL area during this quarterly period is unusual; this is the second March-May quarterly period since this project's monitoring began during which no dolphins were sighted in NWL; no sightings were recorded in March-May 2022.

On review of the past 12 years' March-May quarterly periods (2013-2024), both STG and ANI have markedly decreased since 2015. As yet, there is no evidence that dolphins are returning to NWL, noting that HKLR03 marine works are still ongoing but will be completed soon. This quarter's findings are consistent with the data presented in the

AFCD long-term marine mammal monitoring reports which record only two sightings in the past year April 2023-March 2024[2]; in September 2023 and January 2024.

Conclusion

As the EIA predicted that dolphins will return to northern Lantau waters following the completion of construction work, it is critical to keep monitoring both the NEL and NWL areas to continuously document how the dolphins habitat use is impacted by changes in construction activities, related to HZMB and other projects, and to assess if further mitigation measures can be applied.

References

Agriculture, Fisheries and Conservation Department (AFCD). 2024. Annual Marine Mammal Monitoring Programme April 2023-March 2024) The Agriculture, Fisheries and Conservation Department, Government of the Hong Kong SAR. Retrieved from: https://www.afcd.gov.hk/english/conservation/con_mar/con_mar_chi/con_mar_chi_chi/files/FinalReport2023-24(MM).pdf

Buckland, S. T., Anderson, D., Burnham, K.P., Laake, J. L., Thomas, L. and Borchers, D. 2001. Introduction to Distance Sampling: Estimating Abundance of Biological Populations. Oxford, United Kingdom: *Oxford University Press*.

Buckland, S.T., Anderson, D.R., Burnham, K.P. and Laake, J.L., 2012. Distance sampling: estimating abundance of biological populations. Springer Science & Business Media.

Chan, S. C. Y. and Karczmarski, L. 2017. Indo-Pacific humpback dolphins (*Sousa chinensis*) in Hong Kong: Modelling demographic parameters with mark-recapture techniques. *PLoS ONE*, 12(3): e0174029.

Hung, S. K. and Jefferson, T. A. 2004. Ranging patterns of Indo-Pacific humpback dolphins (*Sousa chinensis*) in the Pearl River Estuary, People's Republic of China. Aquatic Mammals, 30(1): 159-174.

Jefferson, T A. 2000. Population biology of the Indo-Pacific hump-backed dolphin in Hong Kong waters. *Wildlife Monographs*, 144: 1-65.

Jefferson, T. A. and Karczmarski, L. 2000. Sousa chinensis. *Mammalian Species*, 655: 1-9.

Karczmarksi, L. and Cockcroft, V. G. 1998. Matrix photo-identification technique applied in studies of free-ranging bottlenose and humpback dolphins. *Aquatic Mammals*. 24: 143-147.

Parsons, E. M. 1997. Hong Kong's Cetaceans: The biology, socioecology and behaviour of *Sousa chinensis* and *Neophocaena phocaenoides*. PhD Thesis submitted to University of Hong Kong, Hong Kong S.A.R. Retrieved from http://hdl.handle.net/10722/34672.

QGIS Development Team. 2025. QGIS Geographic Information System. Open Source Geospatial Foundation Project. Available from: http://qgis.org.

R Core Team. 2025. R: A Language and Environment for Statistical Computing. R Foundation for Statistical Computing, Vienna, Austria. Available from: https://www.R-project.org.

Thomas, L., Buckland, S.T., Rexstad, E.A., Laake, J.L., Strindberg, S., Hedley, S.L., Bishop, J.R., Marques, T.A. and Burnham, K.P., 2010. Distance software: design and analysis of distance sampling surveys for estimating population size. Journal of Applied Ecology, 47(1), pp.5-14.

Thomas, L., Buckland, S.T., Burnham, K.P., Anderson, D.R., Laake, J.L., Borchers, D.L. and Strindberg, S., 2014. Distance sampling. Wiley StatsRef: Statistics Reference Online.

Würsig, B. and Jefferson, T. A. 1990. Methods of photo-identification for small cetaceans. *Reports of the International Whaling Commission*. 12: 43-52.

[2] The April 2024-March 2025 Report was not available at time of writing

Tables

Table 1. Coordinates (HK80 Grid) of transects in the Northwest (NWL) and Northeast (NEL) Lantau survey areas.

Transect Number	Start		End	
	Easting	Northing	Easting	Northing
1	804671	815456	804671	831404
2	805476	820800	805476	826654
3	806464	821150	806464	822911
4	807518	821500	807518	829230
5	808504	821850	808504	828602
6	809490	822150	809490	825352
7	810499	822000	810499	824613
8	811508	821123	811508	824254
9	812516	821303	812516	824254
10	813425	821176	813425	824657
11	814556	818853	814556	820992
12	815542	818807	815542	824882
13	816506	819480	816506	824859
14	817537	820220	817537	824613
15	818568	820735	818568	824433
16	819532	821420	819532	824209
17	820451	822125	820451	823671
18	821504	822371	821504	823761
19	822513	823268	822513	824321
20	823477	823402	823477	824613
21	805476	827081	805476	830562
22	806464	824033	806464	829598
23	814559	821739	814559	824768
24	805476	815900	805476	819100

Table 2. Encounter rates of Chinese white dolphins (*Sousa chinensis*) in Northwest (NWL) and Northeast (NEL) Lantau for surveys conducted during the current quarterly period (March to May 2025).

Survey Area	Dolphin Monitoring Dates	Encounter Rate (STG) (No. of sightings per 100 km of survey effort)	Encounter Rate (ANI) (No. of dolphins from all sightings per 100 km of survey effort)
		Transect Lines Only (P)	Transect Lines Only (P)
Northeast Lantau	Set 1: March 11th / 12th	0.00	0.00
	Set 2: March 14th / 18th	0.00	0.00
	Set 3: April (23rd/24th May)	0.00	0.00
	Set 4: April (25th/26th May)	0.00	0.00
	Set 5: May 27th / 28th	0.00	0.00
	Set 6: May 29th / 30th	0.00	0.00
Northwest Lantau	Set 1: March 11th / 12th	0.00	0.00
	Set 2: March 14th / 18th	0.00	0.00
	Set 3: April (23rd/24th May)	0.00	0.00
	Set 4: April (25th/26th May)	0.00	0.00
	Set 5: May 27th / 28th	0.00	0.00
	Set 6: May 29th / 30th	0.00	0.00

Table 3. Comparison of average encounter rates of Chinese white dolphins (*Sousa chinensis*) in Northwest (NWL) and Northeast (NEL) Lantau between the current quarterly period (March to May 2025) and the baseline monitoring period (September to November 2011).

	Encounter Rate (STG) (No. of sightings per 100 km of survey effort)		Encounter Rate (ANI) (No. of dolphins from all sightings per 100 km of survey effort)	
	March - May 2025	September - November 2011	March - May 2025	September - November 2011
Northeast Lantau	0.00	6.00 ± 5.05	0.00	22.19 ± 26.81
Northwest Lantau	0.00	9.85 ± 5.85	0.00	44.66 ± 29.85

Note: Encounter rates for the baseline monitoring period have been calculated using effort conducted on the transect lines (P) and under favourable conditions. Encounter rates are presented with ± 1 S.D. (standard deviation).

Table 4. Comparison of average encounter rates of Chinese White dolphins (*Sousa chinensis*) in Northeast (NEL) from all spring quarterly periods (March to May 2013-2024) and the baseline monitoring period (September to November 2011).

	Encounter Rate (STG) (No. of sightings per 100 km of survey effort)	**Encounter Rate (ANI) (No. of dolphins from all sightings per 100 km of survey effort)**
September - November 2011 (Baseline)	6.00 ± 5.05	22.19 ± 26.81
March - May 2013 (HKLR03 Impact)	0.42 ± 1.03	0.42 ± 1.03
March - May 2014 (HKLR03 Impact)	0.00	0.00
March - May 2015 (HKLR03 Impact)	0.00	0.00
March - May 2016 (HKLR03 Impact)	0.00	0.00
March - May 2017 (HKLR03 Impact)	0.00	0.00
March - May 2018 (HKLR03 Impact)	0.00	0.00
March - May 2019 (HKLR03 Impact)	0.00	0.00
March - May 2020 (HKLR03 Impact)	0.00	0.00
March - May 2021 (TMCLKL Post-Construction)	0.00	0.00
March - May 2022 (TMCLKL Post-Construction)	0.00	0.00
March - May 2023 (HKLR03 Impact)	0.00	0.00
March - May 2024 (HKLR03 Impact)	0.48 ± 1.17	0.48 ± 1.17
March - May 2025 (HKLR03 Impact)	0.00	0.00

Note: Encounter rates for the baseline monitoring period have been calculated using effort conducted on the transect lines (P) and under favourable conditions. Encounter rates are presented with ± 1 S.D. (standard deviation).

Table 5. Comparison of average encounter rates of Indo-Pacific humpback dolphins (*Sousa chinensis*) in Northwest (NWL) from all spring quarterly periods (March to May 2013-2024) and the baseline monitoring period (September to November 2011).

	Encounter Rate (STG) (No. of sightings per 100 km of survey effort)	**Encounter Rate (ANI) (No. of dolphins from all sightings per 100 km of survey effort)**
September - November 2011 (Baseline)	9.85 ± 5.85	44.66 ± 29.85
March - May 2013 (HKLR03 Impact)	7.75 ± 3.96	24.23 ± 18.05
March - May 2014 (HKLR03 Impact)	6.51 ± 3.34	19.14 ± 7.19
March - May 2015 (HKLR03 Impact)	0.47 ± 0.73	2.36 ± 4.07
March - May 2016 (HKLR03 Impact)	0.98 ± 1.10	4.78 ± 6.85
March - May 2017 (HKLR03 Impact)	0.93 ± 1.03	5.25 ± 9.53
March - May 2018 (HKLR03 Impact)	2.88 ± 4.81	11.12 ± 22.46
March - May 2019 (HKLR03 Impact)	1.13 ± 1.39	2.54 ± 3.00
March - May 2020 (HKLR03 Impact)	0.56 ± 0.86	0.56 ± 0.86
March - May 2021 (TMCLKL Post-Construction)	1.13 ± 1.37	3.44 ± 4.26
March - May 2022 (TMCLKL Post-Construction)	0.00	0.00
March - May 2023 (HKLR03 Impact)	0.55 ± 0.86	1.35 ± 2.56
March - May 2024 (HKLR03 Impact)	0.57 ± 0.89	1.14 ± 1.77
March - May 2025 (HKLR03 Impact)	0.00	0.00

Note: Encounter rates for the baseline monitoring period have been calculated using effort conducted on the transect lines (P) and under favourable conditions. Encounter rates are presented with ± 1 S.D. (standard deviation).

Figures

Figure 1. Transects in the Northeast (NEL) and Northwest (NWL) Lantau survey areas.

Annexes

Annex I. Survey effort for the quarterly period March to May 2025.

Date	Survey Area	Beaufort Sea State	Effort (km)	Season	Vessel	Type	P/S*
2025-03-11	NWL	2	34.97	SPRING	STANDARD36826	HKLR	P
2025-03-11	NWL	2	14.53	SPRING	STANDARD36826	HKLR	S
2025-03-11	NEL	2	34.82	SPRING	STANDARD36826	HKLR	P
2025-03-11	NEL	2	12.58	SPRING	STANDARD36826	HKLR	S
2025-03-12	NWL	1	12.27	SPRING	STANDARD36826	HKLR	P
2025-03-12	NWL	2	13.20	SPRING	STANDARD36826	HKLR	P
2025-03-12	NWL	1	2.91	SPRING	STANDARD36826	HKLR	S
2025-03-12	NWL	2	8.02	SPRING	STANDARD36826	HKLR	S
2025-03-14	NWL	2	9.10	SPRING	STANDARD36826	HKLR	P
2025-03-14	NWL	3	27.50	SPRING	STANDARD36826	HKLR	P
2025-03-14	NWL	2	2.40	SPRING	STANDARD36826	HKLR	S
2025-03-14	NWL	3	10.50	SPRING	STANDARD36826	HKLR	S
2025-03-14	NEL	2	6.32	SPRING	STANDARD36826	HKLR	P
2025-03-14	NEL	3	29.34	SPRING	STANDARD36826	HKLR	P
2025-03-14	NEL	2	4.10	SPRING	STANDARD36826	HKLR	S
2025-03-14	NEL	3	9.64	SPRING	STANDARD36826	HKLR	S
2025-03-18	NWL	2	2.60	SPRING	STANDARD36826	HKLR	P
2025-03-18	NWL	3	23.76	SPRING	STANDARD36826	HKLR	P
2025-03-18	NWL	2	2.30	SPRING	STANDARD36826	HKLR	S
2025-03-18	NWL	3	6.14	SPRING	STANDARD36826	HKLR	S
2025-05-23	NWL	1	37.01	SPRING	SEAMAR	HKLR	P
2025-05-23	NWL	2	11.06	SPRING	SEAMAR	HKLR	P
2025-05-23	NWL	4	5.93	SPRING	SEAMAR	HKLR	P
2025-05-23	NWL	1	4.76	SPRING	SEAMAR	HKLR	S
2025-05-23	NWL	2	1.15	SPRING	SEAMAR	HKLR	S
2025-05-24	NEL	1	20.55	SPRING	SEAMAR	HKLR	P
2025-05-24	NEL	2	18.12	SPRING	SEAMAR	HKLR	P
2025-05-24	NEL	1	10.62	SPRING	SEAMAR	HKLR	S
2025-05-24	NEL	2	2.42	SPRING	SEAMAR	HKLR	S
2025-05-24	NWL	1	3.68	SPRING	SEAMAR	HKLR	P
2025-05-24	NWL	2	6.49	SPRING	SEAMAR	HKLR	P
2025-05-24	NWL	3	2.21	SPRING	SEAMAR	HKLR	P
2025-05-24	NWL	1	1.75	SPRING	SEAMAR	HKLR	S
2025-05-24	NWL	2	2.93	SPRING	SEAMAR	HKLR	S
2025-05-25	NWL	1	11.04	SPRING	SEAMAR	HKLR	P
2025-05-25	NWL	2	28.78	SPRING	SEAMAR	HKLR	P
2025-05-25	NWL	3	12.37	SPRING	SEAMAR	HKLR	P
2025-05-25	NWL	4	1.15	SPRING	SEAMAR	HKLR	P

2025-05-25	NWL	1	1.28	SPRING	SEAMAR	HKLR	S
2025-05-25	NWL	2	2.62	SPRING	SEAMAR	HKLR	S
2025-05-25	NWL	3	2.88	SPRING	SEAMAR	HKLR	S
2025-05-26	NEL	1	7.07	SPRING	SEAMAR	HKLR	P
2025-05-26	NEL	2	9.06	SPRING	SEAMAR	HKLR	P
2025-05-26	NEL	3	13.11	SPRING	SEAMAR	HKLR	P
2025-05-26	NEL	4	8.08	SPRING	SEAMAR	HKLR	P
2025-05-26	NEL	1	5.80	SPRING	SEAMAR	HKLR	S
2025-05-26	NEL	2	2.44	SPRING	SEAMAR	HKLR	S
2025-05-26	NEL	3	2.42	SPRING	SEAMAR	HKLR	S
2025-05-26	NEL	4	1.18	SPRING	SEAMAR	HKLR	S
2025-05-26	NWL	2	11.06	SPRING	SEAMAR	HKLR	P
2025-05-26	NWL	2	4.41	SPRING	SEAMAR	HKLR	S
2025-05-27	NEL	1	0.43	SPRING	SEAMAR	HKLR	P
2025-05-27	NEL	2	2.63	SPRING	SEAMAR	HKLR	P
2025-05-27	NEL	3	9.22	SPRING	SEAMAR	HKLR	P
2025-05-27	NEL	4	5.43	SPRING	SEAMAR	HKLR	P
2025-05-27	NEL	2	4.91	SPRING	SEAMAR	HKLR	S
2025-05-27	NEL	3	5.37	SPRING	SEAMAR	HKLR	S
2025-05-27	NEL	4	0.41	SPRING	SEAMAR	HKLR	S
2025-05-27	NWL	2	12.77	SPRING	SEAMAR	HKLR	P
2025-05-27	NWL	3	8.75	SPRING	SEAMAR	HKLR	P
2025-05-27	NWL	4	1.32	SPRING	SEAMAR	HKLR	P
2025-05-27	NWL	2	6.30	SPRING	SEAMAR	HKLR	S
2025-05-27	NWL	3	0.18	SPRING	SEAMAR	HKLR	S
2025-05-27	NWL	4	0.81	SPRING	SEAMAR	HKLR	S
2025-05-28	NEL	2	13.43	SPRING	SEAMAR	HKLR	P
2025-05-28	NEL	3	2.58	SPRING	SEAMAR	HKLR	P
2025-05-28	NEL	4	1.34	SPRING	SEAMAR	HKLR	P
2025-05-28	NEL	2	6.68	SPRING	SEAMAR	HKLR	S
2025-05-28	NEL	3	2.92	SPRING	SEAMAR	HKLR	S
2025-05-28	NWL	2	19.27	SPRING	SEAMAR	HKLR	P
2025-05-28	NWL	3	17.91	SPRING	SEAMAR	HKLR	P
2025-05-28	NWL	4	3.96	SPRING	SEAMAR	HKLR	P
2025-05-28	NWL	2	11.90	SPRING	SEAMAR	HKLR	S
2025-05-28	NWL	3	0.36	SPRING	SEAMAR	HKLR	S
2025-05-28	NWL	4	2.33	SPRING	SEAMAR	HKLR	S
2025-05-29	NEL	1	11.99	SPRING	SEAMAR	HKLR	P
2025-05-29	NEL	2	7.49	SPRING	SEAMAR	HKLR	P
2025-05-29	NEL	1	6.03	SPRING	SEAMAR	HKLR	S
2025-05-29	NEL	2	6.01	SPRING	SEAMAR	HKLR	S
2025-05-29	NWL	1	22.98	SPRING	SEAMAR	HKLR	P

2025-05-29	NWL	2	1.69	SPRING	SEAMAR	HKLR	P
2025-05-29	NWL	1	8.94	SPRING	SEAMAR	HKLR	S
2025-05-30	NEL	2	2.83	SPRING	SEAMAR	HKLR	P
2025-05-30	NEL	3	11.72	SPRING	SEAMAR	HKLR	P
2025-05-30	NEL	4	3.42	SPRING	SEAMAR	HKLR	P
2025-05-30	NEL	2	1.65	SPRING	SEAMAR	HKLR	S
2025-05-30	NEL	3	8.28	SPRING	SEAMAR	HKLR	S
2025-05-30	NEL	4	0.13	SPRING	SEAMAR	HKLR	S
2025-05-30	NWL	1	2.34	SPRING	SEAMAR	HKLR	P
2025-05-30	NWL	2	8.91	SPRING	SEAMAR	HKLR	P
2025-05-30	NWL	3	28.40	SPRING	SEAMAR	HKLR	P
2025-05-30	NWL	4	1.16	SPRING	SEAMAR	HKLR	P
2025-05-30	NWL	1	3.58	SPRING	SEAMAR	HKLR	S
2025-05-30	NWL	2	2.95	SPRING	SEAMAR	HKLR	S
2025-05-30	NWL	3	4.78	SPRING	SEAMAR	HKLR	S
2025-05-30	NWL	4	1.98	SPRING	SEAMAR	HKLR	S

* P=distance travelled on transect lines; S=distance travelled transiting between transect lines

APPENDIX K

Waste Flow Table

Monthly Summary Waste Flow Table for 2025

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract *(Note 8)*	Reused in Other Projects *(Note 8)*	Disposed as Public Fill *(Note 6)*	Imported Fill *(Note 6)*	Metals	Paper / Cardboard Packaging	Plastics *(Note 3)*	Chemical Waste	Others, e.g. general refuse *(Note 8)*
	(in '000m^3)	(in '000m^3)	(in '000m^3)	(in '000m^3)	(in '000m^3)	(in '000m^3)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000kg)	(in '000m^3)
Jan	7.890	0.000	0.000	7.890	0.000	0.000	0.000	0.000	0.000	0.000	0.020
Feb	9.063	0.000	0.000	9.063	0.000	0.000	0.000	0.000	0.000	0.000	0.007
Mar	11.782	0.000	0.000	11.782	0.000	0.000	0.000	0.000	0.000	0.000	0.013
Apr	9.866	0.000	0.000	9.866	0.000	0.000	0.000	0.000	0.000	0.000	0.007
May	0.743	0.000	0.000	0.743	0.000	0.000	0.000	0.000	0.000	0.000	0.007
Jun	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Sub-total	39.344	0.000	0.000	39.344	0.000	0.000	0.000	0.000	0.000	0.000	0.052
Jul	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Aug	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Sep	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Oct	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Nov	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Dec	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Sub- total	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Total	39.344	0.000	0.000	39.344	0.000	0.000	0.000	0.000	0.000	0.000	0.052

Forecast of Total Quantities of C&D Materials to be Generated from the Contract*										
Total Quantity Generated	**Hard Rock and Large Broken Concrete**	**Reused in the Contract**	**Reused in Other Projects**	**Disposed as Public Fill**	**Imported Fill**	**Metals**	**Paper / Cardboard Packaging**	**Plastics (see Note 3)**	**Chemical Waste**	**Others, e.g. general refuse**
(in '000m^3)	**(in '000m^3)**	**(in '000m^3)**	**(in '000m^3)**	**(in '000m^3)**	**(in '000m^3)**	**(in '000kg)**	**(in '000kg)**	**(in '000kg)**	**(in '000kg)**	**(in '000m^3)**
310.805	21.788	224.130	40.265	24.622	1362.000	10.000	4.600	0.500	3.400	2.350

Notes:
(1) The performance target are given in ER Appendix 8J Clause 14
(2) The waste flow table shall also include C&D materials that are not specified in the Contract to be imported for use at the Site
(3) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material
(4) The Contractor shall also submit the latest forecast of the amount of C&D materials expected to be generated from the Works, together with a break down of the nature where the total amount of C&D materials expected to be generated from the Works is equal to or exceeding 50,000m^3.
(5) All recyclable materials, including metals, paper / cardboard packaging, plastics, etc. will be collected by registered collector for
(6) Conversion factors for reporting purpose:
excavated (bulk): rock = 2.0 tonnes/m^3; soil = 1.8 tonnes/m^3, sand=1.9tonnes/m^3 Metal=7.85tonnes/m3
(7) Numbers are rounded off to the nearest three decimal places
(8) 30T dump truck carries C&D waste of 8.0m^3; 24T dump truck carries C&D waste of 6.5m^3

APPENDIX L

Summary of Environmental Licenses and Permits

Summary of Environmental Licences and Permits Application and Status

Environmental Permit

Date Application Submitted	Status	Date EP Issued	EP No.	EP Holder	Expiry Date
04.12.2014	VEP issued	22.12.2014	EP-352/2009/D	Highways Department	N/A
24.03.2016	VEP Issued	11.04.2016	EP-353/2009/K	Highways Department	N/A

Notification of Carrying Out Notifiable Works under Air Pollution Control (Construction Dust) Regulation

Date Notification Submitted	Notification Ref. No.	Valid Since	Expiry Date
25.05.2012	345690	01.06.2012	N/A

Notification of Carrying Out Notifiable Works under Air Pollution Control (Construction Dust) Regulation Form NB

Date Notification Submitted	Notification Ref. No.	Valid Since	Expiry Date
31.07.2015	391702	31.07.2015	N/A

Billing Account for Disposal of Construction Waste

Date Application Submitted	Account No	Valid Since	Expiry Date
01.06.2012	7015313	27.06.2012	N/A

Chemical Waste Producer Registration

Date Registration Submitted	Waste Producer No.	Date Registration Issued	Major Waste Type	Expiry Date
20.06.2012	5213-950-C1169-43	12.07.2012	Spent lubricating oil, spent flammable liquid (diesel), surplus paint, spent organic solvent and their containers, spent batteries, soil containing mineral oil	N/A

Construction Noise Permit

Item No.	Date Application Submitted	Works Area Applied	Description	Status	CNP No.	Valid from	Until
1	22.11.2024	All Works Area	All Works	CNP issued on 06.12.2024	GW-RS1167-24	21.12.2024 1900	20.06.2025 2300

APPENDIX M

Record of "Notification of Environmental Quality Limit Exceedances" and
Record of "Notification of Summons and Prosecutions"

Summary of Notifications of Summons and Prosecutions

Total No. of Notifications of Summons / Prosecutions Received	No. of Notifications of Summons / Prosecutions Received during Reporting Period	Status of Notifications of Summons / Prosecutions
0	0	N/A

Contract No. HY/2011/03 -
Hong Kong- Zhuhai- Macao Bridge
Hong Kong Link Road Section between Scenic Hill and Hong Kong Boundary Crossing Facilities
Notifications of Environmental Quality Limits Exceedances Notification No.: 310 ver 0

Date of Notification: 16 April 2025

Works Inspected: 24-hr TSP Monitoring was undertaken on 16 April 2025 and the test report was issued on 22 April 2025.

Monitoring Location: AMS6 – Dragonair Building

Parameter: 24-hour TSP Monitoring

Action & Limit Levels (AL & LL) / Measured Level:

PARAMETER	STATION	AL, $\mu g/m^3$	LL, $\mu g/m^3$	MEASURED LEVEL, $\mu g/m^3$
16 April 2025. 24-hr TSP (0800-0800)	Dragonair Building	173	260	***245***

Notes: ***Bold Italic*** means AL exceedance
Bold Italic with underline means LL exceedance

Possible reason for Action Level Non-compliance:
Action Level exceedance of 24-hr TSP level was recorded at AMS6 – Dragonair Building on 16 April 2025.

According to the information provided by the Contractor, marine based works with dust suppression were conducted at construction site which is located around 720m away from AMS6 during sampling period on 16 April 2025.

During site observation on 9 April and 17 April 2025, no fugitive dust emission was noted by ET at construction site near monitoring station AMS6. It was noted that no Action and Limit Level exceedances of 1-hr TSP were recorded at AMS5 and AMS6 in April 2025, as well as no Action and Limit Level exceedance of 24-hr TSP was recorded at AMS5 in April 2025.

Actions taken/ to be taken:

Based on the weekly audit, i.e. site inspection on 9 April and 17 April 2025, the Contractor has implemented dust control measures throughout the construction phase. No fugitive dust emission was noted by ET on 9 April and 17 April 2025 at construction site near monitoring station AMS6. The exceedance recorded at monitoring station AMS6 is unlikely related to the Contract. ET will continuously monitor 24-hr TSP level at AMS6 to ensure compliance with relevant criteria throughout the construction period. In the meantime, the Contractor is reminded to continuously implement dust control measures throughout the construction phase.

Reviewed by Claudine Lee Title : ET Leader

Date : 12 May 2025

Copied to Supervising Officer, ENPO/ IEC, Contractor

Contract No. HY/2011/03 -
Hong Kong- Zhuhai- Macao Bridge
Hong Kong Link Road Section between Scenic Hill and Hong Kong Boundary Crossing Facilities
Notifications of Environmental Quality Limits Exceedances Notification No.: 311 ver 0

Date of Notification: 04 June 2025

Works Inspected: Not Applicable

Monitoring Location: NEL & NWL

Parameter: Ecology (Chinese White Dolphin Monitoring)

Action & Limit Levels			**Monitoring Results**
	North Lantau Social Cluster		The quarter of March 2025 – May 2025
	Action Level (AL)	Limit Level (LL)	
Northeast Lantau (NEL)	STG < 4.2 & ANI < 15.5	NEL: (STG < 2.4 & ANI <8.9) and NWL: (STG < 3.9 & ANI <17.9)	***STG=0; ANI=0***
Northwest Lantau (NWL)	STG < 6.9 & ANI < 31.3		***STG=0; ANI=0***

Notes:
1. STG means quarterly encounter rate of number of dolphin sightings.
2. ANI means quarterly encounter rate of total number of dolphins.
3. For North Lantau Social Cluster, AL will be triggered if either NEL or NWL falls below the criteria; LL will be triggered if both NEL and NWL fall below the criteria.
4. ***Bold Italic*** means AL exceedances.
5. ***Bold Italic with underline*** means LL exceedances

Possible reason for Limit Level Non-compliance:

There was a Limit Level exceedance of dolphin monitoring for the quarterly monitoring data (between March 2025 and May 2025). According to the contractor's information, reinstatement works were undertaken for HKLR03 during the quarter of March 2025 – May 2025.

There is no evidence showing the current LL non-compliance directly related to the construction works of HKLR03 (where the amounts of working vessels for HKLR03 have been decreasing), although the generally increased amount of vessel traffic in NEL during the impact phase has been partly contributed by HKLR03 works since October 2012. It should also be noted that work area under HKLR03 (adjoining the Airport Island) situates in waters which has rarely been used by dolphins in the past, and the working vessels under HKLR03 have been travelling from source to destination in accordance with the Marine Travel Route to minimize impacts on Chinese White Dolphin (CWD). In addition, the contractor will implement proactive mitigation measures such as avoiding anchoring at Marine Department's designated anchorage site – Sham Shui Kok Anchorage (near Brothers Island) as far as practicable.

Hong Kong-Zhuhai-Macao Bridge Authority (HZMBA) for the Mainland section of Hong Kong-Zhuhai-Macao Bridge (HZMB) has commenced a survey on fisheries resources and CWD in the Mainland waters. During the one-year HZMBA survey between August 2015 to August 2016, the findings of the HZMBA survey on CWD sighting and photo-identification works which provide solid evidence that some CWD that were previously more often sighted in HK waters have expanded their ranges into the Mainland waters, and some with reduced usage in HK waters. These data were mentioned in Monitoring of Chinese White Dolphins in Southwest Lantau Waters – Ninth Quarterly Report (March to May 2017) which is available on ENPO's website.

Actions taken/ to be taken:

Inform the IEC, ENPO, ER/SOR and Contractor

The ETL informed IEC, ENPO, SOR and Contractor via email on 04 June 2025.

Repeat statistical data analysis to confirm findings and check monitoring data:

A two-way ANOVA with repeated measures and unequal sample size was conducted to examine whether there were any significant differences in the average encounter rates between the baseline and impact monitoring periods. The two variables that were examined included the two periods (baseline and impact phases) and two locations (NEL and NWL).

For the comparison between the baseline period and the present quarter (39th quarter of the impact phase being assessed), the p-values for the differences in average dolphin encounter rates of STG and ANI 0.0000 and 0.0000 respectively in the present quarter. Even if the alpha value is set at 0.0001, significant differences were still detected between the baseline and present quarter in both the average dolphin encounter rates of STG and ANI.

For comparison between the baseline period and the cumulative quarters in impact phase (i.e. first 48 quarters of the HKLR03/TMCLKL monitoring programme phase being assessed), the p-values for the differences in average dolphin encounter rates of STG and ANI were 0.000000 and 0.000000 respectively. Even if the alpha value is set at 0.00001, significant differences were still detected in both the average dolphin encounter rates of STG and ANI (i.e. between the two periods and the locations).

Review all available and relevant data, including raw data and statistical analysis results of other parameters covered in the EM&A, to ascertain if differences are as a result of natural variation or previously observed seasonal differences:

Available monitoring data for all quarterly time periods from HKLR project inception have been reviewed. For the area NEL since 2013, surveys from only two of these quarterly periods have yielded any "on effort" sightings from vessel monitoring, i.e., March-May 2013 and March 2024-May 2024. The same quarterly period, in the 10 years between these sightings, resulted in no sightings. For the area NWL since 2013, only one quarter, March-May 2022, resulted in 0 sightings, with a declining trend calculated since project commencement.

The annual AFCD monitoring data for 2023-2024 (the latest available report) and previous years, have been reviewed and it is noted that the AFCD long-term marine mammal monitoring programme has documented a dramatic decline in dolphin occurrence in northern Lantau waters over the past decade. AFCD surveys have not recorded any dolphins in NEL between 2015 and March 2024 and only a few dolphins in NWL in recent years, i.e., for the period April 2023-March 2024, only two sightings are recorded in the AFCD Annual Report; 3 individuals in September 2023 and 2 individuals in January 2024, both sightings outside this quarterly time period. This review concurs with the results of the HKLR03 monitoring surveys conducted in Spring 2025, that dolphin sightings are now rare in NEL and NWL areas.

Recommendations/ mitigation measures/ actions if necessary:

Review to ensure all the dolphin protective measures are fully and properly implemented and advise on additional measures if necessary:

All dolphin protective measures are fully and properly implemented in accordance with the EM&A Manual, EIA report and EP. According to the Regular Marine Travel Route Plan, the travelling speed of vessels must not exceed 5 knots when crossing the edge of the Brothers Marine Park. The Contractor will continue to provide training for skippers to ensure that their working vessels travel from source to destination to minimize impacts on Chinese White Dolphin and avoid anchoring at Marine Department's designated anchorage site - Sham Shui Kok Anchorage (near Brothers Island) as far as practicable. Also, it is recommended to complete the marine works of the Contract as soon as possible so as to reduce the overall duration of impacts and allow the dolphins population to recover as early as possible.

ET will keep reviewing the implementation status of the dolphin related mitigation measures and remind the contractor to implement the relevant measures.

It was also recommended that the marine works footprint (e.g., reduce the size of peripheral silt curtain) and vessels for the marine works should be reduced as much as possible, and vessels idling / mooring in other part of the North Lantau shall be avoided whenever possible.

HyD updated that the draft map of the proposed Brothers Marine Park (BMP) was gazetted in February 2016. ENPO updated that the BMP was approved by the Chief Executive in the Executive Council in August 2016. The ETs were reminded to update the BMP boundary in the Regular Marine Travel Route (RMTR) Plan. The BMP was designated on 30 December 2016. It was suggested that the protection measures (e.g. speed limit control) for the approved BMP shall be brought forward so as to provide a better habitat for dolphin recovery. It was noted that under the latest RMTR Plan, the contractors have committed to reduce the vessel speed in BMP.

The marine travel route will shift along the edge of the Brothers Marine Park as much as practical under the RMTR Plan. It was noted that even though marine vessels may moor within the mooring site of BMP, commercial activities including loading / unloading / transshipment are not allowed except a permit is obtained. The HZMB works vessels were recommended to avoid the BMP.

It was noted that starting from January 2016, HSF from the SkyPier will be re-routed north to the northern edged of the Sha Chau and Lung Kwu Chau Marine Park. While the HSF will reduce speed to 15 knots, the associated disturbance may still affect CWD in the area. It was implied that the CWDs in the area shall be closely followed.

There was a discussion on exploring possible further mitigation measures, for example, controlling the underwater noise. It was noted that the EIA reports for the projects suggested several mitigation measures, all of which have been implemented.

Reviewed by Claudine Lee Title : ET Leader

Date : 22 July 2025

Copied to Supervising Officer, ENPO/ IEC, Contractor

APPENDIX N

Cumulative Statistics on Complaints

HyD Contract No.HY/2011/03
Hong Kong - Zhuhai - Macao Bridge Hong Kong Link Road
Section between Scenic Hill and Hong Kong Boundary Crossing Facilities

Complaint Register

Complaint No.	Received Date	Received Time	Source	Category	Complaint Details	Location	Improvement Measures Taken	Status	Remarks
COM-2012-008	22-Oct-2012	16:41	EPD	Environmental (Water Pollution)	X先生投訴東涌機場對出港珠澳大橋地盤，有污水排到海中（懷疑是油污），污染環境，要求跟進及回覆。(Photos attached). The "phenomenon"was observed over the past week. The photos attached were taken on 19.10.2012, 22.10.2012 and 23.10.2012	Portion X	The pelican barge as shown in the photos provided on 24 October 2012 did not belong to the Contractor.	Closed	-
COM-2012-009	05-Nov-2012	-	1823 CASE: 1-391341859	Environmental (Noise and light)	The citizen complained about noise and light pollution from the barges working on the Zhuhai Macau Bridge project. Barge machinery working to about 10pm at night and sometimes can be heard intermittently through the night. The noise is more audible because the machinery is sited on/over the water.	Portion X	The Contractor has adjusted the emission angle of the lights on working vessels with a view to minimizing the glaring effect to the adjoining residential areas	Closed	-
COM-2012-009(2)	11-Nov-2012	-	1823 CASE: 1-391341859	Environmental (Noise, water quality & air quality)	The complainant noted that the barges are still working on a Sunday, up until 10pm at night, very noisy, causing pollution of the water and at times expelling black smoke from their engines. A photograph taken at 10.40am on Sunday 11 November 2012 was attached.	Portion X	-	Closed	-
COM-2012-009(3)	14-Nov-2012	-	1823 CASE: 1-391341859	Environmental (Noise)	The complainant did not accept the reply. He further said that "All staff has to do is come out either at night or a Sunday to check, so easy. If this continues I will have no choice to call the police out."	Portion X	The Contractor has taken the following further mitigation measures for the reclamation works: (a) Mitigation Measures for Noise Nuisance: • Improvement of noise covers onto the generators / motors on barges; and • Increase frequency of applying lubricant to all moving parts and gear wheels of the working barges. (b) Mitigation Measures for Smoke Emission: • Increase frequency of maintenance and checking of engines on barges that may emit smoke; and • Installation/ replacement of smoke suppression device such as air filter, at engines where necessary.	Closed	-
COM-2012-010(1)	06-Nov-2012	-	<hzmbenquiry@hyd.gov.hk>	Environmental (Noise)	The complainant stated that lately work has started opposite Le Bleu Deux estate using barges. The work in process is generated high level of noise from powered tools used on those barges. Even if the noise was acceptable on weekdays during daytime, it is definitely creating nuisance to local resident at night (past 7pm) and on Sunday. Basically as 5 November 12 evening, he could not leave his window open as the elevel of noise prevent his baby to sleep and he could not even hear the TV in his flat. the noise coming from the site is higher then the sounds from my TV. He would like to know what measure you are planning to put in place to address this issue. He did not think that the current level of noise are acceptable past 7pm and on Sunday.	Portion X	-	Closed	-
COM-2012-010(2)	15-Nov-2012	-	<hzmbenquiry@hyd.gov.hk>	Environmental (Noise & air quality)	The noise can be very annoying, on days depending of the wind direction, you are making more noise than the plane taking off (I measured it myself), to give you an idea of the disturbance you are creating again. *I would also like to bring an other topic beside the noise. Since the beginning of the filling operation, very strong smell of exhaust pipe gas can be smelt in the residential area and I think this is a huge health concern for the local population. On certain days when the wind is blowing towards the residential areas, I have the feeling that there is a diesel engine running in my living room! I would like to know how you are planning to address this?*	Portion X	-	Closed	-

COM-2012-010(3)	15-Nov-2012	-	EPD	Environmental (Noise, water quality & air quality)	The complainant has copied his reply from HyD dated 15 Nov 2012 to EPD and Health Department and he further complained on the following issues: • Noise nuisance generated by diesel engine; • Smell of exhaust pipe gas in his residence; and • Suspected marine water pollution (see enclosed photo). The complainant also requested EPD to install noise and air quality monitoring at Le Bleu Deux estate.	WA6 Portion X	Noise from blowing horn from vessels and barges and Metallic Parts thrown on Ground • Reminded the Contractor to request the captains of the vessels and barges not blowing the horn except in case of emergency or prevention of ship collisions/serious safety matters; • The supervision teams would enhance their tight control on the vessels and barges working at that location, and monitor the situation and take corresponding actions; and • To enhance the work force of RSS to supervise each step of construction activities and the use of hand tools until the completion of the site office erection. Noise from Engines and Cranes of the Barges during Marine Operation • Installation of noise covers onto the generators / motors on all working barges; • Increase frequency of applying lubricant to all moving parts and gear wheels of the working barges to avoid generation of abnormal sound; and • Review of working hours for the reclamation works and switching off all unnecessary machinery and plants at night time and Sundays. Noise from power generators • All generators shall be either screened or covered by adequate sound reducing materials; • All generators situated in front of Le Bleu Deux estate will be switched off at 19:00 hrs, except two generators will be kept running up to 22:00hrs and one generator will be kept running overnight for maintaining minimum power requirement; and • Arrangement with CLP Power HK Ltd (CLP) for the permanent power supply to the site offices has been chased in a matter of urgency. The use of power generators will be terminated in phase starting from 6 December 2012. Exhaust Fume Emission • Tight control on using the machine and generators in the vicinity of Le Bleu Deux estate; and • Closely monitor the frequency on engine cleansing and replacement of dust filter. Change of Sea Water in Yellow • The Contractor was reminded to move their vessels and barges at areas with adequate water depth as practically as possible.	Closed	-
COM-2012-010(4)	19-Nov-2012	22:25 hrs.	EPD	Environmental (Air quality and Noise)	The complainant filed again a complaint for the strong exhaust pipe fumes smell coming for the construction site in Tung Chung tonight as well as the extremely high level of noise as at at 10:30 pm (19/11/12).	WA6			
COM-2012-010(5)	24-Nov-2012

COM-2013-016	18-Jan-2013	-	EPD	Environmental (Water)	The complainant advised that turbid water and concrete/cement has been arising from the Hong Kong-Zhuhai-Macao Bridge Hong Kong Projects to marine water. The complainant did not specify the soure of the turbid water and concrete/cement.	N/A	-	Closed	-
COM-2013-018	02-Mar-2013	-	HyD	Environmental (Noise)	The complainant advised that "It seems that the Contractor's cranes operating on the barges are again in need of bit of lubricant, as this evening i.e. 2 March 2013, the cranes are again polluting the neighborhood with intolerable noise." The complainant requested Mr. Ng from EPD to take note of this complaint and expected a detailed report.	Portion X	The Contractor has been reminded to continue the process of applying lubricant/ grease to all barges which are to be worked in the site area near Le Bleu Deux.	Closed	-
COM-2013-018 (2)	04-Mar-2013	-	EPD	Environmental (Noise)	The complainant complained that the cranes operating on the barges for the HZMB HK project generating squeak noise in the evening of 1 March 2013 causing an annoyance to him/her.	Portion X	The Contractor implemented the following measures : - Briefing given to the operator for the proper operation of marine vessels; - Keep adequate routine maintenance ; - Minimize the quantities of plant after 7pm; & - Review the working hours of night time works and switch off all unnecessary machinery and plants at night time.	Closed	-
COM-2013-018 (3)	13-Mar-2013	-	HyD	Environmental (Noise)	The complainant asked what noise mitigation the Contractor was taking. The complainant pointed out that the noise in question was so strong that it woke up his baby girl.	Portion X	-	Closed	-
COM-2013-018 (4)	22-Mar-2013 24-Mar-2013	14:19 hrs 10:28 hrs	HyD	Environmental (Noise)	The complainant complained that "the lifting appliance was operated gently and softly to keep the noise emission as low as possible" but the noise still woke up his baby. "Lubricant was regularly applied to smoothen all moving parts and gear wheels of the working barges" that did not seem to be the case at all. The complainant pointed that the crane operating at 10:27 hrs on 24 March 2012 needed lubricant.	Portion X	The Contractor will keep on closely monitoring the situation and carry out the necessary noise mitigation measures while barges are working in the site area nearby residential area.	Closed	-
COM-2013-018 (5)	31-Mar-2013 1-Apr-2013	10:25 hrs 10:32 hrs	HyD	Environmental (Noise)	The complainant complained that noise emitted from a crane at 10:19 hrs. The complainant further complained that noise was generated from a barge at 07:30 hrs.	Portion Y	-	Closed	-
COM-2013-018 (6), (7) & (9)	15-Apr-2013	15:41 hrs	EPD	Environmental (Noise)	The complainant complained that machinery noise generated from the construction site near Tung Chung Development Pier operating for the Hong Kong-Zhuhai-Macao Bridge Hong Kong during the normal working hours on 6 April 2013 and 13 April 2013 and the late evening of 10 April 2013 causing nuisance to public.	Portion X	The Contractor has been reminded to comply with CNP conditions for construction works undertaken during restricted hours. To minimize the potential noise impact during restricted hours and non-restricted hours, the Contractor has implemented the following additional measures: - Briefing given to the operator of the barges for proper operation of marine vessels; - Operating barge by experienced operators only; - Keeping adequate routine maintenance for barges e.g. application of lubricants into moving parts in order to minimize squeak noise; - Install noise covers onto noisy equipment where practicable. - Remind subcontractor only well-maintained plant should be operated on-site. - Minimized the quantities of plant used after 7pm as far as practicable; - Speed up of construction works in order to shorten the duration (days) of potential noise impact/nuisance to the surrounding environment; and - Regular review of working hours for night time works and switch off all unnecessary machinery and plants at night time.	Closed	-

COM-2013-018 (11)	28-Apr-2013	15:44	EPD	Environmental (Noise)	The complainant complained that machinery noise generated from the reclamation site near Tung Chung Development Pier at around 22:00 of 28 April 2013 causing nuisance to public.	Portion X	The Contractor has been reminded to comply with CNP conditions for construction works undertaken during restricted hours. To minimize the potential noise impact during restricted hours, the Contractor has implemented the following additional measures: - Briefing given to the operator of the barges for proper operation of marine vessels; - Operating barge by experienced operators only; - Keeping adequate routine maintenance for barges e.g. application of lubricants into moving parts in order to avoid squeak noise; - Install noise covers onto noisy equipment where practicable. - Remind subcontractor only well-maintained plant should be operated on-site. - Speed up of construction works in order to shorten the duration (days) of potential noise impact/nuisance to the surrounding environment; and - Regular review of working hours for night time works and switch off all unnecessary machinery and plants at night time.	Closed	-
COM-2013-022	08-Apr-2013	--	EPD	Environmental (Water)	The complaint alleged that oil was dumped from various vessels operating for HZMB HK projects near Tung Chung Development Pier over the past few months. Photos were provided by the complainant.	Portion X	The Contractor has checked the photos provided by the complainant and confirmed that the vessels and boats shown in the photos do not belong to Contract No. HY/2011/03.As this complaint is not related to this Contract, no follow up action is required. The Contractor has reminded their subcontractors to implement the measures recommended in the Spill Response Plan (SRP) in case of accidental release of oils from vessel.	Closed	-
COM-2013-022(2)	23-May-2013	09:15 hrs	EPD	Environmental (Water)	This complaint was a follow-up of a previous complaint received by EPD on 8 April 2013 regarding oil slicks caused by vessels. It was alleged that oil was still being dumped from various vessels operating for HZMB HK projects near Tung Chung Development Pier over the past few months. On the other hand, the complainant would also like to know whether the owners of the vessels could present engine oil disposal records for the vessels which supported the HZMB project.	Portion X	The Contractor has reminded their subcontractors to implement the measures recommended in the Spill Response Plan in case of accidental release of oils from vessel and handle the chemical waste (waste oil) in accordance with the requirements provided in the EM&A Manual.	Closed	-
COM-2013-023	02-May-2013	--	HyD	Environmental (Noise)	The complainant alleged that there were metal parts dropped on the ground creating noise at 12:58 on 1 May 2013	WA6	If there are metal handling works, the Contractor will not carry out the metal handling works in early morning in order to minimize potential noise disturbance as far as practicable in future.	Closed	-
COM-2013-024	23-May-2013	09:50 hrs	EPD	Environmental (Noise)	A complaint was received on 23 May 2013 regarding noise generated from dropping metal parts on numerous occasion on the pier opposite Le Blau Deux at around 08:45 to 10:00 hrs of 18 May 2013 and loading/unloading activities creating noise disturbance by the contractor of HY/2011/03.	WA6	If there are metal handling works, the Contractor will not carry out the metal handling works in early morning in order to minimize potential noise disturbance as far as practicable in future.	Closed	-
COM-2013-027	29-Jun-2013	10:02 hrs	RSS	Environmental (Noise)	A complaint was received on 29 June 2013 regarding noise generated from the works area near the site office (WA6) around 10:00 hrs on 29 June 2013	WA6	The Contractor was recommended to minimize the potential noise impacts generated from the construction sites as far as practicable in future.	Closed	-
COM-2013-033	13-Sep-2013	Around 22:00 hrs	RSS	Environmental (Noise)	A complaint was received regarding the noise nuisance from barge at about 22:20 hrs on 13 September 2013 and 02:30 hrs on 14 September 2013.	Portion X	The Contractor has been reminded to comply with CNP conditions for construction works undertaken during restricted hours. To minimize the potential noise impact during restricted hours, the Contractor has implemented the following additional measures: - Minimized the quantities of plant used after 7pm as far as practicable; and - Regular review of working hours for night time works and switch off all unnecessary machinery and plants at night time.	Closed	-
COM-2013-034	17-Sep-2013	--	HyD	Environmental (Noise)	A complaint was received on 17 September 2013 regarding the noise nuisance from tree transplanting activities in the morning of 14 September 2013.	Portion Y	The Contractor has been reminded to comply with CNP conditions for construction works undertaken during restricted hours. To minimize the potential noise impact during restricted hours, the Contractor has implemented the following additional measures: - Minimized the quantities of plant used after 7pm as far as practicable; and - Regular review of working hours for night time works and switch off all unnecessary machinery and plants at night time.	Closed	-
COM-2013-037	8-Oct-2013 9-Oct-2013 16-Oct-2013	--	Supervising Officer's Representative	Environmental (Noise)	The complainant complained the noise from barge operation from 21:30 to 22:30 hrs on 4 October 2013. The complainant complained that several loud bangs were heard starting from 21:00 hrs on 7 October 2013. The complainant complained that it was very noisy at the noon of 14 October 2013.	Portion X	The Contractor has been reminded to comply with CNP conditions for construction works undertaken during restricted hours. To minimize the potential noise impact during restricted hours, the Contractor has implemented the following additional measures: -minimize the quantities of plant used during restricted hours as far as practicable; and -regular review of working duration for restricted hours works and switch off all unnecessary machinery and plants during restricted hours.	Closed	-

COM-2013-041	31-Oct-2013	21:52 hrs	EPD	Environmental (Noise)	A complaint was received on 31 October 2013 regarding the noise generated from a barge being moved by a tug boat in the morning of 31 October 2013 (around 05:55).	N/A	The Contractor has been reminded to comply with CNP conditions for construction works undertaken during restricted hours. To minimize the potential noise impact during restricted hours, the Contractor has implemented the following additional measures: - minimize the quantities of plant used during restricted hours as far as practicable; and - regular review of working duration for restricted hours works and switch off all unnecessary machinery and plants during the night-time and early morning period (7pm to 7am).	Closed	-	
COM-2013-043	11-Nov-2013	--	EPD	Environmental (Noise)	A complaint was received on 11 November 2013 regarding a barge moving through the southern channel of HyD's construction site after 23:00 hrs on 8 November 2013.	Portion X	The Contractor has been reminded to comply with CNP conditions for construction works undertaken during restricted hours. To minimize the potential noise impact during restricted hours, the Contractor has implemented the following additional measures: - minimize the quantities of plant used during restricted hours as far as practicable; and - regular review of working duration for restricted hours works and switch off all unnecessary machinery and plants during restricted hours.	Closed	-	
COM-2013-045	27-Dec-2013	--	HyD	Environmental (Noise)	A complaint was received on 27 December 2013 regarding barges operating at the south channel of Portion X in the afternoon of 26 December 2013.	Portion X	The Contractor has been reminded to comply with CNP conditions for construction works undertaken during restricted hours. To minimize the potential noise impact during restricted hours, the Contractor has implemented the following additional measures: - minimize the quantities of plant used during restricted hours as far as practicable; and - regular review of working duration for restricted hours works and switch off all unnecessary machinery and plants during restricted hours.	Closed	-	
COM-2014-046	16-Jan-2014	17:22 hrs	HyD	Environmental (Air Quality)	A complaint was received on 16 January 2014 regarding heavy exhausts generated at around 8 a.m. and 10 a.m. over past few months and or even midnight.	N/A	The Contractor has implemented the following measure to minimize exhaust fumes generated from machinery: - Maintenance for the all machinery regularly.	Closed	-	
COM-2014-048	18-Jan-2014	--	EPD	Environmental (Other: Blackish mud)	A complaint was received on 18 January 2014 regarding blackish mud along the edge of the construction site of Hong Kong-Zhuhai-Macao Bridge Hong Kong Project near the airport in the morning of 18 January 2014.	Portion X	Based on the investigation results, it is considered that the blackish mud raised in the complaint was not related to HKLR03 Contract. In this case, no follow up action is required.	Closed	-	
COM-2014-050	24-Mar-2014	--	EPD	Environmental (Other: Dredged Marine Sediment)	A complaint was received by EPD on 24 March 2014. The complainant advised that there was dredged material found being mixed with soil in the construction site of Hong Kong-Zhuhai-Macao Bridge Hong Kong Link Road Project in the vicinity of CAD headquarters and transported out of the site. The complainant suspected that there was improper disposal of dredged marine sediment.	Portion X	Based on the investigation results, it is considered that the complaint is invalid. In this case, no follow up action is required.	Closed	-	
COM-2014-051	29-Apr-2014	--	SOR	Environmental (Noise)	A complaint was received on 29 April 2014 regarding loud bang coming from the site at 21:37 hrs on 28 April 2014.	Portion X	Based on the Contractor's site dairy and our investigation, no non-compliance was identified.	Closed	-	
COM-2014-053	02-May-2014	--	EPD	Environmental (Noise)	A complaint was received by EPD on 1 May 2014. The complainant advised that there was noise nuisance arising during the evening of 1 May 2014.	Portion X	The Contractor has been reminded to comply with CNP conditions for construction works undertaken during restricted hours. To minimize the potential noise impact during restricted hours, the Contractor has implemented the following additional measures: - minimize the quantities of plant used during restricted hours as far as practicable; and - regular review of working duration for restricted hours works and switch off all unnecessary machinery and plant during restricted hours.	Closed	-	
COM-2014-063	03-Dec-14	--	Arup	Environmental (Noise)	According to Arup's email to CSCE and DCVJV on 3 December 2014, "A resident living in Le Bleu Duex addressed a complaint to CE of HyD at about 20:04 hrs last night. He complained about the noise nuisance coming from site office since 19:30 hrs last night. epetitively metal parts had been dropped on the ground by people who seem to be loading or unloading a boat at the pier. Noise was still going on right now at 20:04."	WA6	Based on the investigation results, it is found that the noise complaint is not related to Contract No. HY/2011/03. In this case, no follow up action is required.	Closed	-	

COM-2014-065	24-Dec-14	Nil	EPD	Environmental (Water Qulity)	A complaint was received on 24 December 2014 regarding the increase of marine refuse (water bottles and debris) along the shore from Yat Tung to Tai O, where the complainant considered might be in relation to the HZMB project(s).	Portion X	Based on the investigation results, it is considered that the complaint is unlikely related to HKLR03 Contract. Nevertheless, the Contractor is reminded to implement all recommended mitigation measures for waste management and avoid dumping rubbish into the sea.	Closed	-	
COM-2015-066	08-Apr-15	Nil	EPD (An email forwarded by Arup)	Environmental (Dust)	According to Arup's email to CSCE on 8 April 2015, the ET was informed that a complaint had been received by EPD at about 18:29 hrs on 2 Apr 2015 regarding construction dust from construction site (S15) at Kwo Lo Wan Road, Tung Chung."	S15	Based on the Contractor's information and our investigation, no non-compliance was identified. The Contractor is reminded to continuously implement the dust suppression measures to minimize potential dust impact.	Closed	-	
COM-2015-068	10-Apr-15	Nil	EPD (An email forwarded by Arup)	Environmental (Noise)	According to Arup's email to CSCE on 10 April 2015, it is noted that EPD received a noise complaint from a resident of Caribbean Coast. According to the complainant, he was disturbed by noise from construction activities of the HZMB Project during weekends and holidays. The complainant was referring to those activities carried out between Scenic Hill and HKBCF because the complainant mentioned the contractor was China State.	N/A	Based on the information provided and our investigation, the Contractor had complied with the conditions laid down in Construction Noise Permit (CNP) Nos. GW-RS0113-15 and GW-RS0356-15. Hence, no non-compliance was identified. The Contractor has been reminded to comply with CNP conditions for construction works undertaken during restricted hours and recommended to implement the following measures to minimize the potential noise impact during restricted hours: minimize the quantities of plant used during restricted hours as far as practicable; and regular review of working duration for restricted hours works and switch off all unnecessary machinery and plant during restricted hours.	Closed	-	
COM-2015-074	16-Jul-15	Nil	EPD	Environmental (Wastewater)	According to EPD's email to Highways Department, ET, SOR and ENPO, a complaint was received on 16 July 2015 regarding wastewater splashing from vehicles to pedestrian at Tung Fai Road. The complainant complained that wastewater was splashed to people waiting at the bus stop near Civil Aviation Department Headquarters Office Building when vehicles leaving the HZMB site to Tung Fai Road.	Tung Fai Road	Based on the investigation results, it is considered that the complaint is unlikely related to HKLR03 Contract. The Contractor has been reminded to slow down their vehicles when leaving the concerned construction site.	Closed	-	
COM-2015-076	17-Jul-15	Nil	EPD (An email forwarded by ENPO)	Environmental (Noise)	According to EPD's email to ENPO on 17 July 2015, it is noted that EPD received a noise complaint from public. The complainant said that he/she was disturbed by the noise generated from construction sites of the HZMB Project during the daytime period of past few Sundays. Afterwards, EPD contacted the complainant and confirmed that the noise was generated from construction sites along Kwo Lo Wan Road and signs of "China State Construction Engineering (HK) Ltd" were noted.	Kwo Lo Wan Road	Based on the information provided and our investigation, the Contractor complied with the conditions laid down in Construction Noise Permit (CNP) Nos. GW-RS0733-15 and GW-RS0740-15 and no noncompliance was found. The Contractor has been reminded to comply with CNP conditions for construction works undertaken during restricted hours and recommended to implement the following measures to minimize the potential noise impact during restricted hours: - minimize the quantities of plant used during restricted hours as far as practicable; and - regular review of working duration for restricted hours works and switch off all unnecessary machinery and plant during restricted hours.	Closed	-	
COM-2015-079	07-Dec-15	Nil	ENPO (EPD referred the email from Complainant to ENPO)	Environmental (Water Quality)	According to ENPO's email to SOR and ET on 7 December 2015, a complaint was received by EPD on 2 December 2015 regarding water quality near HKLR work site. The complainant mentioned that "I moved to Tung Chung since July and it was the second time I saw similar situation polluting the sea. Last time it was even worse in red colour. Please look into this matter and let me know what was being dropped into the sea and whether it was hazardous to the sea.". EPD has contacted the complainant and obtained the additional information from the complainant. EPD suspected that the incident happened in the afternoon on 28 November 2015.	Portion X	According to the information provided by the Contractor, the derrick barge belongs to Contract No. HY/2011/03. The concerned sediment plume was likely to be caused by stirring up of mud in the seabed by the derrick barge sailed at the navigation channel situated at shallow water zone where the water depth ranging from 3.25m – 3.75m. Public fill materials were placed on the derrick barge. The barge was in good conditions with no materials being dumped into the sea. The Contractor has been implementing the mitigation measure as specified in the Implementation Schedule of Environmental Mitigation Measures that is all vessels to be sized such that adequate clearance is maintained between vessels and the sea bed at all states of the tide to ensure that undue turbidity is not generated by turbulence from vessel movement or propeller wash. The Contractor is recommended to arrange vessels to move out of the site area during high tide to avoid the disturbance to the seabed as far as practicable and deploy marine vessels effectively in order to minimize the number of trips and disturbance to seabed in shallow waters.	Closed	-	
COM-2016-087	28-Jun-16	Nil	EPD	Environmental (Water Quality)	According to EPD's email, a complaint was received on 28 June 2016 regarding polluted water discharge incident opposite to Tung Chung Development Pier.	N/A	The Contractor has designated competent persons to operate, check and maintain individual wastewater treatment plant as an existing control measures. In case of breakdown of wastewater treatment plants, no discharge of wastewater will be allowed until repair is completed to resume the normal operation of the treatment plant. Specific toolbox / refreshment training trainings have been providing for the staff and workers for each of the wastewater treatment plants. The Contractor has been reminded to implement the above control measures and ensure no untreated wastewater will be discharged into open channel.	Closed	-	
COM-2016-098	11-Nov-16	16:33	ENPO (EPD referred the email from Complainant to ENPO)	Environmental (Water Quality)	According to ENPO's email to the Environmental Team, Supervising Officer's Representative and Contractor on 11 November 2016, it is noted that EPD received a complaint lodged by a member of the public regarding sediment plume generated by a vessel named "長盛308 (Chang Sheng 308)" during the vessel travelling from construction site of Hong Kong- Zhuhai- Macao Bridge near Scenic Hill to Tung Chung New Development Ferry Pier.	Portion X	The Contractor has been reminded to schedule the vessel to move in / out of the construction site during higher tide and minimize number of trips to avoid the stirring up of the seabed mud when the vessel travelling in very shallow water areas as much as practicable. Also, the Contractor was reminded to implement environmental mitigation measures in accordance with Environmental Mitigation Implementation Schedule (EMIS).	Closed	-	
COM-2016-099	02-Dec-16	Nil	ENPO (EPD referred the email from Complainant to ENPO)	Environmental (Other: Slurry on public road)	It was noted from ENPO's email to the Environmental Team, Supervising Officer's Representative and Contractor on 2 December 2016 that EPD received a complaint lodged by a member of the public regarding slurry on East Coast Road. The complainant considered the slurry might relate to the construction site of China Harbour Engineering Company Limited next to a hotel.	East Coast Road	During the weekly site inspection undertaken on 7 December 2016, no slurry was observed at the section of East Coast Road adjoining the site boundary of Contract No. HY/2011/03. The Contractor has constructed wheel washing facilities at all the site accesses, including the one near the site access of China Harbour Engineering Company Limited next to the Marriott Hotel (which is believed to be the hotel mentioned by the complainant), to wash and clean all vehicles before allowing them to leave the construction site to ensure that no mud or other debris would be brought to the public area. In addition, regular watering is conducted by water truck at least twice per day at the section of East Coast Road adjoining the site boundary of Contract No. HY/2011/03 to minimize dust emission. Based on the investigation results, it is considered that the complaint unlikely related to Contract No. HY/2011/03. Notwithstanding that, the Contractor has been reminded to clean wheels and body of vehicles as usual before allowing them to leave construction site.	Closed	-	
COM-2016-100	14-Dec-16	Nil	ENPO (Contract No. HY/2010/02 project team received an environmental complaint referred by Government's hotline (1823) on 2 December 2016. ENPO forwarded the Complaint to Contract No. HY/2011/03.)	Environmental (Other: mud/ derbris on public road)	It was noted from ENPO's email to the Environmental Team, Supervising Officer's Representative and Contractor on 14 December 2016 that EPD received a complaint lodged by a member of the public regarding mud/debris on public road. The complainant complained that "the whole stretch of East Coast Road & Tung Fai Road is truly disgusting. The stone debris big and small and the mud is a nuisance to those who use the road every day. When dry there is a lot of dust and when it rains or when the road washing trucks are out it becomes a muddy mess. Cars and pedestrians are covered in dust or mud, cars are hit by stones is a daily hazard. Washing of construction vehicles is inadequate as the sand and soil is carried out onto the roads. Oversight of road conditions are not carried out by the Airport Authority. An alternative route should be created for the large number of construction vehicles as they drive fast.".	East Coast Road and Tung Fai Road	During the ET's inspection on 7 December 2016 (weekly routine inspection) and 16 December 2016, no mud or debris was observed at the section of East Coast Road adjoining the site boundary of Contract No. HY/2011/03 as well as the section of Tung Fai Road leading to the site access of Contract No. HY/2011/03. The Contractor provided wheel washing facilities at all the site accesses, including the one accessing East Coast Road and the one accessing Tung Fai Road, to wash and clean all vehicles before allowing them to leave the construction site to ensure that no mud or debris would be brought to the public area. It was observed that the areas of the wheel washing facilities and the respective road section between the wheel washing facilities and the site accesses of East Coastal Road and of Tung Fai Road were paved with concrete. High pressure jets were also provided at the wheel washing facilities for cleaning of vehicles before the vehicles were allowed to leave the construction site. In addition, regular watering at the section of East Coast Road adjoining the site boundary of Contract No. HY/2011/03 was conducted by water trucks at least twice per day to minimize dust emission. Based on our investigation result, it is considered that the complaint is unlikely related to Contract No. HY/2011/03. Notwithstanding that, the Contractor has been reminded to clean the wheels and body of vehicles as usual before allowing them to leave construction site.	Closed	-	
COM-2016-103	14-Dec-16	Nil	ENPO (EPD referred the email from Complainant to ENPO)	Environmental (Noise)	It was noted from ENPO's email to the Environmental Team, Supervising Officer's Representative and Contractor on 14 December 2016 that EPD received a noise complaint lodged by a member of public. The complaint was about hammering noise generated from construction sites at midnight in the past month. The complainant could not identify the source but suspected that the noise was generated from HZMB Project. It was also noted from ENPO's email on 21 December 2016 that EPD supplemented that the complainant lives in Seaview Crescent. The complainant sometimes heard noise created by impacting metals or metal/ground, particularly in December 2016.	N/A	The Contractor confirmed that no hammering works was conducted and no impact noise was generated at midnight in November 2016 and December 2016. The Contractor complied with the conditions laid down CNP No. GW-RS740-16 and no non-compliance was found. Based on our investigation result, it is considered that the complaint is unlikely related to Contract No. HY/2011/03. In this case, no follow up action is required. However, the Contractor has been reminded to comply with the conditions stipulated in the Construction Noise Permit for construction works undertaken during restricted hours and has been recommended to implement the following measures to minimize the potential noise impact during restricted hours: - minimize the number of machinery and plant used during restricted hours as far as practicable; - regularly review the working duration for restricted hours works; and - switch off all unnecessary machinery and plant during restricted hours.	Closed	-	

COM-2017-104	09-Jan-17	Nil	IEC (EPD referred the email from Complainant to IEC)	Environmental (Other: Cleanliness problem at East Coast Road and Tung Fai Road)	It was noted from IEC's email to the Environmental Team, Supervising Officer's Representative and Contractor on 9 January 2017 that EPD received a complaint lodged by a member of the public (a bus operator at the HKIA) regarding cleanliness problem at East Coast Road and Tung Fai Road.	East Coast Road and Tung Fai Road	During the ET's inspection on 10 January 2017, it was observed that the Contractor provided wheel washing facilities at all the site accesses, including the one accessing East Coast Road and the one accessing Tung Fai Road, to wash and clean all vehicles before allowing them to leave the construction site to ensure that no mud or debris would be brought to the public area. No mud was observed at the section of Tung Fai Road leading to the site access of Contract No. HY/2011/03. However, some mud was observed at the section of East Coast Road adjoining the site boundary of Contract No. HY/2011/03. Based on our investigation result, although there is no direct evidence showing that the complaint is related to Contract No. HY/2011/03, the Contractor has been reminded to clean the wheels and body of vehicles as usual before allowing them to leave construction site. Road sweeper will be employed to sweep along the East Coast Road twice per week and remove the deposited mud underneath the water-filled barrier to facilitate the road-washing water to be drained away from the carriageway. It should be of note that the ground level of site boundary of HY/2011/03 adjoining the East Coast Road is lower than that of East Coast Road and the Site of HY/2011/03 receives unidirectional flow of surface runoff from the East Coast Road. In addition, the following measures will be implemented to enhance dust suppression: 1. Stockpile along East Coast Road will be reduced in height and compacted as far as practicable 2. Haul road will be demarcated to prevent vehicles from going into non-wetted surface. 3. Site access S16 will be thoroughly cleaned and all vehicles will be stopped for second washing after being washed in the wheel washing bay. 4. Water sprinklers will be installed and operated at the stockpiles behind the water-filled barriers along East Coast Road.	Closed	-
COM-2017-108	23 February 2017 and 2 March 2017	Nil	Airport Authority Hong Kong (AAHK) via SOR / Referred to ENPO by HyD	Environmental (Air quality, Water quality and Other: Cleanliness problem at East Coast Road)	AAHK stated in their email to SOR on 23 February 2017 that there was sand/muddy water accumulating along the water barriers at East Coast Road Southbound. AAHK also lodged a complaint to HyD, which HyD referred to ENPO on 1 March 2017 (received by ET on 2 March 2017). AAHK reported that the cleanliness of East Coast Road remained unsatisfactory with dust all over the water barriers/traffic aids, and sands accumulating along the carriageway.	East Coast Road	During ET's observation on 3 and 13 March 2017, properly functioning wheel washing facilities were provided to wash all vehicles prior to leaving the site. The section of road between the wheel washing facilities and the site access (S25) was hard paved and no mud/ silt was observed at the concerned road section and the site access. As the ground level of site boundary of HY/2011/03 adjoining the East Coast Road is lower than that of East Coast Road, the possibility of muddy water seepage from S25 to East Coast Road is low.Based on our investigation result, the complaint is unlikely to be related to Contract No. HY/2011/03. Nevertheless, the Contractor has been reminded to strictly upkeep the proper practice of washing all vehicles leaving the site access (S25). Also, the Contractor has raised the majority of the temporary traffic signs to a higher level to avoid muddy water splashing on them. Also, the temporary traffic signs will be cleaned regularly.	Closed	-
COM-2017-112	27 March 2017	Nil	ENPO (EPD referred the email from Complainant to ENPO)	Environmental (Noise and Water quality)	It was noted from ENPO's email to the Environmental Team, Supervising Officer's Representative and Contractor on 28 March 2017 that EPD received a noise complaint lodged by a resident of Century Link on 27 March 2017. The complaint was about "昨晚 (i.e. 26 March 2017) 大約十時起，屋外間歇有非常響亮聲音，經觀察應該是從港珠澳大橋近人工島的工程發出，噪音一直至深夜，另今早發現住處對出海面受到一大遍污染（見相片），以上都應該是大橋工程所造成的污染"i.e. "At around ten o'clock last night (i.e. 26 March 2017), there was intermittent very loud voice outside. According to observation, the noise should be from the Hong Kong-Zhuhai-Macao Bridge project near the artificial island, the noise lasted until late at night. In this morning, there was a plume of pollution found on the sea (see photo). These should be caused by the bridge project.".	Nil	Based on the information provided by the Contractor and our investigation, it was concluded that the Contractor had complied with the conditions laid down in CNPs No. GW-RS-1135-16 and GW-RS0016-17 and that no non-compliance on water quality was found. It is considered that the complaint is unlikely related to Contract No. HY/2011/03. In this case, no follow up action is required. However, the Contractor has been reminded to comply with the conditions stipulated in the Construction Noise Permit for construction works undertaken during restricted hours and has been recommended to implement the following measures to minimize the potential noise impact during restricted hours: - minimize the number of machinery and plant used during restricted hours as far as practicable; - regularly review the working duration for restricted hours works; and - switch off all unnecessary machinery and plant during restricted hours. The Contractor was also reminded to schedule, according to the predicted tides of the Hong Kong Observatory, their working vessels to travel to and from work site at high tide in order to reduce the sediment plume at shallow water areas.	Closed	-
COM-2017-113	20-Apr-17	Nil	ENPO (EPD referred the email from Complainant to ENPO)	Environmental (Water quality)	It was noted from ENPO's email to the Environmental Team, Supervising Officer's Representative and Contractor on 20 April 2017 that EPD received a complaint on 19 April 2017 lodged by a green group. The complaint was about "本會XXX投訴港珠澳大橋承辦商於２０１５年設置隔泥網的方向不當，產生污染，而圖片是由路政署提供，是真確圖片，本會期望環保署調查圖片中的情況，並對承辦商作出警告，以及要求承辦商準確放置現時的隔泥網，確保其雙重設計是有效，"	Portion X	Based on the information provided by the Contractor and ET's investigation, It was suspected that the concerned silt plume may be caused by sea current. There was no evidence that the concerned silt plume was caused by any activities arising from the Contract. The Contractor was reminded once again to implement the mitigation measure as specified in the Implementation Schedule of Environmental Mitigation Measures. The Contractor is also recommended to fully and properly maintain the silt curtain throughout the works in accordance with the requirements in the Updated EM&A Manual through undertaking monthly measurement on the overlapping and separation openings for vessels access for prompt rectification.	Closed	-
COM-2016-095(3)	27-May-17	Nil	SOR (HyD referred the email from Complainant to SOR)	Environmental (Noise)	It was noted from SOR's email to the Environmental Team and Contractor on 26 May 2017 that HyD received a complaint on 12 May 2017 lodged by a member of public. The complaint was about "We'd like to follow up on this case. Pls help take pictures & point out to us where your noise barriers are located. If those seen in the attached pics are so-called noise barriers, then we believe the contractor needs a lot of improvement in helping to reduce this noise pollution".	Near Dragonair / CNAC (Group) Building (HKIA)	Upon the receipt of the complaint in May 2017, the Contractor had been instructed to immediately install additional noise barriers at the appropriate location and cover the breaker tip with acoustic materials as noise mitigation measure against the noise emission associated with the aforesaid construction activities. Moreover, the noise barriers have been located as close as possible to the noise source (rock breaking work). Also, gaps and openings at joints in the barrier material have been minimized. The rock breaking work was completed on 31 May 2017 and the rock breaking machine had been demobilized off site. According to information from Contractor, removal C&D materials will be carried out at the site near CAD and CNAC buildings in the future. As such, noise nuisance generated from a site will be minimized. Notwithstanding that, the Contractor has been reminded to implement noise mitigation measures on the site to minimize any potential nuisance to the public. Based on our investigation result, it is considered that the complaint is likely related to Contract No. HY/2011/03. The Contractor has implemented the following measures to minimize the potential noise impact: - Additional noise barriers have been erected in the active working area to further mitigate the associated noise emissions as far as practicable; - Cover the breaker tip with acoustic material. - Noise barriers have been located as close as possible to the noise source. Also, gaps and openings at joints in the barriers material have been minimized. - Speed up of construction works in order to shorten the duration noise impact/nuisance to the surrounding. - Minimize the quantities of noisy plant as far as practicable. - Regular review of working duration and switch off all unnecessary machinery and plant.	Closed	-
COM-2016-095(4)	15-Aug-17	Nil	HyD	Environmental (Noise)	HyD received a complaint concerning the rock breaking works near CNAC Buildings, as described below: "I am writing to let you know re-captioned works interrupted seriously our staff daily office works. Understand the rock encountered was much stronger than the original expected, the rock breaking works near CNAC Tower has been never ending. Recently a bulldozer is working nearby and no noise barriers/sound proofs were set up. Please take corrective action asap. Kindly advise us when this bulldozing work is scheduled to complete."	Near Dragonair / CNAC (Group) Building (HKIA)	The major rock breaking works near CNAC Tower were substantially completed on 31 May 2017. However, survey record revealed that minor rock breaking/trimming work was required at the formation level for the construction of box culvert no. PR14. Hence, the Contractor used a hydraulic breaker for minor rock breaking/trimming work in the afternoon on 15 August 2017. According to the photos provided by the complainant, movable noise barriers were not located near the noise source (rock breaking/trimming work). As such, noise generated by rock breaking/ trimming work was not efficiently screened by the noise barriers. According to the Contractor's records and the photos provided by the complainant, no bulldozer was used at PR14 on 15 August 2017. In addition, no bulldozing work is scheduled at PR14 in near future. ET conducted an investigation on 16 August 2017. The minor rock breaking/ rock trimming work was completed. Only one excavator was operating for forming the haul road at the concerned location. No significant noisy activity was observed during the investigation on 16 August 2017. Also, bulldozer was not observed on the site. Based on our investigation result, it was likely that concerned noise emission was due to the minor rock breaking/ trimming works by the hydraulic breaker. It is considered that the complaint is likely related to Contract No. HY/2011/03. According to Contractor's information, no substantial rock breaking works will be conducted at near CNAC Tower. Only minor rock breaking/ trimming work may be occasionally conducted at the concerned work area. The Contractor has been recommended to implement the following measures to minimize the potential noise impact when minor rock breaking/ trimming work to be conducted: - Schedule noisy work (i.e. rock breaking) during non-office hours as far as practicable subject to actual site progress; - Cover the breaker tip with acoustic material; - Locate noise barriers as close as possible to the noise source. Also, gaps and openings at joints in the barriers material should be minimized; - Regular review of working duration and switch off all unnecessary machinery and plant; - Speed up of construction works in order to shorten the duration noise impact/nuisance to the surrounding; and	Closed	-

COM-2017-122	03-Oct-17	Nil	1823 Integrated Call Centre received a complaint lodged by a member of the public on 30 September 2017. SOR referred the complaint details from 1823 - HyD to ET on 3 Oct 2017	Environmental (Other: Cleanliness problem at Tung Fai Road)	1823 Integrated Call Centre received a complaint lodged by a member of the public regarding cleanliness problem at Tung Fai Road, as described below: "投訴大嶼山赤鱲角東輝路 11號港龍大廈對出，巴士站附近，是港珠澳大橋地盤其中一個出入口，經常有大量重型工程車輛進出地盤，每逢有巴士或重型車輛經過時，路面沙塵揚起引起"沙塵暴"，等候巴士的乘客便遭殃，以前有灑水車噴水減低沙塵，現在灑水車都沒有出現， 要求部門改善沙塵問題。"	S16	During the ET's inspection on 3 October 2017, it was observed that the Contractor did provide wheel washing facility with high pressure jets at the site access S16 at Tung Fai Road to wash and clean all vehicles before allowing them to leave the construction site to ensure that no mud or debris would be brought to the public area. It was also observed that the Contractor did provide water bowser to thoroughly clean Tung Fai Road. No mud was observed at the section of Tung Fai Road leading to the site access S16 of Contract No. HY/2011/03. Another inspection was conducted on 12 October 2017, the section of the road between the wheel washing facility and the site access S16 was hard paved and no mud/silt was observed at the concerned road section and the site access S16. Although Contract No. HY/2011/03 is the only construction site connecting to the Tung Fai Road and the mentioned bus stop, wheel washing facility with high pressure jets is provided at the site access S16 to wash and clean all vehicles before allowing them to leave the construction site. No mud or debris would be brought to the public area. Therefore, there is no direct evidence showing that the complaint is related to Contract No. HY/2011/03. Nevertheless, in order to enhance dust suppression measures, the Contractor will increase the frequency of road cleaning by water bowser from three times per day to four times per day, subject to regular review with relevant stakeholders in the vicinity.	Closed	-
COM-2017-129	08-Jan-18	Nil	ENPO's email to the Supervising Officer's Representative and Contractor on 8 January 2018 that HyD received a complaint lodged by a member of the public regarding cleanliness problem at East Coast Road on 29 December 2017	Environmental (Other: Cleanliness problem at East Coast Road)	HyD received a complaint lodged by a member of the public regarding cleanliness problem at East Coast Road on 29 December 2017. The complaint details are described below: "投訴人投訴於大嶼山東岸路，因港珠澳大橋工程的沙塵問題，部門安排了有關洗街車及吸塵車處理有關沙塵問題，但有關車輛就上述問題的處理成效未如理想，投訴人表示洗街車在清洗有關路面時，只是向路面灑水，令原本的沙塵變成泥漿，但卻沒有清理有關泥漿，道路問題根本沒有根治，另外，有關吸塵車的隔濾亦未如理想，吸塵車吸了地上的沙塵後所噴出來的氣體佈滿沙塵，以致有關沙塵除了未被吸走外，更導致道路沙塵滾滾，要求部門監察有關承辦商，煩請部門跟進及回覆。"	East Coast Road	Based on our investigation result, there is no direct evidence showing that that the complaint is related to Contract No. HY/2011/03. The Contractor has been reminded to implement the following measures to minimize dust impact/ improve cleanliness at East Coast Road: • display notice at site access to remind drivers to wash the wheels thoroughly before leaving the site. • manual control by rope stopping vehicles entering public road without wheel washing. • provide training for drivers to ensure that they can use water truck and road sweeper properly for road washing. • close monitor on the proper functioning of the road sweeper and water truck and provide maintenance to water truck and road sweeper if necessary. • implement environmental mitigation measures in accordance with Environmental Mitigation Implementation Schedule as per the EM&A Manual. ET will also step up the site inspections to ensure the cleanliness of the concerned section of East Coast Road is properly maintained.	Closed	-
COM-2018-132	13, 14 February 2018	Nil	HyD (SOR referred the email from HyD to Contractor and ET) and EPD (ENPO referred the email from EPD to SOR, SOR sent the email to Contractor and ET)	Dust, Water Quality, Construction Waste, Noise and vibration	The complaint was received from the SOR's email on 13 February 2018 with the following details: *"We have witnessed increased construction activities causing concerns such as nuisance, air and water pollution, construction waste landfill which may cause health and safety to the surroundings.* *Nuisance – construction noise and vibration* *Air and Water Pollution – poor dust control causing air pollution* *Construction Waste Landfill Hill – increased height, size and degree of the slope of the construction waste landfill* *Moreover, we are particularly concerned with the stability of the construction waste landfill hill, and has grown taller and larger in size with steep slopes which may cause potential danger and hazardous to the surrounding area.* *It is appreciated that if you can investigate on the issue, and rectify the situation to a safe and healthy condition. Please confirm when and how the rectification will be completed."* Another complaint to EPD was received from the SOR's email on 14 February 2018. The complaint was the same as the abovementioned with two figures showing the location of Dragonair & CNAC (Group) Building and Cathay Dragon House.	Near Dragonair / CNAC (Group) Building (HKIA)	Based on our investigation result, the complaint was related to Contract No. HY/2011/03. The Contractor has implemented Environmental Mitigation Implementation Schedule as per the EM&A Manual. Also, the Contractor was reminded to remove the concerned stockpile of the fill materials as soon as possible to minimize the potential nuisance caused to the nearby sensitive receivers.	Closed	-
Follow-ups of Complaint No COM-2018-132	16 March 2018 and 21 March 2018	Nil	HyD (SOR referred the email from HyD to the Contractor and ET) and EPD (ENPO referred the email from EPD to SOR, who sent the email to the Contractor and ET)	Dust and Construction Waste,	The complaint of 16 March 2018 was addressed to HyD and its details were as follows: "1) It was observed from daily photos that: a. Inadequate dust suppression measures implemented. b. Green tarp does not cover the entire pile of the waste land fill. c. Dry soil constantly being observed, and constantly picked-up by strong gusty winds within CLK area. d. Large boulders and steep slopes on waste landfill, with inadequate safety measures implemented. 2) It was noted that the open stockpile of construction waste landfill will be removed by the end of March 2018. Please confirm the date of completion of the removal of the stockpile. 3) Please advise if the slope and setting of the piles of earth complies within Building and other relevant Regulations. 4) The works on the site should be within a valid gazetted period, please confirm if the works are within a valid gazette period, within CLK Lot No1 Land lease or otherwise." The complaint of 21 March 2018 was addressed to EPD and its details were as follows: "Re: Large construction landfill waste outside Cathay Dragon House, CLK, We refer to your letter ref: [EP3/N09/RS00004678-18] dated 09 March 2018, would like to further draw your attention to the open stockpile of construction waste landfill, and the enclosed daily photo. We have continued to observe the following: - Inadequate dust suppression measures implemented. o Green tarp does not cover the whole of the waste landfill. o Dry soil constantly observed, and constantly picked-up strong gusty winds within CLK area. - Large boulders and and steep slopes on waste landfill, with inadequate safety measures implemented. - Poor housekeeping of the construction site. Furthermore, we would like to raise the query regarding the validity period for the occupation of the site under the current gazette. It is appreciated that if you can continue to investigate on the issue, provide close monitoring of the situation, and	Near Dragonair / CNAC (Group) Building (HKIA)	Based on our investigation result, the complaint was related to Contract No. HY/2011/03. It was noted that no Action and Limit Level exceedances of 1-hr and 24-hr TSP were recorded at air monitoring station AMS6 - Dragonair Building during the period from 1 February 2018 to 30 April 2018. Part of the stockpile was observed dry during ET's site inspection on 27 March 2018. Proper watering on the stockpiles was observed undertaken afterwards. The Contractor has been continuously reminded to properly implement Environmental Mitigation Measures as per the EM&A Manual. The Contractor was also reminded to remove the concerned stockpile of the fill materials as soon as possible to minimize the potential nuisance caused to the nearby sensitive receivers.	Closed	-
COM-2018-142	29 June 2018 & 6 July 2018	Nil	EPD (ENPO referred the email to SOR, Contractor and ET)	Noise	The complaint of 29 June 2018 was received from EPD and its details were as follows:- EPD have recently received a complaint regarding frequent noise from construction works next to Cathay Dragon House, facing Tung Chung direction. The complaint details are described as below: "We would like to raise your attention and forward a complaint regarding frequent noise from construction works next to our Cathay Dragon House, facing Tung Chung direction. From the video link below, it seems like the noise is mainly from the breaking of rocks using powered mechanical equipment. https://www.dropbox.com/s/634sf2p3op39s9v/IMG_3137.MOV?dl=0 Our colleagues at Cathay Dragon House has complaint that such disturbance has been going on for a week and works are carried out throughout the whole day. Please advise whether: 1. Such noisy works have been carried out with EPD or Highways' "Approved Permit"; 2. The noise level have been limited by your permit; 3. Any regular monitoring works or report have been sent to your department. 4. When will the work/noise stops; Furthermore, 5. Mr Lai mentioned in your previous email 18 April 2018 that the works should have completed end April 2018. Why is the works still going on? 6. Mr Lo mentioned in the letter dated 11 April 2018, you would conduct site inspections. Have you noticed any non-compliance?	Near Dragonair / CNAC (Group) Building (HKIA)	Based on our investigation result, the complaint was related to Contract No. HY/2011/03. The Contractor has implemented Environmental Mitigation Implementation Schedule as per the EM&A Manual, such as cover the breaker tip with muffler, minimize the quantities of noisy plant as far as practicable. Although the rock breaking works outside the Cathay Dragon House/ Dragonair & CNAC (Group) Building were completed on 9 July 2018, the Contractor has been continuously reminded to properly implement Environmental Mitigation Measures as per the EM&A Manual to minimize the potential noise nuisance caused to the public/ surrounding.	Closed	-

					"A further complaint was received on 6 July 2018 from EPD and its details were as follows:- "Further to our previous complaints which are in vain, we would like to continue to put forward the complaint against the noise from the construction works next to Cathay Dragon House at CLK, which has never been ceased and been causing great disturbance to the accommodations (aviation control centre) and staff within our Cathay Dragon building and CNAC tower. Below is the time schedule our staff regarding the noise disturbance from the site which is frequent and continuous. Date Time 3 July 2018 8:30am – 11:30am, 1:30pm – 5:30pm 4 July 2018 8:30am – 11:30am, 1:30pm – 5:30pm 5 July 2018 8:30am – 11:30am, 1:30pm – 5:30pm Please advise what has been your action upon this matter. This has been intolerable for months. If there is nothing that your depts., can impose to stop the disturbance, we may need to seek other alternative complain channel. Your immediate action on this matter is highly appreciated." "We would like to get your urgent attention to the noise nuisance matters that is occurring outside Cathay Dragon House (facing seaside Tung Chung). There have been extreme noisy works conducted, without proper noise mitigation matter, with noise DB levels reaching 70-100dB, and is seriously affecting our company operations. Please urgently attend to the matter and advise further on the email below, and implement the proper noise reducing and mitigation procedures.			
COM-2018-158	24-Dec-18	10:17 AM	HyD (SOR referred the email from HyD to Contractor, ET and IEC/ENPO on 10:17 am, on 24 Dec 2018)	Other: Construction work on Sunday Morning	The details of the complaint were as follows: Email received by HyD on 23 December 2018 at 10:49hrs "How come someone is doing some construction work on sunday morning (23/12/18, 10:30am)??? Looks like your christmas holidays i going to turn into an investigation holiday!!! Looking forwards to hearing from you? I am sure David will be more than happy to assist your investigation over the holidays!!" Email received by HyD on 23 December 2018 at 11:11hrs "by the way have you issue a "permit to annoy people" based on merit to operate a crane this sunday? If not I am looking forwards to know the action you will take. Don't esitate to contact Chief Lam he will surely be very happy to provide any assistance you need to find out who is the rogue employee working under him so you can take the necessary legal action."	N.A.	Based on our investigation result, the concerned work activity complied with the valid CNP. In this case, no follow up action is required. However, the Contractor has been reminded to comply with the conditions stipulated in the Construction Noise Permit for construction works undertaken during restricted hours.	Closed	-
N/A	03-Apr-19	Nil	EPD (ENPO referred the email from EPD to HyD, SOR, Contractor and ET) through email	Dust	Email received by EPD on 3 April 2019 ""投訴人表示海堤灣畔對面有港珠澳大橋的地盤正進行工程，工程期間會揚起大量塵土，引起污染，影響海堤灣畔居民，要求部門跟進事宜。"	N.A.	Based on our investigation result, there is no observation of dust emissions arising from the Contract No. HY/2011/03. The Contractor has implemented the Environmental Mitigation Implementation Schedule as per the EM&A Manual, the Contractor has been reminded to strictly maintain the dust mitigation measures during carrying out of their construction works to minimize the dust nuisances to nearby sensitive receivers.	Closed	-
COM-2019-163	30-Apr-19	Nil	SOR referred details of complaint to Contractor, ET and IEC/ENPO through email	Waste	The details of the complaint were as follows:- "rubbish and refuse pile up by the road near a bus stop breeding numerous flies and pests. huge annoyance and hygiene problem to the public. pls clean up."	Near Dragonair / CNAC (Group) Building (HKIA)	Based on our investigation result, there was no observation of works in the area of complaint on issue of general refuse arising from the Contract No. HY/2011/03. The Contractor has implemented the Environmental Mitigation Implementation Schedule as per the EM&A Manual, the Contractor has been reminded to strictly maintain waste management procedures during their construction works to avoid the hygiene impacts to nearby sensitive receivers.	Closed	-
COM-2020-165	18-Mar-20	Nil	Hotline "1823" (SOR referred details of complaint to Contractor, ET and IEC/ENPO through email)	Waste	The details of the complaint were as follows:- "Rubbish are found along the landscape area at Tung Yiu Road. Dear 1823 officer, Regarding the captioned case, I have previously made my complaint to the Airport Authority (AA) on the subject. Yet, AA advises that the concerned area at Tung Yiu Road is not managed by the AA and suggests me to contact 1823 for follow up."	Landscape area at Tung Yiu Road/ S16	Based on our investigation result, there was no observation of works in the area of complaint on issue of general refuse arising from the Contract No. HY/2011/03. The Contractor has implemented the Environmental Mitigation Implementation Schedule as per the EM&A Manual, the Contractor has been reminded to strictly maintain waste management procedures during their construction works to avoid the hygiene impacts to nearby sensitive receivers.	Closed	-
COM-2022-166	28-Jun-22	Nil	EPD (IEC/ENPO referred details of complaint to Contractor, ET and SOR through email)	Waste	The details of the complaint were as follows:- "有關東涌映灣園與藍天海岸對出海面垃圾問題" 1. 近東涌與赤鱲角機場接駁的大橋附近，即赤鱲角南路附近的海旁有貨櫃辦公室建築材料、廢料及鐵架；及海面有大堆沙丘被棄置數年； 2. 近觀景山隧道旁之海面有大堆沙丘及不少漂浮物件被棄置數年。 上述位置（見附圖）的臨時沙丘及建築廢料懷疑是興建港珠澳大橋時的建築材料，惟現時港珠澳大橋已於2018年落成及通車後，上述提及的建築材料及廢料亦未有妥善處理。此舉不單會造成環境污染，更有機會對船隻航行造成危險。有見及此，我們希望 貴處可派員跟進上述情況並不時作出監察，以避免海上意外發生及造成污染、	S7 and PR10	Based on our investigatyion result, there was no observation of works in the area of complaint on issue of general refuse arising from the Contract No. HY/2011/03. The Contractor has implemented the Environmental Mitigation Implementation Schedule as per the EM&A Manual, the Contractor has been reminded to strictly maintain waste management procedures during their construction works to avoid the hygiene impacts to nearby sensitive receivers.	Closed	-

APPENDIX O

Mudflat Monitoring Results

Figure 2.1. *Locations of sampling zones. The study site was divided into three sampling zones (TC1, TC2, TC3) in Tung Chung Bay and one zone in San Tau (ST) (map generated from Google Map).*

TC1

TC2

TC3

ST

Figure 2.2 *Photographic record of the environment in every sampling zone. (March 2025)*

TC1

Plastic waste

Trash gill net

TC3

Boat wreckage

Trash gill net

ST

Trash gill net and hand trolley

A tangled horseshoe crab on a trash net (record in June 2017)

Figure 2.3 *Examples of photographic record of the big trash found on the mudflat.*

ST

Trash gill net (recorded in September 2024)

Trash nets deposited at ST for several years, where horseshoe crab occasionally tangled on them (record in September 2024)

TC3

Trash gill net (recorded in December 2024)

Trash nets deposited at Tc3, where a horseshoe crab was tangled on it (record in December 2024)

Figure 2.3 (Continued) *Examples of photographic record of the big trash found on the mudflat.*

Trash gill net at TC3 (March 2025)

Trash at ST (March 2025)

Figure 2.3 (Continued) *Examples of photographic record of the big trash found on the mudflat.*

ST *Carcinoscorpius rotundicauda*

ST *Tachypleus tridentatus*

Sep. 2023

Figure 3.1 *Examples of photographic records of horseshoe crab Carcinoscorpius rotundicauda (Mar 2023), Tachypleus tridentatus (September 2023).*

Photo taken in March 2024

Photo taken in September 2024

Photo taken in December 2024

Photographic records of horseshoe crabs, *Tachypleus tridentatus* in March 2025)

Figure 3.1 (Cont'd) *Examples of photographic records of horseshoe crabs.*

Table 3.1. *Summary of horseshoe crab survey in December 2024*

	TC1	TC2	TC3	ST
Search duration (hr)	2	2	3	3
Carcinoscorpius rotundicauda				
No. of individuals	0	0	0	0
Mean prosomal width (mm)	\	\	\	\
Max. prosomal width (mm)	\	\	\	\
Min. prosomal width (mm)	\	\	\	\
Search record (ind. hr-1 person-1)	0	0	0	0
Tachypleus tridentatus				
No. of individuals	0	0	1	3
Mean prosomal width (mm)	\	\	44	54
Max. prosomal width (mm)	\	\	44	62
Min. prosomal width (mm)	\	\	44	46
Search record (ind. hr-1 person-1)	0	0	0.33	1.0

March 2015 - ST

June 2017 – TC2

(Female)

(Male)

June 2017 – TC3

Figure 3.2 Photographic records of mating pairs of horseshoe crab

December 2017 – TC3

June 2018 – TC3

(Female)

(Male)

Figure 3.2(Cont'd) *Photographic records of mating pair of* horseshoe crabs

March 2019 – TC2

June 2019 – TC3

March 2020 – TC1

June 2022 – TC3

Figure 3.2 (Cont'd). *Photographic records of mating pairs of horseshoe crabs*

TC1

TC2

Figure 3.3 *Photographic records of newly hatched individuals of horseshoe crab (September 2018)*

Carcinoscorpius rotundicauda

June 2017

December 2017

December 2018

March 2019

Figure 3.4 *Photographic records of large individuals (>100 mm) of horseshoe crabs were excluded from data analysis*

Tachypleus tridentatus

September 2017

June 2019

March 2020

June 2022

September 2022

September 2023

Figure 3.4 (Cont'd) *Photographic records of large individuals (>100 mm) of horseshoe crabs records were excluded from data analysis*

Carcinoscorpius rotundicauda
December 2024

Dead horseshoe specimen
March 2025

Figure 3.4 (Cont'd) *Photographic records of large individuals (>100 mm) of horseshoe crabs records were excluded from data analysis*

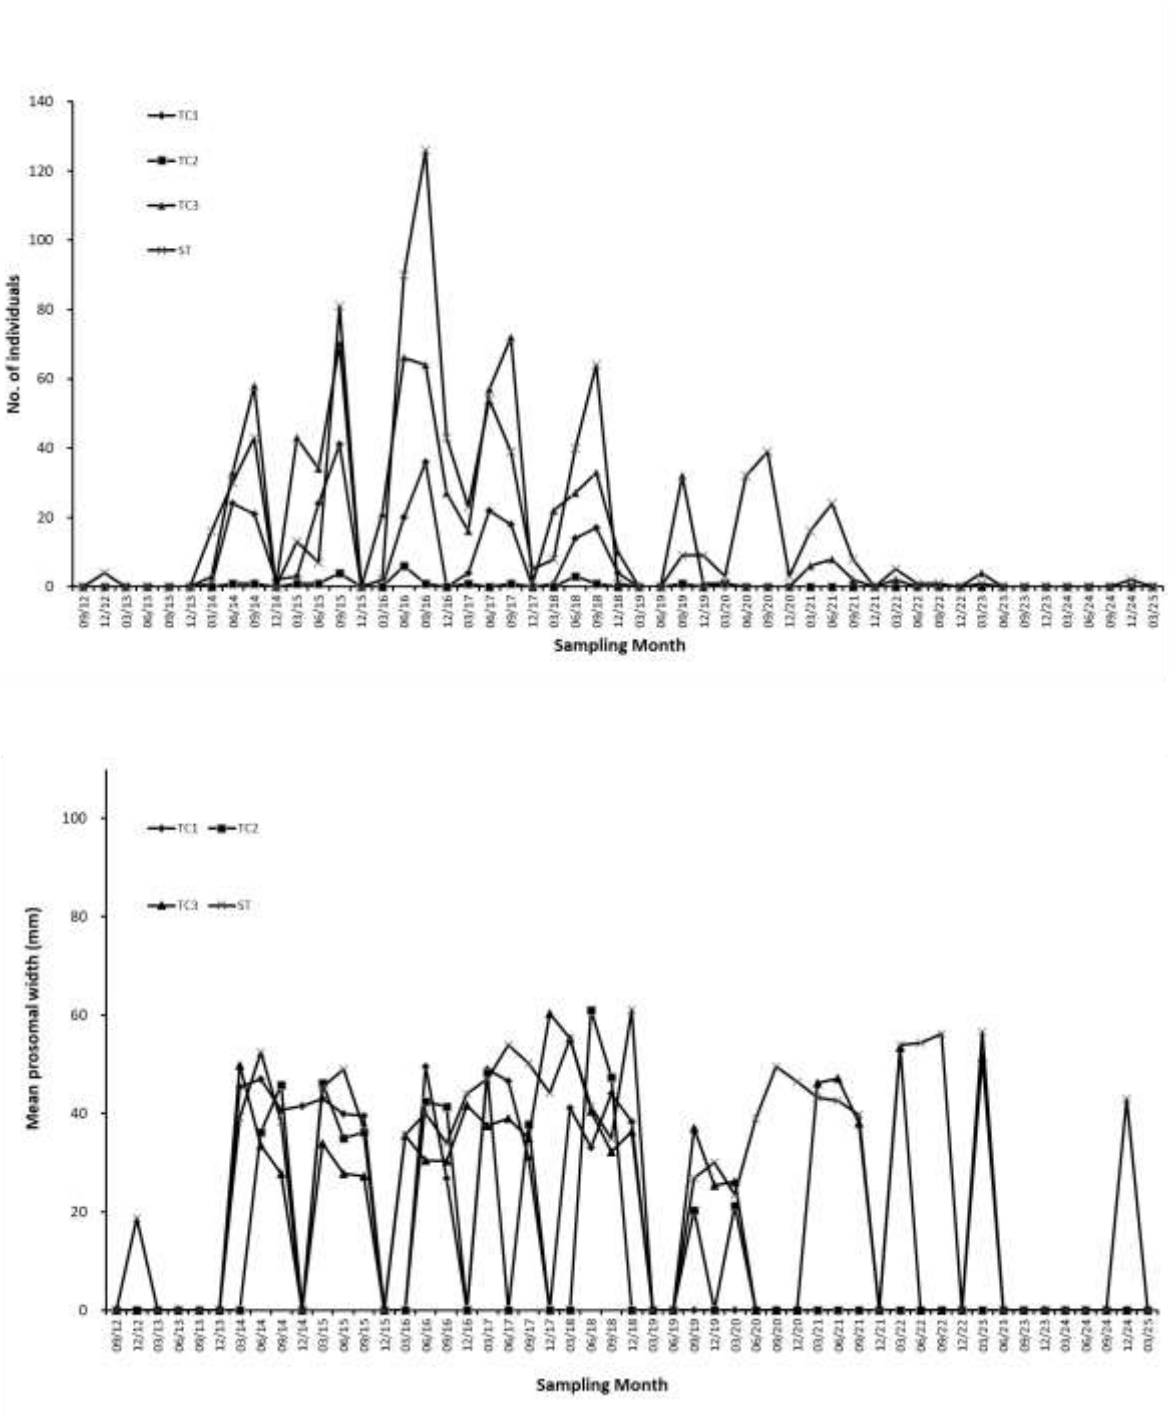

Figure 3.5 *Changes of number of individuals mean prosomal width and search record of horseshoe crab Carcinoscorpius rotundicauda in every sampling zone along the sampling months*

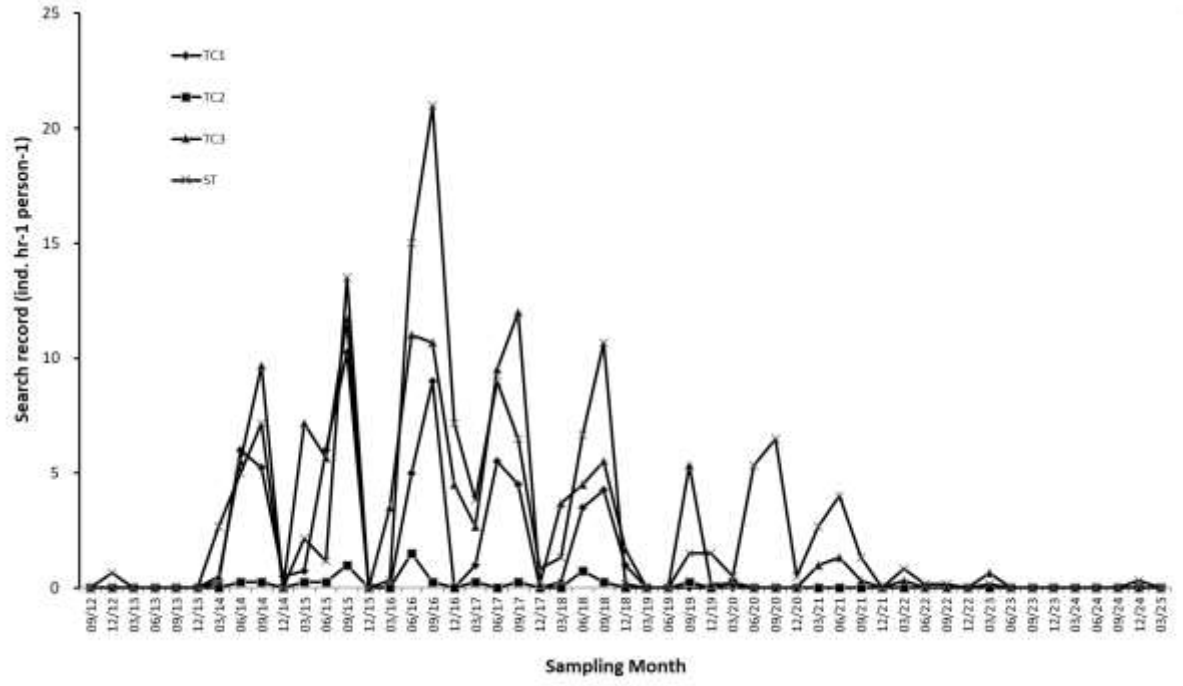

Figure 3.5 (Cont'd) *Changes of number of individuals mean prosomal width and search record of horseshoe crab Carcinoscorpius rotundicauda in every sampling zone along the sampling months*

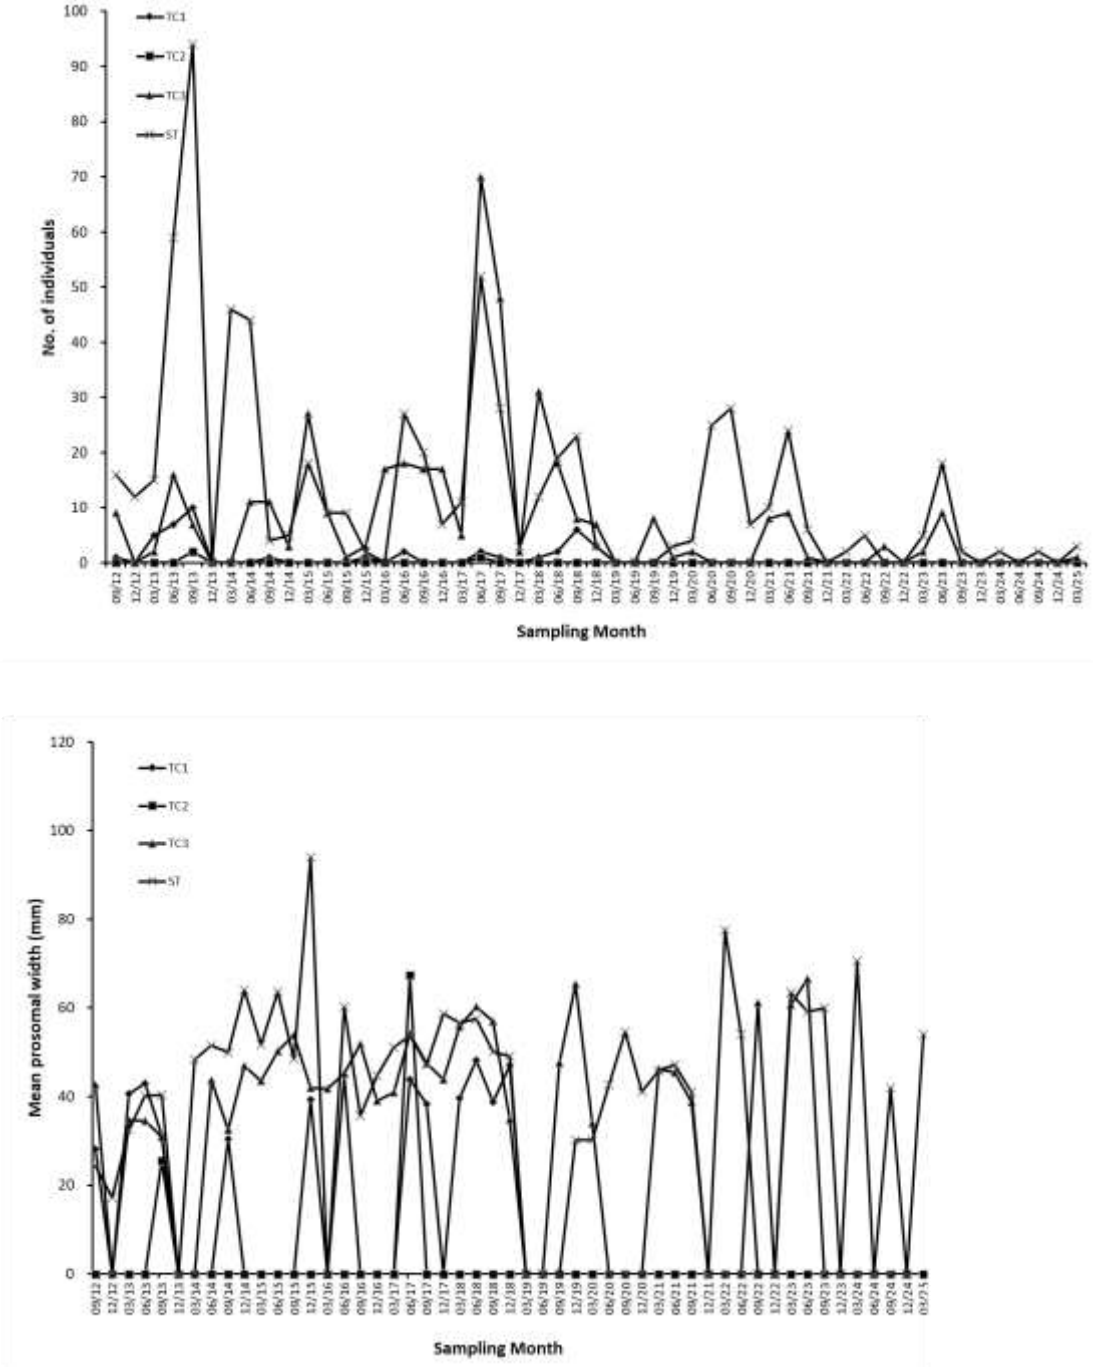

Figure 3.6 *Changes of number of individuals mean prosomal width and search record of horseshoe crab Tachypleus tridentatus in every sampling zone along the sampling months*

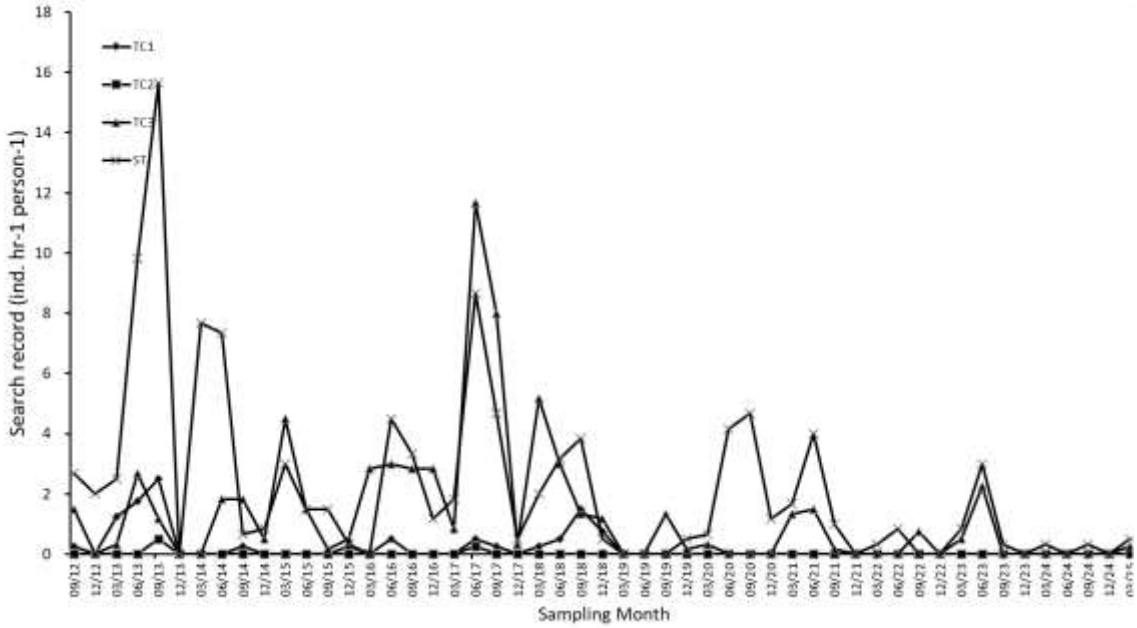

Figure 3.6 (Cont'd) *Changes of number of individuals mean prosomal width and search record of horseshoe crab Tachypleus tridentatus in every sampling zone along the sampling months*

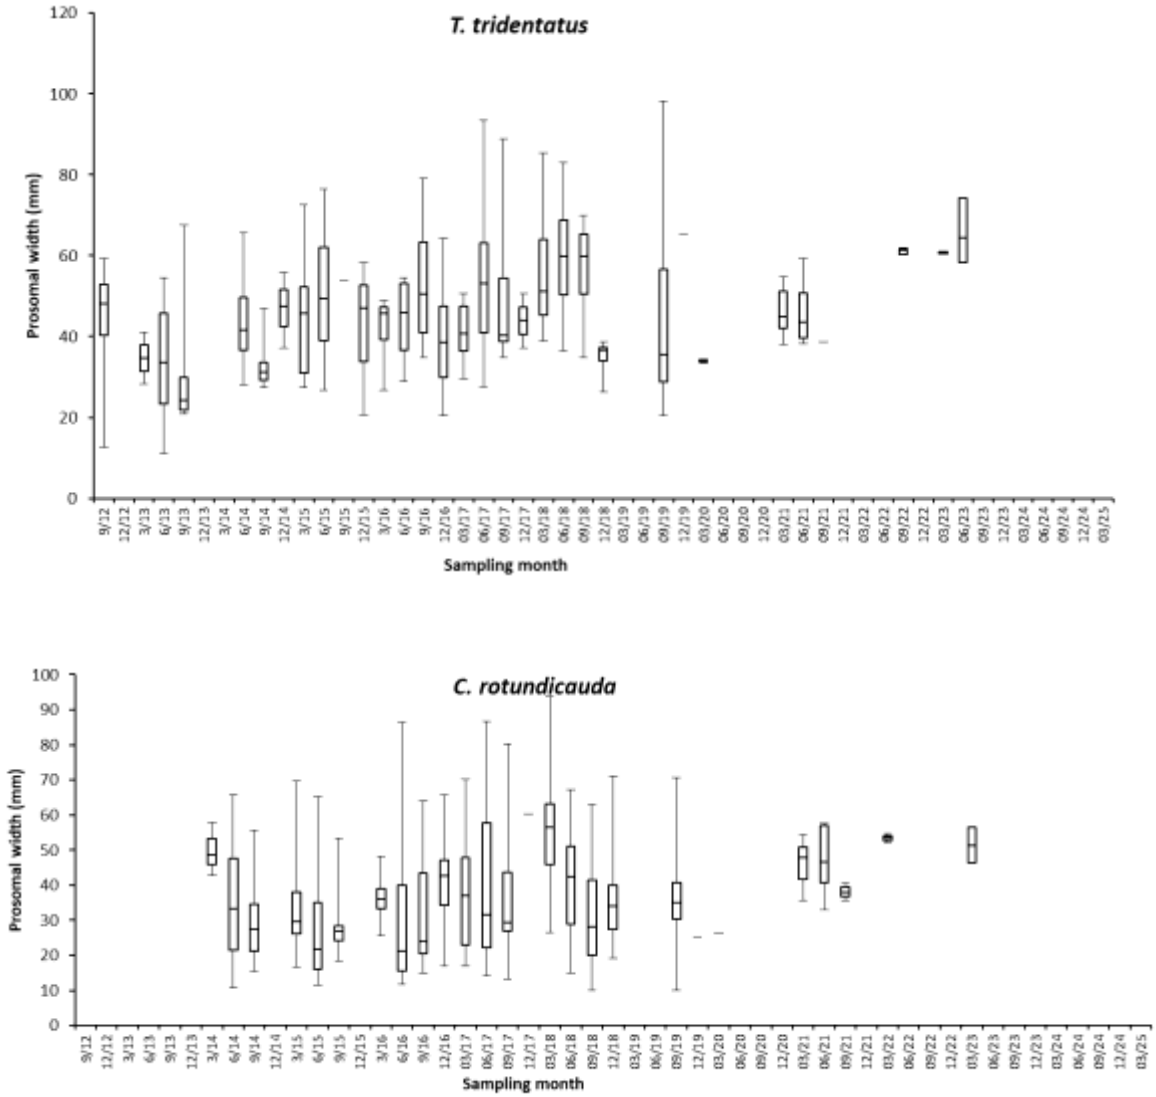

Figure 3.7 *Box plot of prosomal width of horseshoe crab in the sampling zone TC3 along the sampling months. (The box represents 50% of the sample (upper to lower quartile) with a middle line showing the median value. The upper whisker and lower whisker showed the 25% of sample above upper quartile and below the lower quartile respectively)*

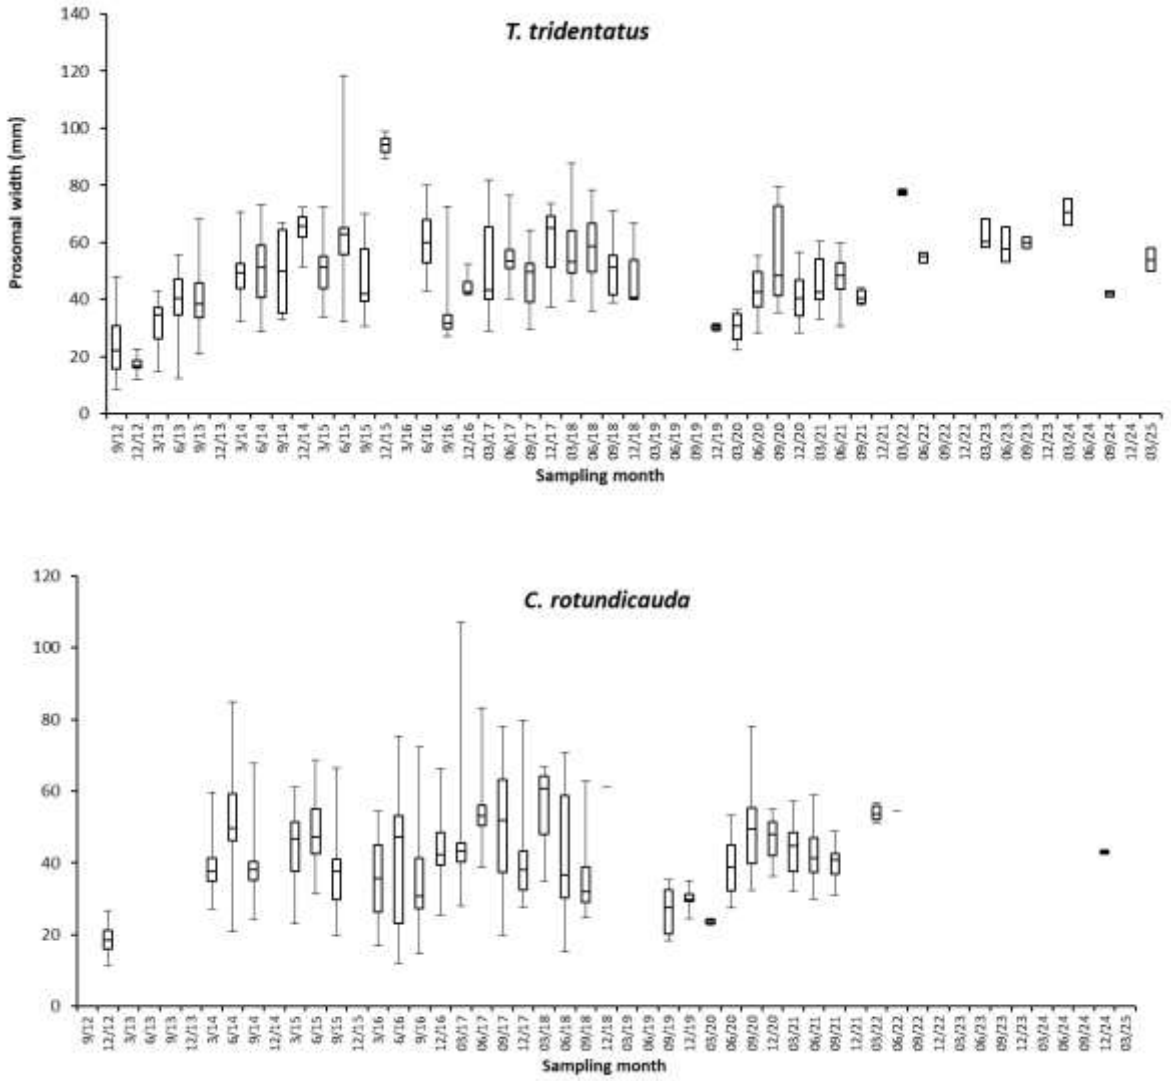

Figure 3.8 *Box plot of prosomal width of horseshoe crab in the sampling zone ST along the sampling months. (The box represents 50% of the sample (upper to lower quartile) with a middle line showing the median value. The upper whisker and lower whisker showed the 25% of sample above upper quartile and below the lower quartile respectively.)*

Photos below: Brown filamentous algae bloom at ST, March 2022

Photos below: **Brown filamentous algae at seagrass bed at ST disappeared, June 2022**

Halophila ovalis covered large area of mudflat

Figure 3.9 Examples of Photographic record of seagrass beds.

Halophila ovalis (left) and *Zostera japonica* (right) in ST June 2024

Halophila ovalis in TC3, September 2024

Seagrass bed (*Zostera japonica*) at ST, March 2025

Figure 3.10 Photographic records of seagrass beds in 2024 and 2025 survey.

Halophila ovalis (below left) and *Zostera japonica* (below right) in ST September 2024

Photo shown disappearance of seagrass bed in December 2024

Photo shown seagrass bed, *Zostera japonica***,** in March 2025

Figure 3.10 (Cont'd) Photographic records of seagrass beds in 2024 and 2025 survey

Table 3.2. Summary *of seagrass beds survey*

Sampling zone	TC3 *Halophila ovalis*	ST *Halophila ovalis*	ST *Zostera japonica*
Number of patches	0	0	1
Total area (m^2)	0	0	25
Average area (m^2)	0	0	25

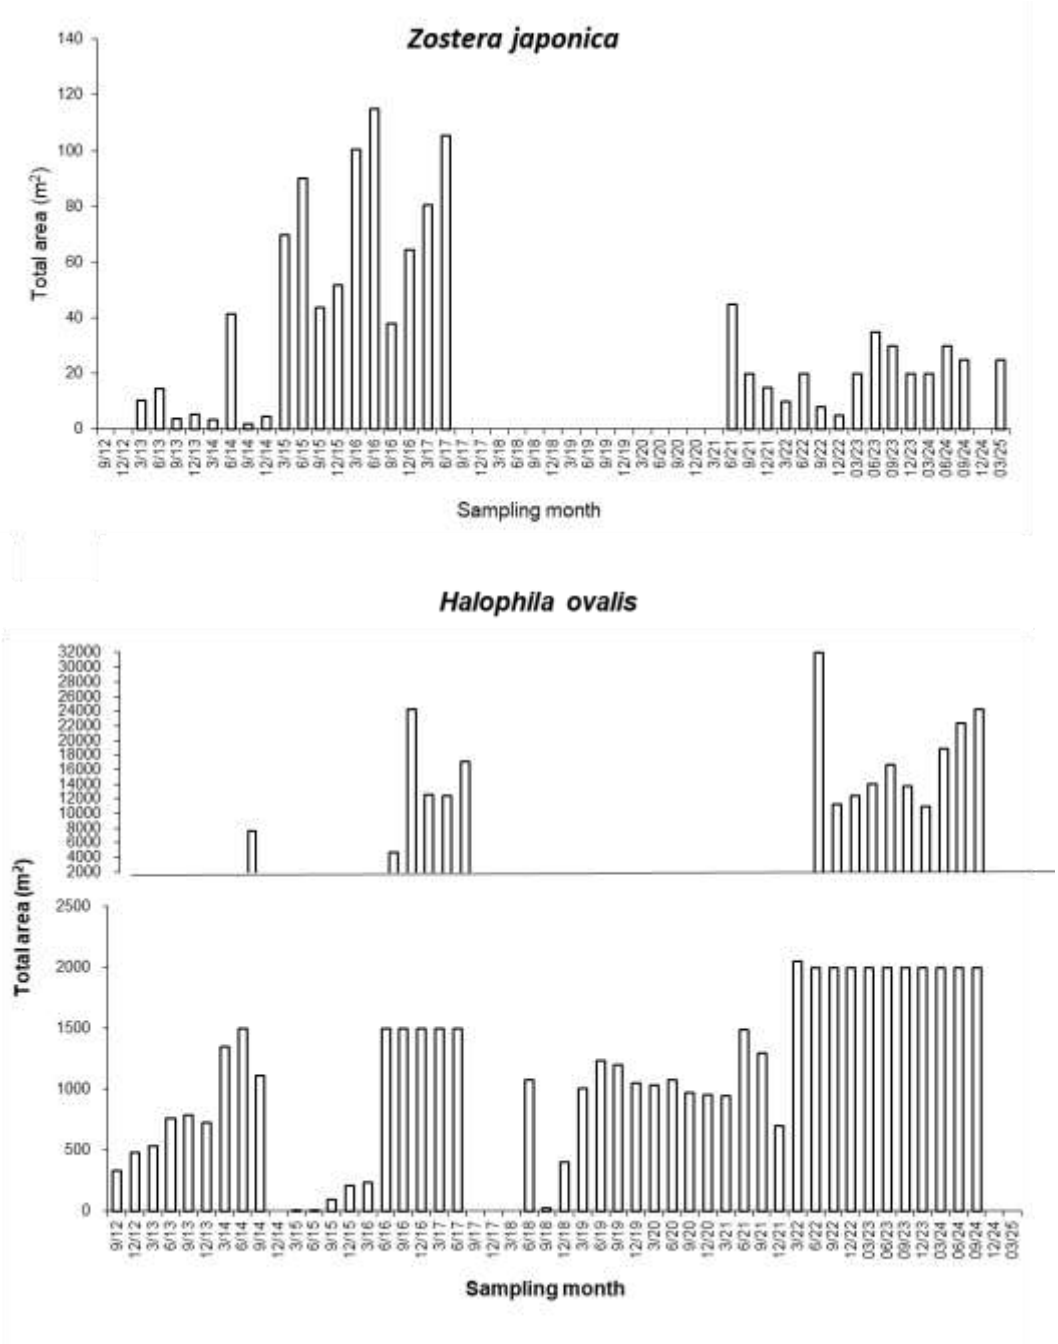

Figure 3.11 *Temporal changes of estimated total area of seagrass beds in ST.*

June 2014

December 2014 (no seagrass)

September 2015

June 2017

September 2017-March 2018 (no seagrass)

September 2018

Figure 3.12 Comparison of pictures taken in different sampling months shows the successive disappearance and recolonization of seagrass beds in ST. The picture of December 2018 was lacking due to night-dawn survey time.

March 2019

June 2019

September 2019

December 2019

March 2020

June 2020

Figure 3.12 (Cont'd) *Comparison of pictures taken in different sampling months shows the successive disappearance and recolonization of seagrass beds in ST.*

September 2020

December 2020

March 2021

June 2021

September 2021

December 2021

Figure 3.12 (Cont'd) *Comparison of pictures taken in different sampling months shows the successive disappearance and recolonization of seagrass beds in ST.*

March 2022

June 2022

September 2022

December 2022

March 2023

June 2023

Figure 3.12 (Cont'd) *Comparison of pictures taken in different sampling months shows the successive disappearance and recolonization of seagrass beds in ST.*

September 2023

December 2023

March 2024

June 2024

September 2024

December 2024 (no seagrass)

Figure 3.12 (Cont'd) *Comparison of pictures taken in different sampling months shows the successive disappearance and recolonization of seagrass beds in ST. All seagrasses disappeared at both ST and CT3 in December 2024.*

Newly re-generated seagrass, March 2025

March 2025 (no seagrass)

Figure 3.12 (Cont'd) *Comparison of pictures taken in different sampling months shows the successive disappearance and recolonization of seagrass beds in ST. All seagrasses disappeared at both ST and CT3 in December 2024, it is partially re-generated at ST in March 2025.*

Table 3.3. *Relative distribution (%) of types of substratum along the horizontal transect at every tidal level and in every sampling zone.*

		Percentage		
Sampling zone	**Tidal level**	**Gravels and Boulders**	**Sands**	**Soft mud**
TC1	H	80	20	0
	M	10	85	5
	L	0	10	90
TC2	H	85	15	0
	M	10	85	5
	L	0	5	95
TC3	H	90	5	5
	M	10	10	80
	L	0	5	95
ST	H	90	10	0
	M	10	85	5
	L	2	8	90

H: 2.0 m above C.D.; M: 1.5 m above C.D.; L: 1.0 m above C.D.

Figure 3.13 *Examples of photographic records of quadrat for intertidal soft shore community survey in March 2025 (H: 2.0 m above C.D.; M: 1.5 m above C.D.; L: 1.0 m above C.D.)*

TC1 H	**TC1 L**
TC2 H	**TC2 L**

TC3 H	**TC3 L**
	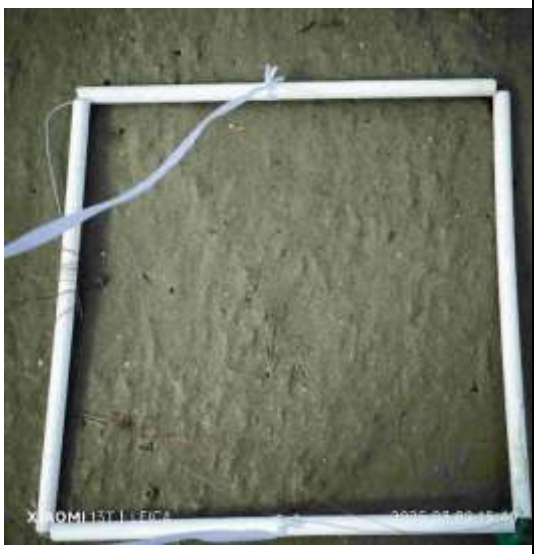
ST H	**ST L**
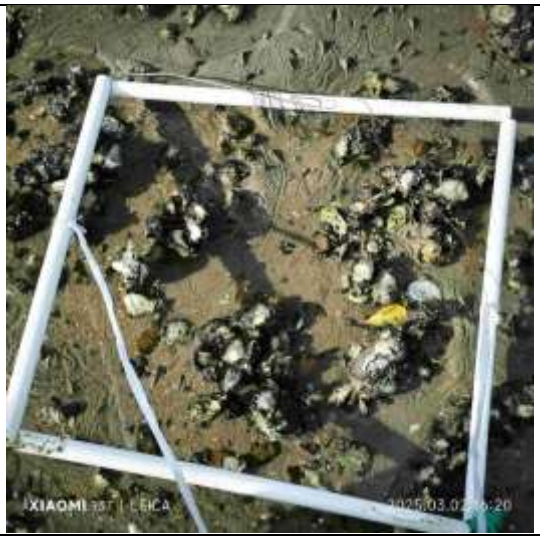	

Figure 3.13.(Cont'd) *Examples of photographic records of quadrat for intertidal soft shore community survey in March 2025 (H: 2.0 m above C.D.; M: 1.5 m above C.D.; L: 1.0 m above C.D.)*

Table 3.4 *Total abundance, density and number of taxon of every phylum*

Phylum	Total Abundance	%	Density (ind. m^{-2})	Number of Taxon
Mar 2025				
Mollusca	6485	87.6	216	32
Arthropoda	519	7.0	17	6
Annelida	98	1.3	3	3
Sipuncula	173	2.3	6	2
Nemertea	46	0.6	2	1
Cnidaria	65	0.9	2	1
Platyhelminthes	15	0.2	1	1
Total	7401			

0.0 %: Total abundance of the phylum is less than 0.1% of relative abundance.

0 ind. m^{-2}: Density of the phylum is less than 1 ind. m^{-2}.

Table 3.5 *The number of individuals, relative abundance (percentage) and density of each phylum in every sampling zone*

Phylum	TC1	%	Density (ind. m^{-2})	TC2	%	Density (ind. m^{-2})	TC3	%	Density (ind. m^{-2})	ST	%	Density (ind. m^{-2})
Mollusca	1577	88.2	210	1496	84.4	199	1755	89.6	234	1657	88.0	221
Arthropoda	124	6.9	17	208	11.7	28	85	4.3	11	102	5.4	14
Annelida	38	2.1	5	0	0.0	0	40	2.0	5	20	1.1	3
Sipuncula	27	1.5	4	23	1.3	3	58	3.0	8	65	3.5	9
Nemertea	0	0.0	0	13	0.7	2	6	0.3	1	27	1.4	4
Cnidaria	21	1.2	3	32	1.8	4	0	0.0	0	12	0.6	2
Platyhelminthes	0	0.0	0	0	0.0	0	15	0.8	2	0	0.0	0
Sub-total	1787			1772			1959			1883		

0.0 %: Total abundance of the phylum is less than 0.1% of relative abundance of the sampling zone.

0 ind. m^{-2}: Density of the phylum is less than 1 ind. m^{-2} of the sampling zone.

Table 3.6 *The abundant species (relative abundance >10%) in every sampling zone*

Sampling zone TC1	Group	Species	Mean density (ind. m^{-2})	Relative abundance (%)	Cumulative relative abundance (%)
High	Bi	*Saccostrea cucullata*	106	39	39
	G	*Monodonta labio*	56	21	60
Mid	Bi	*Saccostrea cucullata*	79	32	32
	G	*Monodonta labio*	48	19	51
	G	*Batillaria zonalis*	32	13	64
Low	G	*Batillaria multiformis*	41	21	21
	G	*Nodilittorina radiata*	38	19	40
	Bi	*Barbatia virescens*	36	18	58

Bi = Bivalve, G = Gastropod

Table 3.6(Cont'd) *The abundant species (relative abundance >10%) in every sampling zone*

Sampling zone TC2	Group	Species	Mean density (ind. m^{-2})	Relative abundance (%)	Cumulative relative abundance (%)
High	Bi	*Saccostrea cucullata*	97	35	35
	G	*Monodonta labio*	57	21	56
	G	*Batillaria multiformis*	40	141	197
Mid	Bi	*Saccostrea cucullata*	76	33	33
	G	*Monodonta labio*	40	16	49
	G	*Batillaria zonalis*	34	14	63
Low	Bi	*Barbatia virescens*	44	23	23
	G	*Batillaria multiformis*	31	16	39

Bi = Bivalve, G = Gastropod

Table 3.6(Cont'd) *The abundant species (relative abundance >10%) in every sampling zone*

Sampling zone TC3	Group	Species	Mean density (ind. m^{-2})	Relative abundance (%)	Cumulative relative abundance (%)
High	Bi	*Saccostrea cucullata*	112	40	40
	G	*Monodonta labio*	58	21	61
Mid	Bi	*Saccostrea cucullata*	102	39	39
	G	*Monodonta labio*	51	19	58
Low	Bi	*Barbatia virescens*	58	25	25
	G	*Lunella granulata*	33	14	39
	G	*Batillaria multiformis*	34	14	53

Bi = Bivalve, G = Gastropod

Table 3.6(Cont'd) *The abundant species (relative abundance >10%) in every sampling zone*

Sampling zone ST	Group	Species	Mean density (ind. m^{-2})	Relative abundance (%)	Cumulative relative abundance (%)
High	Bi	*Saccostrea cucullata*	96	32	32
	G	*Monodonta labio*	52	17	49
Mid	Bi	Saccostrea cucullata	84	34	34
	G	Monodonta labio	45	18	52
Low	G	*Batillaria zonalis*	55	27	27
	G	*Lunella granulata*	38	18	45

Bi = Bivalve, G = Gastropod

Table 3.7 *Mean values of species number, density, Shannon-Weaver Diversity Index (H') and Pielou's Species Evenness (J) at every tidal level and in every sampling zone*

Samling zone	Tidal	Mean species number (spp. 0.25m-2)	Mean species number across tidal levels	Mean density (ind. m-2)	Mean density across tidal levels	Mean H'	Mean H' across tidal levels	Mean J	Mean J across tidal levels
TC1	H	16	16	253	227	2.1	2.17	0.8	0.83
	M	15		235		2.1		0.8	
	L	16		194		2.3		0.9	
TC2	H	16	16	273	226	2.1	2.20	0.7	0.80
	M	16		230		2.2		0.8	
	L	15		175		2.3		0.9	
TC3	H	16	17	285	243	1.9	2.17	0.7	0.77
	M	18		226		2.3		0.8	
	L	16		217		2.3		0.8	
ST	H	16	16	264	258	2.1	2.17	0.8	0.77
	M	17		293		2.1		0.7	
	L	16		216		2.3		0.8	

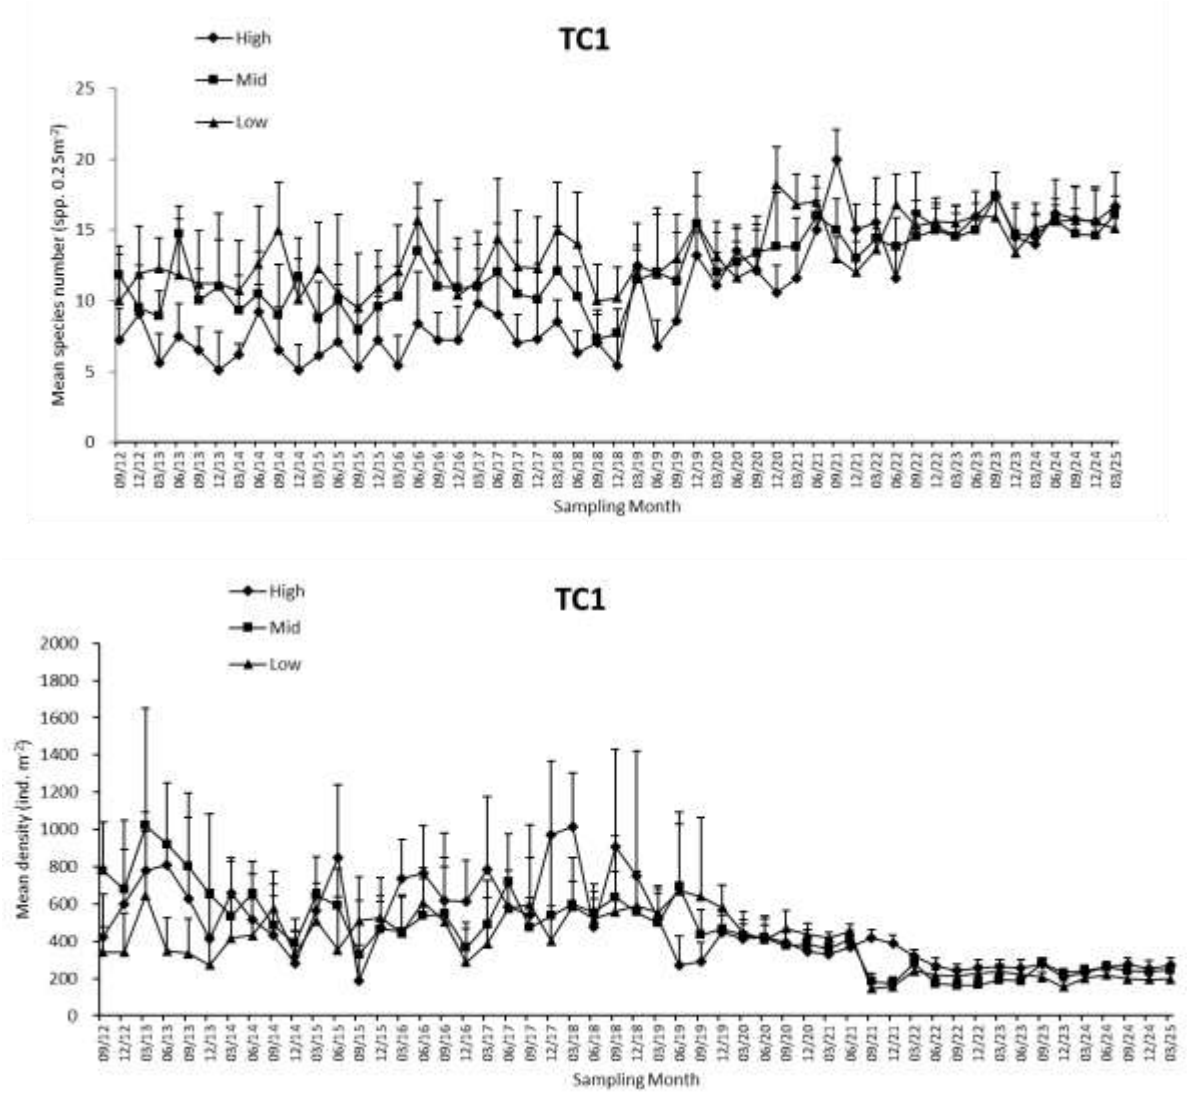

Figure 3.14 *Temporal changes of mean number of species, mean density, Shannon-Weaver Diversity Index (H') and Pielou's Species Evenness (J) (mean + SD)at every tidal level in sampling zone TC1*

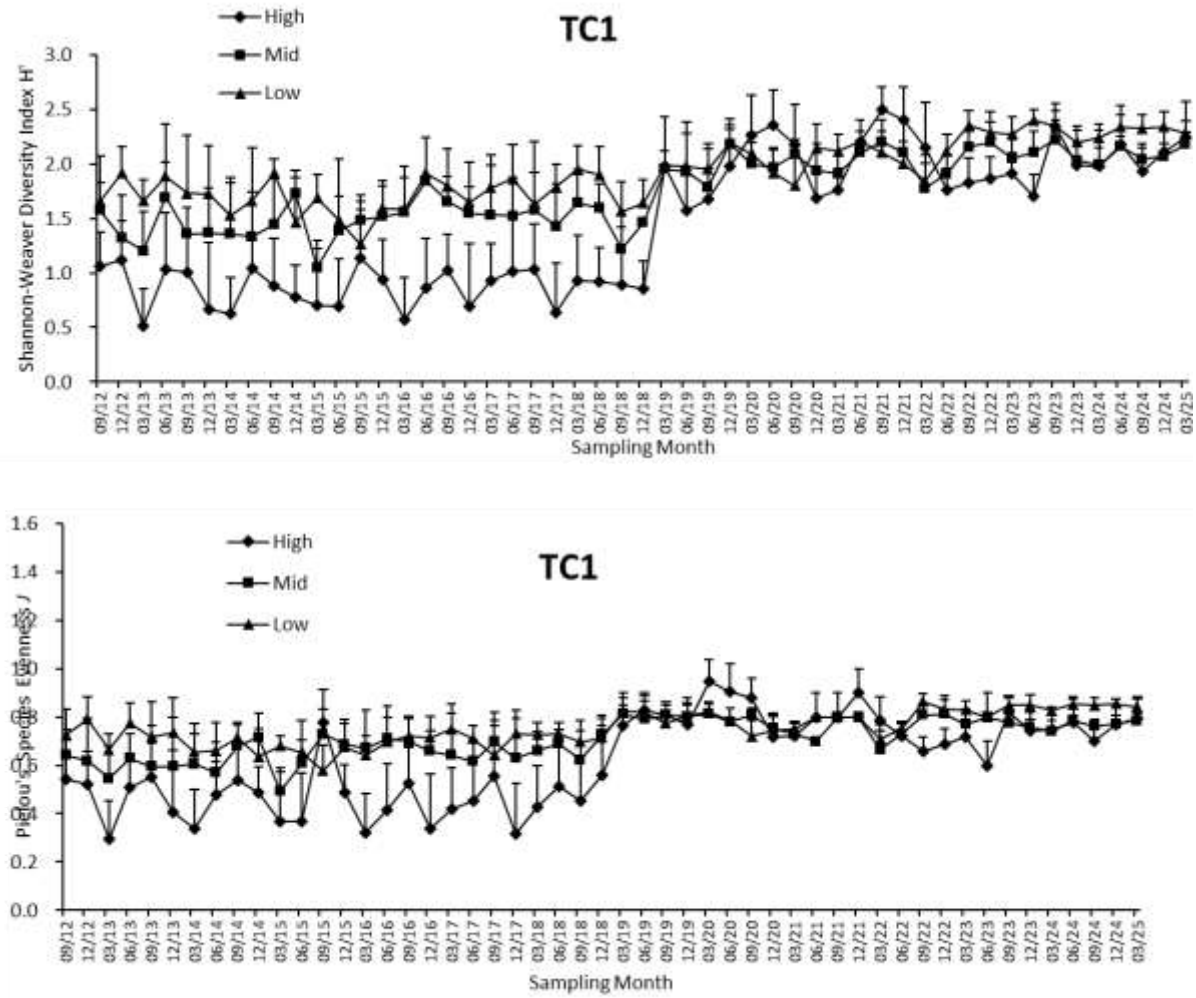

Figure 3.14(Cont'd) *Temporal changes of mean number of species, mean density, Shannon-Weaver Diversity Index (H') and Pielou's Species Evenness (J) (mean + SD)at every tidal level in sampling zone TC1*

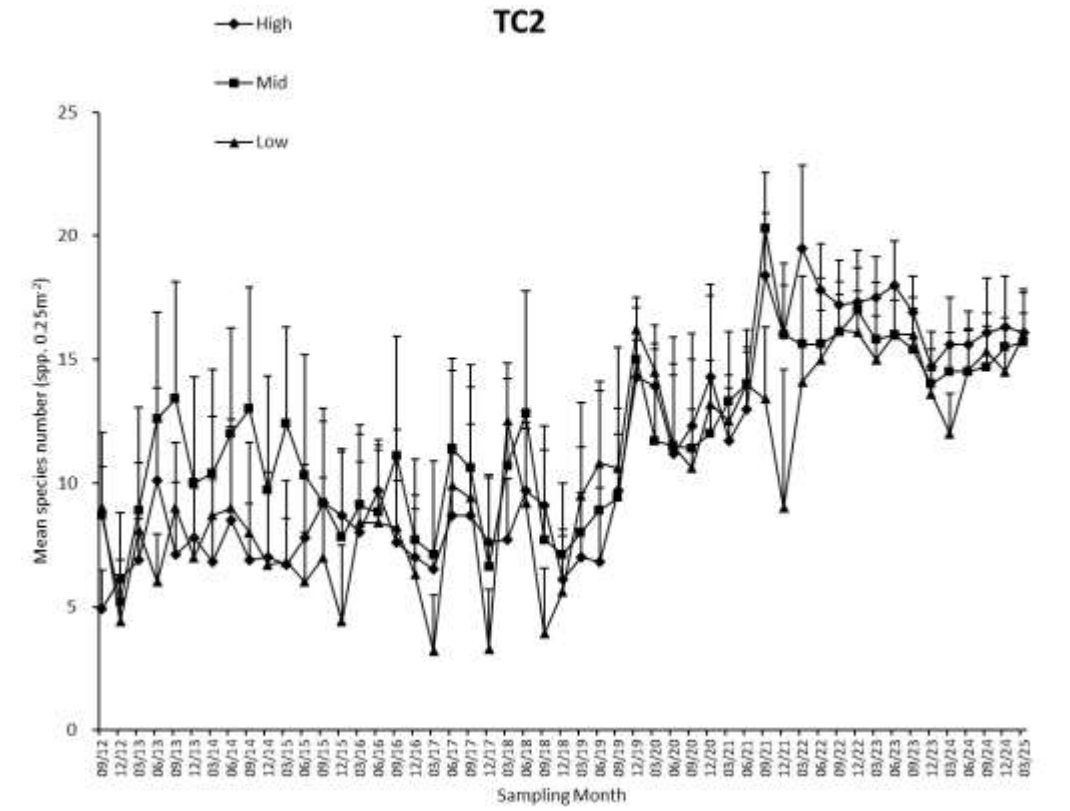

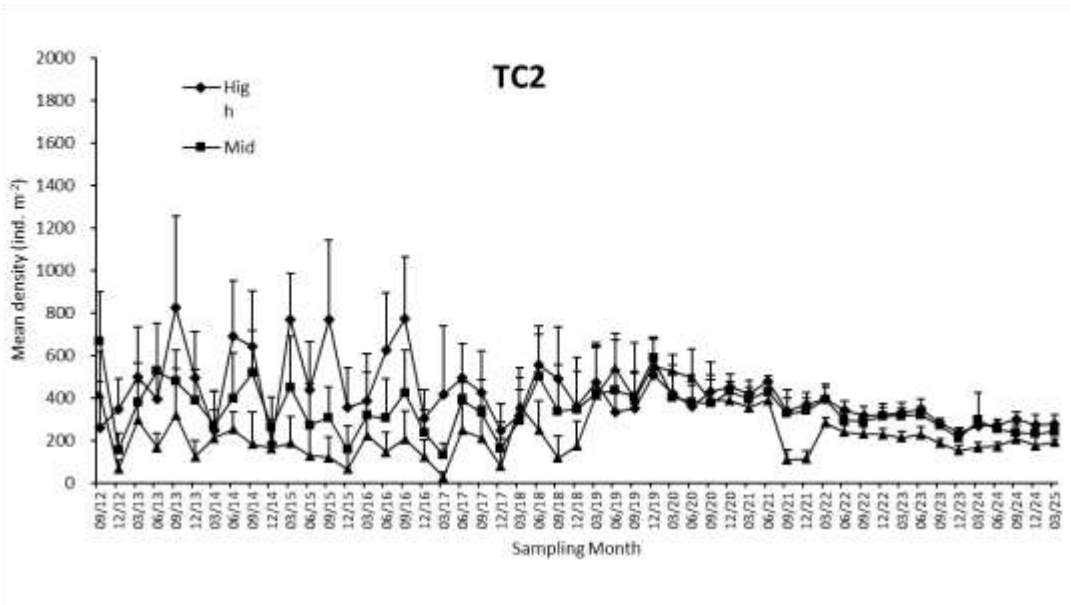

Figure 3.15 *Temporal changes of mean number of species, mean density, Shannon-Weaver Diversity Index (H') and Pielou's Species Evenness (J) (mean + SD) at every tidal level in sampling zone TC2.*

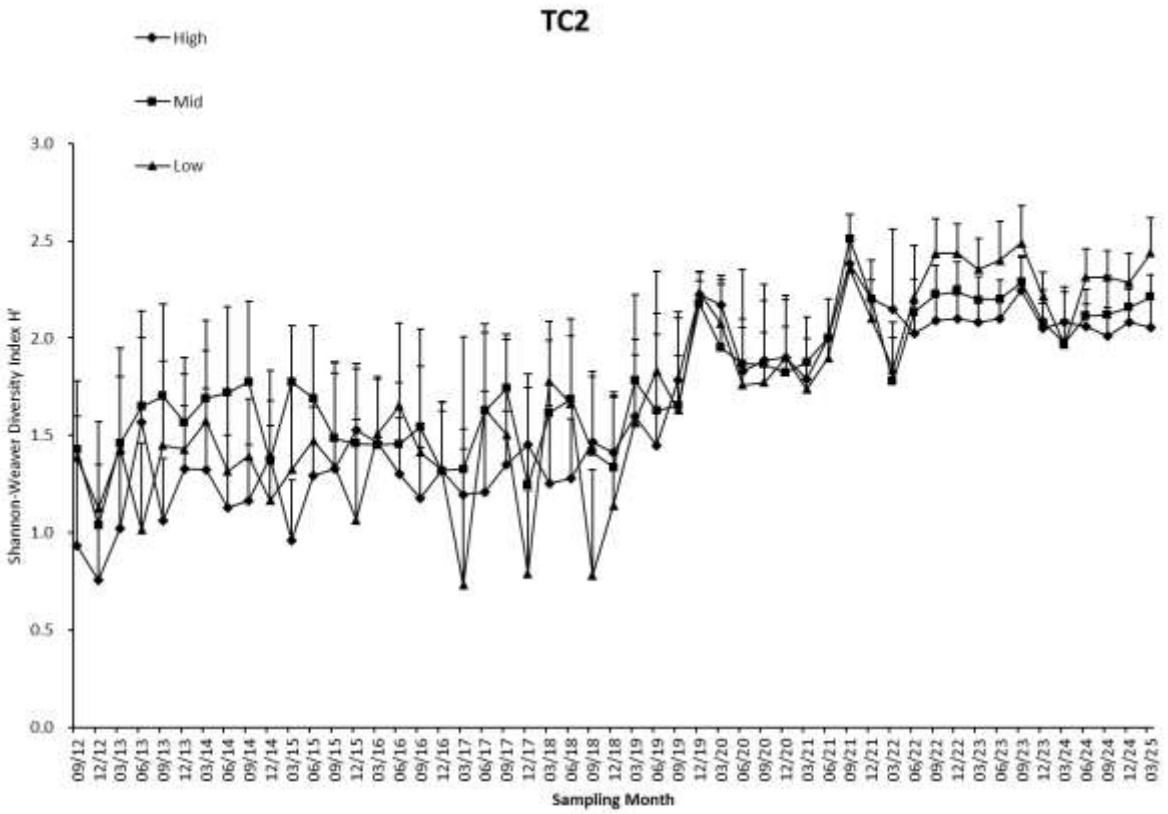

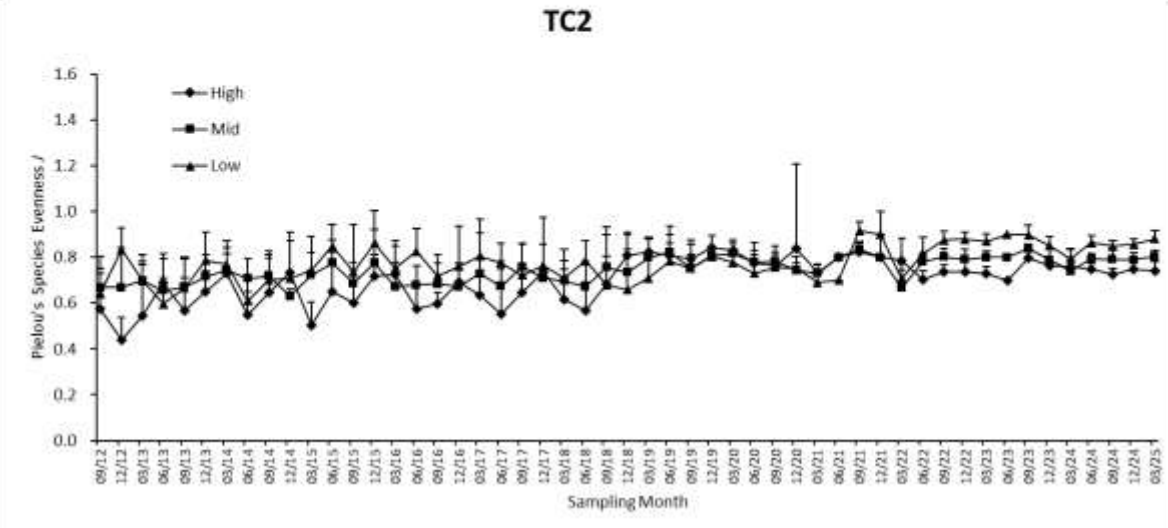

Figure3.15 (Cont'd) *Temporal changes of mean number of species, mean density, Shannon-Weaver Diversity Index (H') and Pielou's Species Evenness (J) (mean + SD) at every tidal level in sampling zone TC2.*

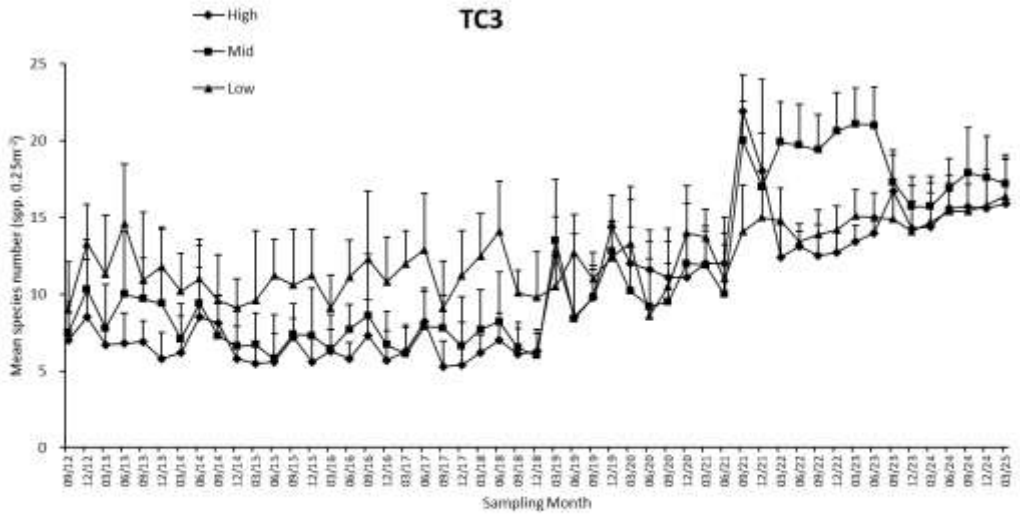

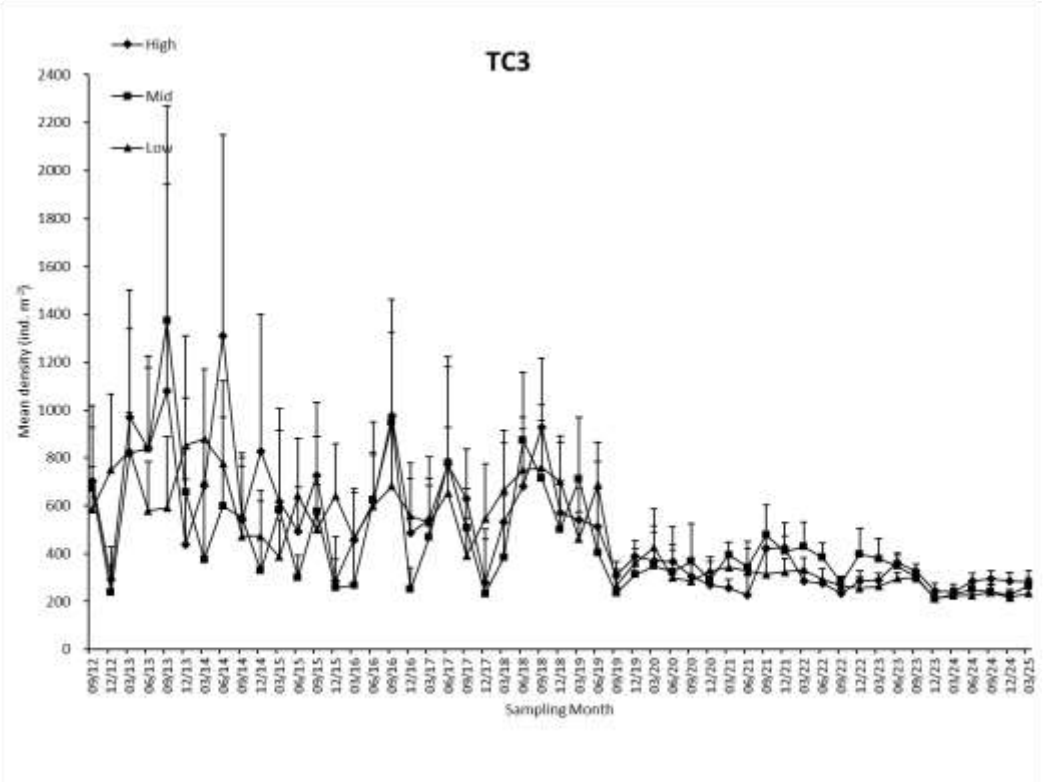

Figure 3.16 *Temporal changes of mean number of species, mean density, Shannon-Weaver Diversity Index (H') and Pielou's Species Evenness (J) (mean + SD) at every tidal level in sampling zone TC3.*

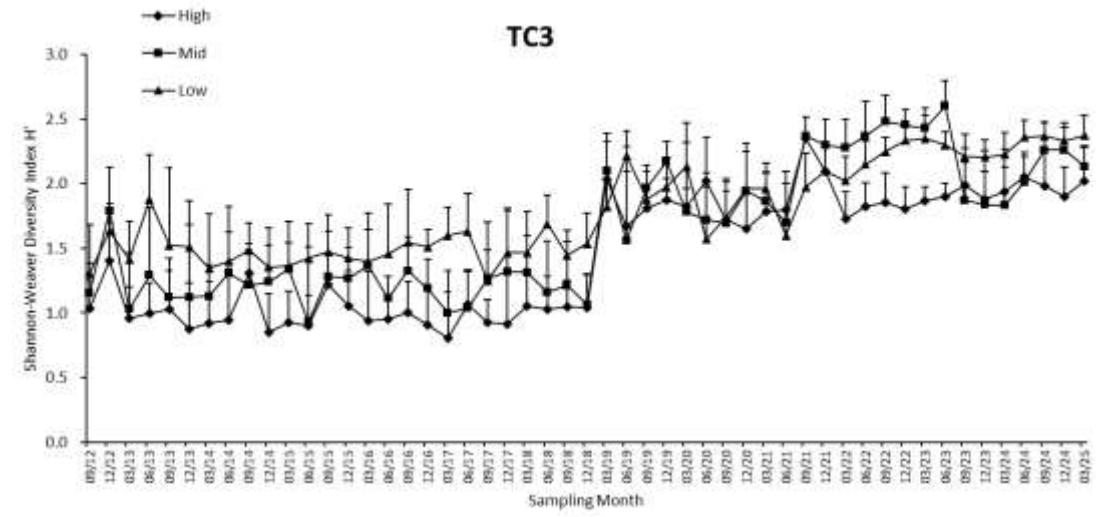

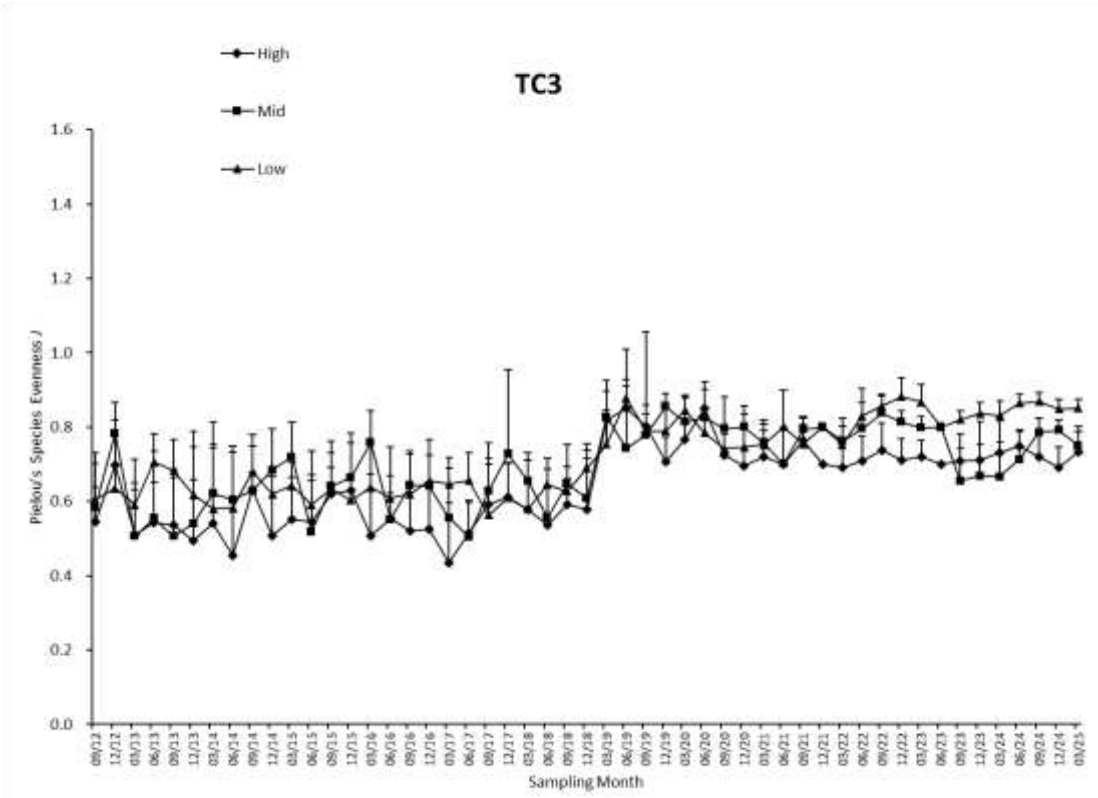

Figure 3.16 (Cont'd) *Temporal changes of mean number of species, mean density, Shannon-Weaver Diversity Index (H') and Pielou's Species Evenness (J) (mean + SD) at every tidal level in sampling zone TC3.*

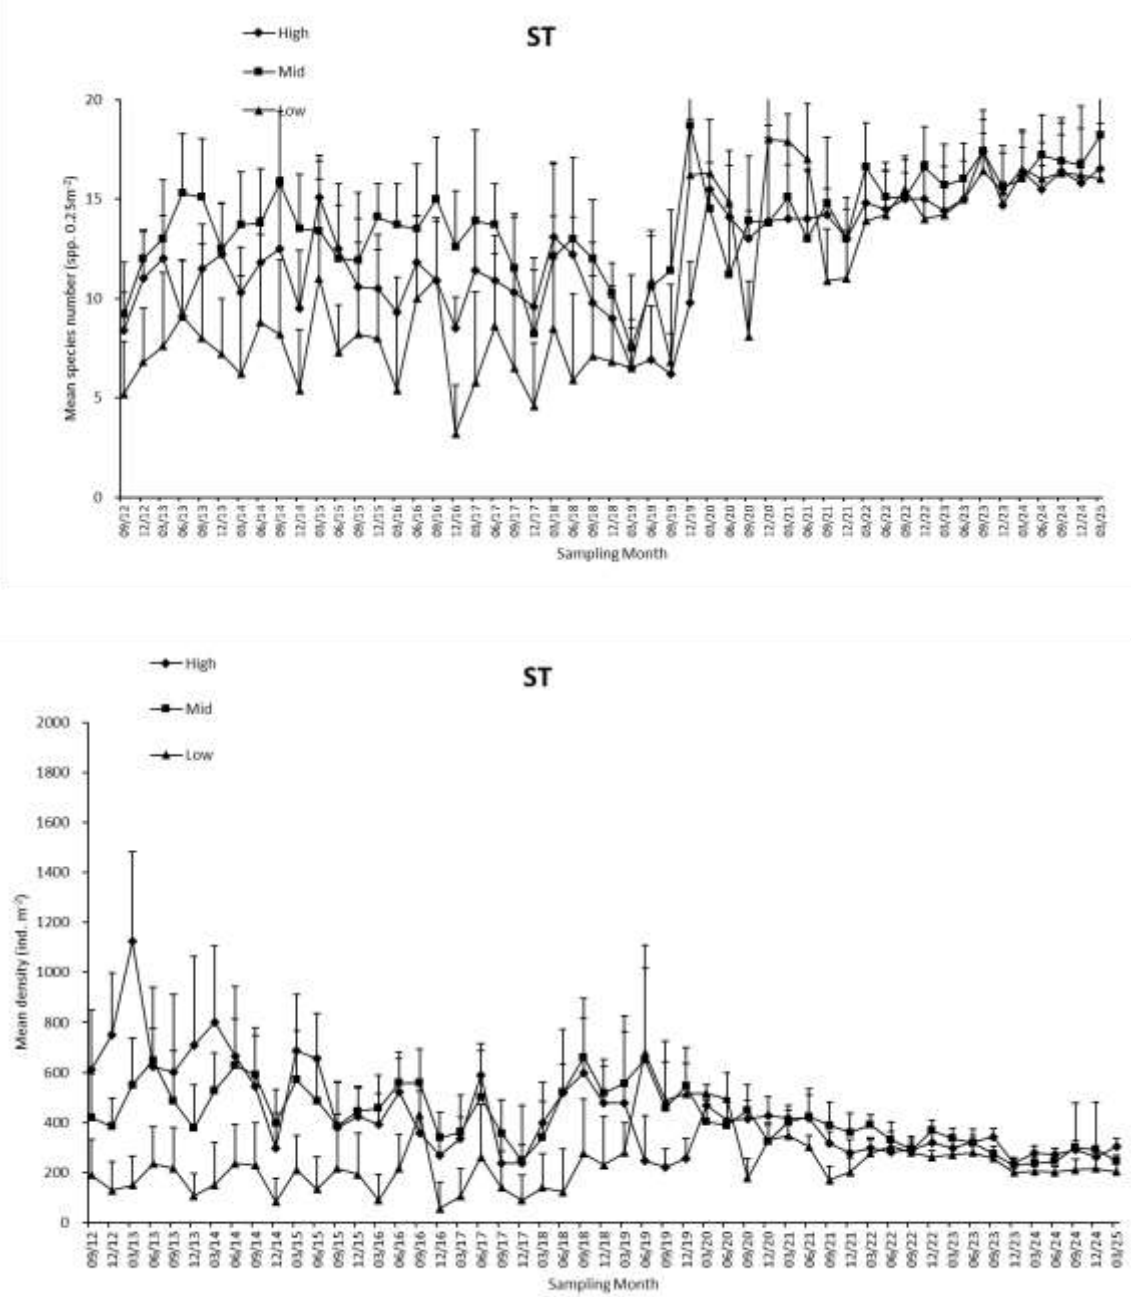

Figure 3.17 *Temporal changes of mean number of species, mean density, Shannon-Weaver Diversity Index (H') and Pielou's Species Evenness (J) (mean + SD) at every tidal level in sampling zone ST.*

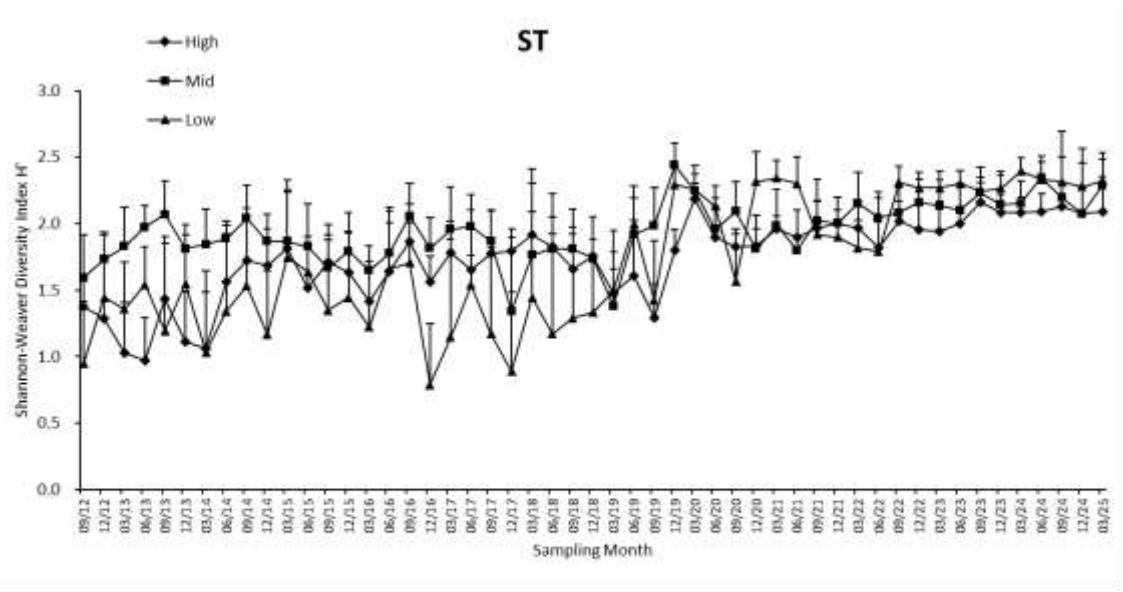

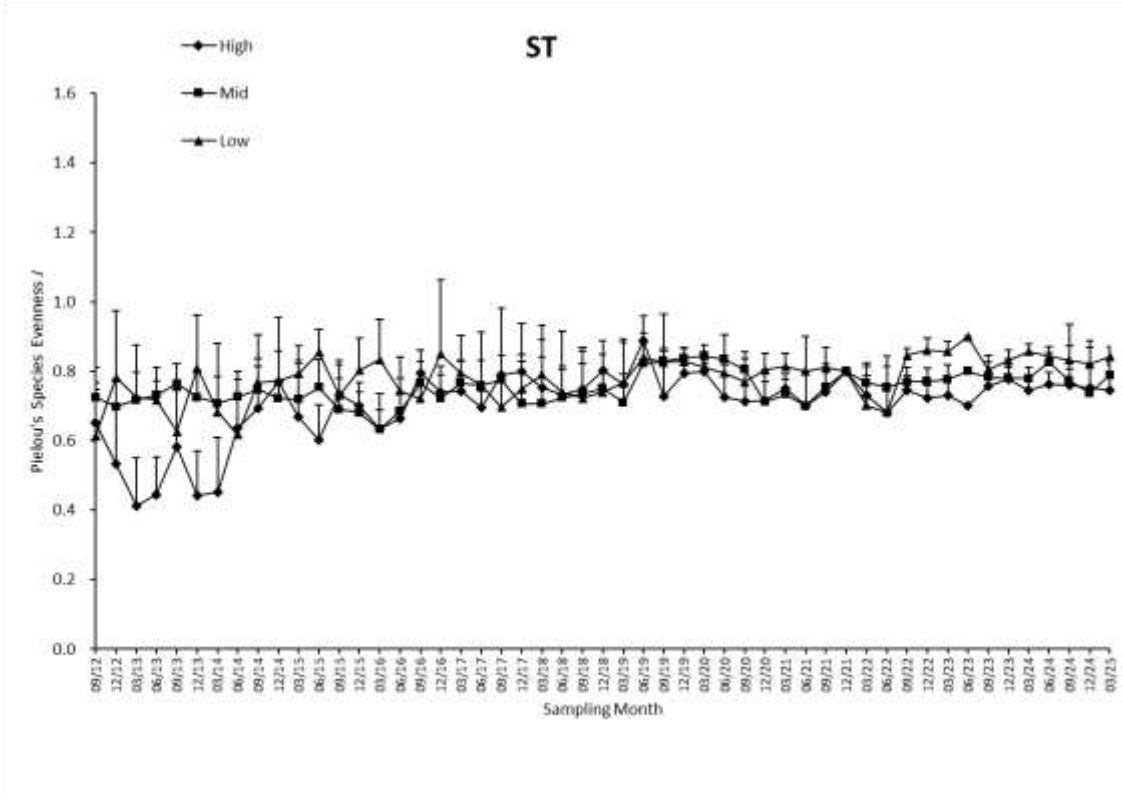

Figure 3.17(Cont'd) *Temporal changes of mean number of species, mean density, Shannon-Weaver Diversity Index (H') and Pielou's Species Evenness (J) (mean + SD) at every tidal level in sampling zone ST.*

4 REFERENCES

AFCD, 2018. Potamidid Snails in Hong Kong Mangrove. Agriculture, Fisheries and Conservation Department Newsletter - Hong Kong Biodiversity Issue #25, 2-11.

Chan, K.K., Caley, K.J., 2003. Sandy Shores, Hong Kong Field Guides 4. The Department of Ecology & Biodiversity, The University of Hong Kong. pp 117.

Dai, A.Y., Yang, S.L., 1991. Crabs of the China Seas. China Ocean Press. Beijing.

Dong, Y.M., 1991. Fauna of Zhe Jiang Crustacea. Zhejiang Science and Technology Publishing House. Zhejiang.

EPD, 1997.Technical Memorandum on Environmental Impact Assessment Process (1st edition). Environmental Protection Department, HKSAR Government.

Fauchald, K., 1977. The polychaete worms. Definitions and keys to the orders, families and genera. Natural History Museum of Los Angeles County, Science Series 28. Los Angeles, U.S.A.

Fong, C.W., 1998. Distribution of Hong Kong seagrasses. In: *Porcupine!* No. 18. The School of Biological Sciences, The University of Hong Kong, in collaboration with Kadoorie Farm & Botanic Garden Fauna Conservation Department, p10-12.

Li, H.Y., 2008. The Conservation of Horseshoe Crabs in Hong Kong. MPhil Thesis, City University of Hong Kong, pp 277.

Longstaff, B.J., Dennison, W.C., 1999. Seagrass survival during pulsed turbidity events: the effects of light deprivation on the seagrasses *Halodule pinifolia* and *Halophila ovalis*. Aquatic Botany 65 (1-4), 105-121.

Longstaff, B.J., Loneragan, N.R., O'Donohue, M.J., Dennison, W.C., 1999. Effects of light deprivation on the survival and recovery of the seagrass *Halophila ovalis* (R. Br.) Hook. Journal of Experimental Marine Biology and Ecology 234 (1), 1-27.

Nakaoka, M., Aioi, K., 1999.Growth of seagrass *Halophila ovalis* at dugong trails compared to existing within-patch variation in a Thailand intertidal flat. Marine Ecology Progress Series 184, 97-103.

Pielou, E.C., 1966. Shannon's formula as a measure of species diversity: its use and misuse. American Naturalist 100, 463-465.

Qi, Z.Y., 2004. Seashells of China. China Ocean Press. Beijing, China.

Qin, H., Chiu, H., Morton, B., 1998. Nursery beaches for Horseshoe Crabs in Hong Kong. In: *Porcupine!* No. 18. The School of Biological Sciences, The University of Hong Kong, in collaboration with Kadoorie Farm & Botanic Garden Fauna Conservation Department, p9-10.

Shannon, C.E., Weaver, W., 1963. The Mathematical Theory of Communication. Urbana: University of Illinois Press, USA.

Shin, P.K.S., Li, H.Y., Cheung, S.G., 2009.Horseshoe Crabs in Hong Kong: Current Population Status and Human Exploitation. Biology and Conservation of Horseshoe Crabs (part 2), 347-360.

Supanwanid, C., 1996. Recovery of the seagrass *Halophila ovalis* after grazing by dugong. In: Kuo, J., Philips, R.C., Walker, D.I., Kirkman, H. (eds), Seagrass biology: Proc Int workshop, Rottenest Island, Western Australia. Faculty of Science, The University of Western Australia, Nedlands, 315-318.

Vermaat, J.E., Agawin, N.S.R., Duarte, C.M., Fortes, M.D., Marba. N., Uri, J.S., 1995. Meadow maintenance, growth and productivity of a mixed Philippine seagrass bed. Marine Ecology Progress Series 124, 215-225.

Yang, D.J, Sun, R.P., 1988.Polychaetous annelids commonly seen from the Chinese waters (Chinese version).China Agriculture Press, China.

Annex I. Location of sampling zones (map from ATKINS China Ltd.)

Annex II *Record of horseshoe crab survey in every sampling zone.*

No.	Sub.	GPS coordinate	Ind. # / Prosomal width (mm)	Ind. # & Prosomal width (mm)
Sampling site TC1 (Search hour = 2 hrs)			*Carcinoscorpius rotundicauda*	*Tachypleus tridentatus*
		No record		
		No. of ind.		
Sampling site TC2 (Search hour = 2 hrs)			*Carcinoscorpius rotundicauda*	*Tachypleus tridentatus*
		No record		
		No. of ind.		
Sampling site TC3 (Search hour = 3 hrs)			*Carcinoscorpius rotundicauda*	*Tachypleus tridentatus*
1	M	22°17'00.3"N 113°55'42.4"E	0	.1 44
		No. of ind.	**0**	1
Sampling site ST (Search hour = 3 hrs)			*Carcinoscorpius rotundicauda*	*Tachypleus tridentatus*
1	M	22°17'13.9"N 113°55'33.4"E	0	1 62
2	M	22°17'12.8"N 113°55'33.4"E	0	1 46
3	M	22°17'12.8"N 113°55'33.4"E		1 54
		No. of ind.	**0**	3

Remark: Ind. #: number of Individuals (individuals in a group are shown in the same row)

Underlined: size of mating pair or large individual (excluded from data analysis)

Sub.: Substratum type; G = Gravel and Boulders, M = Soft mud, S = Sand

Annex III *Record of seagrass beds survey in every sampling zone.*

Estimated area (m^2)	Estimated coverage (%)	GPS coordinate	Remark
TC1& TC2 (search hour = 2 hrs)			
No record			
TC3 *Halophila ovalis* **(search hour = 3 hrs)**			
Disappeared / No record			
ST *Zostera Japonica* **(search hour = 3 hrs)**			
25	40-60	22°17'010"N 113°55'032"E	A horizontal strand of seagrass bed nearby the seaward side of mangrove area at tidal level 2.0 m above C.D.
ST *Halophila ovalis* **(search hour = 3 hrs)**			
Disappeared / No record			

Appendix IV. *Taxonomic resolution of every recorded species of intertidal soft shore community survey.*

Kingdom	Phylum	Class	Order	Family	Species
Animalia	Annelida	Polycheata	Phyllodocida	Nereididae	*Nereididae spp.*
Animalia	Annelida	Polycheata	Sabellida	Sabellidae	*Sabellidae imbricatus*
Animalia	Arthropoda	Malacostraca	Decapoda	Grapsidae	*Gaetice depressus*
Animalia	Arthropoda	Malacostraca	Decapoda	Grapsidae	*Metopograpsus latifrons*
Animalia	Arthropoda	Malacostraca	Decapoda	Grapsidae	*Metopograpsus quadridentatus*
Animalia	Arthropoda	Malacostraca	Decapoda	Paguridae	*Pagurus dubius*
Animalia	Arthropoda	Malacostraca	Decapoda	Varuniae	*Hemigrapsus penicillatus*
Animalia	Arthropoda	Maxillopoda	Sessilia	Balanidae	*Balanus amphitrite*
Animalia	Cnidaria	Anthozoa	Actiniaria	Diadumenidae	*Diadumene lineata*
Animalia	Mollusca	Bivalvia	Arcoida	Arcidae	*Barbatia virescens*
Animalia	Mollusca	Bivalvia	Mytioida	Mytilidae	*Brachidontes variabilis*
Animalia	Mollusca	Bivalvia	Mytioida	Mytilidae	*Xenostrobus atratus*
Animalia	Mollusca	Bivalvia	Ostreoida	Ostreidae	*Saccostrea cucullata*
Animalia	Mollusca	Bivalvia	Venerida	Veneridae	*Ruditapes philippinarum*
Animalia	Mollusca	Bivalvia	Venerida	Glauconomidae	*Glauconome chinensis*
Animalia	Mollusca	Bivalvia	Venerida	Veneridae	*Anomalocardia squamosa*
Animalia	Mollusca	Gastropoda	Archaeogastropoda	Trochidae	*Monodonta labio*
Animalia	Mollusca	Gastropoda	Archaeogastropoda	Turbinidae	*Lunella coronata*
Animalia	Mollusca	Gastropoda	Archaeogastropoda	Turbinidae	*Lunella granulata*
Animalia	Mollusca	Gastropoda	Caenogastropoda	Batillariidae	*Batillaria multiformis*
Animalia	Mollusca	Gastropoda	Caenogastropoda	Batillariidae	*Batillaria zonalis*
Animalia	Mollusca	Gastropoda	Caenogastropoda	Potamididae	*Pirenella asiatica*
Animalia	Mollusca	Gastropoda	Caenogastropoda	Potamididae	*Pirenella incisa*
Animalia	Mollusca	Gastropoda	Cycloneritimorpha	Neritidae	*Clithon faba*
Animalia	Mollusca	Gastropoda	Cycloneritimorpha	Neritidae	*Clithon retropictus*
Animalia	Mollusca	Gastropoda	Cycloneritimorpha	Neritidae	*Nerita chamaeleon*
Animalia	Mollusca	Gastropoda	Cycloneritimorpha	Neritidae	*Nerita lineata*
Animalia	Mollusca	Gastropoda	Cycloneritimorpha	Neritidae	*Nerita polita*
Animalia	Mollusca	Gastropoda	Cycloneritimorpha	Neritidae	*Nerita squamulata*
Animalia	Mollusca	Gastropoda	Littorinimorpha	Littorinidae	*Littoraria articulata*
Animalia	Mollusca	Gastropoda	Neogastropoda	Muricidae	*Thais clavigera*
Animalia	Mollusca	Gastropoda	Neotaenioglossa	Littorinidae	*Nodilittorina radiata*

Animalia	Mollusca	Gastropoda	Patellogastropoda	Lottiidae	*Lottia dorsuosa*
Animalia	Mollusca	Gastropoda	Patellogastropoda	Lottiidae	*Lottia luchuana*
Animalia	Mollusca	Gastropoda	Patellogastropoda	Lottiidae	*Nipponacmea concinna*
Animalia	Mollusca	Gastropoda	Trochida	Tegulidae	*Chlorostoma argyrostomum*
Animalia	Mollusca	Gastropoda		Lottiidae	*Patelloida pygmaea*
Animalia	Mollusca	Polyplacophora	Chitonida	Ischnochitonidae	*Lepidozona spp.*
Animalia	Nemertea				*Nemertea spp.*
Animalia	Platyhelminthes				*Platyhelminthes sp.*
Animalia	Sipuncula	Sipunculidae	Golfingiida	Sipunculidae	*Siphonosoma sp.*
Animalia	Sipuncula	Sipunculidae	Golfingiida	Sipunculidae	*Sipunculus nudus*

Annex V. *List of recorded fauna of intertidal soft shore community survey in every sampling zone time*

Mar 2025 Sampling Zone TC1 High tidal level (2.0 m above C.D.)

Gp	Taxon	1		2		3		4		5		6		7		8		9		10		Sub-total
		Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	
Ba	*Balanus amphitrite*			3		2						1	1			1		1		0		9
Bi	*Barbatia virescens*	0				2	1	0	1	2		0		1		3	1					11
Bi	*Brachidontes variabilis*	1		0		1	1					2						0		2		7
Bi	*Glauconome chinensis*	0				2		0		0		2		1	1	1				0		7
Bi	*Saccostrea cucullata*	24		30		24		30		28		26		21		26		33		23		265
Bi	*Xenostrobus atratus*	0						0		2	1	1		2		2				1		9
C	*Gaetice depressus*	1				3	1	2		2		2		0		1				2		14
C	*Metopograpsus latifrons*	1				3				2		3	1	0		3				0		13
C	*Pagurus dubius*	3		0		0				3		1		1		0		0				8
G	*Batillaria multiformis*			1		2		3				2		3		2		3		0		16
G	*Batillaria zonalis*	1		3	1	1		2				0				2	1	1	1	1		14
Cn	*Diadumene lineata*	1		0				1						3		3		0		1	1	10
G	*Cellana toreuma*			2					1	2		3	1	2				1		0		12
G	*Chlorostoma argyrostomum*	0		3		1		0		4				1	1	2		1	1	0		14
G	*Clithon faba*	1		1		2		1		3	1	0		2		0		1		1	1	14

G	*Littoraria articulata*	0			2		0		2		2		1	1	2	1			0			11									
G	*Lottia dorsuosa*	0					0		0	1	2	1	0		1				0			5									
G	*Lottia luchuana*	1		1	1		3		1						1	1	1		1	1		12									
G	*Lunella coronata*			1	0			1	3		1		0		3	1	2		0			12									
G	*Lunella granulata*	1		1			1		0		0		1		0		1					5									
G	*Monodonta labio*	1 1		1 1	1 7		1 4		1 9		1 3		1 2		13		14		16			140									
G	*Nipponacmea concinna*	2		2	1	1	2	1	0		3		1		1		3		2			19									
G	*Nodilittorina radiata*	1		1			2		1	1			0				1		0			7									
G	*Patelloida pygmaea*	2		1									2		2		2					9									
P	*Nereididae spp.*	0					2		2		2				0	1						7									
G	*Pirenella asiatica*	2	1	0	4			1	1		0		0		2		0		0			11									
P	*Sabellidae imbricatus*			0		1			1				0		1		0		0	1		4									
Po	*Lepidozona spp.*	2		1	2		2				1	1	2		0		2		0			13									
Sp	*Siphonosoma sp.*	1							0		0		1						1			3									
																					Total	**681**									

Key for faunal groups (Gp):

Ba: Barnacle, Bi: Bivalve, C: Crab, Cn: Cnidarin, Eh: Echiuran, F: Fish, G: Gastropod, Hc: Hermit crab, Ne: Nemertean, Ol: Oligochaete,

P: Polychaete, Pl: Platyhelminthes, Po: Polyplacophores, S: Shrimp, Sc: Scaphopods, Sp: Sipunculan

Annex V (Cont'd). *List of recorded fauna of intertidal soft shore community survey in every sampling zone*

Mar 2025	Sampling Zone TC1	Mid tidal level (1.5 m above C.D.)																				
		1		2		3		4		5		6		7		8		9		10		
Gp	Taxon	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Sub-total
Ba	*Balanus amphitrite*	0		1		1		1		0		1		1		1		0		0		6
Bi	*Barbatia virescens*		1	0		0		0				0				0						1
Bi	*Brachidontes variabilis*	0		1		1		1		0	1	1				2		0		0	1	8
Bi	*Glauconome chinensis*					2		2		0		2		1		1						8
Bi	*Saccostrea cucullata*	14		26		15		19		23		23		17		26		18		16		197
Bi	*Xenostrobus atratus*	1								1								0		1		3
C	*Gaetice depressus*	1	2	2	1	2		2		1		1		1		2	1	1		2		19
C	*Hemigrapsus penicillatus*	0		1	2		1	1	2	0		1	1	0		1				0		10
C	*Metopograpsus latifrons*	1		0		0		0		2		1		1		0		2		0		7
G	*Batillaria multiformis*	0			1					0								0	1	3		5
G	*Batillaria zonalis*	5		7		11		11		10	1	11		6		7		4		7		80
G	*Chlorostoma argyrostomum*	2	1							2		1		0				1		0	1	8
G	*Clithon faba*	1		1		0	1	0	1	1		0	1			1	1	2		2		12
G	*Clithon retropictus*	1				1		1		2	1					3		2				11
G	*Littoraria articulata*			2		0		0						2		2				0		6
G	*Lottia dorsuosa*	0				1		1		0	1	2		1		2		2		1	1	12
G	*Lunella coronata*	0		3			1	1		0	1	2	1	1		1		1		2		14

G	*Lunella granulata*	2		0		3		0		3		0				0		1		1		10			
G	*Monodonta labio*	7		11		15		13		15		14		12		10		10		12		119			
G	*Nerita squamulata*	0		0		0		0		0		2		3		0						5			
G	*Nipponacmea concinna*	6		0		2		0		5		0				0				2		15			
G	*Nodilittorina radiata*			2		0		0				3				0						5			
G	*Patelloida pygmaea*	1				1		1		2				1	1	3		1	1			12			
G	*Pirenella asiatica*			2								0		2				1		1		6			
P	*Nereididae spp.*	1					1		1	2		2	1	0			1	0		2		11			
Po	*Lepidozona spp.*			2		0		0						0		0		1	1	0		4			
Sp	*Siphonosoma sp.*	0		0		0		0		0		3				0		2		2		7			
Sp	*Sipunculus nudus*	1	1	1		1		1		1		1			1	1		1		1	1	12			
																				Total		**613**			

Key for faunal groups (Gp):

Ba: Barnacle, Bi: Bivalve, C: Crab, Cn: Cnidarin, Eh: Echiuran, F: Fish, G: Gastropod, Hc: Hermit crab, Ne: Nemertean, Ol: Oligochaete,

P: Polychaete, Pl: Platyhelminthes, Po: Polyplacophores, S: Shrimp, Sc: Scaphopods, Sp: Sipunculan

Annex V (Cont'd). *List of recorded fauna of intertidal soft shore community survey in every sampling zone*

Mar 2025	Sampling Zone TC1	Low tidal level (0.5 m above C.D.)																				
		1		2		3		4		5		6		7		8		9		10		
Gp	Taxon	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Sub-total
Ba	*Balanus amphitrite*			0		1				2		0		2		1		2		1		9
Bi	*Barbatia virescens*	1 1		1 2	1	3		1 0	1	1 3		7		8		12		9		4		91
Bi	*Anomalocardiasquamosa*	0		3		2		0		1	2	2		1		1		1				13
Bi	*Brachidontes variabilis*			0		2										0						2
Bi	*Glauconome chinensis*	2				1						2										5
Bi	*Saccostrea cucullata*					0				1	2	2		1				3		1	1	11
Bi	*Xenostrobus atratus*			2				1								1		1				5
C	*Gaetice depressus*			3		1				0				0		1		0				5
C	*Hemigrapsus penicillatus*	0	2			0				0		1		0		1		0		2		6
C	*Metopograpsus latifrons*					1		1														2
C	*Pagurus dubius*	2		2		2	1	2		1	1	0		1		3		1		0		16
Cn	*Diadumene lineata*			3		0		0		2		1		2		0		2		1		11
G	*Batillaria multiformis*	1 1		1 4		1 1		1 1		1 0		6		1 0		11		11		8		103
G	*Batillaria zonalis*											1				1				1		3
G	*Chlorostoma argyrostomum*	1		0	2	1		1	2	0		2		0				0		3		12

G	*Clithon retropictus*					0		1		1				1	1	2		1															7
G	*Littoraria articulata*	3				1				1		4																					9
G	*Lottia dorsuosa*											0				0				0													0
G	*Lottia luchuana*	1		0				0						4				2															7
G	*Lunella coronata*	2		3		1	2	3		1	2																						14
G	*Lunella granulata*	0		1	1			1	1				1	1				1			1												8
G	*Monodonta labio*			2	2	1		2	2	1				0		0		0															10
G	*Nerita lineata*	1		1		0		1		0				1		0																	4
G	*Nerita polita*	2		0				0																									2
G	*Nerita squamulata*	0	1	2		1		2		1		1		2		1		1		2													14
G	*Nipponacmea concinna*					1				1				0		1	1	1															5
G	*Nodilittorina radiata*	8		1 1	1	9		1 1	1	9		7		8		11		11		7													94
P	*Nereididae spp.*	0		1		2		1		2		0				0				0													6
P	*Sabellidae imbricatus*	2				1				1		2		0		2		0		2													10
Po	*Lepidozona spp.*	1		0		0		0		0		0		1		0		1		1													4
Sp	*Siphonosoma sp.*			1	1	0		1	1	0		0				*1*				*0*													5
Sp	*Sipunculus nudus*	*0*		0				0				0				*0*				*0*													0
																				Total													**493**

Key for faunal groups (Gp):

Ba: Barnacle, Bi: Bivalve, C: Crab, Cn: Cnidarin, Eh: Echiuran, F: Fish, G: Gastropod, Hc: Hermit crab, Ne: Nemertean, Ol: Oligochaete, P: Polychaete, Pl: Platyhelminthes, Po: Polyplacophores, S: Shrimp, Sc: Scaphopods, Sp: Sipunculan

Annex V (Cont'd). *List of recorded fauna of intertidal soft shore community survey in every sampling zone*

Mar 2025	Sampling Zone TC2	High tidal level (2.0 m above C.D.)																				
		1		2		3		4		5		6		7		8		9		10		
Gp	Taxon	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Sub-total
Ba	*Balanus amphitrite*									0				0				0		1		1
Bi	*Barbatia virescens*		1						1	1				1								4
Bi	*Brachidontes variabilis*		1			2														2		5
Bi	*Glauconome chinensis*	0		0		1		1		2		2		2		0		2		1		11
Bi	*Saccostrea cucullata*	28		31		26		30		28		21		22		24		17		15		242
Bi	*Xenostrobus atratus*	3		1		1		3	1	1		1		1	1	3		2		2		20
C	*Gaetice depressus*	0		2	1	0										0				0		3
C	*Hemigrapsus penicillatus*	2	1			0						1		1		1			1	2		9
C	*Metopograpsus latifrons*	1						1			1		1	2								6
C	*Metopograpsus quadridentatus*			1		0		2		3		0		3			2	1		0		12
Cn	*Diadumene lineata*	1		3		0						0			1	3				1		9
G	*Batillaria multiformis*	13		14	0	5		15		13	1	9		10		7		7		5	1	100
G	*Batillaria zonalis*					0		2		2		1		2				0		0		7
G	*Chlorostoma argyrostomum*	1		0				3		1			1			1		1				8
G	*Clithon retropictus*	0		1		0		2		3		0			1	0	1	1		0		9
G	*Littoraria articulata*					1			1	2		1		2				2		1		10
G	*Lottia dorsuosa*	0			1			1		2				0		0		1				5

| | | |

Annex V (Cont'd). *List of recorded fauna of intertidal soft shore community survey in every sampling zone*

Mar 2025 Sampling Zone TC2 Mid tidal level (1.5 m above C.D.)

Gp	Taxon	1		2		3		4		5		6		7		8		9		10		Sub-total
		Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	
Ba	*Balanus amphitrite*	1		3				0		0				2						0		6
Bi	*Barbatia virescens*			2		1		2		2		1		2		2		1				13
Bi	*Brachidontes variabilis*	3	1	1		2		1				2		3		2		3				18
Bi	*Glauconome chinensis*			3		1		0	1		1	1		0		1		2		2		12
Bi	*Saccostrea cucullata*	20		21	1	20		25		16		14		14		16		21		22		190
Bi	*Xenostrobus atratus*	0	1			2		2				1		2		2		2		0		12
C	*Gaetice depressus*	2		1		1				2		1		1	1	1	1	0		2		13
C	*Metopograpsus latifrons*			1		2		3	2	0				0								8
C	*Pagurus dubius*			0		0				0			1					0				1
Cn	*Diadumene lineata*	1		0		0		1		1				1				0		1		5
G	*Batillaria multiformis*	1		2		5		2		8		1		3		1		6		1		30
G	*Batillaria zonalis*	11		6		7		7		8		10		5		8		10		11	1	84
G	*Clithon faba*	2		1		2		2		0		0		1		5		2		2		17
G	*Clithon retropictus*	1		1		0		0		2		1				2		3		1		11
G	*Littoraria articulata*	3								1		0		1		0		1		3		9
G	*Lottia dorsuosa*	0		3		3				1		1				1		0		0		9

G	*Lunella coronata*	1				1		1						2			2		1		8
G	*Lunella granulata*	0		1						1		1				1		0		0	4
G	*Monodonta labio*	12	1	6		8		8	1	7		7		9		14		15		10	1	99
G	*Nipponacmea concinna*	0		0		0		2		2		2	1	0		2		0		0	9
G	*Nodilittorina radiata*			2	1	3				1		1		3		1				5	17
G	*Patelloida pygmaea*			1		1		0				1		0		2			1		6
G	*Pirenella incisa*	2						1	1	3	1	1		1		0				2	12
Ne	*Nemertea spp.*			1		2		2		0		0				0		1			6
Po	*Lepidozona spp.*	1						0		0		0		1		0		0		1	3
Sp	*Sipunculus nudus*	0		0		0		2						1				0		0	3
																				Total	**605**

Key for faunal groups (Gp):

Ba: Barnacle, Bi: Bivalve, C: Crab, Cn: Cnidarin, Eh: Echiuran, F: Fish, G: Gastropod, Hc: Hermit crab, Ne: Nemertean, Ol: Oligochaete,

P: Polychaete, Pl: Platyhelminthes, Po: Polyplacophores, S: Shrimp, Sc: Scaphopods, Sp: Sipunculan

Annex V (Cont'd). *List of recorded fauna of intertidal soft shore community survey in every sampling zone*

Mar 2025 Sampling Zone TC2 Low tidal level (0.5 m above C.D.)

Gp	Taxon	1		2		3		4		5		6		7		8		9		10		Sub-total
		Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	
Ba	*Balanus amphitrite*	0		2		1		0		2		2		0				0		3		10
Bi	*Anomalocardia squamosa*	1						2	1					2	1			1				8
Bi	*Barbatia virescens*	16		8		9		11	2	12		10		12	1	9		10		9		109
Bi	*Brachidontes variabilis*	0		2								0		2					1			5
Bi	*Glauconome chinensis*	3		3		0	1					3		1		1				1		13
Bi	*Isognomon isognomum*			1		2		3		1						3		0		3		13
Bi	*Saccostrea cucullata*	1						0				1		2		0				0		4
Bi	*Xenostrobus atratus*	3	1	0		2	1	1		0		1	1			2		1		2		15
C	*Gaetice depressus*			2				2		2				1					1			8
C	*Hemigrapsus penicillatus*				1	1		2						0			2	2	1	1		10
C	*Metopograpsus latifrons*			3		0				2								1				6
C	*Pagurus dubius*	3		0		2			1	0		3	1	1		1	1	2		2		17
Cn	*Diadumene lineata*	0		2				1		2		0		0	1							6
G	*Batillaria multiformis*	10		6		8		7		8		10		10		5		6		8		78
G	*Batillaria zonalis*	6		4		3		1		3		1				5				5		28
G	*Clithon retropictus*			0		2		0		2		0		0		2		2		2		10

G	*Littoraria articulata*	1	1		3	0		3	0	1	1	2	1		2		15
G	*Lottia dorsuosa*			1	3	2		3	2		0	1			1	1	14
G	*Lunella coronata*			3	0	1		0	0		3	1			2		10
G	*Lunella granulata*	2		1	6	5	1	6			2	1	1	8	5		38
G	*Monodonta labio*			2					0		3	1				1	7
G	*Nipponacmea concinna*	0			0	0		0	1		0	0		0	2		3
G	*Nodilittorina radiata*	1		3		3			3			2		2			14
G	*Patelloida pygmaea*			1	3			3			0	1					8
G	*Pirenella incisa*	1		1	2	1		2	2		1			0	1		11
Po	*Lepidozona spp.*	2		0					2		0	1		1	0		6
Sp	*Siphonosoma sp.*				0	2		0	0		1	1				1	5
Sp	*Sipunculus nudus*	1		0	1	0		1			1	1		1	0		6
															Total		**477**

Key for faunal groups (Gp):

Ba: Barnacle, Bi: Bivalve, C: Crab, Cn: Cnidarin, Eh: Echiuran, F: Fish, G: Gastropod, Hc: Hermit crab, Ne: Nemertean, Ol: Oligochaete,

P: Polychaete, Pl: Platyhelminthes, Po: Polyplacophores, S: Shrimp, Sc: Scaphopods, Sp: Sipunculan

Annex V (Cont'd). *List of recorded fauna of intertidal soft shore community survey in every sampling zone*

Mar 2025 Sampling Zone TC3 High tidal level (2.0 m above C.D.)

Gp	Taxon	1		2		3		4		5		6		7		8		9		10		Sub-total
		Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	
Bi	*Barbatia virescens*			2		0				3		3				3		0		3		12
Bi	*Brachidontes variabilis*	0						0								2				2		3
Bi	*Glauconome chinensis*	0		1		1		0		1		1				1		1		3		11
Bi	*Saccostrea cucullata*	33		30	2	25		26		25		27		31		31		20		29	2	277
Bi	*Xenostrobus atratus*	0		2		2		3		0		3		3		1		0		1		14
C	*Gaetice depressus*	0	1	2	2	1		2		0		2		1		1		0		2	1	10
C	*Metopograpsus latifrons*			5	1					3						2		1				12
C	*Pagurus dubius*	0		2				0				0				1		3				4
G	*Batillaria multiformis*	1		2		0	1	2		2		2		0			1	0	1	2		13
G	*Batillaria zonalis*	0	1	0	2					3						0					2	6
G	*Clithon oualaniensis*	1						1				1								3		6
G	*Clithon retropictus*	1		1						3		2						0				10
G	*Littoraria articulata*	1		1		3	2	1	1	1		3		3			1	2	1	2		20
G	*Lunella coronata*	1		5		1				2				1		3		3		2		18

G	*Lunella granulata*	1		1		2		1				1		2							10
G	*Monodonta labio*	26		11	1	12		9		14		11		15		17		14		16	155
G	*Nerita chamaeleon*			0				0		3		0				0					4
G	*Nerita polita*			2		4		2				3		3		2				3	15
G	*Nerita squamulata*									2		2				1		4		3	17
G	*Nipponacmea concinna*									2						2		2			8
G	*Nodilittorina radiata*	1		1				1		1		1		1		2				2	14
G	*Patelloida pygmaea*				1					1				1						3	7
G	*Pirenella incisa*	4		3		0		4		3		1		3		4		0		4	17
G	*Thais clavigera*					1				0								1			3
P	*Nereididae spp.*					2								1			2	2		2	13
P	*Perinereis sp.*			0						3		0		3						2	13
P	*Sabellidae imbricatus*	1		0		2		1		0		0		0		1		1		0	13
Pl	*Platyhelminthes*	3		0	1			3		0		0	1	3		3				0	1 13
																				Total	**718**

Key for faunal groups (Gp):

Ba: Barnacle, Bi: Bivalve, C: Crab, Cn: Cnidarin, Eh: Echiuran, F: Fish, G: Gastropod, Hc: Hermit crab, Ne: Nemertean, Ol: Oligochaete,

P: Polychaete, Pl: Platyhelminthes, Po: Polyplacophores, S: Shrimp, Sc: Scaphopods, Sp: Sipunculan

Annex V (Cont'd). *List of recorded fauna of intertidal soft shore community survey in every sampling zone*

Mar 2025 Sampling Zone TC3 Mid tidal level (1.5 m above C.D.)

Gp	Taxon	1		2		3		4		5		6		7		8		9		10		Sub-total
		Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	
Ba	*Balanus amphitrite*	1		0		0		1		0		0		0		0		0				2
Bi	*Barbatia virescens*							2		0										1		3
Bi	*Brachidontes variabilis*			0				0		1		0				0						1
Bi	*Glauconome chinensis*	3		2				1		2		3	1	3		2		1		2		20
Bi	*Saccostrea cucullata*	30		35		18		19		22		26		28		24		28		26		256
Bi	*Xenostrobus atratus*	3		1		3				2				1		1		3		0		14
C	*Gaetice depressus*	2				1				0	1	2						1		1		8
C	*Metopograpsus latifrons*	2		2		2		0		3				2	1	2		2	1			17
G	*Batillaria multiformis*			6						1		1				6						14
G	*Batillaria zonalis*	2				2			1	2		1	1	2				2		5		18
G	*Clithon faba*			1	1		1	0		2						5		1				11
G	*Clithon oualaniense*	1			1	2						0		0				2				6
G	*Clithon retropictus*									2		2										4
G	*Littoraria articulata*	2				2		1		1	1	1						2		1		11
G	*Lottia dorsuosa*	0				0				2		2		3	1			0		0		8

G	*Lunella coronata*	1	0	1		0	2	0		1		0	1				6
G	*Lunella granulata*	1	4	1		5	1					4	1		3		20
G	*Monodonta labio*	20	5	15		7	11	14	1	15		12	14		13		127
G	*Nerita chamaeleon*		1	1		0	2			1		1	2		1		9
G	*Nerita lineata*	0	1			0		2		2	1	1			2		9
G	*Nerita polita*			1		1	2						1	1	0		6
G	*Nerita squamulata*		1	2						1		1	3		2		10
G	*Nipponacmea concinna*	2	1			2	0			1		0			0		6
G	*Nodilittorina radiata*	1	1	3		1	1	1		2		2	1		2		15
G	*Patelloida pygmaea*		3			1	0			0		3			3		10
G	*Pirenella asiatica*	1		0	2	1	1	0					0				5
G	*Pirenella incisa*	0	1	0		0	2	1	1			1	0		2		8
Ne	*Nemertea spp.*		1	1			0			0		1	3				6
P	*Sabellidae imbricatus*					0	0	1		0							1
Po	*Lepidozona spp.*		3	1		0	0	1		2	1	3	1				12
Sp	*Siphonosoma sp.*		1			1					1	1			2		6
Sp	*Sipunculus nudus*	2		3		1		2		2			3		2		15
															Total		**664**

Key for faunal groups (Gp):

Ba: Barnacle, Bi: Bivalve, C: Crab, Cn: Cnidarin, Eh: Echiuran, F: Fish, G: Gastropod, Hc: Hermit crab, Ne: Nemertean, Ol: Oligochaete,

P: Polychaete, Pl: Platyhelminthes, Po: Polyplacophores, S: Shrimp, Sc: Scaphopods, Sp: Sipunculan

Annex V (Cont'd). *List of recorded fauna of intertidal soft shore community survey in every sampling zone*

Mar 2025 Sampling Zone TC3 Low tidal level (0.5 m above C.D.)

Gp	Taxon	1		2		3		4		5		6		7		8		9		10		Sub-total
		Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	
Ba	Balanus amphitrite	0		1				0				1		0		2				3		7
Bi	Barbatia virescens	12		11		15		11		10		13		15		17		19		22		145
Bi	Anomalocardia squamosa	0				1		1		0				3		0		1		0		6
Bi	Ruditapes philippinarum	2		0		2		2		2		0										8
Bi	Brachidontes variabilis			1		3		3				0		0		0				0		7
Bi	Glauconome chinensis	0		1	1	0		0		0		3		2				0				7
Bi	Saccostrea cucullata			1		1		1				2				0		0		0		5
Bi	Xenostrobus atratus	0				1		1		0		2		2		0		1		0		7
C	Gaetice depressus	1		0		1	1	1		1		0		0		2		1		1		9
C	Metopograpsus latifrons	0		0		1		1		2	1	0		1		1	1	1		0		9
C	Pagurus dubius	8		6		6		5		12		6		12		11		10		6		82
G	Batillaria multiformis	7		5		2		2		7		5		2		3		4		4		41
G	Batillaria zonalis	0		2		0		0		0		2				0		1		0	1	6
G	Clithon oualaniensis			1		3		3						2		1				3		13
G	Littoraria articulata	1		1		2	1	2		1		1		2				2		0		13
G	Lottia dorsuosa	0		2	1	0		0		0		1		0		0		3		1		8

G	Lunella coronata	6		11	1	10		10		9		12		6		6		9		5		85
G	Lunella granulata	1	1	1		1		4		8		5		2	1	4		4	1	6		39
G	Monodonta labio	1		2		0	1	1		0	2	0				0		0		3		10
G	Nipponacmea concinna	1		3				1				3		0				1				9
G	Patelloida pygmaea	1		1		2		1		2		2				2				2		13
G	Pirenella incisa	2				0	1	2		0						0		1				6
P	Nereididae spp.			2		0				2	1	2		0		0	1	2		1		11
P	Sabellidae imbricatus	0		0		1		0		1		0		2		1		0				5
Sp	Siphonosoma sp.	1				0	1	1		0	1	3		1		0	1	3		3		15
Sp	*Sipunculus nudus*	1		3		2		1	1	2		3		1	1	2		3		2		22
																				Total		**588**

Key for faunal groups (Gp):

Ba: Barnacle, Bi: Bivalve, C: Crab, Cn: Cnidarin, Eh: Echiuran, F: Fish, G: Gastropod, Hc: Hermit crab, Ne: Nemertean, Ol: Oligochaete, P: Polychaete, Pl: Platyhelminthes, Po: Polyplacophores, S: Shrimp, Sc: Scaphopods, Sp: Sipunculan

Annex V (Cont'd). *List of recorded fauna of intertidal soft shore community survey in every sampling zone*

Mar 2025	Sampling Zone ST	High tidal level (2.0 m above C.D.)

Gp	Taxon	1		2		3		4		5		6		7		8		9		10		Sub-total
		Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	
Ba	*Balanus amphitrite*	1		0		1		0		1		0		1		1		0				5
Bi	*Barbatia virescens*			2			1	1		1		1				1				0		7
Bi	*Brachidontes variabilis*			0						1										0		1
Bi	*Glauconome chinensis*	2		1		3		1				1		3		2		2		1		16
Bi	*Saccostrea cucullata*	27		33		25		28		32		25		25		26		0		18		239
Bi	*Xenostrobus atratus*	2		0		0		0		0		2		0		0		27		0		31
C	*Gaetice depressus*	0		0		0		0		3				0		3		2		2		10
C	*Metopograpsus latifrons*			0			1		1	2				0			1			2		7
C	*Pagurus dubius*			2		3		3		1				1				0		2		12
Cn	*Diadumene lineata*	2		1		0		0				2	1	1		2		1		1		11
G	*Batillaria multiformis*	11		14		8		9		9		3		8		11		9		14		96
G	*Batillaria zonalis*	2				0		0		3		3				0						8
G	*Cellana toreuma*			2		3		1		2				2		2				2		14
G	*Clithon faba*	0				0		0		0		1		1		2		0		2		6

G	*Clithon retropictus*			0		0		0			3		0	1			1	1	0			6	
G	*Littoraria articulata*			1		0		0					1		0				3			5	
G	*Lottia dorsuosa*	1	1			2	1	2									1			1		9	
G	*Lunella coronata*	2				3		3	2		3								2			15	
G	*Lunella granulata*			2		0		0	0		0						1					3	
G	*Monodonta labio*	14		17		9		11	15		16		14		13				21			130	
G	*Nerita chamaeleon*	0		0		0		0			2		2		1		11		2			18	
G	*Nerita polita*	1		1	1	2		2	2				3		0		0		2			14	
G	*Nipponacmea concinna*	3		3		2		2	0		0		2		2		2		2			18	
G	*Nodilittorina radiata*	1		1	1	1	1	1			0		2						2			10	
G	*Patelloida pygmaea*					2		2	1						3		3					11	
G	*Pirenella incisa*	0		0		2		2	1		0				2		2		3			12	
P	*Sabellidae imbricatus*	2		2		2		1	0		1				0		0					8	
Po	*Lepidozona spp.*			0				0			0		0		2		2		0			4	
Sp	*Sipunculus nudus*			3				0	2		0		3		3		3		3			17	
Sp	*Siphonosoma sp.*	0		3		0		1	2		1		3		1		1		3			15	
																			Total			**758**	

Key for faunal groups (Gp):

Ba: Barnacle, Bi: Bivalve, C: Crab, Cn: Cnidarin, Eh: Echiuran, F: Fish, G: Gastropod, Hc: Hermit crab, Ne: Nemertean, Ol: Oligochaete, P: Polychaete, Pl: Platyhelminthes, Po: Polyplacophores, S: Shrimp, Sc: Scaphopods, Sp: Sipunculan

Annex V (Cont'd). *List of recorded fauna of intertidal soft shore community survey in every sampling zone*

Mar 2025	Sampling Zone ST	Mid tidal level (1.5 m above C.D.)																				
		1		2		3		4		5		6		7		8		9		10		
Gp	Taxon	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Sub-total
Bi	*Barbatia virescens*	2				1		1		1		1		2				1		2		11
Bi	*Glauconome chinensis*	0				0	1	0		1		0						0		2		4
Bi	*Brachidontes variabilis*	0		3		2				3		2				3		2		0		15
Bi	*Saccostrea cucullata*	18	1	25		23		21		21		18		17		24		21		22		211
Bi	*Xenostrobus atratus*	0	1	3	1	0		2		1		0		1		3		0		0		12
C	*Gaetice depressus*	2		1		2		4		2		2				1		1		2		17
C	*Metopograpsus latifrons*	2				1						2						2				7
C	*Pagurus dubius*	3				3		2				3			1		1			1		14
G	*Batillaria multiformis*		1	2						2		3		7		1				1		17
G	*Batillaria zonalis*			0		1						1				0		2		2		6
G	*Chlorostoma argyrostomum*	0		2	1	0		1		1	1	3		3	1	2		0		0	2	17
G	*Clithon faba*	0		1		2		2		0		1				2		0		0		8
G	*Clithon oualaniense*				1			1	1	2		2										7
G	*Clithon retropictus*	1		0		1		1		1		0		1		0		2		0		7
G	*Littoraria articulata*	3				3		2		2		0		2				0		0		12

| | | |

Annex V (Cont'd). *List of recorded fauna of intertidal soft shore community survey in every sampling zone*

Mar 2025 Sampling Zone ST Low tidal level (0.5 m above C.D.)

Gp	Taxon	1		2		3		4		5		6		7		8		9		10		Sub-total
		Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	Q	C	
Ba	*Balanus amphitrite*	1		1		1						1		2				1		1		8
Bi	*Anomalocardia squamosa*	3		1		0		2		0		2						1		3		12
Bi	*Barbatia virescens*	7		1						7		7		7				4		7		40
Bi	*Brachidontes variabilis*					1		1		2						1		2				7
Bi	*Glauconome chinensis*	0		1		3				1		0		1				1		0		7
Bi	*Saccostrea cucullata*	2		3		1		1		0	1	4		2				4		2		20
Bi	*Xenostrobus atratus*			0		0		0		2				1				0				3
C	*Gaetice depressus*	1								1		0				0		1		1		4
C	*Hemigrapsus penicillatus*	0		0			1					2		2		2			1	0		8
C	*Metopograpsus latifrons*			1		1		2		2				0								6
C	*Metopograpsus quadridentatus*	0		3				1				0				0				0		4
Cn	*Diadumene lineata*	0		2		2		2		1		1				0				0		8
G	*Batillaria multiformis*			2				3				1				1		2				9
G	*Batillaria zonalis*	14		11		16		16		14		13		11		14		14		14		137
G	*Chlorostoma argyrostomum*					1		1		0		2		1		2	1	1				9

G	*Clithon faba*	3			3		3		3		2		0		1		0		3		18
G	*Lottia dorsuosa*							1			1		2								4
G	*Lunella coronata*	0		2		1		1		2	2	1		2		2	0		0		13
G	*Lunella granulata*	2		2		1		2		1		1		1		1	4	2	5		22
G	*Monodonta labio*	12		8		11	1	8		7		9		14		5	7		12		94
G	*Nerita lineata*	3		3		3		0		3		3		1		0			3		19
G	*Nerita squamulata*			3		3		0		0				2		0					8
G	*Nipponacmea concinna*	2						1				2							2		7
G	*Nodilittorina radiata*			1		1		1						4							7
G	*Patelloida pygmaea*	1										1					1		1	1	5
G	*Pirenella incisa*	1		0		0				0		1					1		1		4
Ne	*Nemertea spp.*	2						0		2		2				0			2		8
P	*Sabellidae imbricatus*											3		0			1				4
Po	*Lepidozona spp.*							1		0				3							4
Sp	*Siphonosoma sp.*							2		3				1		2	0				8
Sp	*Sipunculus nudus*	0		0		0		0		1		0		3		0	1		0		5
																			Total		**512**

Key for faunal groups (Gp):

Ba: Barnacle, Bi: Bivalve, C: Crab, Cn: Cnidarin, Eh: Echiuran, F: Fish, G: Gastropod, Hc: Hermit crab, Ne: Nemertean, Ol: Oligochaete,

P: Polychaete, Pl: Platyhelminthes, Po: Polyplacophores, S: Shrimp, Sc: Scaphopods, Sp: Sipunculan

End of the report
