Activity ID	Activity Name	Orig Dur	Planned Start	Planned Finish	Current Start	Current Finish
TMCLK - Northern Connection Sub-Sea Tunnel Section		311	25-Oct-13	30-Sep-14	25-Oct-13A	14-Nov-14
Construction		311	25-Oct-13	30-Sep-14	25-Oct-13A	14-Nov-14
Northern Landfall		311	25-Oct-13	30-Sep-14	25-Oct-13A	14-Nov-14
North Reclamation (Phase 1)		183	25-Oct-13	13-Jun-14	25-Oct-13A	13-Jun-14
Construction		183	25-Oct-13	13-Jun-14	25-Oct-13A	13-Jun-14
DDP10000	Temporary Pontoon Inspection & Obtain License	8	23-Nov-13	02-Dec-13	01-Feb-14A	04-Feb-14A
Ground Investigation		100	25-Oct-13	30-Apr-14	25-Oct-13A	30-Apr-14
DDP09010	Ground Investigation (Phase 2) - Northern Landfall & Sub-sea Tunnel	100	25-Oct-13	30-Apr-14	25-Oct-13A	30-Apr-14
Zone E		156	26-Nov-13	13-Jun-14	08-Jan-14A	13-Jun-14
NRC13810	Temporary Seawall Stage 1 - Band Drain	6	30-Dec-13	06-Jan-14	20-Jan-14A	20-Feb-14A
NRC13820	Temporary Seawall Stage 1 - Rockfill - G200 up to -3.0mPD	9	07-Jan-14	16-Jan-14	21-Feb-14A	02-Mar-14A
NRC13830	Temporary Seawall Stage 1 - Rockfill - G200 up to +4.0mPD	6	17-Jan-14	23-Jan-14	03-Mar-14	08-Mar-14
Vertical Seawall		156	26-Nov-13	13-Jun-14	22-Jan-14A	13-Jun-14
NRC10250	VS - Levelling Stone - Zone E - (CH50 to 100)	4	26-Nov-13	29-Nov-13	04-Feb-14A	08-Feb-14A
NRC10260	VS - Levelling Stone - Zone E - (CH100 to 150)	4	30-Nov-13	04-Dec-13	09-Feb-14A	12-Feb-14A
NRC10270	VS - Levelling Stone - Zone E - (CH150 to 205)	5	11-Dec-13	16-Dec-13	13-Feb-14A	18-Feb-14A
NRC10310	VS - Seawall Block- Zone E - (CH150 to 205)	6	20-Dec-13	02-Jan-14	22-Jan-14A	05-Mar-14
NRC10320	VS - Rockfill Type A - Zone E - (CH0 to 50)	2	12-Dec-13	14-Dec-13	25-Jan-14A	03-Mar-14
NRC10330	VS - Rockfill Type A- Zone E - (CH50 to 100)	2	16-Dec-13	18-Dec-13	05-Feb-14A	04-Mar-14
NRC10340	VS - Rockfill Type A- Zone E - (CH100 to 150)	1	20-Dec-13	23-Dec-13	15-Feb-14A	07-Mar-14
NRC10350	VS - Rockfill Type A- Zone E - (CH150 to 205)	4	03-Jan-14	07-Jan-14	08-Mar-14	12-Mar-14
NRC10360	VS - Geotextile - Zone E - (CH0 to 50)	1	19-Dec-13	20-Dec-13	25-Jan-14A	05-Mar-14
NRC10370	VS - Geotextile - Zone E - (CH50 to 100)	1	21-Dec-13	23-Dec-13	05-Feb-14A	06-Mar-14
NRC10380	VS - Geotextile - Zone E - (CH100 to 150)	1	24-Dec-13	27-Dec-13	15-Feb-14A	10-Mar-14
NRC10390	VS - Geotextile - Zone E - (CH150 to 205)	2	08-Jan-14	09-Jan-14	13-Mar-14	14-Mar-14
NRC10400	VS - Granular Filter - Zone E - (CH0 to 50)	3	24-Dec-13	30-Dec-13	25-Jan-14A	07-Mar-14
NRC10410	VS - Granular Filter - Zone E - (CH50 to 100)	3	31-Dec-13	04-Jan-14	05-Feb-14A	08-Mar-14
NRC10420	VS - Granular Filter - Zone E - (CH100 to 150)	1	06-Jan-14	09-Jan-14	15-Feb-14A	14-Mar-14
NRC10430	VS - Granular Filter - Zone E - (CH150 to 205)	5	10-Jan-14	15-Jan-14	15-Mar-14	20-Mar-14
NRC10480	VS - Mass Concrete Coping - Zone E - (CH0 to 50)	8	02-May-14	12-May-14	02-May-14*	12-May-14
NRC10490	VS - Mass Concrete Coping - Zone E - (CH50 to 100)	8	13-May-14	21-May-14	13-May-14	21-May-14
NRC10500	VS - Mass Concrete Coping - Zone E - (CH100 to 150)	8	22-May-14	30-May-14	22-May-14	30-May-14
NRC10510	VS - Mass Concrete Coping - Zone E - (CH150 to 205)	11	31-May-14	13-Jun-14	31-May-14	13-Jun-14
Reclamation		84	10-Feb-14	30-Apr-14	08-Jan-14A	24-May-14
NRC10540	Reclamation - Geotextile - Zone E - (CH100 to 150)	6	14-Feb-14	20-Feb-14	22-Jan-14A	10-Feb-14A
NRC10550	Reclamation - Geotextile - Zone E - (CH150 to 205)	5	21-Feb-14	27-Feb-14	10-Feb-14A	10-Mar-14
NRC10570	Reclamation - Sand Blanket - Zone E - (CH50 to 100)	2	14-Feb-14	15-Feb-14	08-Jan-14A	27-Feb-14A
NRC10580	Reclamation - Sand Blanket - Zone E - (CH100 to 150)	1	21-Feb-14	22-Feb-14	12-Feb-14A	10-Mar-14
NRC10590	Reclamation - Sand Blanket - Zone E - (CH150 to 205)	2	28-Feb-14	01-Mar-14	11-Mar-14	12-Mar-14
NRC10600	Reclamation - Band Drain - Zone E - (CH0 to 50)	4	10-Feb-14	13-Feb-14	20-Jan-14A	08-Feb-14A
NRC10610	Reclamation - Band Drain - Zone E - (CH50 to 100)	3	17-Feb-14	20-Feb-14	10-Feb-14A	10-Mar-14
NRC10620	Reclamation - Band Drain - Zone E - (CH100 to 150)	4	24-Feb-14	27-Feb-14	11-Mar-14	14-Mar-14
NRC10630	Reclamation - Band Drain - Zone E - (CH150 to 205)	4	03-Mar-14	06-Mar-14	13-Mar-14	17-Mar-14
NRC10640	Public Fill - Zone E - (CH0 to 50) to -2.5mPD	5	15-Feb-14	20-Feb-14	10-Mar-14	14-Mar-14
NRC10650	Public Fill - Zone E - (CH50 to 100) to -2.5mPD	5	21-Feb-14	26-Feb-14	15-Mar-14	20-Mar-14
NRC10660	Public Fill - Zone E - (CH100 to 150) to -2.5mPD	4	07-Mar-14	11-Mar-14	29-Mar-14	02-Apr-14
NRC10670	Public Fill - Zone E - (CH150 to 205) to -2.5mPD	4	28-Mar-14	01-Apr-14	24-Apr-14	28-Apr-14
NRC10680	Public Fill - Zone E - (CH0 to 50) to +2.5mPD	7	27-Feb-14	06-Mar-14	21-Mar-14	28-Mar-14
NRC10690	Public Fill - Zone E - (CH50 to 100) to +2.5mPD	7	12-Mar-14	19-Mar-14	03-Apr-14	11-Apr-14
NRC10700	Public Fill - Zone E - (CH100 to 150) to +2.5mPD	7	20-Mar-14	27-Mar-14	12-Apr-14	23-Apr-14
NRC10710	Public Fill - Zone E - (CH150 to 205) to +2.5mPD	7	29-Mar-14	07-Apr-14	25-Apr-14	03-May-14
NRC10720	Public Fill - Zone E - (CH0 to 50) to +6.0mPD	7	20-Mar-14	27-Mar-14	12-Apr-14	23-Apr-14
NRC10730	Public Fill - Zone E - (CH50 to 100) to +6.0mPD	7	02-Apr-14	10-Apr-14	29-Apr-14	08-May-14
NRC10740	Public Fill - Zone E - (CH100 to 150) to +6.0mPD	7	11-Apr-14	22-Apr-14	09-May-14	16-May-14
NRC10750	Public Fill - Zone E - (CH150 to 205) to +6.0mPD	7	23-Apr-14	30-Apr-14	17-May-14	24-May-14
Zone D1		141	06-Dec-13	29-May-14	16-Jan-14A	06-Jun-14
Vertical Seawall		111	14-Jan-14	29-May-14	20-Jan-14A	06-Jun-14
NRC10880	VS - Rock Grade 400 - Zone D1 - (CH305 to 355)	10	14-Jan-14	24-Jan-14	20-Jan-14A	04-Feb-14A
NRC10910	VS - Levelling Stone - Zone D1 - (CH205 to 255)	2	14-Jan-14	21-Jan-14	06-Feb-14A	08-Mar-14
NRC10920	VS - Levelling Stone - Zone D1 - (CH255 to 305)	4	22-Jan-14	25-Jan-14	10-Mar-14	13-Mar-14
NRC10930	VS - Levelling Stone - Zone D1 - (CH305 to 355)	4	27-Jan-14	30-Jan-14	14-Mar-14	18-Mar-14
NRC10960	VS - Seawall Block - Zone D1 - (CH205 to 255)	9	22-Jan-14	10-Feb-14	06-Feb-14A	11-Mar-14
NRC10970	VS - Seawall Block - Zone D1 - (CH255 to 305)	7	11-Feb-14	18-Feb-14	14-Mar-14	21-Mar-14
NRC10980	VS - Seawall Block - Zone D1 - (CH305 to 355)	7	19-Feb-14	26-Feb-14	22-Mar-14	29-Mar-14
NRC11010	VS - Rockfill Type A- Zone D1 - (CH205 to 255)	6	19-Feb-14	25-Feb-14	22-Mar-14	28-Mar-14
NRC11020	VS - Rockfill Type A- Zone D1 - (CH255 to 305)	3	26-Feb-14	28-Feb-14	29-Mar-14	01-Apr-14
NRC11030	VS - Rockfill Type A- Zone D1 - (CH305 to 355)	3	01-Mar-14	04-Mar-14	02-Apr-14	04-Apr-14
NRC11060	VS - Geotextile - Zone D1 - (CH205 to 255)	3	01-Mar-14	04-Mar-14	02-Apr-14	04-Apr-14
NRC11070	VS - Geotextile - Zone D1 - (CH255 to 305)	2	05-Mar-14	06-Mar-14	07-Apr-14	08-Apr-14
NRC11080	VS - Geotextile - Zone D1 - (CH305 to 355)	2	07-Mar-14	08-Mar-14	09-Apr-14	10-Apr-14
NRC11140	VS - Granular Filter - Zone D1 - (CH205 to 255)	7	07-Mar-14	14-Mar-14	09-Apr-14	16-Apr-14
NRC11210	VS - Granular Filter - Zone D1 - (CH255 to 305)	4	15-Mar-14	19-Mar-14	17-Apr-14	24-Apr-14
NRC11280	VS - Granular Filter - Zone D1 - (CH305 to 355)	4	20-Mar-14	24-Mar-14	25-Apr-14	29-Apr-14
NRC11720	VS - Mass Concrete Coping - Zone D1 - (CH205 to 255)	15	02-May-14	20-May-14	10-May-14*	28-May-14
NRC11790	VS - Mass Concrete Coping - Zone D1 - (CH255 to 305)	8	21-May-14	29-May-14	28-May-14	06-Jun-14
Sloping Seawall		140	06-Dec-13	13-May-14	16-Jan-14A	05-Jun-14
NRC11940	SS - Bulk Dredging - Zone D1 - (CH205 to 355)	3	06-Dec-13	09-Dec-13	16-Jan-14A	09-Feb-14A
NRC1202020	VS - Rock Grade 400 - Zone D1 - RTT	4	11-Dec-13	14-Dec-13	29-Jan-14A	09-Feb-14A
NRC1202030	VS - Levelling Stone - Zone D1 - RTT	2	16-Dec-13	17-Dec-13	03-Mar-14	04-Mar-14
NRC1202040	VS - Seawall Block - Zone D1 - RTT	5	18-Dec-13	24-Dec-13	06-Feb-14A	05-Mar-14
NRC1202050	VS - Rockfill Type A- Zone D1 - RTT	2	27-Dec-13	28-Dec-13	06-Mar-14	07-Mar-14
NRC1202060	VS - Geotextile - Zone D1 - RTT	1	30-Dec-13	30-Dec-13	08-Mar-14	08-Mar-14
NRC1202070	VS - Granular Filter - Zone D1 - RTT	2	31-Dec-13	02-Jan-14	10-Mar-14	11-Mar-14
NRC1202090	VS - Mass Concrete Coping - Zone D1 - RTT	4	29-Apr-14	03-May-14	23-May-14	28-May-14
NRC12110	SS - Dredging - Zone D1 - (CH305 to 355)	2	03-Jan-14	04-Jan-14	27-Jan-14A	07-Feb-14A
NRC12290	SS - Rock Grade 400 - Zone D1 - (CH255 to 305) to +2.5mPD	15	16-Dec-13	04-Jan-14	12-Feb-14A	19-Feb-14A
NRC12330	SS - Rock Grade 400 - Zone D1 - (CH305 to 355) to +2.5mPD	11	06-Jan-14	22-Jan-14	20-Feb-14A	05-Mar-14
NRC13610	SS - Armour Rock Underlayer - Zone D1 - (CH255 to 305)	5	23-Jan-14	28-Jan-14	06-Mar-14	11-Mar-14
NRC13690	SS - Armour Rock Underlayer - Zone D1 - (CH305 to 355)	5	29-Jan-14	10-Feb-14	12-Mar-14	17-Mar-14
NRC14070	SS - Armour Rock - Zone D1 - (CH255 to 305)	4	29-Jan-14	08-Feb-14	12-Mar-14	15-Mar-14
NRC14080	SS - Armour Rock - Zone D1 - (CH305 to 355)	4	10-Feb-14	13-Feb-14	17-Mar-14	20-Mar-14
NRC14120	SS - Mass Concrete Coping - Zone D1 - (CH255 to 305)	7	05-May-14	13-May-14	28-May-14	05-Jun-14
NRC14170	Sloping - Rockfill Type A- Zone D1 - (CH255 to 305)	1	06-Jan-14	06-Jan-14	03-Mar-14	03-Mar-14
NRC14180	Sloping - Rockfill Type A- Zone D1 - (CH305 to 355)	1	23-Jan-14	23-Jan-14	06-Mar-14	06-Mar-14
NRC14220	Sloping - Geotextile - Zone D1 - (CH255 to 305)	1	07-Jan-14	07-Jan-14	04-Mar-14	04-Mar-14
NRC14230	Sloping - Geotextile - Zone D1 - (CH305 to 355)	1	24-Jan-14	24-Jan-14	07-Mar-14	07-Mar-14
NRC14270	Sloping - Granular Filter - Zone D1 - (CH255 to 305)	2	08-Jan-14	09-Jan-14	05-Mar-14	06-Mar-14
NRC14280	Sloping - Granular Filter - Zone D1 - (CH305 to 355)	2	25-Jan-14	27-Jan-14	08-Mar-14	10-Mar-14
NRC14310	Reclamation - Geotextile - Zone D1 - (CH205 to 255)	6	28-Feb-14	06-Mar-14	11-Mar-14	17-Mar-14
NRC14320	Reclamation - Geotextile - Zone D1 - (CH255 to 305)	6	07-Mar-14	13-Mar-14	18-Mar-14	24-Mar-14
NRC14330	Reclamation - Geotextile - Zone D1 - (CH305 to 355)	6	14-Mar-14	20-Mar-14	25-Mar-14	31-Mar-14
NRC14360	Reclamation - Sand Blanket - Zone D1 - (CH205 to 255)	2	07-Mar-14	08-Mar-14	18-Mar-14	19-Mar-14
NRC14370	Reclamation - Sand Blanket - Zone D1 - (CH255 to 305)	2	14-Mar-14	15-Mar-14	25-Mar-14	26-Mar-14
NRC14380	Reclamation - Sand Blanket - Zone D1 - (CH305 to 355)	2	21-Mar-14	22-Mar-14	01-Apr-14	02-Apr-14
NRC14410	Reclamation - Band Drain - Zone D1 - (CH205 to 255)	5	10-Mar-14	14-Mar-14	20-Mar-14	25-Mar-14
NRC14420	Reclamation - Band Drain - Zone D1 - (CH255 to 305)	5	17-Mar-14	21-Mar-14	27-Mar-14	01-Apr-14
NRC14430	Reclamation - Band Drain - Zone D1 - (CH305 to 355)	5	24-Mar-14	28-Mar-14	03-Apr-14	09-Apr-14
Reclamation		27	02-Apr-14	09-May-14	29-Apr-14	31-May-14
NRC13260	Compacted Sandfill - Zone D1 - (CH205 to 255) to -2.5mPD	3	02-Apr-14	04-Apr-14	29-Apr-14	02-May-14
NRC13270	Compacted Sandfill - Zone D1 - (CH255 to 305) to -2.5mPD	3	07-Apr-14	09-Apr-14	03-May-14	07-May-14
NRC13280	Compacted Sandfill - Zone D1 - (CH305 to 355) to -2.5mPD	3	10-Apr-14	12-Apr-14	08-May-14	10-May-14
NRC13290	Public Fill - Zone D1 - (CH205 to 255) to -2.5mPD	1	07-Apr-14	07-Apr-14	03-May-14	03-May-14
NRC13300	Public Fill - Zone D1 - (CH255 to 305) to -2.5mPD	2	10-Apr-14	11-Apr-14	08-May-14	09-May-14
NRC13310	Public Fill - Zone D1 - (CH305 to 355) to -2.5mPD	2	14-Apr-14	15-Apr-14	12-May-14	13-May-14
NRC13320	Compacted Sandfill - Zone D1 - (CH205 to 255) to +2.5mPD	3	08-Apr-14	10-Apr-14	05-May-14	08-May-14
NRC13340	Compacted Sandfill - Zone D1 - (CH255 to 305) to +2.5mPD	3	12-Apr-14	15-Apr-14	10-May-14	13-May-14
NRC13350	Compacted Sandfill - Zone D1 - (CH305 to 355) to +2.5mPD	3	16-Apr-14	22-Apr-14	14-May-14	16-May-14
NRC13360	Public Fill - Zone D1 - (CH205 to 255) to +2.5mPD	4	11-Apr-14	15-Apr-14	09-May-14	13-May-14
NRC13370	Public Fill - Zone D1 - (CH255 to 305) to +2.5mPD	4	16-Apr-14	23-Apr-14	14-May-14	17-May-14
NRC13380	Public Fill - Zone D1 - (CH305 to 355) to +2.5mPD	4	24-Apr-14	28-Apr-14	19-May-14	22-May-14
NRC13390	Compacted Sandfill - Zone D1 - (CH205 to 255)to +5.0mPD	2	02-May-14	03-May-14	26-May-14	27-May-14
NRC13400	Compacted Sandfill - Zone D1 - (CH255 to 305) to +5.0mPD	2	05-May-14	07-May-14	28-May-14	29-May-14
NRC13410	Compacted Sandfill - Zone D1 - (CH305 to 355) to +5.0mPD	2	08-May-14	09-May-14	30-May-14	31-May-14
NRC13420	Public Fill - Zone D1 - (CH205 to 255) to +5.0mPD	4	05-May-14	09-May-14	28-May-14	31-May-14
Zone D2		103	20-Jan-14	14-May-14	27-Jan-14A	03-Jun-14
Vertical Seawall		79	25-Jan-14	02-Apr-14	27-Jan-14A	10-May-14
NRC10890	VS - Rock Grade 400 - Zone D2 - (CH355 to 405)	6	25-Jan-14	07-Feb-14	27-Jan-14A	03-Mar-14
NRC10900	VS - Rock Grade 400 - Zone D2 - (CH405 to 443)	3	08-Feb-14	14-Feb-14	01-Mar-14A	06-Mar-14
NRC10940	VS - Levelling Stone - Zone D2 - (CH355 to 405)	4	07-Feb-14	11-Feb-14	19-Mar-14	22-Mar-14

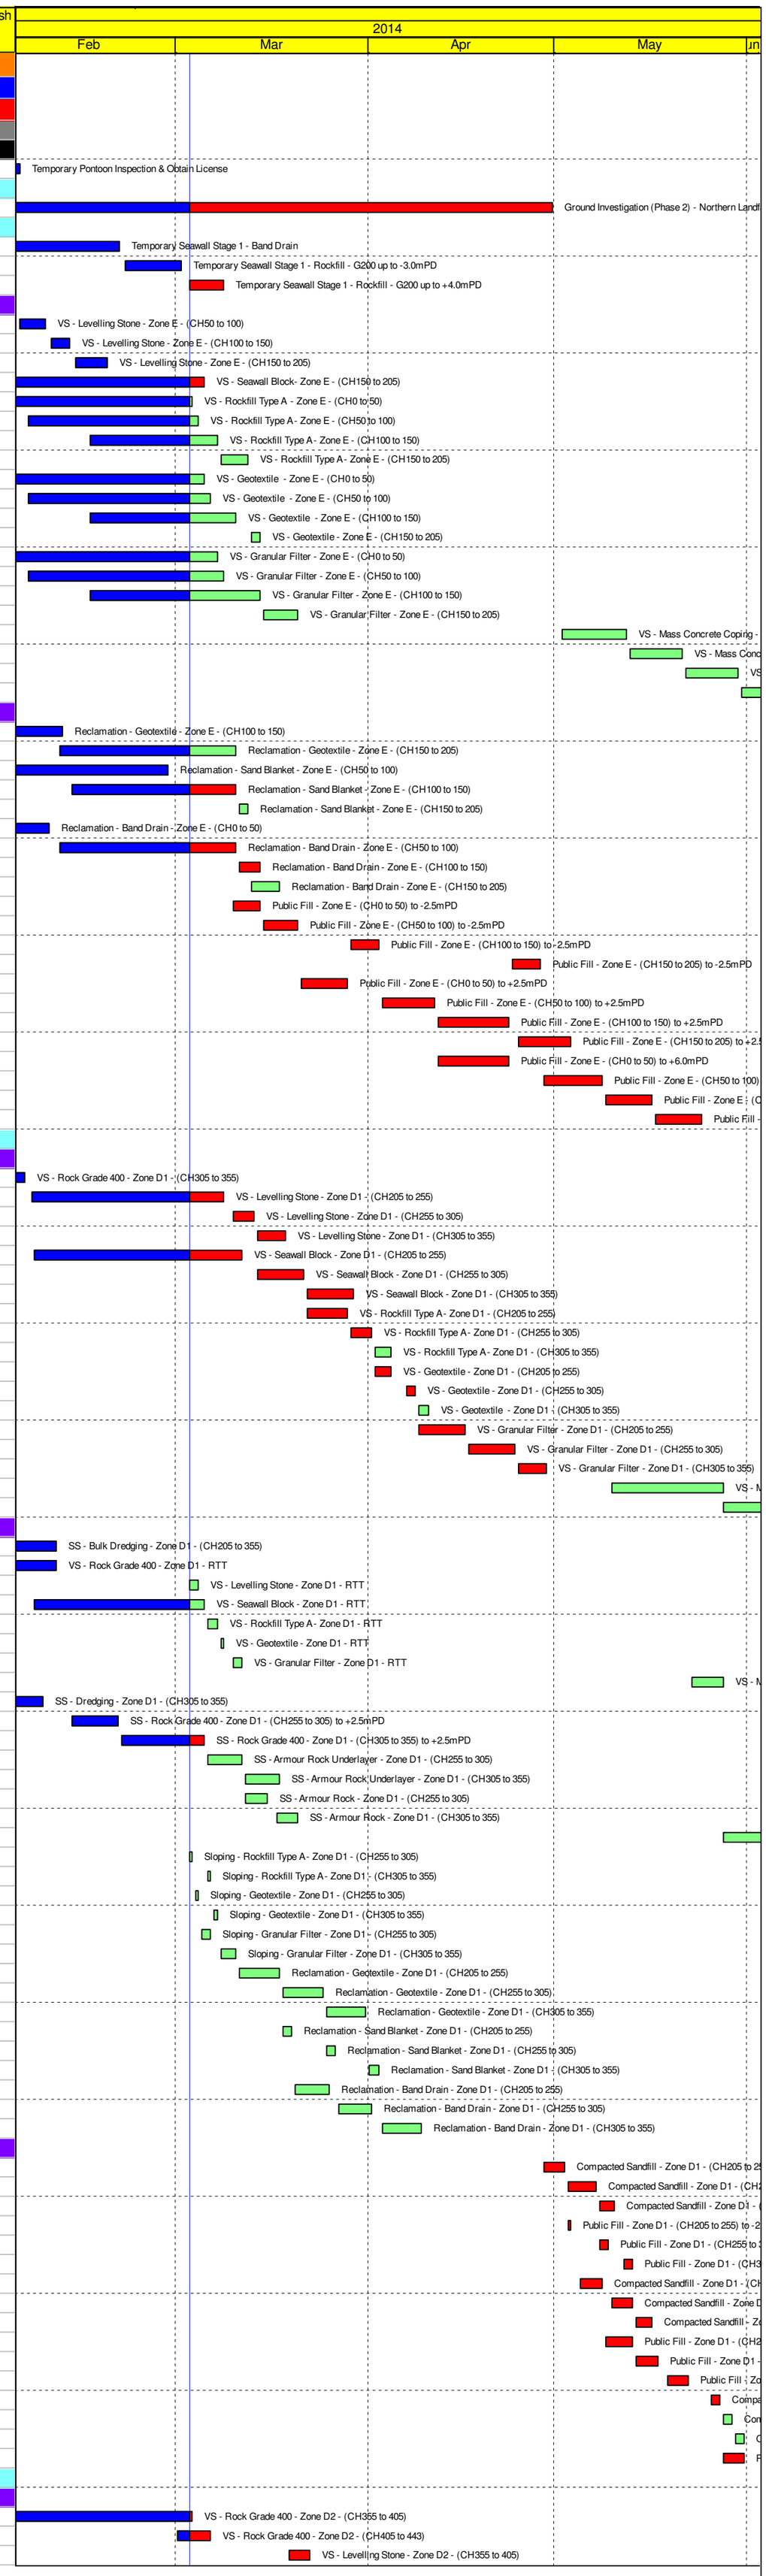

Project ID: TMCLK_I0.0-101 - B1-1 - B3-5 - B4-16

Data Date: 03-Mar-14

Current Bar
Current Bar - Critical
Planned Milestone
Current Milestone
Progress Bar
Progress Milestone

TMCLK - Northern Connection Sub-Sea Tunnel Section

3-Months Rolling Programme - Construction

As of 03-Mar-14 Progress

Dragages HongKong 香港寶嘉 — A member of the Bouygues Construction group — BOUYGUES TRAVAUX PUBLICS

Dragages - Bouygues Joint Venture 寶嘉 - 布依格聯營

Date	Revision	Checked	Approved
21-Feb-14	TMCLK/DBJ/GEN/PRG/98505	SPa	W Yu

Activity ID	Activity Name	Orig Dur	Planned Start	Planned Finish	Current Start	Current Finish
NRC10950	VS - Levelling Stone - Zone D2 - (CH405 to 443)	4	12-Feb-14	15-Feb-14	24-Mar-14	27-Mar-14
NRC10990	VS - Seawall Block - Zone D2 - (CH355 to 405)	7	27-Feb-14	06-Mar-14	31-Mar-14	08-Apr-14
NRC11000	VS - Seawall Block - Zone D2 - (CH405 to 443)	7	07-Mar-14	14-Mar-14	09-Apr-14	16-Apr-14
NRC11040	VS - Rockfill Type A- Zone D2 - (CH355 to 405)	3	07-Mar-14	10-Mar-14	09-Apr-14	11-Apr-14
NRC11050	VS - Rockfill Type A- Zone D2 - (CH405 to 443)	3	15-Mar-14	18-Mar-14	17-Apr-14	23-Apr-14
NRC11090	VS - Geotextile - Zone D2 - (CH355 to 405)	2	11-Mar-14	12-Mar-14	12-Apr-14	14-Apr-14
NRC11100	VS - Geotextile - Zone D2 - (CH405 to 443)	2	19-Mar-14	20-Mar-14	24-Apr-14	25-Apr-14
NRC11350	VS - Granular Filter - Zone D2 - (CH355 to 405)	4	25-Mar-14	28-Mar-14	30-Apr-14	05-May-14
NRC11390	VS - Granular Filter - Zone D2 - (CH405 to 443)	4	29-Mar-14	02-Apr-14	07-May-14	10-May-14
Sloping Seawall		66	20-Jan-14	11-Mar-14	09-Feb-14A	14-Apr-14
NRC12160	SS - Dredging - Zone D2 - (CH355 to 405)	3	20-Jan-14	22-Jan-14	12-Feb-14A	16-Feb-14A
NRC12200	SS - Dredging - Zone D2 - (CH405 to 443)	2	15-Feb-14	17-Feb-14	09-Feb-14A	17-Feb-14A
NRC12430	SS - Rock Grade 400 - Zone D2 - (CH355 to 405) to +2.5mPD	2	23-Jan-14	17-Feb-14	26-Feb-14A	21-Mar-14
NRC12840	SS - Rock Grade 400 - Zone D2 - (CH405 to 443) to +2.5mPD	15	18-Feb-14	06-Mar-14	22-Mar-14	09-Apr-14
NRC13770	SS - Armour Rock Underlayer - Zone D2 - (CH355 to 405)	5	18-Feb-14	22-Feb-14	22-Mar-14	27-Mar-14
NRC13880	SS - Armour Rock Underlayer - Zone D2 - (CH405 to 443)	5	24-Feb-14	28-Feb-14	28-Mar-14	02-Apr-14
NRC14090	SS - Armour Rock - Zone D2 - (CH355 to 405)	4	14-Feb-14	18-Feb-14	21-Mar-14	25-Mar-14
NRC14100	SS - Armour Rock - Zone D2 - (CH405 to 443)	4	19-Feb-14	22-Feb-14	26-Mar-14	29-Mar-14
NRC14190	Sloping - Rockfill Type A- Zone D2 - (CH355 to 405)	1	18-Feb-14	18-Feb-14	22-Mar-14	22-Mar-14
NRC14200	Sloping - Rockfill Type A- Zone D2 - (CH405 to 443)	1	07-Mar-14	07-Mar-14	10-Apr-14	10-Apr-14
NRC14240	Sloping - Geotextile - Zone D2 - (CH355 to 405)	1	19-Feb-14	19-Feb-14	24-Mar-14	24-Mar-14
NRC14250	Sloping - Geotextile - Zone D2 - (CH405 to 443)	1	08-Mar-14	08-Mar-14	11-Apr-14	11-Apr-14
NRC14290	Sloping - Granular Filter - Zone D2 - (CH355 to 405)	2	20-Feb-14	21-Feb-14	25-Mar-14	26-Mar-14
NRC14300	Sloping - Granular Filter - Zone D2 - (CH405 to 443)	2	10-Mar-14	11-Mar-14	12-Apr-14	14-Apr-14
Reclamation		23	29-Mar-14	14-May-14	07-May-14	03-Jun-14
NRC13490	Compacted Sandfill- Zone D2 - (CH355 to 405) to -2.5mPD	3	16-Apr-14	22-Apr-14	14-May-14	16-May-14
NRC13500	Compacted Sandfill - Zone D2 - (CH405 to 443) to -2.5mPD	2	05-May-14	07-May-14	24-May-14	26-May-14
NRC13510	Public Fill - Zone D2 - (CH355 to 405) to -2.5mPD	4	23-Apr-14	26-Apr-14	17-May-14	21-May-14
NRC13520	Public Fill - Zone D2 - (CH405 to 443) to -2.5mPD	4	08-May-14	12-May-14	27-May-14	30-May-14
NRC13540	Compacted Sandfill - Zone D2 - (CH355 to 405) to +2.5mPD	6	08-May-14	14-May-14	27-May-14	03-Jun-14
NRC14340	Reclamation - Geotextile - Zone D2 - (CH355 to 405)	6	29-Mar-14	04-Apr-14	07-May-14	13-May-14
NRC14350	Reclamation - Geotextile - Zone D2 - (CH405 to 443)	6	07-Apr-14	12-Apr-14	14-May-14	20-May-14
NRC14390	Reclamation - Sand Blanket - Zone D2 - (CH355 to 405)	2	07-Apr-14	08-Apr-14	14-May-14	15-May-14
NRC14400	Reclamation - Sand Blanket - Zone D2 - (CH405 to 443)	2	14-Apr-14	15-Apr-14	21-May-14	22-May-14
NRC14440	Reclamation - Band Drain - Zone D2 - (CH355 to 405)	5	09-Apr-14	14-Apr-14	16-May-14	21-May-14
NRC14450	Reclamation - Band Drain - Zone D2 - (CH405 to 443)	5	16-Apr-14	24-Apr-14	23-May-14	28-May-14
Zone C1		89	13-Feb-14	20-May-14	10-Jan-14A	04-Jun-14
Vertical Seawall		89	13-Feb-14	30-Apr-14	15-Jan-14A	04-Jun-14
NRC14460	VS - Dredging - Zone C1 - (CH443 to 493)	2	13-Feb-14	14-Feb-14	15-Jan-14A	21-Feb-14A
NRC14470	VS - Dredging - Zone C1 - (CH493 to 543)	2	20-Feb-14	21-Feb-14	18-Feb-14A	01-Mar-14A
NRC14490	VS - Rock Grade 400 - Zone C1 - (CH443 to 493)	6	15-Feb-14	21-Feb-14	07-Mar-14	13-Mar-14
NRC14500	VS - Rock Grade 400 - Zone C1 - (CH493 to 543)	7	22-Feb-14	01-Mar-14	14-Mar-14	21-Mar-14
NRC14520	VS - Levelling Stone - Zone C1 - (CH443 to 493)	4	03-Mar-14	06-Mar-14	28-Mar-14	01-Apr-14
NRC14530	VS - Levelling Stone - Zone C1 - (CH493 to 543)	4	07-Mar-14	11-Mar-14	02-Apr-14	07-Apr-14
NRC14550	VS - Seawall Block - Zone C1 - (CH443 to 493)	9	15-Mar-14	25-Mar-14	17-Apr-14	30-Apr-14
NRC14560	VS - Seawall Block - Zone C1 - (CH493 to 543)	9	26-Mar-14	04-Apr-14	02-May-14	13-May-14
NRC14580	VS - Rockfill Type A- Zone C1 - (CH443 to 493)	3	07-Apr-14	09-Apr-14	14-May-14	16-May-14
NRC14590	VS - Rockfill Type A- Zone C1 - (CH493 to 543)	3	10-Apr-14	12-Apr-14	17-May-14	20-May-14
NRC14610	VS - Geotextile - Zone C1 - (CH443 to 493)	2	14-Apr-14	15-Apr-14	21-May-14	22-May-14
NRC14620	VS - Geotextile - Zone C1 - (CH493 to 543)	2	16-Apr-14	17-Apr-14	23-May-14	24-May-14
NRC14640	VS - Granular Filter - Zone C1 - (CH443 to 493)	4	22-Apr-14	25-Apr-14	26-May-14	29-May-14
NRC14650	VS - Granular Filter - Zone C1 - (CH493 to 543)	4	26-Apr-14	30-Apr-14	30-May-14	04-Jun-14
Sloping Seawall		51	05-Mar-14	20-May-14	10-Jan-14A	29-May-14
NRC14730	SS - Dredging - Zone C1 - (CH443 to 493)	2	05-Mar-14	06-Mar-14	04-Apr-14	07-Apr-14
NRC14740	SS - Dredging - Zone C1 - (CH493 to 543)	2	22-Mar-14	24-Mar-14	08-Apr-14	09-Apr-14
NRC14770	SS - Rock Grade 400 - Zone C1 - (CH493 to 543) to +2.5mPD	6	25-Mar-14	11-Apr-14	10-Jan-14A	24-Apr-14
NRC14820	SS - Armour Rock Underlayer - Zone C1 - (CH443 to 493)	5	25-Mar-14	29-Mar-14	10-Apr-14	15-Apr-14
NRC14830	SS - Armour Rock Underlayer - Zone C1 - (CH493 to 543)	5	12-Apr-14	17-Apr-14	25-Apr-14	30-Apr-14
NRC14850	SS - Armour Rock - Zone C1 - (CH443 to 493)	4	12-May-14	15-May-14	21-May-14	24-May-14
NRC14860	SS - Armour Rock - Zone C1 - (CH493 to 543)	4	16-May-14	20-May-14	26-May-14	29-May-14
NRC14910	Sloping - Rockfill Type A- Zone C1 - (CH443 to 493)	1	25-Mar-14	25-Mar-14	11-Apr-14	11-Apr-14
NRC14920	Sloping - Rockfill Type A- Zone C1 - (CH493 to 543)	1	12-Apr-14	12-Apr-14	25-Apr-14	25-Apr-14
NRC14940	Sloping - Geotextile - Zone C1 - (CH443 to 493)	1	26-Mar-14	26-Mar-14	12-Apr-14	12-Apr-14
NRC14950	Sloping - Geotextile - Zone C1 - (CH493 to 453)	1	14-Apr-14	14-Apr-14	26-Apr-14	26-Apr-14
NRC14970	Sloping - Granular Filter - Zone C1 - (CH443 to 493)	3	27-Mar-14	29-Mar-14	15-Apr-14	17-Apr-14
NRC14980	Sloping - Granular Filter - Zone C1 - (CH493 to 543)	3	15-Apr-14	17-Apr-14	28-Apr-14	30-Apr-14
Reclamation		11	14-Apr-14	29-Apr-14	21-May-14	03-Jun-14
NRC15000	Reclamation - Geotextile - Zone C1 - (CH443 to 493)	4	14-Apr-14	17-Apr-14	21-May-14	24-May-14
NRC15010	Reclamation - Geotextile - Zone C1 - (CH493 to 543)	4	22-Apr-14	25-Apr-14	26-May-14	29-May-14
NRC15030	Reclamation - Sand Blanket - Zone C1 - (CH443 to 493)	2	22-Apr-14	23-Apr-14	26-May-14	27-May-14
NRC15040	Reclamation - Sand Blanket - Zone C1 - (CH493 to 543)	2	26-Apr-14	28-Apr-14	30-May-14	31-May-14
NRC15060	Reclamation - Band Drain - Zone C1 - (CH443 to 493)	4	25-Apr-14	29-Apr-14	29-May-14	03-Jun-14
Zone C2		76	28-Feb-14	24-May-14	27-Feb-14A	04-Jun-14
Vertical Seawall		70	28-Feb-14	23-Apr-14	27-Feb-14A	27-May-14
NRC14480	VS - Dredging - Zone C2 - (CH543 to 598)	1	28-Feb-14	01-Mar-14	27-Feb-14A	21-Mar-14
NRC14510	VS - Rock Grade 400 - Zone C2 - (CH543 to 598)	8	03-Mar-14	11-Mar-14	22-Mar-14	31-Mar-14
NRC14540	VS - Levelling Stone - Zone C2 - (CH543 to 598)	4	12-Mar-14	15-Mar-14	08-Apr-14	11-Apr-14
NRC14570	VS - Seawall Block - Zone C2 - (CH543 to 598)	9	07-Apr-14	16-Apr-14	14-May-14	23-May-14
NRC14600	VS - Rockfill Type A- Zone C2 - (CH543 to 598)	3	14-Apr-14	16-Apr-14	21-May-14	23-May-14
NRC14630	VS - Geotextile - Zone C2 - (CH543 to 598)	2	22-Apr-14	23-Apr-14	26-May-14	27-May-14
Sloping Seawall		34	10-Apr-14	24-May-14	23-Apr-14	04-Jun-14
NRC14750	SS - Dredging - Zone C2 - (CH543 to 598)	2	10-Apr-14	11-Apr-14	23-Apr-14	24-Apr-14
NRC14780	SS - Rock Grade 400 - Zone C2 - (CH543 to 598) to +2.5mPD	15	12-Apr-14	03-May-14	25-Apr-14	14-May-14
NRC14840	SS - Armour Rock Underlayer - Zone C2 - (CH543 to 598)	5	05-May-14	10-May-14	15-May-14	20-May-14
NRC14870	SS - Armour Rock - Zone C2 - (CH543 to 598)	4	21-May-14	24-May-14	30-May-14	04-Jun-14
NRC14930	Sloping - Rockfill Type A- Zone C2 - (CH543 to 598)	1	05-May-14	05-May-14	15-May-14	15-May-14
NRC14960	Sloping - Geotextile - Zone C2 - (CH543 to 598)	1	07-May-14	07-May-14	16-May-14	16-May-14
NRC14990	Sloping - Granular Filter - Zone C2 - (CH543 to 598)	3	08-May-14	10-May-14	17-May-14	20-May-14
Reclamation		4	12-May-14	15-May-14	30-May-14	04-Jun-14
NRC15020	Reclamation - Geotextile - Zone C2 - (CH543 to 598)	4	12-May-14	15-May-14	30-May-14	04-Jun-14
Zone B		53	08-Mar-14	23-May-14	28-Mar-14	05-Jun-14
Vertical Seawall		53	08-Mar-14	02-May-14	28-Mar-14	05-Jun-14
NRC11110	VS - Dredging - Zone B - (CH598 to 648)	3	08-Mar-14	11-Mar-14	28-Mar-14	31-Mar-14
NRC11120	VS - Dredging - Zone B - (CH648 to 698)	3	19-Mar-14	21-Mar-14	09-Apr-14	11-Apr-14
NRC11130	VS - Dredging - Zone B - (CH698 to 738)	3	29-Mar-14	01-Apr-14	23-Apr-14	25-Apr-14
NRC11150	VS - Rock Grade 400 - Zone B - (CH598 to 648)	9	12-Mar-14	21-Mar-14	01-Apr-14	11-Apr-14
NRC11160	VS - Rock Grade 400 - Zone B - (CH648 to 698)	9	22-Mar-14	01-Apr-14	12-Apr-14	25-Apr-14
NRC11170	VS - Rock Grade 400 - Zone B - (CH698 to 738)	9	02-Apr-14	12-Apr-14	26-Apr-14	08-May-14
NRC11180	VS - Levelling Stone - Zone B - (CH598 to 648)	4	02-Apr-14	07-Apr-14	26-Apr-14	30-Apr-14
NRC11190	VS - Levelling Stone - Zone B - (CH648 to 698)	4	08-Apr-14	11-Apr-14	02-May-14	07-May-14
NRC11200	VS - Levelling Stone - Zone B - (CH698 to 738)	4	12-Apr-14	16-Apr-14	08-May-14	12-May-14
NRC11220	VS - Seawall Block - Zone B - (CH598 to 648)	5	17-Apr-14	25-Apr-14	24-May-14	29-May-14
NRC11230	VS - Seawall Block - Zone B - (CH648 to 698)	5	26-Apr-14	02-May-14	30-May-14	05-Jun-14
Sloping Seawall		19	30-Apr-14	23-May-14	12-May-14	03-Jun-14
NRC11440	SS - Dredging - Zone B - (CH598 to 648)	3	30-Apr-14	03-May-14	12-May-14	14-May-14
NRC11450	SS - Dredging - Zone B - (CH648 to 698)	3	21-May-14	23-May-14	30-May-14	03-Jun-14
NRC11470	SS - Rock Grade 400 - Zone B - (CH598 to 648) to +2.5mPD	16	05-May-14	23-May-14	15-May-14	03-Jun-14
Zone A1		16	10-Apr-14	02-May-14	05-May-14	23-May-14
Vertical Seawall		16	10-Apr-14	02-May-14	05-May-14	23-May-14
NRC12020	VS - Dredging - ZoneA1 - (CH738 to 793)	3	10-Apr-14	12-Apr-14	05-May-14	08-May-14
NRC12040	VS - Rock Grade 400 - ZoneA1 - (CH738 to 793)	9	14-Apr-14	26-Apr-14	09-May-14	19-May-14
NRC12050	VS - Levelling Stone - ZoneA1 - (CH738 to 793)	4	28-Apr-14	02-May-14	20-May-14	23-May-14
Zone A2		22	24-Apr-14	21-May-14	16-May-14	11-Jun-14
Vertical Seawall		22	24-Apr-14	21-May-14	16-May-14	11-Jun-14
NRC12350	VS - Dredging - ZoneA2 - (CH793 to 843)	3	24-Apr-14	26-Apr-14	16-May-14	19-May-14
NRC12360	VS - Dredging - ZoneA2 - (CH843 to 893)	4	03-May-14	08-May-14	24-May-14	28-May-14
NRC12370	VS - Dredging - ZoneA2 - (CH893 to 956)	11	09-May-14	21-May-14	29-May-14	11-Jun-14
NRC12380	VS - Rock Grade 400 - ZoneA2 - (CH793 to 843)	9	28-Apr-14	09-May-14	20-May-14	29-May-14
NRC12390	VS - Rock Grade 400 - ZoneA2 - (CH843 to 893)	10	10-May-14	21-May-14	30-May-14	11-Jun-14
Zone F		113	10-Jan-14	15-Apr-14	22-Feb-14A	05-Jun-14
CH137 to CH184		82	10-Jan-14	08-Mar-14	22-Feb-14A	26-Apr-14
A6416030	F - Marine Sheet Piling (H2) - CH137 to CH184	2	10-Jan-14	13-Jan-14	22-Feb-14A	04-Mar-14
A6416035	F - Marine Sheet Piling (H1) - CH137 to CH184	2	14-Jan-14	15-Jan-14	05-Mar-14	06-Mar-14
A6416100	F - Backfilling up to -7.5mPD & T1 Installation - CH137 to CH184	4	16-Jan-14	19-Jan-14	07-Mar-14	10-Mar-14
A6416110	F - Backfilling up to -4.5mPD - CH137 to CH184	2	20-Jan-14	21-Jan-14	11-Mar-14	12-Mar-14
A6416115	F - Backfilling up to +0.5mPD & T3 Installation - CH137 to CH184	6	22-Jan-14	27-Jan-14	13-Mar-14	18-Mar-14
A6416118	F - Backfilling up to +3.0mPD - CH137 to CH184	2	28-Jan-14	29-Jan-14	19-Mar-14	20-Mar-14
A6416120	F - Backfilling up to +6.0mPD - CH137 to CH184	2	30-Jan-14	31-Jan-14	21-Mar-14	22-Mar-14
A6416320	F - Anchor Wall Installation - CH160 to CH184	2	07-Mar-14	08-Mar-14	25-Apr-14	26-Apr-14
CH184 to CH231		50	16-Jan-14	21-Mar-14	07-Mar-14	10-May-14

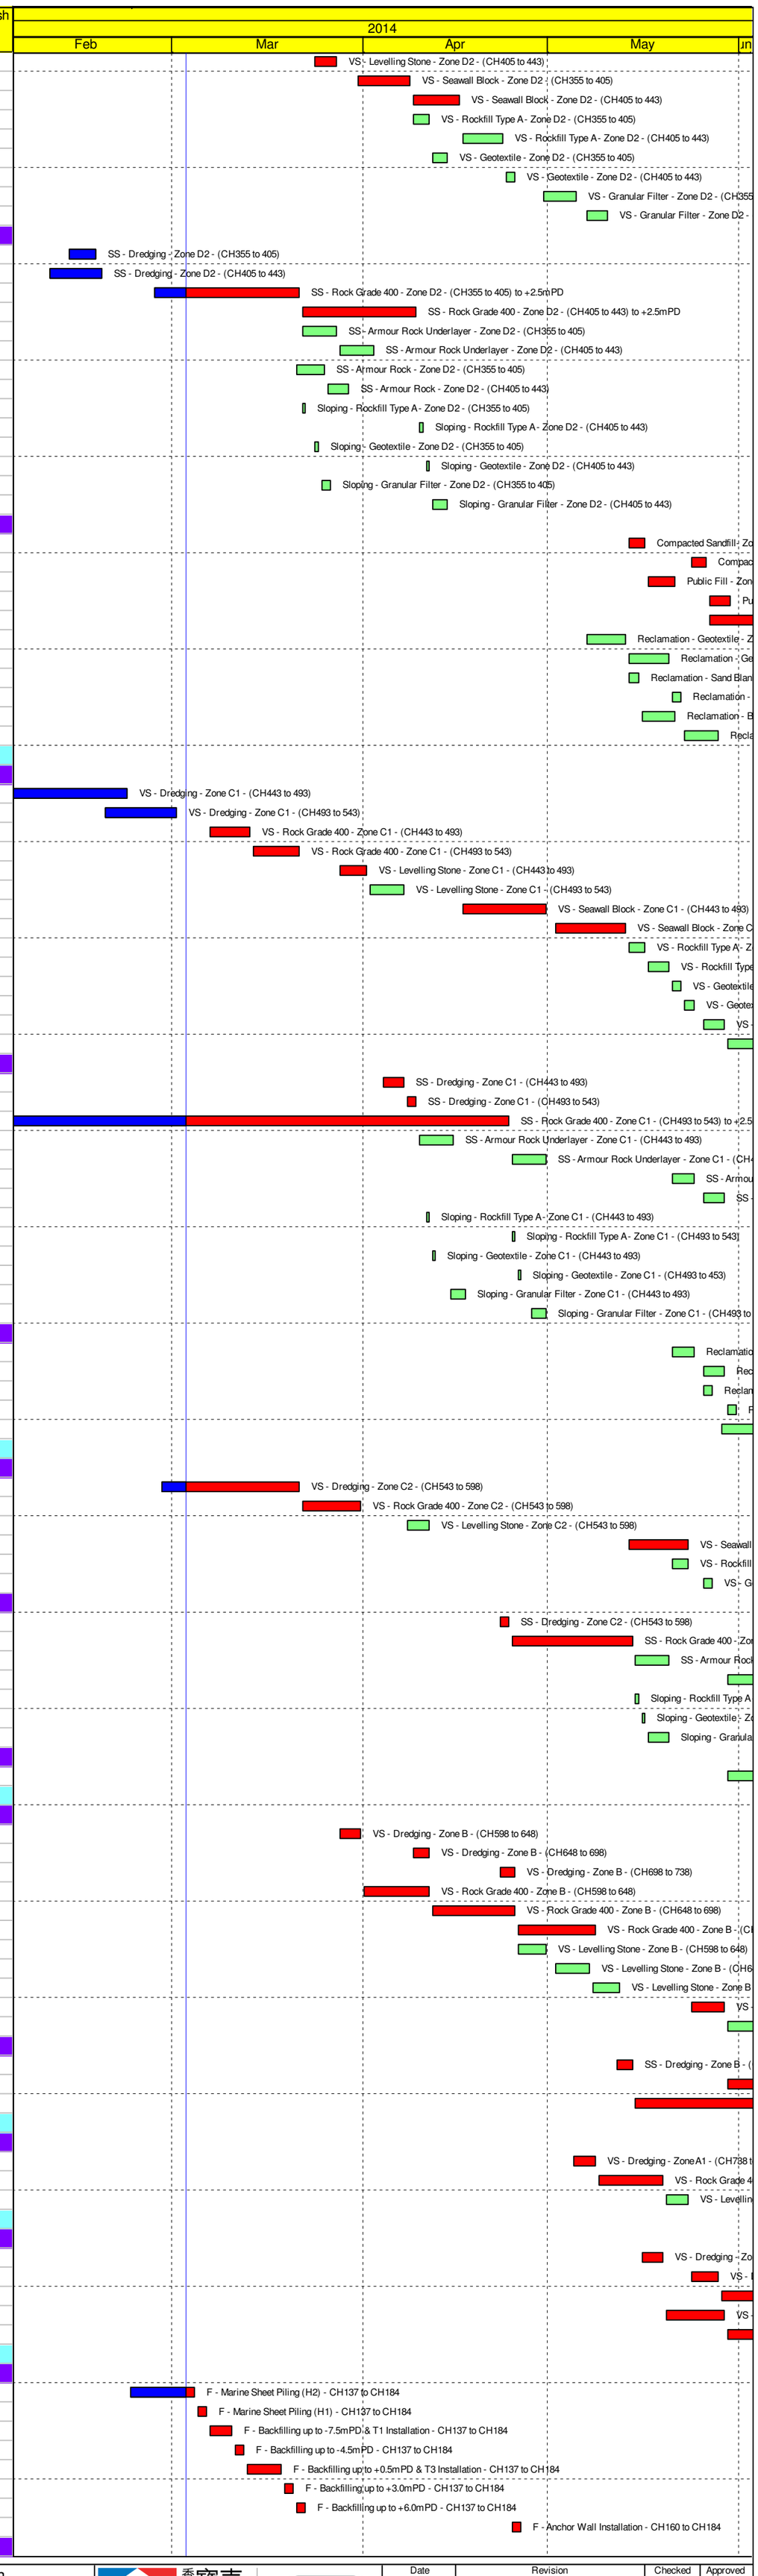

Current Bar
Current Bar - Critical
Planned Milestone
Current Milestone
Progress Bar
Progress Milestone

TMCLK - Northern Connection Sub-Sea Tunnel Section

3-Months Rolling Programme - Construction

As of 03-Mar-14 Progress

Dragages HongKong 香港寶嘉 — A member of the Bouygues Construction group — BOUYGUES TRAVAUX PUBLICS

Dragages - Bouygues Joint Venture 寶嘉 - 布依格聯營

Date	Revision	Checked	Approved
21-Feb-14	TMCLK/DBJ/GEN/PRG/98505	SPa	WYu

Activity ID	Activity Name	Orig Dur	Planned Start	Planned Finish	Current Start	Current Finish
A6416040	F - Marine Sheet Piling (H2) - CH184 to CH231	3	16-Jan-14	18-Jan-14	07-Mar-14	10-Mar-14
A6416050	F - Marine Sheet Piling (H1) - CH184 to CH231	3	20-Jan-14	22-Jan-14	11-Mar-14	13-Mar-14
A6416060	F - Backfilling up to -7.5mPD & T1 Installation - CH184 to CH231	4	23-Jan-14	26-Jan-14	14-Mar-14	17-Mar-14
A6416070	F - Backfilling up to -4.5mPD - CH184 to CH231	2	27-Jan-14	28-Jan-14	18-Mar-14	19-Mar-14
A6416080	F - Backfilling up to +0.5mPD & T3 Installation - CH184 to CH231	6	29-Jan-14	03-Feb-14	20-Mar-14	25-Mar-14
A6416085	F - Backfilling up to +3.0mPD - CH184 to CH231	2	04-Feb-14	05-Feb-14	26-Mar-14	27-Mar-14
A6416090	F - Backfilling up to +6.0mPD - CH184 to CH231	2	06-Feb-14	07-Feb-14	28-Mar-14	29-Mar-14
A6416230	F - Anchor wall Installation - CH184 to CH231	4	10-Mar-14	13-Mar-14	28-Apr-14	02-May-14
A6416290	F - Backfilling up to 0.0mPD & G2 Installation to Anchor Wall- CH184 to CH231	3	14-Mar-14	16-Mar-14	03-May-14	05-May-14
A6416295	F - Backfilling up to +3.0mPD & G1 Installation to Anchor Wall- CH184 to CH231	2	17-Mar-14	18-Mar-14	06-May-14	07-May-14
A6416300	F - Backfilling up to +6.0mPD to Anchor Wall - CH184 to CH231	2	19-Mar-14	20-Mar-14	08-May-14	09-May-14
A6416400	F - Backfilling to +6.0mPD to Existing Seawall - CH184 to CH231	1	21-Mar-14	21-Mar-14	10-May-14	10-May-14
CH231 to CH278		62	23-Jan-14	13-Apr-14	14-Mar-14	02-Jun-14
A6416240	F - Marine Sheet Piling (H1) - CH231 to CH278	4	23-Jan-14	27-Jan-14	14-Mar-14	18-Mar-14
A6416250	F - Marine Sheet Piling (H2) - CH231 to CH278	4	18-Mar-14	21-Mar-14	07-May-14	10-May-14
A6416260	F - Backfilling up to -7.5mPD & T1 Installation - CH231 to CH278	4	22-Mar-14	25-Mar-14	11-May-14	14-May-14
A6416270	F - Backfilling up to -4.5mPD - CH231 to CH278	2	26-Mar-14	27-Mar-14	15-May-14	16-May-14
A6416273	F - Backfilling up to +0.5mPD & T3 Installation - CH231 to CH278	6	28-Mar-14	02-Apr-14	17-May-14	22-May-14
A6416278	F - Backfilling up to +3.0mPD - CH231 to CH278	2	03-Apr-14	04-Apr-14	23-May-14	24-May-14
A6416280	F - Backfilling up to +6.0mPD - CH231 to CH278	2	05-Apr-14	06-Apr-14	25-May-14	26-May-14
A6416310	F - Anchor wall Installation - CH231 to CH278	4	07-Apr-14	10-Apr-14	27-May-14	30-May-14
A6416480	F - Backfilling up to 0.0mPD & G2 Installation to Anchor Wall- CH231 to CH278	3	11-Apr-14	13-Apr-14	31-May-14	02-Jun-14
CH278 to CH327		61	28-Jan-14	15-Apr-14	19-Mar-14	05-Jun-14
A6416180	F - Pre-boring for Marine Sheet Pile - CH278 to CH327	6	28-Jan-14	10-Feb-14	19-Mar-14	25-Mar-14
A6416190	F - Marine Sheet Piling (H1) - CH278 to CH327	5	25-Feb-14	01-Mar-14	10-Apr-14	15-Apr-14
A6416195	F - Marine Sheet Piling (H2) - CH278 to CH327	5	12-Mar-14	17-Mar-14	29-Apr-14	05-May-14
A6416200	F - Backfilling up to -3.5mPD & T2 Installation - CH278 to CH327	5	18-Mar-14	22-Mar-14	06-May-14	10-May-14
A6416210	F - Backfilling up to +0.5mPD - CH278 to CH327	4	23-Mar-14	26-Mar-14	11-May-14	14-May-14
A6416215	F - Backfilling up to +3.0mPD & T4 Installation - CH278 to CH327	5	27-Mar-14	31-Mar-14	15-May-14	19-May-14
A6416220	F - Backfilling up to +6.0mPD - CH278 to CH327	2	01-Apr-14	02-Apr-14	20-May-14	21-May-14
A6416340	F - Anchor wall Installation - CH278 to CH327	4	11-Apr-14	15-Apr-14	31-May-14	05-Jun-14
CH327 to CH381		36	11-Feb-14	26-Mar-14	26-Mar-14	13-May-14
A6416130	F - Pre-boring for Marine Sheet Pile - CH327 to CH381	6	11-Feb-14	17-Feb-14	26-Mar-14	01-Apr-14
A6416140	F - Marine Sheet Piling (H1) - CH327 to CH381	4	03-Mar-14	06-Mar-14	16-Apr-14	23-Apr-14
A6416145	F - Marine Sheet Piling (H2) - CH327 to CH381	4	07-Mar-14	11-Mar-14	24-Apr-14	28-Apr-14
A6416150	F - Backfilling up to -3.5mPD & T2 Installation - CH327 to CH381	4	12-Mar-14	15-Mar-14	29-Apr-14	02-May-14
A6416155	F - Backfilling up to+ 0.5mPD - CH327 to CH381	3	16-Mar-14	18-Mar-14	03-May-14	05-May-14
A6416160	F - Backfilling up to +3.0mPD & T4 Installation - CH327 to CH381	5	19-Mar-14	23-Mar-14	06-May-14	10-May-14
A6416170	F - Backfilling up to +6.0mPD - CH327 to CH381	3	24-Mar-14	26-Mar-14	11-May-14	13-May-14
Box Culvert Extension		192	07-Feb-14	30-Sep-14	24-Mar-14	14-Nov-14
Construction		192	07-Feb-14	30-Sep-14	24-Mar-14	14-Nov-14
CH000 to CH137		24	02-May-14	30-May-14	26-May-14	23-Jun-14
A6416600	Predrilling - CH27 to CH137	24	02-May-14	30-May-14	26-May-14	23-Jun-14
CH137 to CH184		184	07-Feb-14	19-Sep-14	24-Mar-14	05-Nov-14
A6416610	Predrilling - CH137 to CH184	24	07-Feb-14	06-Mar-14	24-Mar-14	24-Apr-14
A6416720	Bored Pile Construction - A42 to A35	160	07-Mar-14	19-Sep-14	25-Apr-14	05-Nov-14
CH184 to CH231		156	22-Mar-14	30-Sep-14	12-May-14	14-Nov-14
A6416620	Predrilling - CH184 to CH231	24	22-Mar-14	23-Apr-14	12-May-14	09-Jun-14
A6416730	Bored Pile Construction - A34 to A27	156	22-Mar-14	30-Sep-14	12-May-14	14-Nov-14
CH381 to CH399 (Box Culvert Connection)		58	18-Feb-14	30-Apr-14	02-Apr-14	16-Jun-14
A6416660	F - Prebored H-piles for CKS Temporary Land Access	6	18-Feb-14	24-Feb-14	02-Apr-14	09-Apr-14
A6417000	F - Steel Bridge Installation for Land Access to Zone E	52	25-Feb-14	30-Apr-14	10-Apr-14	16-Jun-14
North Shafts Construction & Tunnel Structure		46	28-Mar-14	27-May-14	24-Apr-14	19-Jun-14
Construction		46	28-Mar-14	27-May-14	24-Apr-14	19-Jun-14
North Launching Shaft ELS Foundation & Capping Beam (Cell 1 to 3)		18	28-Mar-14	22-Apr-14	24-Apr-14	16-May-14
NSH1180	E - Setup for Launching Shaft ELS	18	28-Mar-14	22-Apr-14	24-Apr-14	16-May-14
North Launching Shaft ELS Foundation & Capping Beam		21	02-May-14	27-May-14	26-May-14	19-Jun-14
NSH1210	E - Cell 4 to 6 - Prebored H-piles - Perm	21	02-May-14	27-May-14	26-May-14	19-Jun-14
CLP Temporary Substation		124	31-Dec-13	31-May-14	27-Jan-14A	27-Jun-14
Construction		124	31-Dec-13	31-May-14	27-Jan-14A	27-Jun-14
DDP12540	Gazette & Traffic Advice Application	28	31-Dec-13	08-Feb-14	03-Mar-14	03-Apr-14
DDP12550	RMO Application for TTMS Implementation	6	10-Feb-14	15-Feb-14	04-Apr-14	11-Apr-14
DDP12720	Trench Excavation & Service Connection	60	17-Feb-14	17-May-14	12-Apr-14	27-Jun-14
DDP1274010	Backfilling , Binding & 500mm Base Slab	16	20-Jan-14	13-Feb-14	27-Jan-14A	14-Feb-14A
DDP1274020	Outerwall & Water Tank up to +6.14mPD - Rebar, Fwk	7	14-Feb-14	21-Feb-14	15-Feb-14A	21-Feb-14A
DDP127402020	Outerwall & Water Tank up to +6.14mPD - Fwk Removal	2	22-Feb-14	24-Feb-14	22-Feb-14A	24-Feb-14A
DDP1274030	Backfilling, Compacted Fill & Earth Mat Top Layer installation	7	24-Feb-14	07-Mar-14	24-Feb-14A	06-Mar-14
DDP1274040	200mm thk on-grade Slab & Cable Trench - Rebar, Fwk	6	08-Mar-14	14-Mar-14	07-Mar-14	13-Mar-14
DDP1274047	200mm thk on-grade Slab & Cable Trench - Remove Fwk	2	15-Mar-14	17-Mar-14	14-Mar-14	15-Mar-14
DDP1274050	Concrete Plinth - Rebar, Fwk & Concreting	6	21-Mar-14	27-Mar-14	20-Mar-14	26-Mar-14
DDP1275010	Oil Intercreptor - Sheet piling & Excavation	7	24-Feb-14	03-Mar-14	24-Feb-14A	28-Feb-14A
DDP1275020	Oil Intercreptor to +4.31mPD - Rebar, Fwk	0	04-Mar-14	06-Mar-14	01-Mar-14A	05-Mar-14
DDP1275027	Oil Intercreptor to +4.31mPD - Fwk Removal	2	07-Mar-14	08-Mar-14	06-Mar-14	07-Mar-14
DDP1275030	Oil Intercreptor to +6.14mPD - Rebar, Fwk with Cast in Pipe	5	07-Mar-14	12-Mar-14	06-Mar-14	11-Mar-14
DDP1275037	Oil Intercreptor to +6.14mPD - Fwk Removal	2	13-Mar-14	14-Mar-14	12-Mar-14	13-Mar-14
DDP127503710	Water Tank Slab at +8.0mPD - Rebar Fwk	5	08-Mar-14	13-Mar-14	07-Mar-14	12-Mar-14
DDP127503730	Water Tank Slab at +8.0mPD - Fwk Removal	2	14-Mar-14	15-Mar-14	13-Mar-14	14-Mar-14
DDP1275040	Outerwall & Water Tank up to +7.7mPD - Rebar, Fwk	4	15-Mar-14	19-Mar-14	14-Mar-14	18-Mar-14
DDP1275055	Outerwall & Water Tank up to +7.7mPD - Remove Fwk	2	20-Mar-14	21-Mar-14	19-Mar-14	20-Mar-14
DDP1275060	Outerwall & Water Tank up to +9.0mPD - Rebar, Fwk	4	20-Mar-14	24-Mar-14	19-Mar-14	22-Mar-14
DDP1275075	Outerwall & Water Tank up to +9.0mPD - Remove Fwk	2	25-Mar-14	26-Mar-14	24-Mar-14	25-Mar-14
DDP127507510	Internal Wall up to +6.14mPD - Rebar, Fwk	7	15-Feb-14	22-Feb-14	15-Feb-14A	22-Feb-14A
DDP127507530	Internal Wall up to +6.14mPD - Fwk Removal	2	24-Feb-14	25-Feb-14	23-Feb-14A	25-Feb-14A
DDP127507540	Internal Wall up to +10.14mPD - Rebar, Fwk	5	15-Mar-14	20-Mar-14	14-Mar-14	19-Mar-14
DDP127507560	Internal Wall up to +10.14mPD - Fwk Removal	2	21-Mar-14	22-Mar-14	20-Mar-14	21-Mar-14
DDP1275080	Substation - Roof Structure - Rebar, Fwk	5	25-Mar-14	29-Mar-14	24-Mar-14	28-Mar-14
DDP1275095	Substation - Roof Strucuture - Fwk Removal	2	31-Mar-14	01-Apr-14	29-Mar-14	31-Mar-14
DDP1275100	Internal Wall up to +13.14mPD - Rebar, Fwk	8	25-Mar-14	02-Apr-14	24-Mar-14	01-Apr-14
DDP1275120	Internal Wall up to +13.14 - Fwk Removal	2	03-Apr-14	04-Apr-14	02-Apr-14	03-Apr-14
DDP1275140	CLP Substation - E&M, BS Installation	46	02-Apr-14	31-May-14	01-Apr-14	30-May-14
DDP1276010	Substation - ABWF works	12	02-Apr-14	16-Apr-14	01-Apr-14	15-Apr-14
DDP1276020	Substation - Metal works & Remaining civil works	18	17-Apr-14	13-May-14	16-Apr-14	12-May-14
DDP1276030	Substation - E&M works	46	02-Apr-14	31-May-14	01-Apr-14	30-May-14
North Surface works for TBM Tunnelling		60	10-May-14	08-Jul-14	01-Jun-14	30-Jul-14
Construction		60	10-May-14	08-Jul-14	01-Jun-14	30-Jul-14
Zone D1		60	10-May-14	08-Jul-14	01-Jun-14	30-Jul-14
NRC13940	Zone D1 - Vibro-compaction (CH205 to 255)	60	10-May-14	08-Jul-14	01-Jun-14	30-Jul-14

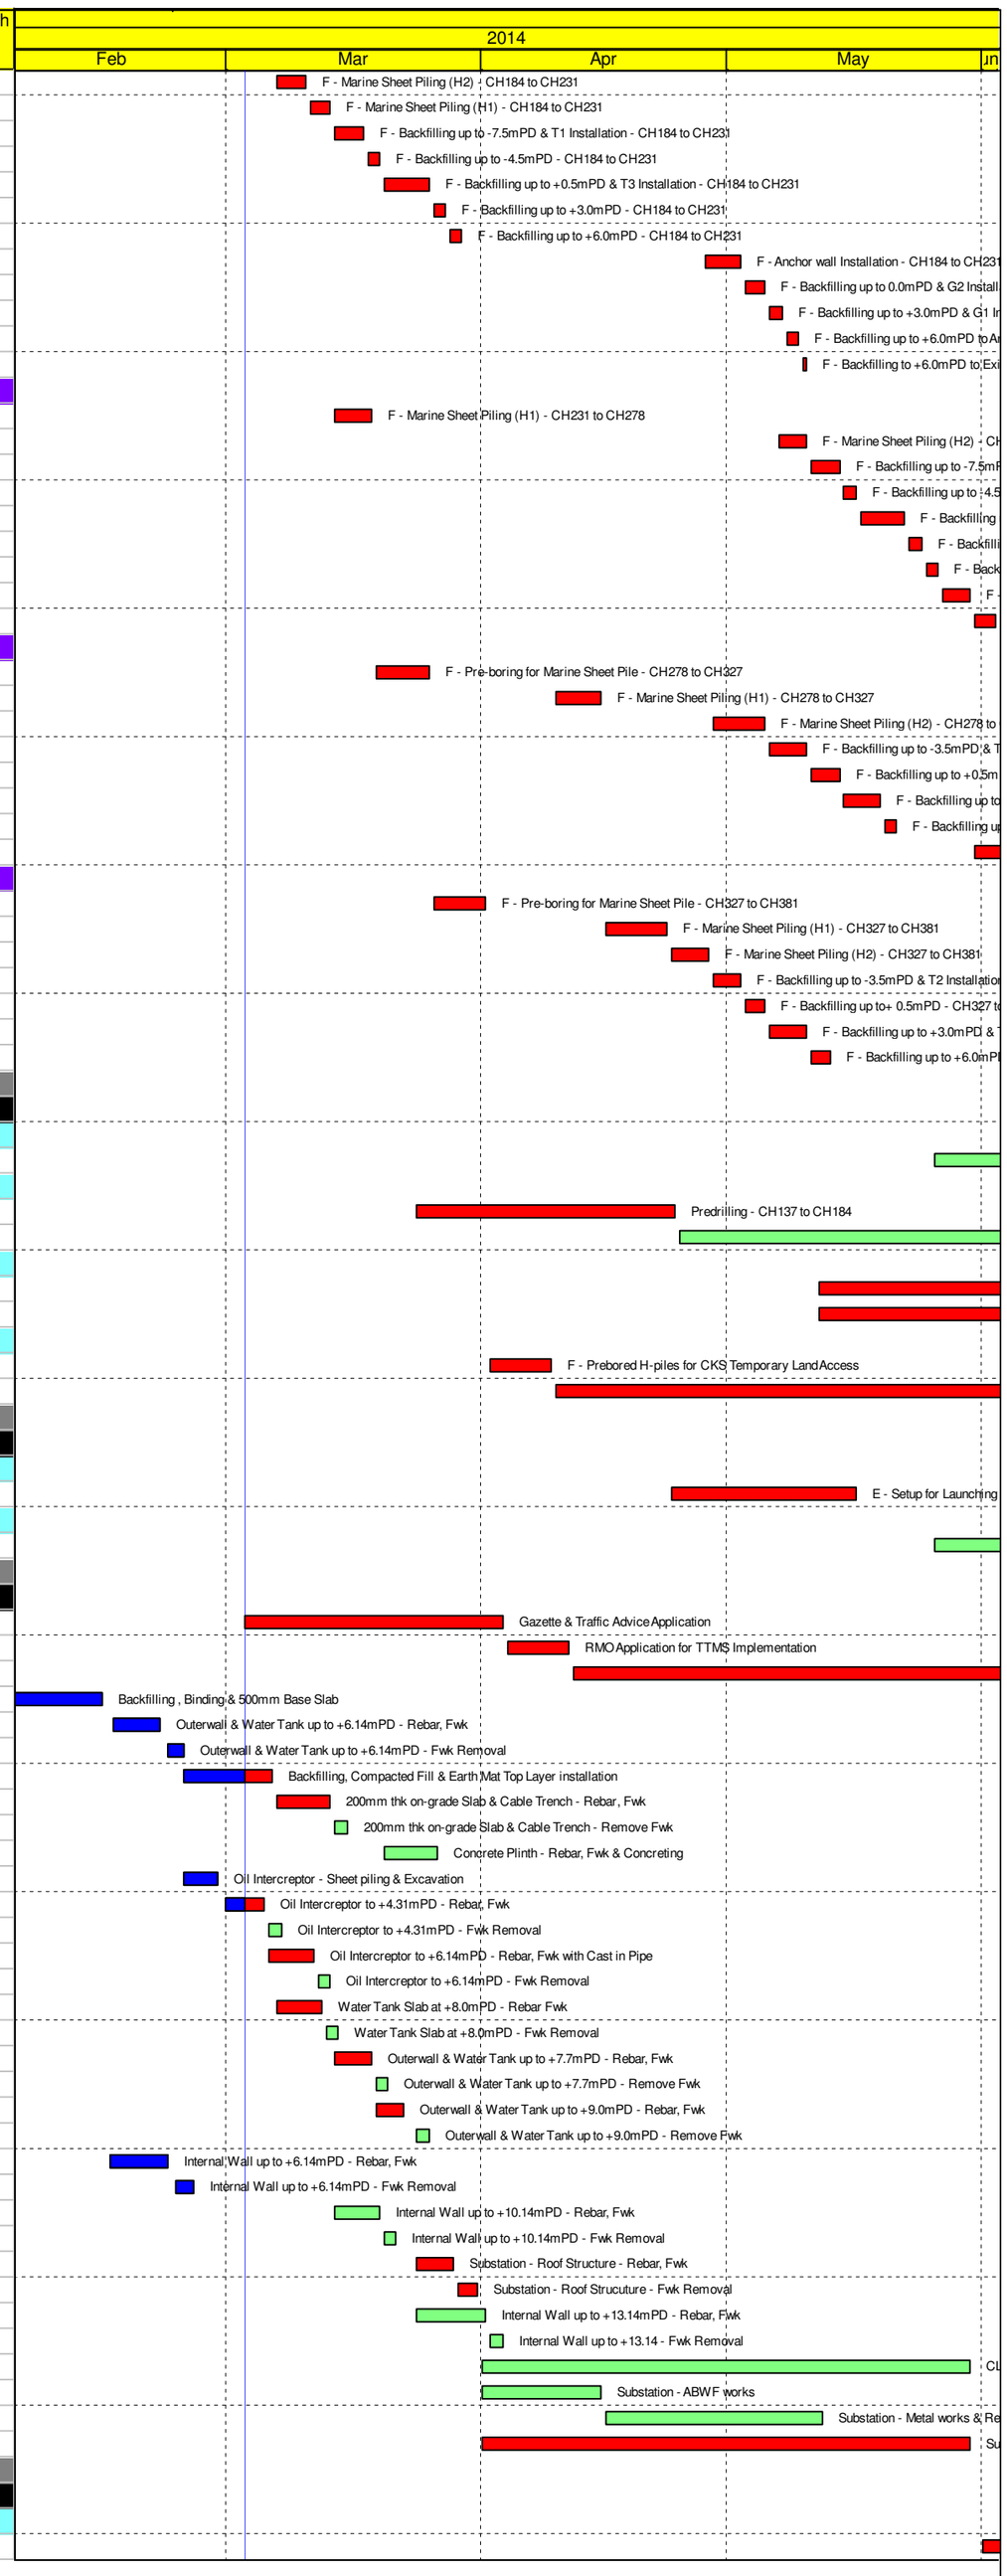

Project ID: TMCLK_I0.0-101 - B1-1 - B3-5 - B4-16

Data Date: 03-Mar-14

Current Bar
Current Bar - Critical
Planned Milestone
Current Milestone
Progress Bar
Progress Milestone

TMCLK - Northern Connection Sub-Sea Tunnel Section

3-Months Rolling Programme - Construction

As of 03-Mar-14 Progress

Dragages HongKong 香港寶嘉
A member of the Bouygues Construction group
BOUYGUES TRAVAUX PUBLICS
Dragages - Bouygues Joint Venture 寶嘉 - 布依格聯營

Date	Revision	Checked	Approved
21-Feb-14	TMCLK/DBJ/GEN/PRG/98505	SPa	WYu
